# SAVANNAH ARENA



## GMP AMENDMENT
## August 4, 2020

AECOM HUNT

*in association with*

Brownstone Construction Group
Pat Mathis Construction Company
A. Riley Consultants

# TABLE OF CONTENTS



## *GAURANTEED MAXIMUM PRICE*


| | |
|---|---|
| **SECTION 1** | Executive Summary |
| **SECTION 2** | GMP Estimate |
| **SECTION 3** | Disadvantaged Business Enterprise (DBE) Schedule of Values |
| **SECTION 4** | List of Contract Documents |
| **SECTION 5** | Clarifications and Qualifications |
| **SECTION 6** | Responsibility Matrix |
| **SECTION 7** | FFE Responsibility Matrix |
| **SECTION 8** | Schedule and Logistics |
| **SECTION 9** | VE Log |



AECOM HUNT

*in association with*

**Brownstone Construction Group**
**Pat Mathis Construction Company**
**A. Riley Consultants**

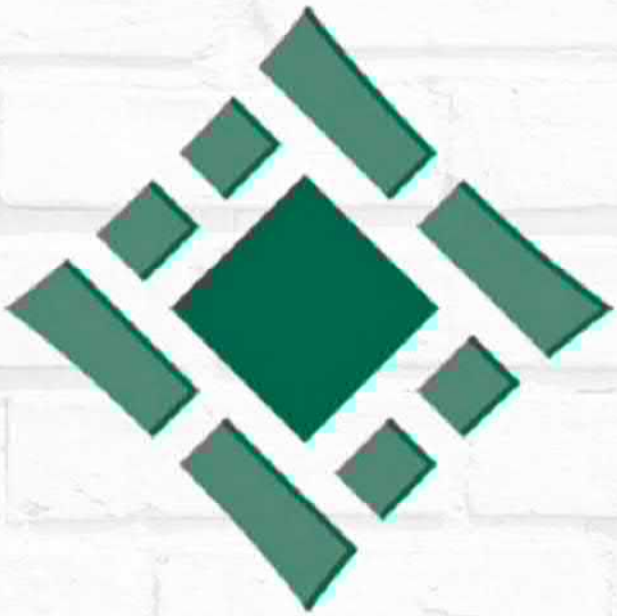

*Section 01*

# *Executive Summary*

AECOM HUNT

*in association with*

**Brownstone Construction Group**
**Pat Mathis Construction Company**
**A. Riley Consultants**

AECOM HUNT
in association with
Brownstone Construction Group
Pat Mathis Construction Company
A. Riley Consultants

August 4, 2020

Bret Bell
Mayor and Aldermen of the City of Savannah
2 East Bay St.
Savannah, GA 31401

Jim Curry
Jones Lang LaSalle Americas, Inc. (JLL)
3344 Peachtree Road NE, Suite 1100
Atlanta, GA 30326

RE: Savannah Arena
Savannah, GA
Hunt Project No. 00117400
GMP Amendment

AECOM Hunt, in association with Brownstone Construction Group, Pat Mathis Construction Company, and A. Riley Consultants, is pleased to submit its Guaranteed Maximum Price (GMP) proposal amendment for the Savannah Arena. This Guaranteed Maximum Price (GMP) was generated using the Construction Documents issued on February 17th, 2020, Stiles Avenue documents issued April 3, 2020, Savannah Arena Bulkhead documents issued February 12th, 2020, and Force Main documents issued April 14, 2020 as well as clarifications provided through the RFI process and review meetings, all of which are further detailed within this document.

For cost tracking purposes, and in order to accurately compare the current Arena estimate to the previous version, we have separated the estimate into the following sections:

- Arena (to the dripline)
- Sitework
- Stiles Avenue
- Lift Station and Force Main
- Savannah Arena Bulkhead (SAB)

Section 9 provides the Value Engineering Log, which contains some cost savings alternatives for the project team to consider with pricing valid until September 15, 2020. While we understand that some of these alternatives may not be implemented, we felt it prudent to include all options at this time.

We look forward to reviewing the estimate in greater detail with the overall project team. If you have any questions, please do not hesitate to contact me.

**HUNT CONSTRUCTION GROUP, INC.**

Wipperman, Patrick J.
Digitally signed by Wipperman, Patrick J.
DN: cn=Wipperman, Patrick J., ou=USNYC40
Date: 2020.08.05 13:02:30 -04'00'

**Patrick Wipperman**
Project Executive

AECOM Hunt
2450 South Tibbs Ave. Indianapolis, IN 46241
P 317.227.7800 • F 317.227.7830 • aecomhunt.com

*Section 02*

# *GMP Estimate*

AECOM HUNT

*in association with*

**Brownstone Construction Group**
**Pat Mathis Construction Company**
**A. Riley Consultants**

# Savannah Arena

Savannah, GA

Estimate Date: 08/04/20

Estimate Type: GMP

| | | Arena Costs | | | | | |
|---|---|---|---|---|---|---|---|
| | | Arena | Sitework | Stiles Avenue | Force Main | SAB | TOTAL |
| GSF | | 216,290 | 216,290 | 216,290 | 216,290 | 216,290 | 216,290 |
| LOA Authorized | | $80,108,446 | $2,791,255 | $0 | $0 | $0 | $82,899,701 |
| Bid Value | | $27,943,533 | $2,987,474 | $3,515,000 | $1,204,584 | $2,156,772 | $37,807,363 |
| Estimated Trade Cost | | $4,087,999 | $500,000 | $150,000 | $434,750 | $0 | $5,172,749 |
| Design Estimate Contingency | | $0 | $0 | $0 | $0 | $0 | $0 |
| TOTAL TRADE COST | | $112,139,978 | $6,278,729 | $3,665,000 | $1,639,334 | $2,156,772 | $125,879,813 |
| Construction Cost | | | | | | | |
| Subcontractor Bonds (In Trade Cost) | | $0 | $0 | $0 | $0 | $0 | $0 |
| CM Contingency | 2.25% | $2,523,150 | $141,271 | $82,463 | $36,885 | $48,527 | $2,832,296 |
| Management General Conditions | | $7,015,436 | | | | | $7,015,436 |
| Non-Management General Conditions | | $2,331,684 | | | | | $2,331,684 |
| General Liability | 0.70% | $910,108 | $46,899 | $27,376 | $12,245 | $16,110 | $1,012,737 |
| Bonding | 0.80% | $1,040,123 | $53,598 | $31,286 | $13,994 | $18,411 | $1,157,414 |
| SUBTOTAL CONSTRUCTION COST | | $13,820,501 | $241,769 | $141,124 | $63,124 | $83,049 | $14,349,566 |
| TOTAL CONSTRUCTION COST BEFORE FEE | | $125,960,479 | $6,520,498 | $3,806,124 | $1,702,458 | $2,239,821 | $140,229,379 |
| CM Base Fee | 2.75% | $3,463,913 | $179,314 | $104,668 | $46,818 | $61,595 | $3,856,308 |
| Preconstruction Management Fee | | $591,011 | | | | | $591,011 |
| TOTAL CONSTRUCTION COST ARENA | | $130,015,403 | $6,699,811 | $3,910,793 | $1,749,276 | $2,301,416 | $144,676,698 |
| OCOs 001 and 002 | | $865,574 | | | | | $865,574 |
| Pending PCI's | | $579,689 | | | | | $579,689 |
| TOTAL CONSTRUCTION COST ARENA with PCI's | | $131,460,666 | $6,699,811 | $3,910,793 | $1,749,276 | $2,301,416 | $146,121,961 |
| Owner Contingency | 1.00% | | | | | | $1,461,220 |
| GMP Value with Owner Contingency | | | | | | | $147,583,181 |

AECOM HUNT

**AECOM Hunt**

# *GMP - Recap*

## Savannah Arena

**Savannah, GA**

Project Size: 216290 GSF  9000 Seats

Estimate Date: 08/04/2020
Print Date: 8/5/2020


| Description | Total $ | $/ GSF | $ / Seats | % of Est |
|---|---|---|---|---|
| **A Arena** | **112,139,978** | **518.47** | **12,460** | **89.08%** |
| 01X General Requirements | 5,749,046 | 26.58 | 638.78 | 4.57% |
| 03A Concrete | 4,828,193 | 22.32 | 536.47 | 3.84% |
| 03C Structural Precast Stadia | 3,304,462 | 15.28 | 367.16 | 2.63% |
| 04A Masonry | 3,024,404 | 13.98 | 336.04 | 2.40% |
| 05A Structural Steel | 14,385,090 | 66.51 | 1,598 | 11.43% |
| 05C Metal Railings | 2,316,046 | 10.71 | 257.34 | 1.84% |
| 05D Misc Metal | 600,000 | 2.77 | 66.67 | 0.48% |
| 06A Architectural Woodwork | 1,978,560 | 9.15 | 219.84 | 1.57% |
| 07A Roofing | 2,419,350 | 11.19 | 268.82 | 1.92% |
| 07B Curtainwall & Interior Glazing | 4,156,358 | 19.22 | 461.82 | 3.30% |
| 07C Joint Sealants | 949,154 | 4.39 | 105.46 | 0.75% |
| 07D Spray Fireproofing | 1,148,360 | 5.31 | 127.60 | 0.91% |
| 07E Metal Panels | 2,173,800 | 10.05 | 241.53 | 1.73% |
| 08B Overhead Doors | 141,101 | 0.65 | 15.68 | 0.11% |
| 08C Doors Frames & Hardware | 776,557 | 3.59 | 86.28 | 0.62% |
| 09A Exterior Stud Framing | 2,268,820 | 10.49 | 252.09 | 1.80% |
| 09B Interior Drywall & Ceilings | 6,454,199 | 29.84 | 717.13 | 5.13% |
| 09C Tile and Stone | 1,092,632 | 5.05 | 121.40 | 0.87% |
| 09D Resilient, Carpet, Base | 359,864 | 1.66 | 39.98 | 0.29% |
| 09F Polished Concrete Flooring | 258,018 | 1.19 | 28.67 | 0.20% |

## Savannah Arena

**Savannah, GA**

Project Size: 216290 GSF 9000 Seats

Estimate Date: 08/04/2020
Print Date: 8/5/2020


| Description | Total $ | $/ GSF | $ / Seats | % of Est |
|---|---|---|---|---|
| 09G Painting and Wallcovering | 950,808 | 4.40 | 105.65 | 0.76% |
| 09H Epoxy Flooring | 193,531 | 0.89 | 21.50 | 0.15% |
| 10A Div 10 Specialties | 706,682 | 3.27 | 78.52 | 0.56% |
| 10B Signage | 1,350,000 | 6.24 | 150.00 | 1.07% |
| 11B Food Service Equipment | 2,712,301 | 12.54 | 301.37 | 2.15% |
| 11C Scoreboards / Video Boards | 2,182,265 | 10.09 | 242.47 | 1.73% |
| 12A Blackout / House Curtains | 724,116 | 3.35 | 80.46 | 0.58% |
| 12C Seating | 2,957,324 | 13.67 | 328.59 | 2.35% |
| 13A Ice Rink System | 2,917,000 | 13.49 | 324.11 | 2.32% |
| 14A Vertical Transportation | 882,520 | 4.08 | 98.06 | 0.70% |
| 21A Fire Protection | 1,388,182 | 6.42 | 154.24 | 1.10% |
| 22A Plumbing | 5,355,000 | 24.76 | 595.00 | 4.25% |
| 23A HVAC | 12,658,000 | 58.52 | 1,406 | 10.06% |
| 26B Electrical & Fire Alarm | 12,065,205 | 55.78 | 1,341 | 9.58% |
| 26D Sports Lighting | 725,000 | 3.35 | 80.56 | 0.58% |
| 27A Low Voltage Telecom, Sec, Data, etc. | 3,998,780 | 18.49 | 444.31 | 3.18% |
| 31B Piles / Deep Foundations | 1,989,250 | 9.20 | 221.03 | 1.58% |
| **B Sitework** | **6,278,729** | **29.03** | **697.64** | **4.99%** |
| 01X General Requirements | | | | |
| 02D Demolition | 342,210 | 1.58 | 38.02 | 0.27% |
| 31A Sitework / Site Utilities | 2,499,045 | 11.55 | 277.67 | 1.99% |
| 32A Landscape | 775,968 | 3.59 | 86.22 | 0.62% |
| 32B Hardscape | 2,661,506 | 12.31 | 295.72 | 2.11% |

## Savannah Arena

**Savannah, GA**

Project Size: 216290 GSF 9000 Seats

Estimate Date: 08/04/2020
Print Date: 8/5/2020


| Description | Total $ | $/ GSF | $ / Seats | % of Est |
|---|---|---|---|---|
| **C Stiles Avenue** | **3,665,000** | **16.94** | **407.22** | **2.91%** |
| **01X General Requirements** | | | | |
| **31C Stiles Ave Widening** | **3,665,000** | **16.94** | **407.22** | **2.91%** |
| **D Arena Bulkhead** | **2,156,772** | **9.97** | **239.64** | **1.71%** |
| **35A Canal Widening** | **2,156,772** | **9.97** | **239.64** | **1.71%** |
| **E Lift Station and Force Main** | **1,639,334** | **7.58** | **182.15** | **1.30%** |
| **01X General Requirements** | | | | |
| **31D Force Main** | **1,639,334** | **7.58** | **182.15** | **1.30%** |
| ***ESTIMATE TOTAL*** | **$125,879,813** | **582.00** | **13,987** | **100.00%** |

*Section 03*

# *Disadvantaged Business Enterprise (DBE) Schedule of Values*

AECOM HUNT

*in association with*

Brownstone Construction Group
Pat Mathis Construction Company
A. Riley Consultants

AECOM HUNT

*in association with*

**Brownstone Construction Group**
**Pat Mathis Construction Company**
**A. Riley Consultants**

| | | | | Bid Pacakage DBE Participation | | | | | | | | Bid Package LOCAL Participation | | | | | |
|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|
| Contract ID | Savannah Arena Project<br>DBE/LDBE & LOCAL TRACKING | | | Potential Overall DBE Participation | | Potential L/DBE Participation | | Potential Chatham/DBE County Participation | | Potential MSA/DBE Participation | | Potential Local Savannah Participation | | Potential Chatham County Participation | | Potential MSA Participation | |
| Total Awards | $125,820,313 | Status | Scope of Work | $ 32,859,634.83 | 26.1% | $ 16,228,148 | 12.9% | $ 16,754,657 | 13.3% | $ 17,197,572 | 13.7% | $ 29,496,367 | 23.4% | $ 31,910,569 | 25.4% | $ 32,399,778 | 25.8% |
| | | | | Dollars | % | Dollars | % | Dollars | % | Dollars | % | Dollars | % | Dollars | % | Dollars | % |
| | General Services | | | | | | | | | | | | | | | | |
| | Image Keepers | Contracted | Trailer Janitorial | $ 700.00 | | $ 700 | | $ 700 | | $ 700 | | $ 700 | | $ 700 | | $ 700 | |
| | B and B Demolition | Contracted | Groundbreaking | $ 6,100.00 | | $ 6,100 | | $ 6,100 | | $ 6,100 | | $ 6,100 | | $ 6,100 | | $ 6,100 | |
| | B and B Demolition | Contracted | Temp Trailer set up | $ 17,414.00 | | $ 17,414 | | $ 17,414 | | $ 17,414 | | $ 17,414 | | $ 17,414 | | $ 17,414 | |
| | Staples | Contracted | Office Supplies | | | | | | | | | $ 75 | | $ 75 | | $ 75 | |
| | Home Depot | Contracted | Job Site Supplies | | | | | | | | | $ 1,127 | | $ 1,127 | | $ 1,127 | |
| | Clayton Digital | Contracted | Print Services | | | | | | | | | | | $ 7,219 | | $ 7,219 | |
| | Event Works Rental | Contracted | Events | | | | | | | | | | | $ 736 | | $ 736 | |
| | ABC Waste of Savannah | Contracted | Dumpsters | | | | | | | | | $ 200 | | $ 200 | | $ 200 | |
| | Multivista | Contracted | Time Lapse Photos | | | | | | | | | $ 940 | | $ 940 | | $ 940 | |
| | Williams Scotsman | Contracted | Office Trailers | | | | | | | | | $ 25,432 | | $ 166,158 | | $ 166,158 | |
| | Republic Services | Contracted | Trash | | | | | | | | | | | $ 56,472 | | $ 56,472 | |
| | Diamond Concrete | Contracted | Concrete | | | | | | | | | | | | | $ 43,294 | |
| | | | | | | | | | | | | | | | | | |
| 01B | BP-01B Site Security | Within GMP | | | | | | | | | | | | | | | |
| | PENDING AWARD | | Site Security | TBD | TBD | TBD | TBD | TBD | TBD | TBD | TBD | TBD | TBD | TBD | TBD | TBD | TBD |
| | Hourly Contract $TBD at completion | | | | | | | | | | | | | | | | |
| 02D | BP- 02D Site Fence and Demolition | Contracted | | | | | | | | | | | | | | | |
| | ALS Sand Hill Construction | | Prime | $ 324,210 | 95% | ~ | ~ | $ 324,210 | 95% | $ 324,210 | 95% | ~ | ~ | $ 324,210 | 95% | $ 324,210 | 95% |
| | PT Construction | | hauling and demo | $ 18,000 | 5% | $ 18,000 | 5% | $ 18,000 | 5% | $ 18,000 | 5% | $ 18,000 | 5% | $ 18,000 | 5% | $ 18,000 | 5% |
| | $342,210 | | | | | | | | | | | | | | | | |
| 03A | BP- 03A Concrete Structure | Contracted | | | | | | | | | | | | | | | |
| | Precision Concrete | | Prime | | | | | | | | | | | | | | |
| | Technique Concrete | | Turn Key Slab Concrete | $ 1,090,489 | 25% | | | | | | | | | | | | |
| | $4,381,957 | | | | | | | | | | | | | | | | |
| 03C | BP- 03C Precast | Contracted | | | | | | | | | | | | | | | |
| | Metromont | | Prime | | | | | | | | | | | | | | |
| | Cardinal Transportation | | Trucking | $ 264,875 | 8% | | | | | | | | | | | | |
| | $3,304,462 | | | | | | | | | | | | | | | | |
| 04A/04B | BP- 04A Interior/Exterior Masonry | Within GMP | | | | | | | | | | | | | | | |
| | PENDING AWARD | | Prime | | | | | | | | | | | | | | |
| | PENDING AWARD | | Labor/Staffing | $ 53,539 | 2% | $ 53,539 | 2% | $ 53,539 | 2% | $ 53,539 | 2% | $ 53,539 | 2% | $ 53,539 | 2% | $ 53,539 | 2% |
| | PENDING AWARD | | Carpentry/DF install | $ 1,070,785 | 36% | $ 1,070,785 | 36% | $ 1,070,785 | 36% | $ 1,070,785 | 36% | $ 1,070,785 | 36% | $ 1,070,785 | 36% | $ 1,070,785 | 36% |
| | PENDING AWARD | | Turnkey Masonry | $ 211,183 | 7% | $ 211,183 | 7% | $ 211,183 | 7% | $ 211,183 | 7% | $ 211,183 | 7% | $ 211,183 | 7% | $ 211,183 | 7% |
| | PENDING AWARD | | Turnkey Masonry | $ 264,722 | 9% | $ 264,722 | 9% | $ 264,722 | 9% | $ 264,722 | 9% | $ 264,722 | 9% | $ 264,722 | 9% | $ 264,722 | 9% |
| | $2,974,404 | | | | | | | | | | | | | | | | |
| 05A | BP- 05A Structural Steel | Contracted | | | | | | | | | | | | | | | |
| | Banker Steel | | Prime | | | | | | | | | | | | | | |
| | Commercial Fabricators, Inc. | | Fabrication | $ 225,187 | 2% | | | | | | | | | | | | |
| | Commercial Fabricators, Inc. | | Misc. Steel | $ 1,280,437 | 10% | | | | | | | | | | | | |
| | Commercial Fabricators, Inc. | | Material Supplier | $ 1,800,630 | 14% | | | | | | | | | | | | |
| | $12,950,000 | | | | | | | | | | | | | | | | |
| 05C | BP- 05C Metal Railings | Within GMP | | | | | | | | | | | | | | | |
| | PENDING AWARD | | Prime | | | | | | | | | | | | | | |
| | PENDING AWARD | | Installation | $ 500,000 | 23% | | | | | | | | | | | | |
| | $2,176,930 | | | | | | | | | | | | | | | | |
| 05D | BP-05D Misc.Metals | Contracted | | | | | | | | | | | | | | | |

AECOM HUNT

*in association with*

**Brownstone Construction Group**
**Pat Mathis Construction Company**
**A. Riley Consultants**

| | | | | Bid Pacakage DBE Participation | | | | | | | | Bid Package LOCAL Participation | | | | | |
|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|
| Contract ID | Savannah Arena Project<br>DBE/LDBE & LOCAL TRACKING | | | Potential Overall DBE Participation | | Potential L/DBE Participation | | Potential Chatham/DBE County Participation | | Potential MSA/DBE Participation | | Potential Local Savannah Participation | | Potential Chatham County Participation | | Potential MSA Participation | |
| Total Awards | $125,820,313 | Status | Scope of Work | $ 32,859,634.83 | 26.1% | $ 16,228,148 | 12.9% | $ 16,754,657 | 13.3% | $ 17,197,572 | 13.7% | $ 29,496,367 | 23.4% | $ 31,910,569 | 25.4% | $ 32,399,778 | 25.8% |
| | | | | Dollars | % | Dollars | % | Dollars | % | Dollars | % | Dollars | % | Dollars | % | Dollars | % |
| | Banker Steel | | Prime | | | | | | | | | | | | | | |
| | Commercial Fabricators, Inc. | | Fabrication | $ 351,996 | 39% | | | | | | | | | | | | |
| | $900,000 | | | | | | | | | | | | | | | | |
| 06A | BP- 06A Architectural Woodwork | Within GMP | | | | | | | | | | | | | | | |
| | PENDING AWARD | | Prime | | | | | | | | | | | | | | |
| | PENDING AWARD | | Material | $ 560,419 | 28% | $ 560,419 | 28% | $ 560,419 | 28% | $ 560,419 | 28% | $ 560,419 | 28% | $ 560,419 | 28% | $ 560,419 | 28% |
| | PENDING AWARD | | Labor | $ 19,605 | 1% | $ 19,605 | 1% | $ 19,605 | 1% | $ 19,605 | 1% | $ 19,605 | 1% | $ 19,605 | 1% | $ 19,605 | 1% |
| | $1,978,560 | | | | | | | | | | | | | | | | |
| 07A | BP- 07A Roofing | Within GMP | | | | | | | | | | | | | | | |
| | PENDING AWARD | | Prime | | | | | | | | | | | | | | |
| | PENDING AWARD | | Material | $ 200,000 | 8% | $ 200,000 | 8% | $ 200,000 | 8% | $ 200,000 | 8% | $ 200,000 | 8% | $ 200,000 | 8% | $ 200,000 | 8% |
| | $2,419,350 | | | | | | | | | | | | | | | | |
| 07B | BP- 07B Curtain Wall, Storefront, Glass & Glazing | Contracted | | | | | | | | | | | | | | | |
| | Crown Corr | | Prime | | | | | | | | | | | | | | |
| | EGM | | Glass & Glazing | $ 388,136 | 10% | | | | | | | | | | | | |
| | DFH and Associates, LLC | | Doors, Harware & Glass | $ 582,204 | 15% | $ 582,204 | 15% | $ 582,204 | 15% | $ 582,204 | 15% | $ 582,204 | 15% | $ 582,204 | 15% | $ 582,204 | 15% |
| | $3,881,358 | | | | | | | | | | | | | | | | |
| 07C | BP- 07C Waterproofing | Within GMP | | | | | | | | | | | | | | | |
| | PENDING AWARD | | Prime | | | | | | | | | | | | | | |
| | PENDING AWARD | | Floor Caulking | $ 122,813 | 14% | | | | | | | | | | | | |
| | PENDING AWARD | | Caulking | $ 81,876 | 10% | $ 81,876 | 10% | $ 81,876 | 10% | $ 81,876 | 10% | $ 81,876 | 10% | $ 81,876 | 10% | $ 81,876 | 10% |
| | $849,154 | | | | | | | | | | | | | | | | |
| 07D | BP- 07D Spray Fireproofing | Within GMP | | | | | | | | | | | | | | | |
| | PENDING AWARD | | Prime | | | | | | | | | | | | | | |
| | PENDING AWARD | | Turnkey Painting | $ 274,590 | 25% | | | | | | | | | | | | |
| | $1,098,360 | | | | | | | | | | | | | | | | |
| 07E | BP- 07E Metal Panels | Contracted | | | | | | | | | | | | | | | |
| | Kistler McDougall | | Prime | | | | | | | | | | | | | | |
| | 360 Specialties | | Installation | $ 192,863 | 9% | | | | | | | | | | | | |
| | $2,073,800 | | | | | | | | | | | | | | | | |
| 08B | BP- 08B Overhead Doors and Loading Dock Equipment | Within GMP | | | | | | | | | | | | | | | |
| | PENDING AWARD | | Prime | | | | | | | | | | | | | | |
| | PENDING AWARD | | Installation | $ 6,525 | 5% | $ 6,525 | 5% | $ 6,525 | 5% | $ 6,525 | 5% | $ 6,525 | 5% | $ 6,525 | 5% | $ 6,525 | 5% |
| | $141,101 | | | | | | | | | | | | | | | | |
| 08D | BP-08D Doors, Frames, Hardware | Contracted | | | | | | | | | | | | | | | |
| | DFH and Associates | | Prime | $ 599,636 | 100% | $ 599,636 | 100% | $ 599,636 | 100% | $ 599,636 | 100% | $ 599,636 | 100% | $ 599,636 | 100% | $ 599,636 | 100% |
| | $599,636 | | | | | | | | | | | | | | | | |
| 09A | BP- 09A Exterior Framing | Contracted | | | | | | | | | | | | | | | |
| | Colby Enterprises | | Prime | | | | | | | | | | | | | | |
| | A1 Staffing | | Labor | $ 22,688 | 1% | $ 22,688 | 1% | $ 22,688 | 1% | $ 22,688 | 1% | $ 22,688 | 1% | $ 1,701,616 | 75% | $ 1,701,616 | 75% |
| | 360 Specialties | | Turnkey Installation | $ 476,452 | 21% | | | | | | | | | $ 22,688 | 1% | $ 22,688 | 1% |
| | Ivy League Maintenance, LLC League | | Turnkey Installation | $ 68,064 | 3% | $ 68,064 | 3% | $ 68,064 | 3% | $ 68,064 | 3% | $ 68,064 | 3% | $ 68,064 | 3% | $ 68,064 | 3% |
| | $2,268,820 | | | | | | | | | | | | | | | | |
| 09B | BP- 09B Drywall and Ceiling | Within GMP | | | | | | | | | | | | | | | |

AECOM HUNT

*in association with*

**Brownstone Construction Group**
**Pat Mathis Construction Company**
**A. Riley Consultants**

| | | | | Bid Pacakage DBE Participation | | | | | | | | Bid Package LOCAL Participation | | | | | |
|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|
| Contract ID | Savannah Arena Project<br>DBE/LDBE & LOCAL TRACKING | | | Potential Overall DBE Participation | | Potential L/DBE Participation | | Potential Chatham/DBE County Participation | | Potential MSA/DBE Participation | | Potential Local Savannah Participation | | Potential Chatham County Participation | | Potential MSA Participation | |
| Total Awards | $125,820,313 | Status | Scope of Work | $ 32,859,634.83 | 26.1% | $ 16,228,148 | 12.9% | $ 16,754,657 | 13.3% | $ 17,197,572 | 13.7% | $ 29,496,367 | 23.4% | $ 31,910,569 | 25.4% | $ 32,399,778 | 25.8% |
| | | | | Dollars | % | Dollars | % | Dollars | % | Dollars | % | Dollars | % | Dollars | % | Dollars | % |
| | PENDING AWARD | | Prime | $6,945,000 | 100% | | | | | | | | | | | | |
| | $6,945,000 | | | | | | | | | | | | | | | | |
| 09C | BP- 09C Tile | Within GMP | | | | | | | | | | | | | | | |
| | PENDING AWARD | | Prime | | | | | | | | | | | | | | |
| | PENDING AWARD | | Turnkey Installation | $ 180,000 | 18% | | | | | | | | | | | | |
| | $992,632 | | | | | | | | | | | | | | | | |
| 09D | BP- 09D Carpet and Resilient Flooring | Within GMP | | | | | | | | | | | | | | | |
| | PENDING AWARD | | Prime | | | | | | | | | | | | | | |
| | PENDING AWARD | | Turnkey Installtion | $ 77,466 | 25% | $ 77,466 | 25% | $ 77,466 | 25% | $ 77,466 | 25% | $ 77,466 | 25% | $ 77,466 | 25% | $ 77,466 | 25% |
| | $309,864 | | | | | | | | | | | | | | | | |
| 09F | BP- 09F Polished Concrete | Within GMP | | | | | | | | | | | | | | | |
| | PENDING AWARD | | Prime | | | | | | | | | | | | | | |
| | PENDING AWARD | | Turnkey Installation | $ 52,005 | 25% | | | | | | | | | | | | |
| | $208,018 | | | | | | | | | | | | | | | | |
| 09G | BP- 09G Painting | Within GMP | | | | | | | | | | | | | | | |
| | PENDING AWARD | | Prime | | | | | | | | | | | | | | |
| | PENDING AWARD | | Turnkey Installtion | $ 127,621 | 15% | $ 127,621 | 15% | $ 127,621 | 15% | $ 127,621 | 15% | $ 127,621 | 15% | $ 127,621 | 15% | $ 127,621 | 15% |
| | $850,808 | | | | | | | | | | | | | | | | |
| 10A | BP- 10A Specialties | Within GMP | | | | | | | | | | | | | | | |
| | PENDING AWARD | | Prime | | | | | | | | | | | | | | |
| | PENDING AWARD | | Turnkey Installation | $ 129,571 | 20% | | | | | | | | | | | | |
| | PENDING AWARD | | Material Supply | $ 32,393 | 5% | | | | | | | | | | | | |
| | PENDING AWARD | | Labor Supply | $ 12,957 | 2% | $ 12,957 | 2% | $ 12,957 | 2% | $ 12,957 | 2% | $ 12,957 | 2% | $ 12,957 | 2% | $ 12,957 | 2% |
| | $647,854 | | | | | | | | | | | | | | | | |
| 10B | BP- 10B Signage | OWNER ALLOWANCE ONLY | | | | | | | | | | | | | | | |
| 11B | BP- 11B Food Service Equipment | Contracted | | | | | | | | | | | | | | | |
| | Johnson-Landcaster | | Prime | | | | | | | | | | | | | | |
| | S&S Supply II, Inc. | | Material Supply | $ 678,075 | 25% | $ 678,075 | 25% | $ 678,075 | 25% | $ 678,075 | 25% | $ 678,075 | 25% | $ 678,075 | 25% | $ 678,075 | 25% |
| | $2,712,301 | | | | | | | | | | | | | | | | |
| 11C | BP- 11C Scoreboards and Video | Contracted | | | | | | | | | | | | | | | |
| | Daktronics | | Prime | | | | | | | | | | | | | | |
| | Cyntech | | Turnkey Installation | $ 161,504 | 8% | $ 161,504 | 8% | $ 161,504 | 8% | $ 161,504 | 8% | $ 161,504 | 8% | $ 161,504 | 8% | $ 161,504 | 8% |
| | $2,096,801 | | | | | | | | | | | | | | | | |
| ~~11D~~ | ~~BP- 11D Fall Arrest Systems~~ | ~~BY OWNER~~ | | | | | | | | | | | | | | | |
| 12A | BP- 12A Arena Curtains | Within GMP | | | | | | | | | | | | | | | |
| | PENDING AWARD | | Prime | | | | | | | | | | | | | | |
| | PENDING AWARD | | Turnkey Installation | $ 145,299 | 22% | $ 145,299 | 22% | $ 145,299 | 22% | $ 145,299 | 22% | $ 145,299 | 22% | $ 145,299 | 22% | $ 145,299 | 22% |
| | $655,045 | | | | | | | | | | | | | | | | |
| 12C | BP- 12C Seating | Within GMP | | | | | | | | | | | | | | | |
| | PENDING AWARD | | Prime | | | | | | | | | | | | | | |
| | PENDING AWARD | | Labor | $ 83,300 | 3% | $ 83,300 | 3% | $ 83,300 | 3% | $ 83,300 | 3% | $ 83,300 | 3% | $ 83,300 | 3% | $ 83,300 | 3% |
| | PENDING AWARD | | Turnkey Installation | $ 22,970 | 1% | $ 22,970 | 1% | $ 22,970 | 1% | $ 22,970 | 1% | $ 22,970 | 1% | $ 22,970 | 1% | $ 22,970 | 1% |
| | PENDING AWARD | | Turnkey Installation | $ 158,631 | 5% | | | | | | | | | | | | |

AECOM HUNT

*in association with*

**Brownstone Construction Group**
**Pat Mathis Construction Company**
**A. Riley Consultants**

| | | | | Bid Pacakage DBE Participation | | | | | | | | Bid Package LOCAL Participation | | | | | |
|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|
| Contract ID | Savannah Arena Project<br>DBE/LDBE & LOCAL TRACKING | | | Potential Overall DBE Participation | | Potential L/DBE Participation | | Potential Chatham/DBE County Participation | | Potential MSA/DBE Participation | | Potential Local Savannah Participation | | Potential Chatham County Participation | | Potential MSA Participation | |
| Total Awards | $125,820,313 | Status | Scope of Work | $ 32,859,634.83 | 26.1% | $ 16,228,148 | 12.9% | $ 16,754,657 | 13.3% | $ 17,197,572 | 13.7% | $ 29,496,367 | 23.4% | $ 31,910,569 | 25.4% | $ 32,399,778 | 25.8% |
| | | | | Dollars | % | Dollars | % | Dollars | % | Dollars | % | Dollars | % | Dollars | % | Dollars | % |
| | PENDING AWARD | | Freight | $ 71,400 | 2% | | | | | | | | | | | | |
| | $2,931,324 | | | | | | | | | | | | | | | | |
| 13A | BP- 13A Ice Rink System | Contracted | | | | | | | | | | | | | | | |
| | Cimco | | Prime | | | | | | | | | | | | | | |
| | S&S Supply II, Inc. | | Material Supply | $ 109,400 | 5% | $ 109,400 | 5% | $ 109,400 | 5% | $ 109,400 | 5% | $ 109,400 | 5% | $ 109,400 | | $ 109,400 | 5% |
| | $1,995,000 | | | | | | | | | | | | | | | | |
| 14A | BP- 14A Vertical Transportation | Contracted | | | | | | | | | | | | | | | |
| | Schindler | | Prime | | | | | | | | | | | | | | |
| | Anything Logistics | | Freight | $ 25,777 | 3% | | | $ 25,777 | 3% | $ 25,777 | 3% | | | $ 25,777 | 3% | $ 25,777 | 3% |
| | $880,000 | | | | | | | | | | | | | | | | |
| 21A | BP- 21A Fire Protection | Contracted | | | | | | | | | | | | | | | |
| | Northstar Fire Protection | | Prime | | | | | | | | | | | | | | |
| | Prayor Fire Protection | | Turnkey Installation | $ 214,109 | 16% | | | | | | | | | | | | |
| | A-1 Staffing | | Labor | $ 26,764 | 2% | $ 26,764 | 2% | $ 26,764 | 2% | $ 26,764 | 2% | $ 26,764 | 2% | $ 26,764 | 2% | $ 26,764 | 2% |
| | Adjacent Solutions | | Labor | $ 26,764 | 2% | $ 26,764 | 2% | $ 26,764 | 2% | $ 26,764 | 2% | $ 26,764 | 2% | $ 26,764 | 2% | $ 26,764 | 2% |
| | $1,338,182 | | | | | | | | | | | | | | | | |
| 22A | BP- 22A Plumbing | Contracted | | | | | | | | | | | | | | | |
| | Campbell Plumbing | | Prime | | | | | | | | | | | | | | |
| | S&S Supply II, Inc. | | Material Supply | $ 1,425,000 | 25% | $ 1,425,000 | 25% | $ 1,425,000 | 25% | $ 1,425,000 | 25% | $ 1,425,000 | 25% | $ 1,425,000 | 25% | $ 1,425,000 | 25% |
| | $5,700,000 | | | | | | | | | | | | | | | | |
| 23A | BP- 23A Mechanical | Contracted | | | | | | | | | | | | | | | |
| | Erickson and Associates | | Local | | | | | | | | | $ 9,100,000 | 73% | $ 9,100,000 | 73% | $ 9,100,000 | 73% |
| | Climate Control | | Turnkey Installation | $ 100,000 | 1% | | | $ 100,000 | 1% | $ 100,000 | 1% | | | $ 100,000 | 1% | $ 100,000 | 1% |
| | S&S Supply II, Inc. | | Material Supply | $ 3,300,000 | 26% | $ 3,300,000 | 26% | $ 3,300,000 | 26% | $ 3,300,000 | 26% | $ 3,300,000 | 26% | $ 3,300,000 | 26% | $ 3,300,000 | 26% |
| | $12,500,000 | | | | | | | | | | | | | | | | |
| 26B | BP- 26B Electrical & Fire Alarm | Contracted | | | | | | | | | | | | | | | |
| | Ace Electric | | Prime | | | | | | | | | | | | | | |
| | Cyntech | | Turnkey Installation | $ 3,159,000 | 27% | $ 3,159,000 | 27% | $ 3,159,000 | 27% | $ 3,159,000 | 27% | $ 3,159,000 | 27% | $ 3,159,000 | 27% | $ 3,159,000 | 27% |
| | $11,700,000 | | | | | | | | | | | | | | | | |
| 26D | BP- 26D Sports Lighting | Contracted | | | | | | | | | | | | | | | |
| | Musco | | Prime | | | | | | | | | | | | | | |
| | A1 Staffing | | Labor | $ 25,000 | 3.5% | $ 25,000 | 3.5% | $ 25,000 | 3.5% | $ 25,000 | 3.5% | $ 25,000 | 3.5% | $ 25,000 | 3.5% | $ 25,000 | 3.5% |
| | PT Construction | | Freight | $ 1,780 | 0.3% | $ 1,780 | 0.3% | $ 1,780 | 0.3% | $ 1,780 | 0.3% | $ 1,780 | 0.3% | $ 1,780 | 0.3% | $ 1,780 | 0.3% |
| | Paige Courier | | Freight | $ 1,780 | 0.3% | $ 1,780 | 0.3% | $ 1,780 | 0.3% | $ 1,780 | 0.3% | $ 1,780 | 0.3% | $ 1,780 | 0.3% | $ 1,780 | 0.3% |
| | B and B Demolition | | Freight | $ 1,780 | 0.3% | $ 1,780 | 0.3% | $ 1,780 | 0.3% | $ 1,780 | 0.3% | $ 1,780 | 0.3% | $ 1,780 | 0.3% | $ 1,780 | 0.3% |
| | $710,887 | | | | | | | | | | | | | | | | |
| 27A | BP- 27A Audio - Visual/Broadcast/PTV | Contracted | | | | | | | | | | | | | | | |
| | Baker | | Prime | | | | | | | | | | | | | | |
| | Cyntech | | Turnkey Installation | $ 203,320 | 10% | $ 203,320 | 10% | $ 203,320 | 10% | $ 203,320 | 10% | $ 203,320 | 10% | $ 203,320 | 10% | $ 203,320 | 10% |
| | $2,033,198 | | | | | | | | | | | | | | | | |
| 27B | BP- 27A Audio - Visual/Broadcast/PTV | Contracted | | | | | | | | | | | | | | | |
| | Net Planner | | Prime | | | | | | | | | | | | | | |
| | Cyntech | | Turnkey Installation | $ 428,896 | 25% | $ 428,896 | 25% | $ 428,896 | 25% | $ 428,896 | 25% | $ 428,896 | 25% | $ 428,896 | 25% | $ 428,896 | 25% |
| | $1,715,582 | | | | | | | | | | | | | | | | |
| 31A | BP- 31A Sitework & Site Utilities | Contracted | | | | | | | | | | | | | | | |

AECOM HUNT

*in association with*

**Brownstone Construction Group**
**Pat Mathis Construction Company**
**A. Riley Consultants**

| | | | | Bid Pacakage DBE Participation | | | | | | | | Bid Package LOCAL Participation | | | | | |
|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|
| Contract ID | Savannah Arena Project<br>DBE/LDBE & LOCAL TRACKING | | | Potential Overall DBE Participation | | Potential L/DBE Participation | | Potential Chatham/DBE County Participation | | Potential MSA/DBE Participation | | Potential Local Savannah Participation | | Potential Chatham County Participation | | Potential MSA Participation | |
| Total Awards | $125,820,313 | Status | Scope of Work | $ 32,859,634.83 | 26.1% | $ 16,228,148 | 12.9% | $ 16,754,657 | 13.3% | $ 17,197,572 | 13.7% | $ 29,496,367 | 23.4% | $ 31,910,569 | 25.4% | $ 32,399,778 | 25.8% |
| | | | | Dollars | % | Dollars | % | Dollars | % | Dollars | % | Dollars | % | Dollars | % | Dollars | % |
| | CA Murren | | Prime | | | | | | | | | $ 1,837,360 | 75% | $ 1,837,360 | 75% | $ 1,837,360 | 75% |
| | Frankie Thompson | | Material Supplier | $ 243,406 | 10% | $ 243,406 | 10% | $ 246,406 | 10% | $ 243,406 | 10% | $ 243,406 | 10% | $ 243,406 | 10% | $ 243,406 | 10% |
| | Scott and Sons | | Hauling | $ 436,210 | 18% | | | | | $ 436,210 | 18% | | | | | $ 436,210 | 18% |
| | LDM Trucking | | Hauling | TBD | TBD | | | $ 4,590 | 0.2% | $ 4,590 | 0.2% | | | $ 4,590 | 0.2% | $ 4,590 | 0.2% |
| | ED Trucking | | Hauling | $ 2,165 | 0.1% | $ 2,165 | 0.1% | $ 2,165 | 0.1% | $ 2,165 | 0.1% | $ 2,165 | 0.1% | $ 2,165 | 0.1% | $ 2,165 | 0.1% |
| | Candy Trucking | | Hauling | | | | | TBD | | TBD | | TBD | | TBD | | TBD | |
| | Flores Trucking | | Hauling | $ 4,900 | 0.2% | | | $ 4,900 | 0.2% | $ 4,900 | 0.2% | | | $ 4,900 | 0.2% | $ 4,900 | 0.2% |
| | Alex Montana,LLC | | Hauling | $ 5,946 | 0.2% | | | $ 5,946 | 0.2% | $ 5,946 | 0.2% | $ 5,946 | 0.2% | $ 5,946 | 0.2% | $ 5,946 | 0.2% |
| | Sabur Trucking | | Hauling | $ 10,131 | 0.4% | | | $ 10,131 | 0.4% | $ 10,131 | 0.4% | $ 10,131 | 0.4% | $ 10,131 | 0.4% | $ 10,131 | 0.4% |
| | $2,449,045 | | | | | | | | | | | | | | | | |
| 31B | BP- 31B Piles/Deep Foundations | Contracted | | | | | | | | | | | | | | | |
| | Morris Shea Bridge Co. | | Prime | | | | | | | | | | | | | | |
| | Associated Cost Engineers Inc. | | Material Supplier | $ 449,510 | 19% | | | | | | | | | | | | |
| | $2,319,350.00 | | | | | | | | | | | | | | | | |
| 31C | BP- 31C Stiles Avenue Widening ** | Contracted | | | | | | | | | | | | | | | |
| | APAC | | Prime | | | | | | | | | | | | | | |
| | Middle GA Signs | | Material Supply | $ 20,000 | 1% | | | | | | | | | | | | |
| | TJR Group | | Turnkey Install | $ 445,000 | 13% | | | | | | | | | | | | |
| | OIH Inc. | | Material Supply | $ 10,500 | 0.31% | | | | | | | | | | | | |
| | ED Trucking | | Hauling | $ 362,000 | 11% | $ 362,000 | 11% | $ 362,000 | 11.0% | $ 362,000 | 11% | $ 362,000 | 11% | $ 362,000 | 11% | $ 362,000 | 11.0% |
| | $3,349,750 | | | | | | | | | | | | | | | | |
| 31D | BP- 31D Force Main | Within GMP | | | | | | | | | | | | | | | |
| | PENDING AWARD | | Prime | | | | | | | | | $ 1,007,622 | 84% | $ 1,007,622 | 84% | $ 1,007,622 | 84% |
| | PENDING AWARD | | Material Supply | $ 98,481 | 8.2% | $ 108,413 | 9% | $ 108,413 | 9% | $ 108,413 | 9% | $ 108,413 | 9% | $ 108,413 | 9% | $ 108,413 | 9% |
| | PENDING AWARD | | Hauling | $ 87,225 | 7.2% | $ 87,225 | 7% | $ 87,225 | 7% | $ 87,225 | 7% | $ 87,225 | 7% | $ 87,225 | 7% | $ 87,225 | 7% |
| | PENDING AWARD | | Hauling | $ 7,145 | 0.6% | $ 7,145 | 1% | $ 7,145 | 1% | $ 7,145 | 1% | $ 7,145 | 1% | $ 7,145 | 1% | $ 7,145 | 1% |
| | PENDING AWARD | | Hauling | $ 3,385 | 0.3% | | | $ 3,385 | 0.3% | $ 3,385 | 0% | | | $ 3,385 | 0.3% | $ 3,385 | 0.3% |
| | PENDING AWARD | | Turnkey Installation | $ 12,218 | 1.0% | | | $ 12,218 | 1% | $ 12,218 | 1% | | | $ 12,218 | 1% | $ 12,218 | 1% |
| | PENDING AWARD | | Turnkey Installation | $ 98,481 | 8.2% | $ 98,481 | 8% | $ 98,481 | 8% | $ 98,481 | 8% | $ 98,481 | 8% | $ 98,481 | 8% | $ 98,481 | 8% |
| | $1,204,584 | | | | | | | | | | | | | | | | |
| 32A | BP- 32A Landscape | Within GMP | | | | | | | | | | | | | | | |
| | PENDING AWARD | | Prime | | | | | | | | | $ 223,000 | 96% | $ 223,000 | 96% | $ 223,000 | 96% |
| | PENDING AWARD | | Turnkey Installation | $ 10,000 | 4% | $ 10,000 | 2% | $ 10,000 | 2% | $ 10,000 | 2% | $ 10,000 | 4% | $ 10,000 | 4% | $ 10,000 | 4% |
| | $233,000 | | | | | | | | | | | | | | | | |
| 32B | BP- 32B Hardscape | Within GMP | | | | | | | | | | | | | | | |
| | PENDING AWARD | | Prime | | | | | | | | | | | | | | |
| | PENDING AWARD | | Turnkey Installation | $ 439,143 | 25% | $ 439,143 | 25% | $ 439,143 | 25% | $ 439,143 | 25% | $ 439,143 | 25% | $ 439,143 | 25% | $ 439,143 | 25% |
| | $1,756,571 | | | | | | | | | | | | | | | | |
| 35A | BP- 35A Canal Widening | Within GMP | | | | | | | | | | | | | | | |
| | PENDING AWARD | | Prime | | | | | | | | | $ 1,056,387 | 49% | $ 1,056,387 | 49% | $ 1,056,387 | 49% |
| | PENDING AWARD | | Material Supply | $ 32,352 | 2% | | | $ 32,352 | 2% | $ 32,352 | 2% | | | $ 32,352 | 2% | $ 32,352 | 2% |
| | PENDING AWARD | | Hauling | $ 9,705 | .45% | | | | | $ 9,705 | .45% | | | | | $ 9,705 | .45% |
| | PENDING AWARD | | Material Supply | $ 172,542 | 8% | $ 172,542 | 8% | $ 172,542 | 8% | $ 172,542 | 8% | $ 172,542 | 8% | $ 172,542 | 8% | $ 172,542 | 8% |
| | PENDING AWARD | | Hauling | $ 895,492 | 42% | $ 895,492 | 42% | $ 895,492 | 42% | $ 895,492 | 42% | $ 895,492 | 42% | $ 895,492 | 42% | $ 895,492 | 42% |
| | $2,156,772 | | | | | | | | | | | | | | | | |
| | Savannah Arena Project<br>DBE/LDBE & LOCAL TRACKING | | Overview | Potential Overall DBE Participation<br>GOAL = 25% | | Potential L/DBE Participation | | Potential Chatham/DBE County Participation | | Potential MSA/DBE Participation | | Potential Local Savannah Participation | | Potential Chatham County Participation | | Potential MSA Participation | |

AECOM HUNT

*in association with*

**Brownstone Construction Group**
**Pat Mathis Construction Company**
**A. Riley Consultants**

| | | | | Bid Pacakage DBE Participation | | | | | | | | | Bid Package LOCAL Participation | | | | | | | |
|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|
| Contract ID | Savannah Arena Project<br>DBE/LDBE & LOCAL TRACKING | | | Potential Overall DBE Participation | | Potential L/DBE Participation | | Potential Chatham/DBE County Participation | | Potential MSA/DBE Participation | | | Potential Local Savannah Participation | | Potential Chatham County Participation | | Potential MSA Participation | | | |
| Total Awards | $125,820,313 | Status | Scope of Work | $ 32,859,634.83 | 26.1% | $ 16,228,148 | 12.9% | $ 16,754,657 | 13.3% | $ 17,197,572 | 13.7% | | $ 29,496,367 | 23.4% | $ 31,910,569 | 25.4% | $ 32,399,778 | 25.8% | | |
| | | | | Dollars | % | Dollars | % | Dollars | % | Dollars | % | | Dollars | % | Dollars | % | Dollars | % | | |
| Total Construciton | $125,820,313 | | | Dollars | % | Dollars | % | Dollars | % | Dollars | % | | Dollars | % | Dollars | % | Dollars | % | | |
| | Totals | | | $ 32,859,634.83 | 26.1% | $ 16,228,148 | 12.9% | $ 16,754,657 | 13.3% | $ 17,197,572 | 13.7% | | $ 29,496,367 | 23.4% | $ 31,910,569 | 25.4% | $ 32,399,778 | 25.8% | | |

*Section 04*

# *List of Contract Documents*

AECOM HUNT

*in association with*

**Brownstone Construction Group**
**Pat Mathis Construction Company**
**A. Riley Consultants**

Arena Drawings

| Document Number | Description | Issuance | Date | Version |
|---|---|---|---|---|
| *Main Title Sheet | *Main Title Sheet | 100% CD | Feb 17, 2020 | V2 |
| A00-31 | EXTERIOR 3D AXONS | 100% CD | Feb 17, 2020 | V2 |
| A00-32 | EXTERIOR 3D AXON BUILD-UPS | 100% CD | Feb 17, 2020 | V2 |
| A10-00 | GRID PLAN | RFI 42 | Mar 12, 2020 | V4 |
| A10-10 | EVENT LEVEL - OVERALL FLOOR PLAN | 100% CD | Feb 17, 2020 | V2 |
| A10-10-SE | EVENT LEVEL - OVERALL SLAB EDGE PLAN | RFI 150 | May 5, 2020 | V2 |
| A10-11 | EVENT LEVEL FLOOR PLAN - QUAD 1 | 100% CD | Feb 17, 2020 | V2 |
| A10-12 | EVENT LEVEL FLOOR PLAN - QUAD 2 | 100% CD | Feb 17, 2020 | V2 |
| A10-13 | EVENT LEVEL FLOOR PLAN - QUAD 3 | 100% CD | Feb 17, 2020 | V2 |
| A10-14 | EVENT LEVEL FLOOR PLAN - QUAD 4 | 100% CD | Feb 17, 2020 | V2 |
| A10-20 | CONCOURSE LEVEL - OVERALL FLOOR PLAN | 100% CD | Feb 17, 2020 | V2 |
| A10-20-SE | CONCOURSE LEVEL - OVERALL SLAB EDGE PLAN | 100% CD | Feb 17, 2020 | V1 |
| A10-21 | CONCOURSE LEVEL FLOOR PLAN - QUAD 1 | 100% CD | Feb 17, 2020 | V2 |
| A10-22 | CONCOURSE LEVEL FLOOR PLAN - QUAD 2 | 100% CD | Feb 17, 2020 | V2 |
| A10-23 | CONCOURSE LEVEL FLOOR PLAN - QUAD 3 | 100% CD | Feb 17, 2020 | V2 |
| A10-24 | CONCOURSE LEVEL FLOOR PLAN - QUAD 4 | 100% CD | Feb 17, 2020 | V2 |
| A10-30 | SUITE LEVEL - OVERALL FLOOR PLAN | 100% CD | Feb 17, 2020 | V2 |
| A10-30-SE | SUITE LEVEL - OVERALL SLAB EDGE PLAN | 100% CD | Feb 17, 2020 | V1 |
| A10-31 | SUITE LEVEL FLOOR PLAN - QUAD 1 | 100% CD | Feb 17, 2020 | V2 |
| A10-32 | SUITE LEVEL FLOOR PLAN - QUAD 2 | 100% CD | Feb 17, 2020 | V2 |
| A10-40 | OVERLOOK LEVEL - OVERALL FLOOR PLAN | 100% CD | Feb 17, 2020 | V2 |
| A10-40-SE | OVERLOOK LEVEL - OVERALL SLAB EDGE PLAN | 100% CD | Feb 17, 2020 | V1 |
| A10-41 | OVERLOOK LEVEL FLOOR PLAN - QUAD 1 | 100% CD | Feb 17, 2020 | V2 |
| A10-42 | OVERLOOK LEVEL FLOOR PLAN - QUAD 2 | 100% CD | Feb 17, 2020 | V2 |
| A10-43 | OVERLOOK LEVEL FLOOR PLAN - QUAD 3 | 100% CD | Feb 17, 2020 | V2 |
| A10-44 | OVERLOOK LEVEL FLOOR PLAN - QUAD 4 | 100% CD | Feb 17, 2020 | V2 |
| A10-50 | CATWALK LEVEL - OVERALL FLOOR PLAN | 100% CD | Feb 17, 2020 | V2 |
| A10-50-SE | CATWALK LEVEL - OVERALL SLAB EDGE PLAN | 100% CD | Feb 17, 2020 | V1 |
| A10-51 | CATWALK LEVEL FLOOR PLAN - QUAD 1 | 100% CD | Feb 17, 2020 | V2 |
| A10-52 | CATWALK LEVEL FLOOR PLAN - QUAD 2 | 100% CD | Feb 17, 2020 | V2 |
| A10-53 | CATWALK LEVEL FLOOR PLAN - QUAD 3 | 100% CD | Feb 17, 2020 | V2 |
| A10-54 | CATWALK LEVEL FLOOR PLAN - QUAD 4 | 100% CD | Feb 17, 2020 | V2 |
| A10-60 | ROOF LEVEL - OVERALL PLAN | 100% CD | Feb 17, 2020 | V2 |
| A10-61 | ROOF LEVEL FLOOR PLAN - QUAD 1 | 100% CD | Feb 17, 2020 | V2 |
| A10-62 | ROOF LEVEL FLOOR PLAN - QUAD 2 | 100% CD | Feb 17, 2020 | V2 |
| A10-63 | ROOF LEVEL FLOOR PLAN - QUAD 3 | 100% CD | Feb 17, 2020 | V2 |
| A10-64 | ROOF LEVEL FLOOR PLAN - QUAD 4 | 100% CD | Feb 17, 2020 | V2 |
| A12-10 | EVENT LEVEL - OVERALL RCP | 100% CD | Feb 17, 2020 | V2 |
| A12-11 | EVENT LEVEL RCP - QUAD 1 | 100% CD | Feb 17, 2020 | V2 |
| A12-12 | EVENT LEVEL RCP - QUAD 2 | 100% CD | Feb 17, 2020 | V2 |
| A12-13 | EVENT LEVEL RCP - QUAD 3 | 100% CD | Feb 17, 2020 | V2 |

| | | | | |
|---|---|---|---|---|
| A12-14 | EVENT LEVEL RCP - QUAD 4 | 100% CD | Feb 17, 2020 | V2 |
| A12-20 | CONCOURSE LEVEL - OVERALL RCP | 100% CD | Feb 17, 2020 | V2 |
| A12-21 | CONCOURSE LEVEL RCP - QUAD 1 | 100% CD | Feb 17, 2020 | V2 |
| A12-22 | CONCOURSE LEVEL RCP - QUAD 2 | 100% CD | Feb 17, 2020 | V2 |
| A12-23 | CONCOURSE LEVEL RCP - QUAD 3 | 100% CD | Feb 17, 2020 | V2 |
| A12-24 | CONCOURSE LEVEL RCP - QUAD 4 | 100% CD | Feb 17, 2020 | V2 |
| A12-30 | SUITE LEVEL - OVERALL RCP | 100% CD | Feb 17, 2020 | V2 |
| A12-31 | SUITE LEVEL RCP - QUAD 1 | 100% CD | Feb 17, 2020 | V2 |
| A12-32 | SUITE LEVEL RCP - QUAD 2 | 100% CD | Feb 17, 2020 | V2 |
| A12-33 | SUITE LEVEL RCP - QUAD 3 | 100% CD | Feb 17, 2020 | V1 |
| A12-34 | SUITE LEVEL RCP - QUAD 4 | 100% CD | Feb 17, 2020 | V1 |
| A12-40 | OVERLOOK LEVEL - OVERALL RCP | 100% CD | Feb 17, 2020 | V2 |
| A12-41 | OVERLOOK LEVEL RCP - QUAD 1 | 100% CD | Feb 17, 2020 | V2 |
| A12-42 | OVERLOOK LEVEL RCP - QUAD 2 | 100% CD | Feb 17, 2020 | V2 |
| A12-43 | OVERLOOK LEVEL RCP - QUAD 3 | 100% CD | Feb 17, 2020 | V2 |
| A12-44 | OVERLOOK LEVEL RCP - QUAD 4 | 100% CD | Feb 17, 2020 | V2 |
| A12-50 | ACOUSTICAL BAFFLE RCP - CATWALK LEVEL | RFI 178 | May 20, 2020 | V3 |
| A12-51 | ACOUSTIC VERTICAL BAFFLE ELEVATIONS | 100% CD | Feb 17, 2020 | V2 |
| A12-60 | HALF HOUSE REDUCTION CURTAINS RCP | 100% CD | Feb 17, 2020 | V1 |
| A12-61 | HALF HOUSE REDUCTION CURTAIN ELEVATION | 100% CD | Feb 17, 2020 | V1 |
| A13-01 | FINISH LEGEND | ASI - 007 | Jun 3, 2020 | V7 |
| A13-02 | ROOM FINISH SCHEDULE | RFI 163 | May 6, 2020 | V4 |
| A13-11 | EVENT LEVEL - FINISH PLAN - QUAD 1 FLOOR PLAN | 100% CD | Feb 17, 2020 | V2 |
| A13-12 | EVENT LEVEL - FINISH PLAN - QUAD 2 FLOOR PLAN | 100% CD | Feb 17, 2020 | V2 |
| A13-13 | EVENT LEVEL - FINISH PLAN - QUAD 3 FLOOR PLAN | RFI 140 | May 1, 2020 | V4 |
| A13-14 | EVENT LEVEL - FINISH PLAN - QUAD 4 FLOOR PLAN | RFI 140 | May 1, 2020 | V4 |
| A13-21 | CONCOURSE LEVEL - FINISH PLAN - QUAD 1 FLOOR PLAN | RFI 77 | Mar 25, 2020 | V3 |
| A13-22 | CONCOURSE LEVEL - FINISH PLAN - QUAD 2 FLOOR PLAN | RFI 77 | Mar 25, 2020 | V3 |
| A13-23 | CONCOURSE LEVEL - FINISH PLAN - QUAD 3 FLOOR PLAN | RFI 77 | Mar 25, 2020 | V3 |
| A13-24 | CONCOURSE LEVEL - FINISH PLAN - QUAD 4 FLOOR PLAN | RFI 77 | Mar 25, 2020 | V3 |
| A13-31 | SUITE LEVEL - FINISH PLAN - QUAD 1 FLOOR PLAN | RFI 77 | Mar 25, 2020 | V3 |
| A13-32 | SUITE LEVEL - FINISH PLAN - QUAD 2 FLOOR PLAN | RFI 163 | May 6, 2020 | V4 |
| A13-41 | OVERLOOK LEVEL - FINISH PLAN - QUAD 1 FLOOR PLAN | RFI 77 | Mar 25, 2020 | V3 |
| A13-42 | OVERLOOK LEVEL - FINISH PLAN - QUAD 2 FLOOR PLAN | RFI 77 | Mar 25, 2020 | V3 |
| A13-43 | OVERLOOK LEVEL - FINISH PLAN - QUAD 3 FLOOR PLAN | RFI 77 | Mar 25, 2020 | V3 |
| A20-01 | OVERALL EXTERIOR ELEVATIONS | 100% CD | Feb 17, 2020 | V2 |
| A20-02 | OVERALL EXTERIOR ELEVATIONS | 100% CD | Feb 17, 2020 | V2 |
| A20-03 | SOUTH EXTERIOR ELEVATIONS | RFI 181 | May 21, 2020 | V4 |
| A20-04 | NORTH EXTERIOR ELEVATIONS | 100% CD | Feb 17, 2020 | V2 |
| A20-05 | WEST EXTERIOR ELEVATIONS | 100% CD | Feb 17, 2020 | V2 |

| | | | | |
|---|---|---|---|---|
| A20-06 | EAST EXTERIOR ELEVATIONS | 100% CD | Feb 17, 2020 | V2 |
| A20-07 | EXTERIOR ELEVATIONS - ENLARGED | RFI 181 | May 21, 2020 | V3 |
| A20-09 | EXTERIOR GLAZING SYSTEM TYPES | 100% CD | Feb 17, 2020 | V1 |
| A20-10 | EXTERIOR GLAZING SYSTEM TYPES | 100% CD | Feb 17, 2020 | V1 |
| A21-01 | OVERALL BUILDING SECTIONS | 100% CD | Feb 17, 2020 | V2 |
| A21-04 | BUILDING SECTIONS ENLARGED - EAST | 100% CD | Feb 17, 2020 | V2 |
| A21-05 | BUILDING SECTIONS ENLARGED - WEST | 100% CD | Feb 17, 2020 | V2 |
| A21-06 | BUILDING SECTIONS ENLARGED - NORTH | 100% CD | Feb 17, 2020 | V2 |
| A21-07 | BUILDING SECTIONS ENLARGED - SOUTH | 100% CD | Feb 17, 2020 | V2 |
| A30-00 | EXTERIOR ENVELOPE ASSEMBLIES | 100% CD | Feb 17, 2020 | V1 |
| A31-10 | WALL SECTIONS - SOUTH | 100% CD | Feb 17, 2020 | V1 |
| A31-11 | WALL SECTIONS - SOUTH | RFI 66 | Mar 30, 2020 | V2 |
| A31-12 | WALL SECTIONS - SOUTH | RFI 66 | Mar 30, 2020 | V2 |
| A31-13 | WALL SECTIONS - S/E STAIR TOWER | RFI 66 | Mar 30, 2020 | V2 |
| A31-20 | WALL SECTIONS - EAST | RFI 66 | Mar 30, 2020 | V2 |
| A31-21 | WALL SECTIONS AND DETAILS - SOUTH EAST BAR | RFI 38 | Mar 17, 2020 | V1 |
| A31-30 | WALL SECTIONS - NORTH | 100% CD | Feb 17, 2020 | V1 |
| A31-40 | WALL SECTIONS - WEST | RFI 66 | Mar 30, 2020 | V2 |
| A32-10 | EXTERIOR DETAILS - SOUTH | 100% CD | Feb 17, 2020 | V1 |
| A32-11 | EXTERIOR DETAILS - SOUTH | RFI 66 | Mar 30, 2020 | V2 |
| A32-12 | EXTERIOR PLAN DETAILS - SOUTH | RFI 66 | Mar 30, 2020 | V2 |
| A32-13 | EXTERIOR PLAN DETAILS - S/E STAIR TOWER | RFI 66 | Mar 30, 2020 | V2 |
| A32-14 | EXTERIOR DETAILS - S/E STAIR TOWER | 100% CD | Feb 17, 2020 | V1 |
| A32-15 | EXTERIOR DETAILS - S/E STAIR TOWER | 100% CD | Feb 17, 2020 | V1 |
| A32-16 | EXTERIOR DETAILS - S/E STAIR TOWER | 100% CD | Feb 17, 2020 | V1 |
| A32-17 | EXTERIOR DETAILS -S/E STAIR TOWER | 100% CD | Feb 17, 2020 | V1 |
| A32-20 | EXTERIOR DETAILS - EAST | RFI 66 | Mar 30, 2020 | V3 |
| A32-21 | EXTERIOR PLAN DETAILS - EAST | 100% CD | Feb 17, 2020 | V1 |
| A32-40 | EXTERIOR DETAILS - WEST | 100% CD | Feb 17, 2020 | V1 |
| A32-41 | EXTERIOR DETAILS - WEST | 100% CD | Feb 17, 2020 | V1 |
| A32-42 | EXTERIOR PLAN DETAILS - WEST | 100% CD | Feb 17, 2020 | V1 |
| A33-00 | TYPICAL EXTERIOR DETAILS | 100% CD | Feb 17, 2020 | V1 |
| A34-00 | EXTERIOR DOOR AND FRAME DETAILS | 100% CD | Feb 17, 2020 | V1 |
| A35-00 | EXTERIOR GLAZING DETAILS | RFI 66 | Mar 30, 2020 | V2 |
| A36-00 | ROOF DETAILS | 100% CD | Feb 17, 2020 | V1 |
| A36-01 | ROOF DETAILS | 100% CD | Feb 17, 2020 | V1 |
| A36-02 | ROOF DETAILS | 100% CD | Feb 17, 2020 | V1 |
| A36-03 | ROOF DETAILS | 100% CD | Feb 17, 2020 | V1 |
| A40-01 | LOBBY STAIR AND ESCALATOR PLANS AND SECTIONS | 100% CD | Feb 17, 2020 | V2 |
| A40-02 | LOBBY STAIR AND ESCALATOR PLANS AND SECTIONS | 100% CD | Feb 17, 2020 | V2 |
| A40-03 | STAIR NW AND ELEVATOR PLANS AND SECTIONS | 100% CD | Feb 17, 2020 | V2 |
| A40-04 | STAIR NE AND ELEVATOR PLANS AND SECTIONS | 100% CD | Feb 17, 2020 | V2 |
| A40-05 | STAIR SE AND ELEVATOR PLANS AND SECTIONS | 100% CD | Feb 17, 2020 | V2 |

| | | | | |
|---|---|---|---|---|
| A40-06 | STAIR SW PLANS AND SECTIONS | 100% CD | Feb 17, 2020 | V2 |
| A41-01 | STAIR AND RAILING DETAILS | 100% CD | Feb 17, 2020 | V2 |
| A42-01 | CONCOURSE LEVEL - BOWL RAIL KEY PLAN | ASI-005 | Jun 2, 2020 | V3 |
| A42-01A | CONCOURSE LEVEL - BOWL RAIL PLAN 1 QUAD 1 | ASI-005 | Jun 2, 2020 | V1 |
| A42-01B | CONCOURSE LEVEL - BOWL RAILING PLAN QUAD 2 | ASI-005 | Jun 2, 2020 | V1 |
| A42-01C | CONCOURSE LEVEL - BOWL RAILING PLAN 1 QUAD 3 | ASI-005 | Jun 2, 2020 | V1 |
| A42-01D | CONCOURSE LEVEL - BOWL RAILING PLAN 1 QUAD 4 | ASI-005 | Jun 2, 2020 | V1 |
| A42-02 | SUITE LEVEL - BOWL RAIL KEY PLAN | ASI-005 | Jun 2, 2020 | V4 |
| A42-02A | SUITE LEVEL - BOWL RAILING PLAN QUAD 1 AND 2 | ASI-005 | Jun 2, 2020 | V1 |
| A42-03 | OVERLOOK LEVEL - BOWL RAIL KEY PLAN | ASI-005 | Jun 2, 2020 | V4 |
| A42-03A | OVERLOOK LEVEL - BOWL RAILING PLAN QUAD 1 AND 2 | ASI-005 | Jun 2, 2020 | V1 |
| A42-03B | OVERLOOK LEVEL - BOWL RAILING PLAN QUAD 3 AND 4 | ASI-005 | Jun 2, 2020 | V1 |
| A42-05 | BOWL STAIR/VOM PLAN AND SECTION | ASI-005 | Jun 2, 2020 | V1 |
| A42-06 | BOWL STAIR/VOM PLAN AND SECTION | ASI-005 | Jun 2, 2020 | V1 |
| A42-20 | HANDRAIL / GUARDRAIL DETAILS | ASI-005 | Jun 2, 2020 | V3 |
| A42-21 | HANDRAIL / GUARDRAIL DETAILS | ASI-005 | Jun 2, 2020 | V4 |
| A42-22 | HANDRAIL / GUARDRAIL DETAILS 1 | ASI-005 | Jun 2, 2020 | V1 |
| A42-40 | CATWALK MISC METALS DETAILS | 100% CD | Feb 17, 2020 | V2 |
| A42-50 | ICE MELT PIT LAYOUT AND DETAILS | 100% CD | Feb 17, 2020 | V2 |
| A43-01 | TOILET ACCESSORIES AND MISC EQUIPMENT | 100% CD | Feb 17, 2020 | V2 |
| A43-10 | EVENT LEVEL - Q1 - RESTROOM ENLARGED PLANS & ELEVATIONS | 100% CD | Feb 17, 2020 | V2 |
| A43-11 | EVENT LEVEL - Q2 & Q3 - HOME LOCKER ROOM ENLARGED PLANS | 100% CD | Feb 17, 2020 | V2 |
| A43-12 | EVENT LEVEL - Q2 & Q3 - HOME LOCKER ROOM ENLARGED PLANS | RFI 140 | May 1, 2020 | V3 |
| A43-13 | EVENT LEVEL - Q2 & Q3 - HOME LOCKER ROOM ENLARGED PLANS | 100% CD | Feb 17, 2020 | V2 |
| A43-14 | EVENT LEVEL - Q2 & Q3 - HOME LOCKER ROOM ELEVATIONS | RFI 139 | Apr 29, 2020 | V3 |
| A43-15 | EVENT LEVEL - Q2 & Q3 - HOME LOCKER ROOM ELEVATIONS | RFI 140 | May 1, 2020 | V3 |
| A43-16 | EVENT LEVEL - Q2 & Q3 - HOME LOCKER ROOM ELEVATIONS | 100% CD | Feb 17, 2020 | V2 |
| A43-17 | EVENT LEVEL - Q3 - RESTROOM ENLARGED PLANS & ELEVATIONS | 100% CD | Feb 17, 2020 | V2 |
| A43-18 | EVENT LEVEL - Q3 - RESTROOM ENLARGED PLANS & ELEVATIONS | 100% CD | Feb 17, 2020 | V2 |
| A43-19 | EVENT LEVEL - Q3 & Q4 - VISITOR LOCKER ROOM ENLARGED PLANS & ELEVATIONS | ASI-006 | Jun 3, 2020 | V3 |
| A43-19A | EVENT LEVEL - Q4 - VISITOR LOCKER ROOM ENLARGED PLANS & ELEVATIONS | ASI-006 | Jun 3, 2020 | V3 |

| | | | | |
|---|---|---|---|---|
| A43-19B | EVENT LEVEL - Q4 - STAR ROOM ENLARGED PLANS & ELEVATIONS | 100% CD | Feb 17, 2020 | V1 |
| A43-20 | CONCOURSE LEVEL - Q1 - RESTROOM/GRILL/PREP ENLARGED PLANS | 100% CD | Feb 17, 2020 | V1 |
| A43-21 | CONCOURSE LEVEL - Q1 - RESTROOM ENLARGED PLANS & ELEVATIONS | 100% CD | Feb 17, 2020 | V2 |
| A43-22 | CONCOURSE LEVEL - Q2 - RESTROOM ENLARGED PLANS & ELEVATIONS | 100% CD | Feb 17, 2020 | V2 |
| A43-23 | CONCOURSE LEVEL - Q2 - RESTROOM ENLARGED PLANS & ELEVATIONS | 100% CD | Feb 17, 2020 | V2 |
| A43-24 | CONCOURSE LEVEL - Q2 - RESTROOM/FIRST AID ENLARGED PLANS & ELEVATIONS | 100% CD | Feb 17, 2020 | V2 |
| A43-25 | CONCOURSE LEVEL - Q3 - RESTROOM ENLARGED PLANS & ELEVATIONS | 100% CD | Feb 17, 2020 | V2 |
| A43-26 | CONCOURSE LEVEL - Q3 - RESTROOM ENLARGED PLANS & ELEVATIONS | 100% CD | Feb 17, 2020 | V2 |
| A43-27 | CONCOURSE LEVEL - Q3 - RESTROOM ENLARGED PLANS & ELEVATIONS | 100% CD | Feb 17, 2020 | V1 |
| A43-28 | CONCOURSE LEVEL - Q3 & Q4 - RESTROOM ENLARGED PLANS & ELEVATIONS | 100% CD | Feb 17, 2020 | V1 |
| A43-29 | CONCOURSE LEVEL - Q4 - RESTROOM ENLARGED PLANS & ELEVATIONS | 100% CD | Feb 17, 2020 | V1 |
| A43-32 | SUITE LEVEL - Q1 - RESTROOM ENLARGED PLANS & ELEVATIONS | 100% CD | Feb 17, 2020 | V2 |
| A43-33 | SUITE LEVEL - Q2 - RESTROOM ENLARGED PLANS & ELEVATIONS | 100% CD | Feb 17, 2020 | V1 |
| A43-40 | OVERLOOK LEVEL - Q1 - RESTROOM ENLARGED PLANS & ELEVATIONS | 100% CD | Feb 17, 2020 | V1 |
| A43-41 | OVERLOOK LEVEL - Q2 - RESTROOM ENLARGED PLANS & ELEVATIONS | 100% CD | Feb 17, 2020 | V2 |
| A44-10A | EVENT LEVEL - Q1 - ENLARGED PLANS & ELEVATIONS | ASI-006 | Jun 3, 2020 | V2 |
| A44-10B | EVENT LEVEL - Q1 - ENLARGED PLANS & ELEVATIONS | 100% CD | Feb 17, 2020 | V1 |
| A44-11A | EVENT LEVEL - Q2 - ENLARGED PLANS & ELEVATIONS | 100% CD | Feb 17, 2020 | V1 |
| A44-11B | EVENT LEVEL - Q2 - ENLARGED PLANS & ELEVATIONS | 100% CD | Feb 17, 2020 | V1 |
| A44-12 | EVENT LEVEL - Q3 - ENLARGED PLANS & ELEVATIONS | 100% CD | Feb 17, 2020 | V2 |
| A44-13A | EVENT LEVEL -Q2 & Q3 - ENLARGED PLANS & ELEVATIONS | RFI 123 | May 1, 2020 | V2 |
| A44-13B | EVENT LEVEL - Q2 & Q3 - ENLARGED PLANS AND ELEVATIONS | 100% CD | Feb 17, 2020 | V1 |
| A44-13C | EVENT LEVEL - Q2 & Q3 - ENLARGED PLANS AND ELEVATIONS | 100% CD | Feb 17, 2020 | V1 |
| A44-13D | EVENT LEVEL - Q2 & Q3 - ENLARGED PLANS & ELEVATIONS | RFI 123 | May 1, 2020 | V2 |
| A44-14 | EVENT LEVEL - Q3 - ENLARGED PLANS & ELEVATIONS | 100% CD | Feb 17, 2020 | V2 |
| A44-15 | EVENT LEVEL - Q3 & Q4 - ENLARGED PLANS & ELEVATIONS | 100% CD | Feb 17, 2020 | V1 |
| A44-16A | EVENT LEVEL - Q4 - ENLARGED PLANS & ELEVATIONS | 100% CD | Feb 17, 2020 | V1 |
| A44-16B | EVENT LEVEL - Q4 - ENLARGED PLANS & ELEVATIONS | 100% CD | Feb 17, 2020 | V1 |

| | | | | |
|---|---|---|---|---|
| A44-20 | CONCOURSE LEVEL - Q1 & Q2 - ENLARGED PLANS & ELEVATIONS | RFI 77 | Mar 25, 2020 | V3 |
| A44-21A | CONCOURSE LEVEL - Q2 - ENLARGED PLANS & ELEVATIONS | 100% CD | Feb 17, 2020 | V1 |
| A44-21B | CONCOURSE LEVEL - Q2 - ENLARGED PLANS & ELEVATIONS | 100% CD | Feb 17, 2020 | V1 |
| A44-22 | CONCOURSE LEVEL - Q3 - ENLARGED PLANS & ELEVATIONS | 100% CD | Feb 17, 2020 | V2 |
| A44-23 | CONCOURSE LEVEL - Q3 - ENLARGED PLANS & ELEVATIONS | 100% CD | Feb 17, 2020 | V2 |
| A44-24 | CONCOURSE LEVEL - Q3 - ENLARGED PLANS & ELEVATIONS | 100% CD | Feb 17, 2020 | V2 |
| A44-25 | CONCOURSE LEVEL - Q3 & Q4 - ENLARGED PLANS & ELEVATIONS | 100% CD | Feb 17, 2020 | V2 |
| A44-26 | CONCOURSE LEVEL - Q4 - ENLARGED PLANS & ELEVATIONS | 100% CD | Feb 17, 2020 | V2 |
| A44-27 | CONCOURSE LEVEL - Q4 - ENLARGED PLANS & ELEVATIONS | 100% CD | Feb 17, 2020 | V1 |
| A44-28 | CONCOURSE LEVEL - Q4 - ENLARGED PLANS & ELEVATION | 100% CD | Feb 17, 2020 | V1 |
| A44-29 | CONCOURSE LEVEL - Q4 - ENLARGED PLANS & ELEVATIONS | 100% CD | Feb 17, 2020 | V1 |
| A44-30 | SUITE LEVEL - Q1 - ENLARGED PLANS & ELEVATIONS | RFI 143 | Apr 28, 2020 | V3 |
| A44-31 | SUITE LEVEL - Q1 - ENLARGED PLANS & ELEVATIONS | ASI-006 | Jun 3, 2020 | V3 |
| A44-32 | SUITE LEVEL - Q1 - ENLARGED PLANS | 100% CD | Feb 17, 2020 | V2 |
| A44-33 | SUITE LEVEL - Q2 - ENLARGED PLANS | 100% CD | Feb 17, 2020 | V2 |
| A44-34 | SUITE LEVEL - Q1 & Q2 - ELEVATIONS | 100% CD | Feb 17, 2020 | V2 |
| A44-35 | SUITE LEVEL - Q2 - ENLARGED PLANS | 100% CD | Feb 17, 2020 | V2 |
| A44-36 | SUITE LEVEL - Q2 - ENLARGED PLANS & ELEVATIONS | 100% CD | Feb 17, 2020 | V1 |
| A44-38 | SUITE LEVEL - Q2 - ENLARGED PLANS & ELEVATIONS | 100% CD | Feb 17, 2020 | V1 |
| A44-39 | OVERLOOK LEVEL - Q1 & Q3 - ENLARGED PLANS & ELEVATIONS | 100% CD | Feb 17, 2020 | V1 |
| A44-40 | OVERLOOK LEVEL - Q4 ENLARGED PLANS & ELEVATIONS | 100% CD | Feb 17, 2020 | V2 |
| A50-00 | STANDARD MILLWORK LEGEND | 100% CD | Feb 17, 2020 | V2 |
| A50-01 | STANDARD MILLWORK DETAILS | 100% CD | Feb 17, 2020 | V2 |
| A50-10 | LOCKER ROOM MILLWORK DETAILS | 100% CD | Feb 17, 2020 | V2 |
| A50-30 | TICKETING MILLWORK DETAILS | 100% CD | Feb 17, 2020 | V2 |
| A50-31 | CONCESSIONS / BAR MILLWORK DETAILS | 100% CD | Feb 17, 2020 | V2 |
| A50-32 | BAR (CONT.) & MISC. MILLWORK DETAILS | 100% CD | Feb 17, 2020 | V2 |
| A50-33 | MISC. MILLWORK DETAILS | RFI 123 | May 1, 2020 | V2 |
| A51-01 | TYPICAL CEILING DETAILS | 100% CD | Feb 17, 2020 | V2 |
| A51-02 | TYPICAL CEILING DETAILS | 100% CD | Feb 17, 2020 | V2 |
| A51-03 | CUSTOM CEILING DETAILS | 100% CD | Feb 17, 2020 | V1 |
| A51-04 | SEISMIC CEILING DETAILS | 100% CD | Feb 17, 2020 | V1 |
| A52-01 | INTERIOR DETAILS | RFI 123 | May 1, 2020 | V3 |
| A52-02 | INTERIOR DETAILS | 100% CD | Feb 17, 2020 | V2 |
| A52-03 | INTERIOR DETAILS | 100% CD | Feb 17, 2020 | V1 |

| | | | | |
|---|---|---|---|---|
| A52-04 | INTERIOR DETAILS | 100% CD | Feb 17, 2020 | V1 |
| A61-00 | INTERIOR FRAMING NOTES | 100% CD | Feb 17, 2020 | V2 |
| A61-01 | INTERIOR PARTITION TYPE CHARTS | 100% CD | Feb 17, 2020 | V2 |
| A61-02 | INTERIOR PARTITION TYPE CHARTS | 100% CD | Feb 17, 2020 | V1 |
| A61-50 | PARTITION FRAMING CRITERIA AND DETAILS | 100% CD | Feb 17, 2020 | V2 |
| A61-51 | SHAFTWALL FRAMING CRITERIA AND DETAILS | 100% CD | Feb 17, 2020 | V2 |
| A62-01 | DOOR, FRAME AND HARDWARE SCHEDULE | RFI 38 | Mar 17, 2020 | V3 |
| A62-02 | DOOR, FRAME AND HARDWARE SCHEDULE | 100% CD | Feb 17, 2020 | V1 |
| A62-03 | DOOR AND FRAME DETAILS | 100% CD | Feb 17, 2020 | V2 |
| A62-60 | SPECIALITY DOOR DETAILS | 100% CD | Feb 17, 2020 | V2 |
| A63-01 | INTERIOR WINDOW & FRAME DETAILS | 100% CD | Feb 17, 2020 | V1 |
| A66-01 | TV MONITOR SCHEDULE | 100% CD | Feb 17, 2020 | V2 |
| A72-01 | 02 CONCOURSE LEVEL EXPOSED STEEL PLAN | ASI - 007 | Jun 3, 2020 | V1 |
| A72-02 | 02 CONCOURSE LEVEL EXPOSED STEEL RCP | ASI - 007 | Jun 3, 2020 | V1 |
| A72-03 | EXPOSED STEEL SECTIONS | ASI - 007 | Jun 3, 2020 | V1 |
| A72-04 | EXPOSED STEEL ELEVATIONS | ASI - 007 | Jun 3, 2020 | V1 |
| A72-05 | EXPOSED STEEL ELEVATIONS | ASI - 007 | Jun 3, 2020 | V1 |
| AS72-10 | EVENT SEATING - HOCKEY | 100% CD | Feb 17, 2020 | V2 |
| AS72-11 | EVENT SEATING - END STAGE CONCERT | 100% CD | Feb 17, 2020 | V2 |
| AS72-12 | EVENT SEATING - CENTER STAGE CONCERT | 100% CD | Feb 17, 2020 | V2 |
| AS72-20 | SEATING MANIFEST - LOWER BOWL - CS EVENT | 100% CD | Feb 17, 2020 | V2 |
| AS72-21 | SEATING MANIFEST - UPPER BOWL / PREMIUM LEVELS | 100% CD | Feb 17, 2020 | V2 |
| AV-000 | COVER PAGE | ASI-006 | Jun 3, 2020 | V3 |
| AV00-00 | GENERAL NOTES AND LEGENDS | 100% CD | Feb 17, 2020 | V2 |
| AV100-00 | BROADCAST FUNCTIONAL LEGEND AND STANDARD DETAILS | 100% CD | Feb 17, 2020 | V1 |
| AV100-01 | BROADCAST RISER DIAGRAM | 100% CD | Feb 17, 2020 | V1 |
| AV100-60 | JBT TYPICAL | 100% CD | Feb 17, 2020 | V1 |
| AV100-61 | PHOTOSTROBES | 100% CD | Feb 17, 2020 | V1 |
| AV100-62 | OFFICIAL'S REPLAY DETAILS | 100% CD | Feb 17, 2020 | V1 |
| AV100-80 | BROADCAST BOX MOUNTING DETAILS | 100% CD | Feb 17, 2020 | V1 |
| AV100-81 | BROADCAST BOX DETAILS | 100% CD | Feb 17, 2020 | V1 |
| AV100-90 | BROADCAST BOX SCHEDULE | 100% CD | Feb 17, 2020 | V2 |
| AV10-11 | EVENT LEVEL FLOOR PLAN - QUAD 1 | 100% CD | Feb 17, 2020 | V2 |
| AV10-12 | EVENT LEVEL FLOOR PLAN - QUAD 2 | 100% CD | Feb 17, 2020 | V2 |
| AV10-13 | EVENT LEVEL FLOOR PLAN - QUAD 3 | 100% CD | Feb 17, 2020 | V2 |
| AV10-14 | EVENT LEVEL FLOOR PLAN - QUAD 4 | 100% CD | Feb 17, 2020 | V2 |
| AV10-15 | EVENT LEVEL FLOOR PLAN - GARAGE WEST | 100% CD | Feb 17, 2020 | V2 |
| AV10-21 | CONCOURSE LEVEL FLOOR PLAN - QUAD 1 | 100% CD | Feb 17, 2020 | V2 |
| AV10-22 | CONCOURSE LEVEL FLOOR PLAN - QUAD 2 | 100% CD | Feb 17, 2020 | V2 |
| AV10-31 | SUITE LEVEL FLOOR PLAN - QUAD 1 | 100% CD | Feb 17, 2020 | V2 |
| AV10-32 | SUITE LEVEL FLOOR PLAN - QUAD 2 | 100% CD | Feb 17, 2020 | V2 |
| AV10-33 | SUITE LEVEL FLOOR PLAN - QUAD 3 | 100% CD | Feb 17, 2020 | V2 |
| AV10-34 | SUITE LEVEL FLOOR PLAN - QUAD 4 | 100% CD | Feb 17, 2020 | V2 |

| | | | | |
|---|---|---|---|---|
| AV10-41 | OVERLOOK LEVEL FLOOR PLAN - QUAD 1 | 100% CD | Feb 17, 2020 | V2 |
| AV10-42 | OVERLOOK LEVEL FLOOR PLAN - QUAD 2 | 100% CD | Feb 17, 2020 | V2 |
| AV10-51 | CATWALK LEVEL FLOOR PLAN - QUAD 1 | 100% CD | Feb 17, 2020 | V2 |
| AV10-52 | CATWALK LEVEL FLOOR PLAN - QUAD 2 | 100% CD | Feb 17, 2020 | V2 |
| AV10-53 | CATWALK LEVEL FLOOR PLAN - QUAD 3 | 100% CD | Feb 17, 2020 | V2 |
| AV10-54 | CATWALK LEVEL FLOOR PLAN - QUAD 4 | 100% CD | Feb 17, 2020 | V2 |
| AV110-00 | AUDIO-VIDEO FUNCTIONAL LEGEND AND STANDARD DETAILS | 100% CD | Feb 17, 2020 | V1 |
| AV110-10 | AUDIO SYSTEM NETWORK DIAGRAMS | 100% CD | Feb 17, 2020 | V1 |
| AV110-11 | CONTROL ROOM FUNCTIONAL DIAGRAM | 100% CD | Feb 17, 2020 | V1 |
| AV110-12 | AV FUNCTIONAL DIAGRAM - 1 | 100% CD | Feb 17, 2020 | V1 |
| AV110-13 | AV FUNCTIONAL DIAGRAM - 2 | 100% CD | Feb 17, 2020 | V1 |
| AV110-14 | BOWL ARRAYS FUNCTIONALS - 1 | 100% CD | Feb 17, 2020 | V1 |
| AV110-15 | BOWL ARRAYS FUNCTIONALS - 2 | 100% CD | Feb 17, 2020 | V1 |
| AV110-18 | INTERCOM SYSTEM DETAILS | 100% CD | Feb 17, 2020 | V1 |
| AV110-21 | AV DEVICE & SPEAKER SCHEDULES | 100% CD | Feb 17, 2020 | V1 |
| AV110-22 | AV FUNCTIONAL DETAILS | 100% CD | Feb 17, 2020 | V1 |
| AV110-71 | AV PLATES & PANELS | 100% CD | Feb 17, 2020 | V1 |
| AV110-90 | AUDIO-VIDEO EQUIPMENT RACK DETAILS | 100% CD | Feb 17, 2020 | V1 |
| AV120-00 | VIDEO PRODUCTION SYSTEM LEGEND AND NOTES | 100% CD | Feb 17, 2020 | V1 |
| AV120-01 | VIDEO PRODUCTION FUNCTIONALS - TECHNICAL & RACK ELEVATIONS | 100% CD | Feb 17, 2020 | V1 |
| AV120-05 | VIDEO PRODUCTION DETAILS | 100% CD | Feb 17, 2020 | V1 |
| AV120-20 | VIDEO PRODUCTION FUNCTIONALS - CAMERAS | 100% CD | Feb 17, 2020 | V1 |
| AV120-22 | VIDEO PRODUCTION FUNCTIONALS - SWITCHER, SLOMO & CG | 100% CD | Feb 17, 2020 | V1 |
| AV120-23 | VIDEO PRODUCTION FUNCTIONALS - ICOM & SWITCH | 100% CD | Feb 17, 2020 | V1 |
| AV120-24 | VIDEO PRODUCTION FUNCTIONALS - UTLITY EQUIPMENT | 100% CD | Feb 17, 2020 | V1 |
| AV120-30 | VIDEO PRODUCTION FUNCTIONALS - OPERATIONAL POSITIONS | 100% CD | Feb 17, 2020 | V1 |
| AV120-40 | VIDEO PRODUCTION FUNCTIONALS - REFERENCE & TIMING | 100% CD | Feb 17, 2020 | V1 |
| AV120-50 | LED DISPLAY AND CONTROL | 100% CD | Feb 17, 2020 | V1 |
| AV12-11 | EVENT LEVEL RCP - QUAD 1 | 100% CD | Feb 17, 2020 | V2 |
| AV12-12 | EVENT LEVEL RCP - QUAD 2 | 100% CD | Feb 17, 2020 | V2 |
| AV12-13 | EVENT LEVEL RCP - QUAD 3 | 100% CD | Feb 17, 2020 | V2 |
| AV12-14 | EVENT LEVEL RCP - QUAD 4 | 100% CD | Feb 17, 2020 | V2 |
| AV12-21 | CONCOURSE LEVEL RCP - QUAD 1 | 100% CD | Feb 17, 2020 | V2 |
| AV12-22 | CONCOURSE LEVEL RCP - QUAD 2 | 100% CD | Feb 17, 2020 | V2 |
| AV12-31 | SUITE LEVEL RCP - QUAD 1 | 100% CD | Feb 17, 2020 | V2 |
| AV12-32 | SUITE LEVEL RCP - QUAD 2 | 100% CD | Feb 17, 2020 | V2 |
| AV12-33 | SUITE LEVEL RCP - QUAD 3 | 100% CD | Feb 17, 2020 | V2 |
| AV12-34 | SUITE LEVEL RCP - QUAD 4 | 100% CD | Feb 17, 2020 | V2 |
| AV12-41 | PARTY LEVEL RCP - QUAD 1 | 100% CD | Feb 17, 2020 | V2 |
| AV12-42 | PARTY LEVEL RCP - QUAD 2 | 100% CD | Feb 17, 2020 | V2 |

| | | | | |
|---|---|---|---|---|
| AV12-43 | PARTY LEVEL RCP - QUAD 3 | 100% CD | Feb 17, 2020 | V2 |
| AV12-44 | PARTY LEVEL RCP - QUAD 4 | 100% CD | Feb 17, 2020 | V2 |
| AV-210 | 01 - EVENT LEVEL OVERALL PLAN | 100% CD | Feb 17, 2020 | V2 |
| AV-211 | 01 - EVENT LEVEL QUAD 1 PLAN | ASI-006 | Jun 3, 2020 | V3 |
| AV-212 | 01 - EVENT LEVEL QUAD 2 PLAN | ASI-006 | Jun 3, 2020 | V2 |
| AV-213 | 01 - EVENT LEVEL QUAD 3 PLAN | ASI-006 | Jun 3, 2020 | V3 |
| AV-214 | 01 - EVENT LEVEL QUAD 4 PLAN | ASI-006 | Jun 3, 2020 | V3 |
| AV-220 | 02 - CONCOURSE LEVEL OVERALL PLAN | 100% CD | Feb 17, 2020 | V2 |
| AV-221 | 02 - CONCOURSE LEVEL QUAD 1 PLAN | 100% CD | Feb 17, 2020 | V1 |
| AV-222 | 02 - CONCOURSE LEVEL QUAD 2 PLAN | 100% CD | Feb 17, 2020 | V2 |
| AV-223 | 02 - CONCOURSE LEVEL QUAD 3 PLAN | 100% CD | Feb 17, 2020 | V2 |
| AV-224 | 02 - CONCOURSE LEVEL QUAD 4 PLAN | 100% CD | Feb 17, 2020 | V2 |
| AV-230 | 03 - SUITE LEVEL OVERALL PLAN | 100% CD | Feb 17, 2020 | V2 |
| AV-231 | 03 - SUITE LEVEL QUAD 1 PLAN | ASI-006 | Jun 3, 2020 | V2 |
| AV-232 | 03 - SUITE LEVEL QUAD 2 PLAN | ASI-006 | Jun 3, 2020 | V2 |
| AV-240 | 04 - OVERLOOK LEVEL OVERALL PLAN | ASI-006 | Jun 3, 2020 | V1 |
| AV-241 | 04 - OVERLOOK LEVEL QUAD 1 PLAN | ASI-006 | Jun 3, 2020 | V1 |
| AV-242 | 04 - OVERLOOK LEVEL QUAD 2 PLAN | ASI-006 | Jun 3, 2020 | V1 |
| AV-310 | 01 - EVENT LEVEL OVERALL RCP | 100% CD | Feb 17, 2020 | V2 |
| AV31-01 | SECTIONS | 100% CD | Feb 17, 2020 | V2 |
| AV31-02 | SECTIONS | 100% CD | Feb 17, 2020 | V2 |
| AV-313 | 01 - EVENT LEVEL QUAD 3 RCP | 100% CD | Feb 17, 2020 | V1 |
| AV-314 | 01 - EVENT LEVEL QUAD 4 RCP | 100% CD | Feb 17, 2020 | V2 |
| AV32-01 | VIDEO PRODUCTION ELEVATIONS | 100% CD | Feb 17, 2020 | V2 |
| AV40-01 | VIDEO PRODUCTION ENLARGED PLANS | 100% CD | Feb 17, 2020 | V2 |
| AV-401 | LARGE SCALES | 100% CD | Feb 17, 2020 | V2 |
| AV-402 | LARGE SCALES | 100% CD | Feb 17, 2020 | V2 |
| AV-501 | ONE-LINE DIAGRAM | 100% CD | Feb 17, 2020 | V2 |
| AV-502 | ONE-LINE DIAGRAM | 100% CD | Feb 17, 2020 | V2 |
| AV-503 | ONE-LINE DIAGRAM | ASI-006 | Jun 3, 2020 | V3 |
| AV-601 | DETAILS | 100% CD | Feb 17, 2020 | V2 |
| AV-602 | DETAILS | ASI-006 | Jun 3, 2020 | V3 |
| AV-603 | DETAILS | ASI-006 | Jun 3, 2020 | V3 |
| AV-604 | DETAILS | 100% CD | Feb 17, 2020 | V1 |
| AV-605 | DETAILS | 100% CD | Feb 17, 2020 | V1 |
| AV-701 | DISPLAY SCHEDULE | ASI-006 | Jun 3, 2020 | V2 |
| C02-01 | CONSTRUCTION NOTES AND LEGEND | 100% CD | Feb 17, 2020 | V2 |
| C03-01 | TOPOGRAPHIC SURVEY PLAN | 100% CD | Feb 17, 2020 | V2 |
| C04-01 | STAKING AND TRAFFIC CONTROL PLAN | 100% CD | Feb 17, 2020 | V2 |
| C05-01 | PAVING, GRADING, AND DRAINAGE PLAN | 100% CD | Feb 17, 2020 | V2 |
| C06-01 | SANITARY SEWER AND WATER DISTRIBUTION PLAN | 100% CD | Feb 17, 2020 | V2 |
| C07-01 | SEWER PROFILES | 100% CD | Feb 17, 2020 | V2 |
| C07-02 | WATER PROFILES | 100% CD | Feb 17, 2020 | V2 |

| | | | | |
|---|---|---|---|---|
| C07-03 | DRAINAGE PROFILES | 100% CD | Feb 17, 2020 | V2 |
| C08-01 | CONSTRUCTION DETAILS | 100% CD | Feb 17, 2020 | V2 |
| C08-02 | CONSTRUCTION DETAILS | 100% CD | Feb 17, 2020 | V2 |
| C08-03 | CONSTRUCTION DETAILS | 100% CD | Feb 17, 2020 | V2 |
| C08-04 | CONSTRUCTION DETAILS | 100% CD | Feb 17, 2020 | V2 |
| C08-05 | CONSTRUCTION DETAILS | 100% CD | Feb 17, 2020 | V2 |
| C09-01 | EROSION AND SEDIMENT CONTROL NOTES | 100% CD | Feb 17, 2020 | V2 |
| C09-02 | EROSION AND SEDIMENT CONTROL NOTES | 100% CD | Feb 17, 2020 | V2 |
| C10-01 | EROSION AND SEDIMENT CONTROL PLAN - INITIAL PHASE | 100% CD | Feb 17, 2020 | V2 |
| C10-02 | EROSION AND SEDIMENT CONTROL PLAN - INTERMEDIATE PHASE | 100% CD | Feb 17, 2020 | V2 |
| C10-03 | EROSION AND SEDIMENT CONTROL PLAN - FINAL PHASE | 100% CD | Feb 17, 2020 | V2 |
| C11-01 | EROSION AND SEDIMENT CONTROL DETAILS | 100% CD | Feb 17, 2020 | V2 |
| E00-01 | ELECTRICAL GENERAL NOTES, SYMBOLS, LEGENDS AND ABBREVIATIONS | 100% CD | Feb 17, 2020 | V2 |
| E00-02 | ELECTRICAL SERVICE ONE-LINE | 100% CD | Feb 17, 2020 | V2 |
| E00-03 | ELECTRICAL ONE-LINE - QUAD 1 | 100% CD | Feb 17, 2020 | V2 |
| E00-04 | ELECTRICAL ONE-LINE - QUAD 2 | 100% CD | Feb 17, 2020 | V2 |
| E00-05 | ELECTRICAL ONE-LINE - QUAD 3 | 100% CD | Feb 17, 2020 | V2 |
| E00-06 | ELECTRICAL ONE-LINE - QUAD 4 | 100% CD | Feb 17, 2020 | V2 |
| E00-07 | ELECTRICAL ONE-LINE - EM/LR STBY | 100% CD | Feb 17, 2020 | V2 |
| E00-08 | ELECTRICAL ONE-LINE - STBY | 100% CD | Feb 17, 2020 | V2 |
| E00-20 | ELECTRICAL SCHEDULES | 100% CD | Feb 17, 2020 | V2 |
| E00-30 | LOAD SUMMARIES- MSS1 - RISER 1 | 100% CD | Feb 17, 2020 | V1 |
| E00-31 | PANEL SCHEDULES - MSS1 - RISER1 | 100% CD | Feb 17, 2020 | V1 |
| E00-32 | PANEL SCHEDULES - MSS1 - RISER 1 | 100% CD | Feb 17, 2020 | V1 |
| E00-33 | PANEL SCHEDULES - MSS1 - RISER 1 | 100% CD | Feb 17, 2020 | V1 |
| E00-34 | PANEL SCHEDULES - MSS1 - RISER 1 | 100% CD | Feb 17, 2020 | V1 |
| E00-35 | PANEL SCHEDULES - MSS1 - RISER 1 | 100% CD | Feb 17, 2020 | V1 |
| E00-36 | PANEL SCHEDULES - MSS1 - RISER 1 | 100% CD | Feb 17, 2020 | V1 |
| E00-37 | PANEL SCHEDULES - MSS1 - RISER 1 | 100% CD | Feb 17, 2020 | V1 |
| E00-38 | PANEL SCHEDULES - MSS1 - RISER 1 | 100% CD | Feb 17, 2020 | V1 |
| E00-39 | PANEL SCHEDULES - MSS1 - RISER 1 | 100% CD | Feb 17, 2020 | V1 |
| E00-40 | LOAD SUMMARIES - MSS2 - RISER 2 | 100% CD | Feb 17, 2020 | V1 |
| E00-41 | PANEL SCHEDULES - MSS2 - RISER 2 | 100% CD | Feb 17, 2020 | V1 |
| E00-42 | PANEL SCHEDULES - MSS2 - RISER 2 | 100% CD | Feb 17, 2020 | V1 |
| E00-43 | PANEL SCHEDULES - MSS2 - RISER 2 | 100% CD | Feb 17, 2020 | V1 |
| E00-44 | PANEL SCHEDULES - MSS2 - RISER 2 | 100% CD | Feb 17, 2020 | V1 |
| E00-45 | PANEL SCHEDULES - MSS2 - RISER 2 | 100% CD | Feb 17, 2020 | V1 |
| E00-46 | PANEL SCHEDULES - MSS2 - RISER 2 | 100% CD | Feb 17, 2020 | V1 |
| E00-50 | LOAD SUMMARIES - MSS3 - RISER 3 | 100% CD | Feb 17, 2020 | V1 |
| E00-51 | PANEL SCHEDULES - MSS3 - RISER 3 | 100% CD | Feb 17, 2020 | V1 |
| E00-52 | PANEL SCHEDULES - MSS3 - RISER 3 | 100% CD | Feb 17, 2020 | V1 |
| E00-53 | PANEL SCHEDULES - MSS3 - RISER 3 | 100% CD | Feb 17, 2020 | V1 |

| | | | | |
|---|---|---|---|---|
| E00-54 | PANEL SCHEDULES - MSS3 - RISER 3 | 100% CD | Feb 17, 2020 | V1 |
| E00-55 | PANEL SCHEDULES - MSS3 - RISER 3 | 100% CD | Feb 17, 2020 | V1 |
| E00-60 | LOAD SUMMARIES - MSS3 - RISER 4 | 100% CD | Feb 17, 2020 | V1 |
| E00-61 | PANEL SCHEDULES - MSS3 - RISER 4 | ASI-006 | Jun 3, 2020 | V2 |
| E00-62 | PANEL SCHEDULES - MSS3 - RISER 4 | 100% CD | Feb 17, 2020 | V1 |
| E00-63 | PANEL SCHEDULES - MSS3 - RISER 4 | 100% CD | Feb 17, 2020 | V1 |
| E01-01 | ELECTRICAL SITE PLAN | 100% CD | Feb 17, 2020 | V2 |
| E10-10 | ELECTRICAL EVENT LEVEL - OVERALL FLOOR PLAN | 100% CD | Feb 17, 2020 | V2 |
| E10-11 | ELECTRICAL EVENT LEVEL FLOOR PLAN - QUAD 1 | ASI-006 | Jun 3, 2020 | V3 |
| E10-12 | ELECTRICAL EVENT LEVEL FLOOR PLAN - QUAD 2 | 100% CD | Feb 17, 2020 | V2 |
| E10-13 | ELECTRICAL EVENT LEVEL FLOOR PLAN - QUAD 3 | ASI-006 | Jun 3, 2020 | V3 |
| E10-14 | ELECTRICAL EVENT LEVEL FLOOR PLAN - QUAD 4 | ASI-006 | Jun 3, 2020 | V3 |
| E10-20 | ELECTRICAL CONCOURSE LEVEL - OVERALL FLOOR PLAN | 100% CD | Feb 17, 2020 | V2 |
| E10-21 | ELECTRICAL CONCOURSE LEVEL FLOOR PLAN - QUAD 1 | 100% CD | Feb 17, 2020 | V2 |
| E10-22 | ELECTRICAL CONCOURSE LEVEL FLOOR PLAN - QUAD 2 | 100% CD | Feb 17, 2020 | V2 |
| E10-23 | ELECTRICAL CONCOURSE LEVEL FLOOR PLAN - QUAD 3 | 100% CD | Feb 17, 2020 | V2 |
| E10-24 | ELECTRICAL CONCOURSE LEVEL FLOOR PLAN - QUAD 4 | 100% CD | Feb 17, 2020 | V2 |
| E10-30 | ELECTRICAL SUITE LEVEL - OVERALL FLOOR PLAN | 100% CD | Feb 17, 2020 | V2 |
| E10-31 | ELECTRICAL SUITE LEVEL FLOOR PLAN - QUAD 1 | ASI-006 | Jun 3, 2020 | V3 |
| E10-32 | ELECTRICAL SUITE LEVEL FLOOR PLAN - QUAD 2 | 100% CD | Feb 17, 2020 | V2 |
| E10-33 | ELECTRICAL SUITE LEVEL FLOOR PLAN - QUAD 3 | 100% CD | Feb 17, 2020 | V2 |
| E10-34 | ELECTRICAL SUITE LEVEL FLOOR PLAN - QUAD 4 | 100% CD | Feb 17, 2020 | V2 |
| E10-40 | ELECTRICAL OVERLOOK LEVEL - OVERALL FLOOR PLAN | 100% CD | Feb 17, 2020 | V2 |
| E10-41 | ELECTRICAL OVERLOOK LEVEL FLOOR PLAN - QUAD 1 | 100% CD | Feb 17, 2020 | V2 |
| E10-42 | ELECTRICAL OVERLOOK LEVEL FLOOR PLAN - QUAD 2 | 100% CD | Feb 17, 2020 | V2 |
| E10-43 | ELECTRICAL OVERLOOK LEVEL FLOOR PLAN - QUAD 3 | 100% CD | Feb 17, 2020 | V2 |
| E10-44 | ELECTRICAL OVERLOOK LEVEL FLOOR PLAN - QUAD 4 | 100% CD | Feb 17, 2020 | V2 |
| E10-50 | ELECTRICAL CATWALK LEVEL - OVERALL FLOOR PLAN | 100% CD | Feb 17, 2020 | V2 |
| E10-51 | ELECTRICAL CATWALK LEVEL FLOOR PLAN - QUAD 1 | 100% CD | Feb 17, 2020 | V2 |
| E10-52 | ELECTRICAL CATWALK LEVEL FLOOR PLAN - QUAD 2 | 100% CD | Feb 17, 2020 | V2 |
| E10-53 | ELECTRICAL CATWALK LEVEL FLOOR PLAN - QUAD 3 | 100% CD | Feb 17, 2020 | V2 |
| E10-54 | ELECTRICAL CATWALK LEVEL FLOOR PLAN - QUAD 4 | 100% CD | Feb 17, 2020 | V2 |

| | | | | |
|---|---|---|---|---|
| E10-60 | ELECTRICAL ROOF LEVEL - OVERALL PLAN | 100% CD | Feb 17, 2020 | V2 |
| E20-01 | ELECTRICAL ENLARGED PLANS - QUAD 1 | 100% CD | Feb 17, 2020 | V2 |
| E20-02 | ELECTRICAL ENLARGED PLANS - QUAD 1 | 100% CD | Feb 17, 2020 | V2 |
| E20-03 | ELECTRICAL ENLARGED PLANS - QUAD 2 | 100% CD | Feb 17, 2020 | V2 |
| E20-04 | ELECTRICAL ENLARGED PLANS - QUAD 3 & 4 | 100% CD | Feb 17, 2020 | V2 |
| E20-05 | ENLARGED ELECTRICAL PLANS - TYPICAL VIEWS | 100% CD | Feb 17, 2020 | V2 |
| E80-01 | ELECTRICAL DETAILS | 100% CD | Feb 17, 2020 | V2 |
| E80-02 | ELECTRICAL DETAILS | 100% CD | Feb 17, 2020 | V2 |
| E80-03 | ELECTRICAL DETAILS | 100% CD | Feb 17, 2020 | V2 |
| E80-04 | ELECTRICAL DETAILS | 100% CD | Feb 17, 2020 | V2 |
| E80-05 | ELECTRICAL DETAILS | 100% CD | Feb 17, 2020 | V1 |
| EFS00-01 | ELECTRICAL GENERAL NOTES, SYMBOLS, LEGENDS, AND ABBREVIATIONS | 100% CD | Feb 17, 2020 | V2 |
| EFS20-10 | ELECTRICAL FOOD SERVICE EVENT LEVEL - OVERALL FLOOR PLAN | 100% CD | Feb 17, 2020 | V2 |
| EFS20-11 | ELECTRICAL FOOD SERVICE ENLARGED PLANS EVENT LEVEL - QUADS 1&2 | 100% CD | Feb 17, 2020 | V2 |
| EFS20-12 | ELECTRICAL FOOD SERVICE ENLARGED PLANS EVENT LEVEL - QUAD 3 | 100% CD | Feb 17, 2020 | V2 |
| EFS20-20 | ELECTRICAL FOOD SERVICE CONCOURSE LEVEL - OVERALL FLOOR PLAN | 100% CD | Feb 17, 2020 | V2 |
| EFS20-21 | ELECTRICAL FOOD SERVICE ENLARGED PLANS CONCOURSE LEVEL - QUAD 1 | 100% CD | Feb 17, 2020 | V2 |
| EFS20-22 | ELECTRICAL FOOD SERVICE ENLARGED PLANS CONCOURSE LEVEL - QUAD 2 | 100% CD | Feb 17, 2020 | V2 |
| EFS20-23 | ELECTRICAL FOOD SERVICE ENLARGED PLANS CONCOURSE LEVEL - QUAD 3 | 100% CD | Feb 17, 2020 | V2 |
| EFS20-24 | ELECTRICAL FOOD SERVICE ENLARGED PLANS CONCOURSE LEVEL - QUAD 4 | 100% CD | Feb 17, 2020 | V2 |
| EFS20-30 | ELECTRICAL FOOD SERVICE SUITE LEVEL - OVERALL FLOOR PLAN | 100% CD | Feb 17, 2020 | V2 |
| EFS20-31 | ELECTRICAL FOOD SERVICE ENLARGED PLANS SUITE LEVEL - QUAD 1 | 100% CD | Feb 17, 2020 | V2 |
| EFS20-32 | ELECTRICAL FOOD SERVICE ENLARGED PLANS SUITE LEVEL - QUAD 2 | 100% CD | Feb 17, 2020 | V2 |
| EFS20-40 | ELECTRICAL FOOD SERVICE OVERLOOK LEVEL - OVERALL FLOOR PLAN | 100% CD | Feb 17, 2020 | V2 |
| EFS20-41 | ELECTRICAL FOOD SERVICE ENLARGED PLANS OVERLOOK LEVEL - QUAD 1 | 100% CD | Feb 17, 2020 | V2 |
| EFS20-42 | ELECTRICAL FOOD SERVICE ENLARGED PLANS OVERLOOK LEVEL - QUAD 2 | 100% CD | Feb 17, 2020 | V2 |
| EFS20-43 | ELECTRICAL FOOD SERVICE ENLARGED PLANS OVERLOOK LEVEL - QUAD 3 | 100% CD | Feb 17, 2020 | V2 |
| EFS20-50 | ELECTRICAL FOOD SERVICE CATWALK LEVEL - OVERALL FLOOR PLAN | 100% CD | Feb 17, 2020 | V1 |
| EFS20-51 | ELECTRICAL FOOD SERVICE CATWALK LEVEL - QUAD 1 | 100% CD | Feb 17, 2020 | V1 |

| | | | | |
|---|---|---|---|---|
| EFS20-52 | ELECTRICAL FOOD SERVICE CATWALK LEVEL - QUAD 2 | 100% CD | Feb 17, 2020 | V1 |
| EFS20-53 | ELECTRICAL FOOD SERVICE CATWALK LEVEL - QUAD 3 | 100% CD | Feb 17, 2020 | V1 |
| EFS20-54 | ELECTRICAL FOOD SERVICE CATWALK LEVEL - QUAD 4 | 100% CD | Feb 17, 2020 | V1 |
| EFS50-10 | ELECTRICAL FOOD SERVICE DETAIL | 100% CD | Feb 17, 2020 | V1 |
| EFS90-01 | ELECTRICAL FOOD SERVICE SCHEDULES | 100% CD | Feb 17, 2020 | V1 |
| EFS90-02 | ELECTRICAL FOOD SERVICE SCHEDULES | 100% CD | Feb 17, 2020 | V1 |
| EFS90-03 | ELECTRICAL FOOD SERVICE SCHEDULES | 100% CD | Feb 17, 2020 | V1 |
| EFS90-04 | ELECTRICAL FOOD SERVICE SCHEDULES | 100% CD | Feb 17, 2020 | V1 |
| EFS90-05 | ELECTRICAL FOOD SERVICE SCHEDULES | 100% CD | Feb 17, 2020 | V1 |
| EL00-01 | NETWORK LIGHTING CONTROL ONE-LINE | 100% CD | Feb 17, 2020 | V2 |
| EL00-02 | SPORTS LIGHTING CONTROL ONE-LINE | 100% CD | Feb 17, 2020 | V2 |
| EL00-03 | DIMMING CONTROL ONE-LINES AND DETAILS | 100% CD | Feb 17, 2020 | V2 |
| EL00-04 | LIGHTING CONTROL MATRIX AND NARRATIVE | 100% CD | Feb 17, 2020 | V2 |
| EL00-10 | PREMIUM LIGHTING FIXTURE SCHEDULE | 100% CD | Feb 17, 2020 | V2 |
| EL00-11 | PREMIUM LIGHTING FIXTURE SCHEDULE | 100% CD | Feb 17, 2020 | V1 |
| EL00-20 | LIGHTING COMPLIANCE REPORT | 100% CD | Feb 17, 2020 | V1 |
| EL01-01 | LIGHTING SITE PLAN | 100% CD | Feb 17, 2020 | V1 |
| EL01-02 | LIGHTING SITE ENLARGED PLANS | 100% CD | Feb 17, 2020 | V1 |
| EL10-11 | PREMIUM LIGHTING EVENT LEVEL FLOOR PLAN - QUAD 1 | 100% CD | Feb 17, 2020 | V2 |
| EL10-12 | PREMIUM LIGHTING EVENT LEVEL FLOOR PLAN - QUAD 2 | 100% CD | Feb 17, 2020 | V2 |
| EL10-13 | PREMIUM LIGHTING EVENT LEVEL FLOOR PLAN - QUAD 3 | 100% CD | Feb 17, 2020 | V2 |
| EL10-14 | PREMIUM LIGHTING EVENT LEVEL FLOOR PLAN - QUAD 4 | 100% CD | Feb 17, 2020 | V2 |
| EL10-21 | PREMIUM LIGHTING CONCOURSE LEVEL FLOOR PLAN - QUAD 1 | 100% CD | Feb 17, 2020 | V2 |
| EL10-22 | PREMIUM LIGHTING CONCOURSE LEVEL FLOOR PLAN - QUAD 2 | 100% CD | Feb 17, 2020 | V2 |
| EL10-23 | PREMIUM LIGHTING CONCOURSE LEVEL FLOOR PLAN - QUAD 3 | 100% CD | Feb 17, 2020 | V2 |
| EL10-24 | PREMIUM LIGHTING CONCOURSE LEVEL FLOOR PLAN - QUAD 4 | 100% CD | Feb 17, 2020 | V2 |
| EL10-31 | PREMIUM LIGHTING SUITE LEVEL FLOOR PLAN - QUAD 1 | 100% CD | Feb 17, 2020 | V2 |
| EL10-32 | PREMIUM LIGHTING SUITE LEVEL FLOOR PLAN - QUAD 2 | 100% CD | Feb 17, 2020 | V2 |
| EL10-33 | PREMIUM LIGHTING SUITE LEVEL FLOOR PLAN - QUAD 3 | 100% CD | Feb 17, 2020 | V2 |
| EL10-34 | PREMIUM LIGHTING SUITE LEVEL FLOOR PLAN - QUAD 4 | 100% CD | Feb 17, 2020 | V1 |
| EL10-41 | PREMIUM LIGHTING OVERLOOK LEVEL FLOOR PLAN - QUAD 1 | 100% CD | Feb 17, 2020 | V2 |
| EL10-42 | PREMIUM LIGHTING OVERLOOK LEVEL FLOOR PLAN - QUAD 2 | 100% CD | Feb 17, 2020 | V2 |
| EL10-43 | PREMIUM LIGHTING OVERLOOK LEVEL FLOOR PLAN - QUAD 3 | 100% CD | Feb 17, 2020 | V2 |

| | | | | |
|---|---|---|---|---|
| EL10-44 | PREMIUM LIGHTING OVERLOOK LEVEL FLOOR PLAN - QUAD 4 | 100% CD | Feb 17, 2020 | V2 |
| EL10-51 | PREMIUM LIGHTING CATWALK LEVEL FLOOR PLAN - QUAD 1 | 100% CD | Feb 17, 2020 | V2 |
| EL10-52 | PREMIUM LIGHTING CATWALK LEVEL FLOOR PLAN - QUAD 2 | 100% CD | Feb 17, 2020 | V2 |
| EL10-53 | PREMIUM LIGHTING CATWALK LEVEL FLOOR PLAN - QUAD 3 | 100% CD | Feb 17, 2020 | V2 |
| EL10-54 | PREMIUM LIGHTING CATWALK LEVEL FLOOR PLAN - QUAD 4 | 100% CD | Feb 17, 2020 | V2 |
| EL20-01 | ELECTRICAL GENERAL NOTES, SYMBOLS, LEGENDS, AND ABBREVIATIONS | 100% CD | Feb 17, 2020 | V2 |
| EL20-05 | ELECTRICAL LIGHTING FIXTURE SCHEDULE | 100% CD | Feb 17, 2020 | V2 |
| EL20-10 | ELECTRICAL LIGHTING EVENT LEVEL - OVERALL FLOOR PLAN | 100% CD | Feb 17, 2020 | V1 |
| EL20-11 | ELECTRICAL LIGHTING EVENT LEVEL FLOOR PLAN - QUAD 1 | 100% CD | Feb 17, 2020 | V2 |
| EL20-12 | ELECTRICAL LIGHTING EVENT LEVEL FLOOR PLAN - QUAD 2 | 100% CD | Feb 17, 2020 | V2 |
| EL20-13 | ELECTRICAL LIGHTING EVENT LEVEL FLOOR PLAN - QUAD 3 | 100% CD | Feb 17, 2020 | V2 |
| EL20-14 | ELECTRICAL LIGHTING EVENT LEVEL FLOOR PLAN - QUAD 4 | 100% CD | Feb 17, 2020 | V2 |
| EL20-20 | ELECTRICAL LIGHTING CONCOURSE LEVEL - OVERALL FLOOR PLAN | 100% CD | Feb 17, 2020 | V1 |
| EL20-21 | ELECTRICAL LIGHTING CONCOURSE LEVEL FLOOR PLAN - QUAD 1 | 100% CD | Feb 17, 2020 | V2 |
| EL20-22 | ELECTRICAL LIGHTING CONCOURSE LEVEL FLOOR PLAN - QUAD 2 | 100% CD | Feb 17, 2020 | V2 |
| EL20-23 | ELECTRICAL LIGHTING CONCOURSE LEVEL FLOOR PLAN - QUAD 3 | 100% CD | Feb 17, 2020 | V2 |
| EL20-24 | ELECTRICAL LIGHTING CONCOURSE LEVEL FLOOR PLAN - QUAD 4 | 100% CD | Feb 17, 2020 | V2 |
| EL20-30 | ELECTRICAL LIGHTING SUITE LEVEL - OVERALL FLOOR PLAN | 100% CD | Feb 17, 2020 | V1 |
| EL20-31 | ELECTRICAL LIGHTING SUITE LEVEL FLOOR PLAN - QUAD 1 | 100% CD | Feb 17, 2020 | V2 |
| EL20-32 | ELECTRICAL LIGHTING SUITE LEVEL FLOOR PLAN - QUAD 2 | 100% CD | Feb 17, 2020 | V2 |
| EL20-33 | ELECTRICAL LIGHTING SUITE LEVEL FLOOR PLAN - QUAD 3 | 100% CD | Feb 17, 2020 | V2 |
| EL20-40 | ELECTRICAL LIGHTING OVERLOOK LEVEL - OVERALL FLOOR PLAN | 100% CD | Feb 17, 2020 | V1 |
| EL20-41 | ELECTRICAL LIGHTING OVERLOOK LEVEL FLOOR PLAN - QUAD 1 | 100% CD | Feb 17, 2020 | V2 |
| EL20-42 | ELECTRICAL LIGHTING OVERLOOK LEVEL FLOOR PLAN - QUAD 2 | 100% CD | Feb 17, 2020 | V2 |
| EL20-43 | ELECTRICAL LIGHTING OVERLOOK LEVEL FLOOR PLAN - QUAD 3 | 100% CD | Feb 17, 2020 | V2 |
| EL20-51 | ELECTRICAL LIGHTING CATWALK LEVEL FLOOR PLAN- QUAD 1 | 100% CD | Feb 17, 2020 | V1 |
| EL20-53 | ELECTRICAL LIGHTING CATWALK LEVEL FLOOR PLAN- QUAD 3 | 100% CD | Feb 17, 2020 | V1 |
| EL30-00 | LIGHTING ENLARGED PLANS- TYPICAL VIEWS | 100% CD | Feb 17, 2020 | V2 |
| EL30-01 | LIGHTING SECTIONS | 100% CD | Feb 17, 2020 | V1 |

| | | | | |
|---|---|---|---|---|
| EL40-00 | SPORTS LIGHTING REFERENCE PLAN | 100% CD | Feb 17, 2020 | V2 |
| EL40-01 | SPORTS LIGHTING SECTIONS & DETAILS | 100% CD | Feb 17, 2020 | V2 |
| EL41-00 | AISLE LIGHTING REFERNCE PLAN | 100% CD | Feb 17, 2020 | V2 |
| FA20-00 | ELECTRICAL GENERAL NOTES, SYMBOLS, LEGENDS, AND ABBREVIATIONS | 100% CD | Feb 17, 2020 | V1 |
| FA20-10 | FIRE ALARM EVENT LEVEL - OVERALL FLOOR PLAN | 100% CD | Feb 17, 2020 | V2 |
| FA20-11 | FIRE ALARM EVENT LEVEL FLOOR PLAN - QUAD 1 | 100% CD | Feb 17, 2020 | V2 |
| FA20-12 | FIRE ALARM EVENT LEVEL FLOOR PLAN - QUAD 2 | 100% CD | Feb 17, 2020 | V2 |
| FA20-13 | FIRE ALARM EVENT LEVEL FLOOR PLAN - QUAD 3 | 100% CD | Feb 17, 2020 | V2 |
| FA20-14 | FIRE ALARM EVENT LEVEL FLOOR PLAN - QUAD 4 | 100% CD | Feb 17, 2020 | V2 |
| FA20-20 | FIRE ALARM CONCOURSE LEVEL - OVERALL FLOOR PLAN | 100% CD | Feb 17, 2020 | V2 |
| FA20-21 | FIRE ALARM CONCOURSE LEVEL FLOOR PLAN - QUAD 1 | 100% CD | Feb 17, 2020 | V2 |
| FA20-22 | FIRE ALARM CONCOURSE LEVEL FLOOR PLAN - QUAD 2 | 100% CD | Feb 17, 2020 | V2 |
| FA20-23 | FIRE ALARM CONCOURSE LEVEL FLOOR PLAN - QUAD 3 | 100% CD | Feb 17, 2020 | V2 |
| FA20-24 | FIRE ALARM CONCOURSE LEVEL FLOOR PLAN - QUAD 4 | 100% CD | Feb 17, 2020 | V2 |
| FA20-30 | FIRE ALARM SUITE LEVEL - OVERALL FLOOR PLAN | 100% CD | Feb 17, 2020 | V2 |
| FA20-31 | FIRE ALARM SUITE LEVEL FLOOR PLAN - QUAD 1 | 100% CD | Feb 17, 2020 | V2 |
| FA20-32 | FIRE ALARM SUITE LEVEL FLOOR PLAN - QUAD 2 | 100% CD | Feb 17, 2020 | V2 |
| FA20-33 | FIRE ALARM SUITE LEVEL FLOOR PLAN - QUAD 3 | 100% CD | Feb 17, 2020 | V2 |
| FA20-34 | FIRE ALARM SUITE LEVEL FLOOR PLAN - QUAD 4 | 100% CD | Feb 17, 2020 | V2 |
| FA20-40 | FIRE ALARM OVERLOOK LEVEL - OVERALL FLOOR PLAN | 100% CD | Feb 17, 2020 | V2 |
| FA20-41 | FIRE ALARM OVERLOOK LEVEL FLOOR PLAN - QUAD 1 | 100% CD | Feb 17, 2020 | V2 |
| FA20-42 | FIRE ALARM OVERLOOK LEVEL FLOOR PLAN - QUAD 2 | 100% CD | Feb 17, 2020 | V2 |
| FA20-43 | FIRE ALARM OVERLOOK LEVEL FLOOR PLAN - QUAD 3 | 100% CD | Feb 17, 2020 | V2 |
| FA20-44 | FIRE ALARM OVERLOOK LEVEL FLOOR PLAN - QUAD 4 | 100% CD | Feb 17, 2020 | V2 |
| FA20-50 | FIRE ALARM CATWALK LEVEL - OVERALL FLOOR PLAN | 100% CD | Feb 17, 2020 | V2 |
| FA20-51 | FIRE ALARM CATWALK LEVEL FLOOR PLAN - QUAD 1 | 100% CD | Feb 17, 2020 | V2 |
| FA20-52 | FIRE ALARM CATWALK LEVEL FLOOR PLAN - QUAD 2 | 100% CD | Feb 17, 2020 | V2 |
| FA20-53 | FIRE ALARM CATWALK LEVEL FLOOR PLAN - QUAD 3 | 100% CD | Feb 17, 2020 | V2 |
| FA20-54 | FIRE ALARM CATWALK LEVEL FLOOR PLAN - QUAD 4 | 100% CD | Feb 17, 2020 | V2 |
| FP00-1 | FIRE PROTECTION GENERAL NOTES, SYMBOLS, LEGENDS AND ABBREVIATIONS | 100% CD | Feb 17, 2020 | V2 |
| FP10-10 | FIRE PROTECTION EVENT LEVEL - OVERALL FLOOR PLAN | 100% CD | Feb 17, 2020 | V2 |
| FP10-100 | FIRE PROTECTION CONCOURSE LEVEL FLOOR PLAN - QUAD 4 | 100% CD | Feb 17, 2020 | V2 |

| | | | | |
|---|---|---|---|---|
| FP10-110 | FIRE PROTECTION SUITE LEVEL - OVERALL FLOOR PLAN | 100% CD | Feb 17, 2020 | V2 |
| FP10-120 | FIRE PROTECTION SUITE LEVEL FLOOR PLAN - QUAD 1 | 100% CD | Feb 17, 2020 | V2 |
| FP10-130 | FIRE PROTECTION SUITE LEVEL FLOOR PLAN - QUAD 2 | 100% CD | Feb 17, 2020 | V2 |
| FP10-140 | FIRE PROTECTION SUITE LEVEL FLOOR PLAN - QUAD 3 | 100% CD | Feb 17, 2020 | V2 |
| FP10-150 | FIRE PROTECTION SUITE LEVEL FLOOR PLAN - QUAD 4 | 100% CD | Feb 17, 2020 | V2 |
| FP10-160 | FIRE PROTECTION OVERLOOK LEVEL - OVERALL FLOOR PLAN | 100% CD | Feb 17, 2020 | V2 |
| FP10-170 | FIRE PROTECTION OVERLOOK LEVEL FLOOR PLAN - QUAD 1 | 100% CD | Feb 17, 2020 | V2 |
| FP10-180 | FIRE PROTECTION OVERLOOK LEVEL FLOOR PLAN - QUAD 2 | 100% CD | Feb 17, 2020 | V2 |
| FP10-190 | FIRE PROTECTION OVERLOOK LEVEL FLOOR PLAN - QUAD 3 | 100% CD | Feb 17, 2020 | V2 |
| FP10-20 | FIRE PROTECTION EVENT LEVEL FLOOR PLAN - QUAD 1 | 100% CD | Feb 17, 2020 | V2 |
| FP10-200 | FIRE PROTECTION OVERLOOK LEVEL FLOOR PLAN - QUAD 4 | 100% CD | Feb 17, 2020 | V2 |
| FP10-30 | FIRE PROTECTION EVENT LEVEL FLOOR PLAN - QUAD 2 | 100% CD | Feb 17, 2020 | V2 |
| FP10-40 | FIRE PROTECTION EVENT LEVEL FLOOR PLAN - QUAD 3 | 100% CD | Feb 17, 2020 | V2 |
| FP10-50 | FIRE PROTECTION EVENT LEVEL FLOOR PLAN - QUAD 4 | 100% CD | Feb 17, 2020 | V2 |
| FP10-60 | FIRE PROTECTION CONCOURSE LEVEL - OVERALL FLOOR PLAN | 100% CD | Feb 17, 2020 | V2 |
| FP10-70 | FIRE PROTECTION CONCOURSE LEVEL FLOOR PLAN - QUAD 1 | 100% CD | Feb 17, 2020 | V2 |
| FP10-80 | FIRE PROTECTION CONCOURSE LEVEL FLOOR PLAN - QUAD 2 | 100% CD | Feb 17, 2020 | V2 |
| FP10-90 | FIRE PROTECTION CONCOURSE LEVEL FLOOR PLAN - QUAD 3 | 100% CD | Feb 17, 2020 | V2 |
| FP50-10 | FIRE PROTECTION DETAILS | 100% CD | Feb 17, 2020 | V2 |
| FP50-20 | FIRE PROTECTION DETAILS | 100% CD | Feb 17, 2020 | V2 |
| FSMEP-01 | SCHEDULES | 100% CD | Feb 17, 2020 | V1 |
| FSMEP-02 | SCHEDULES | 100% CD | Feb 17, 2020 | V1 |
| G00-01 | GENERAL NOTES, SYMBOLS, LEGENDS AND ABBREVIATIONS | 100% CD | Feb 17, 2020 | V2 |
| G00-02 | DRAWING INDEX - VOLUME 1 | 100% CD | Feb 17, 2020 | V2 |
| G00-03 | DRAWING INDEX - VOLUME 2 | 100% CD | Feb 17, 2020 | V2 |
| G00-04 | DRAWING INDEX - VOLUME 3 | 100% CD | Feb 17, 2020 | V2 |
| G00-05 | DRAWING INDEX - VOLUME 4 | 100% CD | Feb 17, 2020 | V1 |
| G01-01 | CODE COMPLIANCE DATA | ASI-003 | Apr 20, 2020 | V3 |
| G01-02 | FIRE RESISTIVE ASSEMBLY REFERENCE SHEET | 100% CD | Feb 17, 2020 | V2 |
| G01-03 | FIRE RESISTIVE ASSEMBLY REFERENCE SHEET | 100% CD | Feb 17, 2020 | V2 |
| G01-04 | FIRE RESISTIVE ASSEMBLY REFERENCE SHEET | 100% CD | Feb 17, 2020 | V2 |
| G01-05 | FIRE RESISTIVE ASSEMBLY REFERENCE SHEET | 100% CD | Feb 17, 2020 | V2 |
| G01-06 | FIRE RESISTANCE DETAILS AND DIAGRAMS | 100% CD | Feb 17, 2020 | V1 |

| | | | | |
|---|---|---|---|---|
| G01-07 | FIRE RESISTANCE DETAILS AND DIAGRAMS | 100% CD | Feb 17, 2020 | V1 |
| G01-11 | CODE COMPLIANCE PLAN - EVENT LEVEL 1 01 | ASI-003 | Apr 20, 2020 | V3 |
| G01-12 | CODE COMPLIANCE 1 PLAN - CONCOURSE LEVEL 02 | ASI-003 | Apr 20, 2020 | V3 |
| G01-13 | CODE COMPLIANCE PLAN - SUITE LEVEL 03 | ASI-003 | Apr 20, 2020 | V3 |
| G01-14 | CODE COMPLIANCE 1 PLAN - OVERLOOK LEVEL 04 | ASI-003 | Apr 20, 2020 | V3 |
| IS0-1 | ICE SYSTEM LEGEND AND SCHEDULES | 100% CD | Feb 17, 2020 | V2 |
| IS1-1 | REFERENCE PLAN - EVENT LEVEL ICE SHEET | 100% CD | Feb 17, 2020 | V2 |
| IS3-1 | ICE SHEET ENLARGED PLANS | 100% CD | Feb 17, 2020 | V2 |
| IS4-1 | ICE SHEET SCHEMATIC DIAGRAMS | 100% CD | Feb 17, 2020 | V2 |
| IS8-1 | ICE SHEET DETAILS | 100% CD | Feb 17, 2020 | V2 |
| L-01 | LANDSCAPE PLAN | Amendment 1 | Mar 19, 2020 | V1 |
| L-02 | LANDSCAPE PLAN | Amendment 1 | Mar 19, 2020 | V1 |
| L-03 | SITE ACCESSORIES PLAN | Amendment 1 | Mar 19, 2020 | V1 |
| LV-000 | COVER PAGE | ASI-006 | Jun 3, 2020 | V3 |
| LV-100 | SITE PLAN | 100% CD | Feb 17, 2020 | V2 |
| LV-210 | 01 - EVENT LEVEL OVERALL PLAN | 100% CD | Feb 17, 2020 | V2 |
| LV-211 | 01 - EVENT LEVEL QUAD 1 PLAN | ASI-006 | Jun 3, 2020 | V3 |
| LV-212 | 01 - EVENT LEVEL QUAD 2 PLAN | ASI-006 | Jun 3, 2020 | V3 |
| LV-213 | 01 - EVENT LEVEL QUAD 3 PLAN | ASI-006 | Jun 3, 2020 | V3 |
| LV-214 | 01 - EVENT LEVEL QUAD 4 PLAN | ASI-006 | Jun 3, 2020 | V3 |
| LV-220 | 02 - CONCOURSE LEVEL OVERALL PLAN | 100% CD | Feb 17, 2020 | V2 |
| LV-221 | 02 - CONCOURSE LEVEL QUAD 1 PLAN | 100% CD | Feb 17, 2020 | V2 |
| LV-222 | 02 - CONCOURSE LEVEL QUAD 2 PLAN | 100% CD | Feb 17, 2020 | V2 |
| LV-223 | 02 - CONCOURSE LEVEL QUAD 3 PLAN | 100% CD | Feb 17, 2020 | V2 |
| LV-224 | 02 - CONCOURSE LEVEL QUAD 4 PLAN | 100% CD | Feb 17, 2020 | V2 |
| LV-230 | 03 - SUITE LEVEL OVERALL PLAN | 100% CD | Feb 17, 2020 | V2 |
| LV-231 | 03 - SUITE LEVEL QUAD 1 PLAN | ASI-006 | Jun 3, 2020 | V3 |
| LV-232 | 03 - SUITE LEVEL QUAD 2 PLAN | 100% CD | Feb 17, 2020 | V2 |
| LV-233 | 03 - SUITE LEVEL QUAD 3 PLAN | 100% CD | Feb 17, 2020 | V2 |
| LV-234 | 03 - SUITE LEVEL QUAD 4 PLAN | 100% CD | Feb 17, 2020 | V2 |
| LV-240 | 04 - OVERLOOK LEVEL OVERALL PLAN | 100% CD | Feb 17, 2020 | V2 |
| LV-241 | 04 - OVERLOOK LEVEL QUAD 1 PLAN | 100% CD | Feb 17, 2020 | V2 |
| LV-242 | 04 - OVERLOOK LEVEL QUAD 2 PLAN | 100% CD | Feb 17, 2020 | V2 |
| LV-243 | 04 - OVERLOOK LEVEL QUAD 3 PLAN | 100% CD | Feb 17, 2020 | V2 |
| LV-244 | 04 - OVERLOOK LEVEL QUAD 4 PLAN | 100% CD | Feb 17, 2020 | V2 |
| LV-250 | 05 - CATWALK LEVEL OVERALL PLAN | 100% CD | Feb 17, 2020 | V2 |
| LV-251 | 05 - CATWALK LEVEL QUAD 1 PLAN | 100% CD | Feb 17, 2020 | V2 |
| LV-252 | 05 - CATWALK LEVEL QUAD 2 PLAN | 100% CD | Feb 17, 2020 | V2 |
| LV-253 | 05 - CATWALK LEVEL QUAD 3 PLAN | 100% CD | Feb 17, 2020 | V2 |
| LV-254 | 05 - CATWALK LEVEL QUAD 4 PLAN | 100% CD | Feb 17, 2020 | V2 |
| LV-401 | LARGE SCALES | ASI-006 | Jun 3, 2020 | V3 |
| LV-402 | LARGE SCALES | ASI-006 | Jun 3, 2020 | V3 |

| | | | | |
|---|---|---|---|---|
| LV-403 | LARGE SCALES | ASI-006 | Jun 3, 2020 | V3 |
| LV-404 | LARGE SCALES | ASI-006 | Jun 3, 2020 | V3 |
| LV-405 | LARGE SCALES | ASI-006 | Jun 3, 2020 | V3 |
| LV-406 | LARGE SCALES | ASI-006 | Jun 3, 2020 | V3 |
| LV-407 | LARGE SCALES | ASI-006 | Jun 3, 2020 | V3 |
| LV-408 | LARGE SCALES | 100% CD | Feb 17, 2020 | V2 |
| LV-501 | ONE-LINE DIAGRAM - CONDUIT/CABLE TRAY | 100% CD | Feb 17, 2020 | V2 |
| LV-502 | ONE-LINE DIAGRAM - DATA | ASI-006 | Jun 3, 2020 | V3 |
| LV-503 | ONE-LINE DIAGRAM - VOICE | 100% CD | Feb 17, 2020 | V2 |
| LV-504 | ONE-LINE DIAGRAM - GROUNDING | 100% CD | Feb 17, 2020 | V2 |
| LV-505 | ONE-LINE DIAGRAM - VIDEO SURVEILLANCE | ASI-006 | Jun 3, 2020 | V3 |
| LV-506 | ONE-LINE DIAGRAM - ACCESS CONTROL | 100% CD | Feb 17, 2020 | V2 |
| LV-601 | TELECOM DETAILS | 100% CD | Feb 17, 2020 | V2 |
| LV-602 | TELECOM DETAILS | 100% CD | Feb 17, 2020 | V2 |
| LV-603 | TELECOM DETAILS | 100% CD | Feb 17, 2020 | V2 |
| LV-604 | TELECOM DETAILS | 100% CD | Feb 17, 2020 | V2 |
| LV-605 | SECURITY DETAILS | 100% CD | Feb 17, 2020 | V1 |
| LV-606 | SECURITY DETAILS | 100% CD | Feb 17, 2020 | V1 |
| LV-607 | TELECOM DETAILS | 100% CD | Feb 17, 2020 | V1 |
| LV-608 | SECURITY DETAILS | ASI-006 | Jun 3, 2020 | V2 |
| LV-609 | SECURITY DETAILS | ASI-006 | Jun 3, 2020 | V2 |
| LV-610 | SECURITY DETAILS | ASI-006 | Jun 3, 2020 | V2 |
| LV-701 | CAMERA SCHEDULE | 100% CD | Feb 17, 2020 | V2 |
| M00-01 | MECHANICAL GENERAL NOTES, SYMBOLS, LEGENDS AND ABBREVIATIONS | 100% CD | Feb 17, 2020 | V2 |
| M00-02 | MECHANICAL GENERAL NOTES | 100% CD | Feb 17, 2020 | V2 |
| M10-10 | MECHANICAL EVENT LEVEL - OVERALL FLOOR PLAN | 100% CD | Feb 17, 2020 | V2 |
| M10-11 | MECHANICAL EVENT LEVEL FLOOR PLAN - QUAD 1 | 100% CD | Feb 17, 2020 | V2 |
| M10-12 | MECHANICAL EVENT LEVEL FLOOR PLAN - QUAD 2 | 100% CD | Feb 17, 2020 | V2 |
| M10-13 | MECHANICAL EVENT LEVEL FLOOR PLAN - QUAD 3 | 100% CD | Feb 17, 2020 | V2 |
| M10-14 | MECHANICAL EVENT LEVEL FLOOR PLAN - QUAD 4 | 100% CD | Feb 17, 2020 | V2 |
| M10-20 | MECHANICAL CONCOURSE LEVEL - OVERALL FLOOR PLAN | 100% CD | Feb 17, 2020 | V2 |
| M10-21 | MECHANICAL CONCOURSE LEVEL FLOOR PLAN - QUAD 1 | 100% CD | Feb 17, 2020 | V2 |
| M10-22 | MECHANICAL CONCOURSE LEVEL FLOOR PLAN - QUAD 2 | 100% CD | Feb 17, 2020 | V2 |
| M10-23 | MECHANICAL CONCOURSE LEVEL FLOOR PLAN - QUAD 3 | 100% CD | Feb 17, 2020 | V2 |
| M10-24 | MECHANICAL CONCOURSE LEVEL FLOOR PLAN - QUAD 4 | 100% CD | Feb 17, 2020 | V2 |
| M10-30 | MECHANICAL SUITE LEVEL - OVERALL FLOOR PLAN | 100% CD | Feb 17, 2020 | V2 |
| M10-31 | MECHANICAL SUITE LEVEL FLOOR PLAN - QUAD 1 | 100% CD | Feb 17, 2020 | V2 |
| M10-32 | MECHANICAL SUITE LEVEL FLOOR PLAN - QUAD 2 | 100% CD | Feb 17, 2020 | V2 |
| M10-33 | MECHANICAL SUITE LEVEL FLOOR PLAN - QUAD 3 | 100% CD | Feb 17, 2020 | V2 |
| M10-34 | MECHANICAL SUITE LEVEL FLOOR PLAN - QUAD 4 | 100% CD | Feb 17, 2020 | V2 |

| | | | | |
|---|---|---|---|---|
| M10-40 | MECHANICAL OVERLOOK LEVEL - OVERALL FLOOR PLAN | 100% CD | Feb 17, 2020 | V2 |
| M10-41 | MECHANICAL OVERLOOK LEVEL FLOOR PLAN - QUAD 1 | 100% CD | Feb 17, 2020 | V2 |
| M10-42 | MECHANICAL OVERLOOK LEVEL FLOOR PLAN - QUAD 2 | 100% CD | Feb 17, 2020 | V2 |
| M10-43 | MECHANICAL OVERLOOK LEVEL FLOOR PLAN - QUAD 3 | 100% CD | Feb 17, 2020 | V2 |
| M10-44 | MECHANICAL OVERLOOK LEVEL FLOOR PLAN - QUAD 4 | 100% CD | Feb 17, 2020 | V2 |
| M10-50 | MECHANICAL CATWALK LEVEL - OVERALL FLOOR PLAN | 100% CD | Feb 17, 2020 | V2 |
| M10-51 | MECHANICAL CATWALK LEVEL FLOOR PLAN - QUAD 1 | 100% CD | Feb 17, 2020 | V2 |
| M10-52 | MECHANICAL CATWALK LEVEL FLOOR PLAN - QUAD 2 | 100% CD | Feb 17, 2020 | V2 |
| M10-53 | MECHANICAL CATWALK LEVEL FLOOR PLAN - QUAD 3 | 100% CD | Feb 17, 2020 | V2 |
| M10-54 | MECHANICAL CATWALK LEVEL FLOOR PLAN - QUAD 4 | 100% CD | Feb 17, 2020 | V2 |
| M11-11 | MECHANICAL PIPING EVENT LEVEL FLOOR PLAN - QUAD 1 | 100% CD | Feb 17, 2020 | V2 |
| M11-12 | MECHANICAL PIPING EVENT LEVEL FLOOR PLAN - QUAD 2 | 100% CD | Feb 17, 2020 | V2 |
| M11-13 | MECHANICAL PIPING EVENT LEVEL FLOOR PLAN - QUAD 3 | 100% CD | Feb 17, 2020 | V2 |
| M11-14 | MECHANICAL PIPING EVENT LEVEL FLOOR PLAN - QUAD 4 | 100% CD | Feb 17, 2020 | V2 |
| M11-15 | MECHANICAL PIPING EVENT LEVEL FLOOR PLAN - GARAGE WEST | 100% CD | Feb 17, 2020 | V2 |
| M11-21 | MECHANICAL PIPING CONCOURSE LEVEL FLOOR PLAN - QUAD 1 | 100% CD | Feb 17, 2020 | V2 |
| M11-22 | MECHANICAL PIPING CONCOURSE LEVEL FLOOR PLAN - QUAD 2 | 100% CD | Feb 17, 2020 | V2 |
| M11-23 | MECHANICAL PIPING CONCOURSE LEVEL FLOOR PLAN - QUAD 3 | 100% CD | Feb 17, 2020 | V2 |
| M11-24 | MECHANICAL PIPING CONCOURSE LEVEL FLOOR PLAN - QUAD 4 | 100% CD | Feb 17, 2020 | V2 |
| M11-31 | MECHANICAL PIPING SUITE LEVEL FLOOR PLAN - QUAD 1 | 100% CD | Feb 17, 2020 | V2 |
| M11-32 | MECHANICAL PIPING SUITE LEVEL FLOOR PLAN - QUAD 2 | 100% CD | Feb 17, 2020 | V2 |
| M11-33 | MECHANICAL PIPING SUITE LEVEL FLOOR PLAN - QUAD 3 | 100% CD | Feb 17, 2020 | V2 |
| M11-34 | MECHANICAL PIPING SUITE LEVEL FLOOR PLAN - QUAD 4 | 100% CD | Feb 17, 2020 | V2 |
| M11-41 | MECHANICAL PIPING OVERLOOK LEVEL FLOOR PLAN - QUAD 1 | 100% CD | Feb 17, 2020 | V2 |
| M11-42 | MECHANICAL PIPING OVERLOOK LEVEL FLOOR PLAN - QUAD 2 | 100% CD | Feb 17, 2020 | V2 |
| M11-43 | MECHANICAL PIPING OVERLOOK LEVEL FLOOR PLAN - QUAD 3 | 100% CD | Feb 17, 2020 | V2 |
| M11-44 | MECHANICAL PIPING OVERLOOK LEVEL FLOOR PLAN - QUAD 4 | 100% CD | Feb 17, 2020 | V2 |
| M11-51 | MECHANICAL PIPING CATWALK LEVEL FLOOR PLAN - QUAD 1 | 100% CD | Feb 17, 2020 | V2 |

| | | | | |
|---|---|---|---|---|
| M11-52 | MECHANICAL PIPING CATWALK LEVEL FLOOR PLAN - QUAD 2 | 100% CD | Feb 17, 2020 | V2 |
| M11-53 | MECHANICAL PIPING CATWALK LEVEL FLOOR PLAN - QUAD 3 | 100% CD | Feb 17, 2020 | V2 |
| M11-54 | MECHANICAL PIPING CATWALK LEVEL FLOOR PLAN - QUAD 4 | 100% CD | Feb 17, 2020 | V2 |
| M20-01 | MECHANICAL ENLARGED PLANS | 100% CD | Feb 17, 2020 | V2 |
| M30-00 | MECHANICAL SCHEMATIC DIAGRAMS | 100% CD | Feb 17, 2020 | V1 |
| M30-01 | MECHANICAL SCHEMATIC DIAGRAMS | 100% CD | Feb 17, 2020 | V1 |
| M40-01 | MECHANICAL SECTIONS AND ISOMETRICS | 100% CD | Feb 17, 2020 | V1 |
| M50-00 | MECHANICAL CONTROLS | 100% CD | Feb 17, 2020 | V2 |
| M50-01 | MECHANICAL CONTROLS | 100% CD | Feb 17, 2020 | V2 |
| M50-02 | MECHANICAL CONTROLS | 100% CD | Feb 17, 2020 | V2 |
| M50-03 | MECHANICAL CONTROLS | 100% CD | Feb 17, 2020 | V2 |
| M50-04 | MECHANICAL CONTROLS | 100% CD | Feb 17, 2020 | V2 |
| M50-05 | MECHANICAL CONTROLS | 100% CD | Feb 17, 2020 | V2 |
| M50-06 | MECHANICAL CONTROLS | 100% CD | Feb 17, 2020 | V2 |
| M50-07 | MECHANICAL CONTROLS | 100% CD | Feb 17, 2020 | V1 |
| M60-00 | MECHANICAL CALCULATIONS | 100% CD | Feb 17, 2020 | V1 |
| M60-01 | MECHANICAL CALCULATIONS | 100% CD | Feb 17, 2020 | V1 |
| M70-00 | MECHANICAL COMPLIANCE | 100% CD | Feb 17, 2020 | V1 |
| M70-01 | MECHANICAL COMPLIANCE | 100% CD | Feb 17, 2020 | V1 |
| M80-01 | MECHANICAL DETAILS | 100% CD | Feb 17, 2020 | V2 |
| M80-02 | MECHANICAL DETAILS | 100% CD | Feb 17, 2020 | V2 |
| M80-03 | MECHANICAL DETAILS | 100% CD | Feb 17, 2020 | V2 |
| M80-04 | MECHANICAL DETAILS | 100% CD | Feb 17, 2020 | V1 |
| M80-05 | MECHANICAL DETAILS | 100% CD | Feb 17, 2020 | V1 |
| M80-06 | MECHANICAL DETAILS | 100% CD | Feb 17, 2020 | V1 |
| MEP-01 | MEP SCHEDULES | 100% CD | Feb 17, 2020 | V1 |
| MEP-02 | MEP SCHEDULES | 100% CD | Feb 17, 2020 | V1 |
| MEP-03 | MEP SCHEDULES | 100% CD | Feb 17, 2020 | V1 |
| MEP-04 | MEP SCHEDULES | 100% CD | Feb 17, 2020 | V1 |
| MEP-05 | MEP SCHEDULES | 100% CD | Feb 17, 2020 | V1 |
| MEP-06 | MEP SCHEDULES | 100% CD | Feb 17, 2020 | V1 |
| MFS-00-01 | MECHANICAL GENERAL NOTES, SYMBOLS, LEGENDS AND ABBREVIATIONS | 100% CD | Feb 17, 2020 | V1 |
| MFS-03 | SHEET NUMBER MFS-03 | 100% CD | Feb 17, 2020 | V1 |
| MFS-10-10 | MFS EVENT LEVEL - OVERALL FLOOR PLAN | 100% CD | Feb 17, 2020 | V1 |
| MFS-10-100 | MFS SUITE LEVEL - ENLARGED FOOD SERVICE Q1 FLOOR PLAN | 100% CD | Feb 17, 2020 | V1 |
| MFS-10-110 | MFS SUITE LEVEL - ENLARGED FOOD SERVICE Q2 FLOOR PLAN | 100% CD | Feb 17, 2020 | V1 |
| MFS-10-120 | MFS SUITE LEVEL - ENLARGED FOOD SERVICE Q3 FLOOR PLAN | 100% CD | Feb 17, 2020 | V1 |
| MFS-10-130 | MFS SUITE LEVEL - ENLARGED FOOD SERVICE Q4 FLOOR PLAN | 100% CD | Feb 17, 2020 | V1 |
| MFS-10-140 | MFS OVERLOOK LEVEL - OVERALL FLOOR PLAN | 100% CD | Feb 17, 2020 | V1 |

| | | | | |
|---|---|---|---|---|
| MFS-10-150 | MFS OVERLOOK LEVEL - ENLARGED FOOD SERVICE Q1 FLOOR PLAN | 100% CD | Feb 17, 2020 | V1 |
| MFS-10-160 | MFS OVERLOOK LEVEL - ENLARGED FOOD SERVICE Q2 FLOOR PLAN | 100% CD | Feb 17, 2020 | V1 |
| MFS-10-170 | MFS OVERLOOK LEVEL - ENLARGED FOOD SERVICE Q3 FLOOR PLAN | 100% CD | Feb 17, 2020 | V1 |
| MFS-10-180 | MFS CATWALK (ROOF) LEVEL - OVERALL FLOOR PLAN | 100% CD | Feb 17, 2020 | V1 |
| MFS-10-190 | MFS CATWALK (ROOF) LEVEL - ENLARGED FOOD SERVICE Q1 FLOOR PLAN | 100% CD | Feb 17, 2020 | V1 |
| MFS-10-20 | MFS EVENT LEVEL - ENLARGED FOOD SERVICE Q2 FLOOR PLAN | 100% CD | Feb 17, 2020 | V1 |
| MFS-10-200 | MFS CATWALK (ROOF) LEVEL - ENLARGED FOOD SERVICE Q2 FLOOR PLAN | 100% CD | Feb 17, 2020 | V1 |
| MFS-10-210 | MFS CATWALK (ROOF) LEVEL - ENLARGED FOOD SERVICE Q3 FLOOR PLAN | 100% CD | Feb 17, 2020 | V1 |
| MFS-10-220 | MFS CATWALK (ROOF) LEVEL - ENLARGED FOOD SERVICE Q4 FLOOR PLAN | 100% CD | Feb 17, 2020 | V1 |
| MFS-10-30 | MFS EVENT LEVEL - ENLARGED FOOD SERVICE Q3 FLOOR PLAN | 100% CD | Feb 17, 2020 | V1 |
| MFS-10-40 | MFS CONCOURSE LEVEL - OVERALL FLOOR PLAN | 100% CD | Feb 17, 2020 | V1 |
| MFS-10-50 | MFS CONCOURSE LEVEL- ENLARGED FOOD SERVICE Q1 PLAN | 100% CD | Feb 17, 2020 | V1 |
| MFS-10-60 | MFS CONCOURSE LEVEL- ENLARGED FOOD SERVICE Q2 PLAN | 100% CD | Feb 17, 2020 | V1 |
| MFS-10-70 | MFS CONCOURSE LEVEL- ENLARGED FOOD SERVICE Q3 PLAN | 100% CD | Feb 17, 2020 | V1 |
| MFS-10-80 | MFS CONCOURSE LEVEL- ENLARGED FOOD SERVICE Q4 PLAN | 100% CD | Feb 17, 2020 | V1 |
| MFS-10-90 | MFS SUITE LEVEL - OVERALL FLOOR PLAN | 100% CD | Feb 17, 2020 | V1 |
| MFS-80-10 | MFS DETAILS | 100% CD | Feb 17, 2020 | V1 |
| MFS-80-20 | MFS DETAILS | 100% CD | Feb 17, 2020 | V1 |
| P00-01 | PLUMBING GENERAL NOTES, SYMBOLS, LEGENDS AND ABBREVIATIONS | 100% CD | Feb 17, 2020 | V2 |
| P00-02 | PLUMBING SCHEDULES | 100% CD | Feb 17, 2020 | V2 |
| P00-03 | PLUMBING SCHEDULES | 100% CD | Feb 17, 2020 | V2 |
| P10-00 | UNDERGROUND PLUMBING EVENT LEVEL - OVERALL FLOOR PLAN | 100% CD | Feb 17, 2020 | V2 |
| P10-01 | UNDERGROUND PLUMBING EVENT LEVEL FLOOR PLAN - QUAD 1 | 100% CD | Feb 17, 2020 | V2 |
| P10-02 | UNDERGROUND PLUMBING EVENT LEVEL FLOOR PLAN - QUAD 2 | 100% CD | Feb 17, 2020 | V2 |
| P10-03 | UNDERGROUND PLUMBING EVENT LEVEL FLOOR PLAN - QUAD 3 | 100% CD | Feb 17, 2020 | V2 |
| P10-04 | UNDERGROUND PLUMBING EVENT LEVEL FLOOR PLAN - QUAD 4 | 100% CD | Feb 17, 2020 | V2 |
| P10-10 | PLUMBING EVENT LEVEL - OVERALL FLOOR PLAN | 100% CD | Feb 17, 2020 | V2 |
| P10-11 | PLUMBING EVENT LEVEL FLOOR PLAN - QUAD 1 | 100% CD | Feb 17, 2020 | V2 |
| P10-12 | PLUMBING EVENT LEVEL FLOOR PLAN - QUAD 2 | 100% CD | Feb 17, 2020 | V2 |
| P10-13 | PLUMBING EVENT LEVEL FLOOR PLAN - QUAD 3 | 100% CD | Feb 17, 2020 | V2 |
| P10-14 | PLUMBING EVENT LEVEL FLOOR PLAN - QUAD 4 | 100% CD | Feb 17, 2020 | V2 |
| P10-20 | PLUMBING CONCOURSE LEVEL - OVERALL FLOOR PLAN | 100% CD | Feb 17, 2020 | V2 |

| | | | | |
|---|---|---|---|---|
| P10-21 | PLUMBING CONCOURSE LEVEL FLOOR PLAN - QUAD 1 | 100% CD | Feb 17, 2020 | V2 |
| P10-22 | PLUMBING CONCOURSE LEVEL FLOOR PLAN - QUAD 2 | 100% CD | Feb 17, 2020 | V2 |
| P10-23 | PLUMBING CONCOURSE LEVEL FLOOR PLAN - QUAD 3 | 100% CD | Feb 17, 2020 | V2 |
| P10-24 | PLUMBING CONCOURSE LEVEL FLOOR PLAN - QUAD 4 | 100% CD | Feb 17, 2020 | V2 |
| P10-30 | PLUMBING SUITE LEVEL - OVERALL FLOOR PLAN | 100% CD | Feb 17, 2020 | V2 |
| P10-31 | PLUMBING SUITE LEVEL FLOOR PLAN - QUAD 1 | 100% CD | Feb 17, 2020 | V2 |
| P10-32 | PLUMBING SUITE LEVEL FLOOR PLAN - QUAD 2 | 100% CD | Feb 17, 2020 | V2 |
| P10-33 | PLUMBING SUITE LEVEL FLOOR PLAN - QUAD 3 | 100% CD | Feb 17, 2020 | V2 |
| P10-34 | PLUMBING SUITE LEVEL FLOOR PLAN - QUAD 4 | 100% CD | Feb 17, 2020 | V2 |
| P10-40 | PLUMBING OVERLOOK LEVEL - OVERALL FLOOR PLAN | 100% CD | Feb 17, 2020 | V2 |
| P10-41 | PLUMBING OVERLOOK LEVEL FLOOR PLAN - QUAD 1 | 100% CD | Feb 17, 2020 | V2 |
| P10-42 | PLUMBING OVERLOOK LEVEL FLOOR PLAN - QUAD 2 | 100% CD | Feb 17, 2020 | V2 |
| P10-43 | PLUMBING OVERLOOK LEVEL FLOOR PLAN - QUAD 3 | 100% CD | Feb 17, 2020 | V2 |
| P10-44 | PLUMBING OVERLOOK LEVEL FLOOR PLAN - QUAD 4 | 100% CD | Feb 17, 2020 | V2 |
| P10-50 | PLUMBING CATWALK LEVEL - OVERALL FLOOR PLAN | 100% CD | Feb 17, 2020 | V2 |
| P10-51 | PLUMBING CATWALK LEVEL FLOOR PLAN - QUAD 1 | 100% CD | Feb 17, 2020 | V2 |
| P10-52 | PLUMBING CATWALK LEVEL FLOOR PLAN - QUAD 2 | 100% CD | Feb 17, 2020 | V2 |
| P10-53 | PLUMBING CATWALK LEVEL FLOOR PLAN - QUAD 3 | 100% CD | Feb 17, 2020 | V2 |
| P10-54 | PLUMBING CATWALK LEVEL FLOOR PLAN - QUAD 4 | 100% CD | Feb 17, 2020 | V2 |
| P10-60 | PLUMBING ROOF LEVEL - OVERALL PLAN | 100% CD | Feb 17, 2020 | V2 |
| P10-61 | PLUMBING ROOF LEVEL FLOOR PLAN - QUAD 1 | 100% CD | Feb 17, 2020 | V2 |
| P10-62 | PLUMBING ROOF LEVEL FLOOR PLAN - QUAD 2 | 100% CD | Feb 17, 2020 | V2 |
| P10-63 | PLUMBING ROOF LEVEL FLOOR PLAN - QUAD 3 | 100% CD | Feb 17, 2020 | V2 |
| P10-64 | PLUMBING ROOF LEVEL FLOOR PLAN - QUAD 4 | 100% CD | Feb 17, 2020 | V2 |
| P40-01 | PLUMBING ENLARGED PLANS - EVENT LEVEL | 100% CD | Feb 17, 2020 | V2 |
| P40-02 | PLUMBING ENLARGED PLANS - EVENT LEVEL | 100% CD | Feb 17, 2020 | V2 |
| P40-03 | PLUMBING ENLARGED PLANS - EVENT LEVEL | 100% CD | Feb 17, 2020 | V2 |
| P40-04 | PLUMBING ENLARGED PLANS - CONCOURSE LEVEL | 100% CD | Feb 17, 2020 | V2 |
| P40-05 | PLUMBING ENLARGED PLANS - CONCOURSE LEVEL | 100% CD | Feb 17, 2020 | V2 |
| P40-06 | PLUMBING ENLARGED PLANS - CONCOURSE LEVEL | 100% CD | Feb 17, 2020 | V2 |
| P40-07 | PLUMBING ENLARGED PLANS - SUITE LEVEL | 100% CD | Feb 17, 2020 | V2 |
| P40-08 | PLUMBING ENLARGED PLANS - OVERLOOK LEVEL | 100% CD | Feb 17, 2020 | V2 |
| P50-01 | PLUMBING ISOMETRICS | 100% CD | Feb 17, 2020 | V1 |
| P50-02 | PLUMBING ISOMETRICS | 100% CD | Feb 17, 2020 | V1 |
| P50-03 | PLUMBING ISOMETRICS | 100% CD | Feb 17, 2020 | V1 |
| P50-04 | PLUMBING ISOMETRICS | 100% CD | Feb 17, 2020 | V1 |
| P50-05 | PLUMBING ISOMETRICS | 100% CD | Feb 17, 2020 | V1 |
| P50-06 | PLUMBING ISOMETRICS | 100% CD | Feb 17, 2020 | V1 |
| P50-07 | PLUMBING ISOMETRICS | 100% CD | Feb 17, 2020 | V1 |

| | | | | |
|---|---|---|---|---|
| P50-08 | PLUMBING ISOMETRICS | 100% CD | Feb 17, 2020 | V1 |
| P70-01 | PLUMBING RISER DIAGRAMS | 100% CD | Feb 17, 2020 | V2 |
| P70-02 | PLUMBING RISER DIAGRAMS | 100% CD | Feb 17, 2020 | V2 |
| P70-03 | PLUMBING RISER DIAGRAMS | 100% CD | Feb 17, 2020 | V2 |
| P80-01 | PLUMBING DETAILS | 100% CD | Feb 17, 2020 | V2 |
| P80-02 | PLUMBING DETAILS | 100% CD | Feb 17, 2020 | V2 |
| P80-03 | PLUMBING DETAILS | 100% CD | Feb 17, 2020 | V2 |
| P80-04 | PLUMBING DETAILS | 100% CD | Feb 17, 2020 | V2 |
| PFS00-01 | PLUMBING - GENERAL NOTES & LEGENDS | 100% CD | Feb 17, 2020 | V2 |
| PFS00-02 | PLUMBING FOOD SERVICE SCHEDULES | 100% CD | Feb 17, 2020 | V2 |
| PFS00-03 | PLUMBING FOOD SERVICE SCHEDULES | 100% CD | Feb 17, 2020 | V2 |
| PFS00-04 | PLUMBING FOOD SERVICE SCHEDULES | 100% CD | Feb 17, 2020 | V2 |
| PFS00-05 | PLUMBING FOOD SERVICE SCHEDULES | 100% CD | Feb 17, 2020 | V2 |
| PFS00-06 | PLUMBING FOOD SERVICE SCHEDULES | 100% CD | Feb 17, 2020 | V2 |
| PFS00-07 | PLUMBING FOOD SERVICE SCHEDULES | 100% CD | Feb 17, 2020 | V2 |
| PFS10-10 | PFS EVENT LEVEL - OVERALL FLOOR PLAN | 100% CD | Feb 17, 2020 | V2 |
| PFS10-100 | PFS CONCOURSE LEVEL - ENLARGED Q2 SANITARY FLOOR PLAN | 100% CD | Feb 17, 2020 | V2 |
| PFS10-110 | PFS CONCOURSE LEVEL - ENLARGED Q3 DOMESTIC FLOOR PLAN | 100% CD | Feb 17, 2020 | V2 |
| PFS10-120 | PFS CONCOURSE LEVEL - ENLARGED Q3 SANITARY FLOOR PLAN | 100% CD | Feb 17, 2020 | V2 |
| PFS10-130 | PFS CONCOURSE LEVEL - ENLARGED Q4 DOMESTIC FLOOR PLAN | 100% CD | Feb 17, 2020 | V2 |
| PFS10-140 | PFS CONCOURSE LEVEL - ENLARGED Q4 SANITARY FLOOR PLAN | 100% CD | Feb 17, 2020 | V2 |
| PFS10-141 | PFS CONCOURSE LEVEL QUAD 1 ENLARGED PLAN | 100% CD | Feb 17, 2020 | V2 |
| PFS10-142A | PFS CONCOURSE LEVEL QUAD 2 ENLARGED PLAN | 100% CD | Feb 17, 2020 | V1 |
| PFS10-142B | PFS CONCOURSE LEVEL-QUAD 2 ENLARGED PLAN | 100% CD | Feb 17, 2020 | V1 |
| PFS10-143 | PFS CONCOURSE LEVEL QUAD 3 ENLARGED PLANS | 100% CD | Feb 17, 2020 | V2 |
| PFS10-144 | PFS CONCOURSE LEVEL QUAD 4 ENLARGED PLAN | 100% CD | Feb 17, 2020 | V1 |
| PFS10-150 | PFS SUITE LEVEL - OVERALL FLOOR PLAN | 100% CD | Feb 17, 2020 | V2 |
| PFS10-160 | PFS SUITE LEVEL - ENLARGED Q1 DOMESTIC FLOOR PLAN | 100% CD | Feb 17, 2020 | V2 |
| PFS10-170 | PFS SUITE LEVEL - ENLARGED Q1 SANITARY FLOOR PLAN | 100% CD | Feb 17, 2020 | V2 |
| PFS10-180 | PFS SUITE LEVEL - ENLARGED Q2 DOMESTIC FLOOR PLAN | 100% CD | Feb 17, 2020 | V2 |
| PFS10-190 | PFS SUITE LEVEL - ENLARGED Q2 SANITARY FLOOR PLAN | 100% CD | Feb 17, 2020 | V2 |
| PFS10-191 | PFS SUITE LEVEL QUAD 1 AND QUAD 2 ENLARGED PLAN | 100% CD | Feb 17, 2020 | V2 |
| PFS10-20 | PFS EVENT LEVEL - Enlarged Q2 DOMESTIC FLOOR PLAN | 100% CD | Feb 17, 2020 | V2 |
| PFS10-200 | PFS OVERLOOK LEVEL - OVERALL FLOOR PLAN | 100% CD | Feb 17, 2020 | V2 |
| PFS10-210 | PFS OVERLOOK LEVEL - ENLARGED Q1 DOMESTIC FLOOR PLAN | 100% CD | Feb 17, 2020 | V2 |
| PFS10-220 | PFS OVERLOOK LEVEL - ENLARGED Q1 SANITARY FLOOR PLAN | 100% CD | Feb 17, 2020 | V2 |

| | | | | |
|---|---|---|---|---|
| PFS10-230 | PFS OVERLOOK LEVEL - ENLARGED Q2 DOMESTIC FLOOR PLAN | 100% CD | Feb 17, 2020 | V2 |
| PFS10-240 | PFS OVERLOOK LEVEL - ENLARGED Q2 SANITARY FLOOR PLAN | 100% CD | Feb 17, 2020 | V2 |
| PFS10-250 | PFS OVERLOOK LEVEL - ENLARGED Q3 DOMESTIC FLOOR PLAN | 100% CD | Feb 17, 2020 | V2 |
| PFS10-260 | PFS OVERLOOK LEVEL - ENLARGEDQ3 SANITARY FLOOR PLAN | 100% CD | Feb 17, 2020 | V2 |
| PFS10-261 | PFS OVERLOOK LEVEL QUAD 1, 2, AND 3 ENLARGED PLAN | 100% CD | Feb 17, 2020 | V2 |
| PFS10-30 | PFS EVENT LEVEL - Enlarged Q2 SANITARY FLOOR PLAN | 100% CD | Feb 17, 2020 | V2 |
| PFS10-40 | PFS EVENT LEVEL - Enlarged Q3 DOMESTIC FLOOR PLAN | 100% CD | Feb 17, 2020 | V2 |
| PFS10-50 | PFS EVENT LEVEL - Enlarged Q3 SANITARY FLOOR PLAN | 100% CD | Feb 17, 2020 | V2 |
| PFS10-51 | PFS EVENT LEVEL QUAD 1, 2 DOMESTIC ENLARGED PLAN | 100% CD | Feb 17, 2020 | V2 |
| PFS10-52 | PFS EVENT LEVEL QUAD 1 , 2 SANITARY ENLARGED PLAN | 100% CD | Feb 17, 2020 | V2 |
| PFS10-53 | PFS EVENT LEVEL QUAD 3 ENLARGED PLAN | 100% CD | Feb 17, 2020 | V2 |
| PFS10-60 | PFS CONCOURSE LEVEL - OVERALL FLOOR PLAN | 100% CD | Feb 17, 2020 | V2 |
| PFS10-70 | PFS CONCOURSE LEVEL - ENLARGED Q1 DOMESTIC FLOOR PLAN | 100% CD | Feb 17, 2020 | V2 |
| PFS10-80 | PFS CONCOURSE LEVEL - ENLARGED Q1 SANITARY FLOOR PLAN | 100% CD | Feb 17, 2020 | V2 |
| PFS10-90 | PFS CONCOURSE LEVEL - ENLARGED Q2 DOMESTIC FLOOR PLAN | 100% CD | Feb 17, 2020 | V2 |
| PFS50-10 | PLUMBING FOOD SERVICE DETAILS | 100% CD | Feb 17, 2020 | V2 |
| P.O. Box 1027 | City of Savannah P.O. Box 1027 2 East Bay St., Savannah, GA 31401 | | | V5 |
| QF000-1 | INDEX SHEET | 100% CD | Feb 17, 2020 | V2 |
| QF110-1 | FOODSERVICE KEY PLAN | 100% CD | Feb 17, 2020 | V2 |
| QF110-2 | FOODSERVICE BEVERAGE CONDUIT & CO2 DIAGRAM | 100% CD | Feb 17, 2020 | V1 |
| QF120-1 | FOODSERVICE KEY PLAN | 100% CD | Feb 17, 2020 | V2 |
| QF120-2 | FOODSERVICE BEVERAGE CONDUIT DIAGRAM | 100% CD | Feb 17, 2020 | V1 |
| QF130-1 | FOODSERVICE KEY PLAN | 100% CD | Feb 17, 2020 | V2 |
| QF130-2 | FOODSERVICE BEVERAGE CONDUIT DIAGRAM | 100% CD | Feb 17, 2020 | V1 |
| QF140-1 | FOODSERVICE KEY PLAN | 100% CD | Feb 17, 2020 | V2 |
| QF140-2 | FOODSERVICE BEVERAGE CONDUIT DIAGRAM | 100% CD | Feb 17, 2020 | V1 |
| QF411-1 | FOODSERVICE EQUIPMENT PLAN - LEVEL1 - QUAD 1 | 100% CD | Feb 17, 2020 | V2 |
| QF411-2 | FOODSERVICE UTILITY SCHEDULE - LEVEL 1 - QUAD 1 | 100% CD | Feb 17, 2020 | V2 |
| QF411-3 | FOODSERVICE BC&V PLAN - LEVEL 1 - QUAD 1 | 100% CD | Feb 17, 2020 | V1 |
| QF411-4 | FOODSERVICE PLUMBING PLAN - LEVEL 1 - QUAD 1 | 100% CD | Feb 17, 2020 | V1 |
| QF411-5 | FOODSERVICE ELECTRICAL PLAN - LEVEL 1 - QUAD 1 | 100% CD | Feb 17, 2020 | V1 |
| QF412-1A | FOODSERVICE EQUIPMENT PLAN - LEVEL 1 - QUAD 2 | 100% CD | Feb 17, 2020 | V2 |
| QF412-1B | FOODSERVICE EQUIPMENT SCHEDULE - LEVEL 1 - QUAD 2 | 100% CD | Feb 17, 2020 | V2 |

| | | | | |
|---|---|---|---|---|
| QF412-2 | FOODSERVICE UTILITY SCHEDULE - LEVEL 1 - QUAD 2 | 100% CD | Feb 17, 2020 | V2 |
| QF412-3 | FOODSERVICE BC&V PLAN - LEVEL 1 - QUAD 2 | 100% CD | Feb 17, 2020 | V1 |
| QF412-4 | FOODSERVICE PLUMBING PLAN - LEVEL 1 - QUAD 2 | 100% CD | Feb 17, 2020 | V1 |
| QF412-5 | FOODSERVICE ELECTRICAL PLAN - LEVEL 1 - QUAD 2 | 100% CD | Feb 17, 2020 | V1 |
| QF413-1A | FOODSERVICE EQUIPMENT PLAN - LEVEL 1 - QUAD 3 | 100% CD | Feb 17, 2020 | V2 |
| QF413-1B | FOODSERVICE EQUIPMENT SCHEDULE - LEVEL 1 - QUAD 3 | 100% CD | Feb 17, 2020 | V2 |
| QF413-2 | FOODSERVICE UTILITY SCHEDULE - LEVEL 1 - QUAD 3 | 100% CD | Feb 17, 2020 | V2 |
| QF413-3 | FOODSERVICE BC&V PLAN - LEVEL 1 - QUAD 3 | 100% CD | Feb 17, 2020 | V1 |
| QF413-4 | FOODSERVICE PLUMBING PLAN - LEVEL 1 - QUAD 3 | 100% CD | Feb 17, 2020 | V1 |
| QF413-5 | FOODSERVICE ELECTRICAL PLAN - LEVEL 1 - QUAD 3 | 100% CD | Feb 17, 2020 | V1 |
| QF421-1A | FOODSERVICE EQUIPMENT PLAN - LEVEL 2 - QUAD 1 | 100% CD | Feb 17, 2020 | V2 |
| QF421-1B | FOODSERVICE EQUIPMENT SCHEDULE - LEVEL 2 - QUAD 1 | 100% CD | Feb 17, 2020 | V2 |
| QF421-2 | FOODSERVICE UTILITY SCHEDULE - LEVEL 2 - QUAD 1 | 100% CD | Feb 17, 2020 | V2 |
| QF421-3 | FOODSERVICE BC&V PLAN - LEVEL 2 - QUAD 1 | 100% CD | Feb 17, 2020 | V1 |
| QF421-4 | FOODSERVICE PLUMBING PLAN - LEVEL 2 - QUAD 1 | 100% CD | Feb 17, 2020 | V1 |
| QF421-5 | FOODSERVICE ELECTRICAL PLAN - LEVEL 2 - QUAD 1 | 100% CD | Feb 17, 2020 | V1 |
| QF422-1A | FOODSERVICE EQUIPMENT PLAN - LEVEL 2 - QUAD 2 | 100% CD | Feb 17, 2020 | V2 |
| QF422-1B | FOODSERVICE EQUIPMENT SCHEDULE - LEVEL 2 - QUAD 2 | 100% CD | Feb 17, 2020 | V2 |
| QF422-2A | FOODSERVICE UTILITY SCHEDULE - LEVEL 2 - QUAD 2 | 100% CD | Feb 17, 2020 | V2 |
| QF422-2B | FOODSERVICE UTILITY SCHEDULE - LEVEL 2 - QUAD 2 | 100% CD | Feb 17, 2020 | V2 |
| QF422-2C | FOODSERVICE UTILITY SCHEDULE - LEVEL 2 - QUAD 2 | 100% CD | Feb 17, 2020 | V1 |
| QF422-3A | FOODSERVICE BC&V PLAN - LEVEL 2 - QUAD 2 | 100% CD | Feb 17, 2020 | V1 |
| QF422-3B | FOODSERVICE BC&V PLAN - LEVEL 2 - QUAD 2 | 100% CD | Feb 17, 2020 | V1 |
| QF422-4A | FOODSERVICE PLUMBING PLAN - LEVEL 2 - QUAD 2 | 100% CD | Feb 17, 2020 | V1 |
| QF422-4B | FOODSERVICE PLUMBING PLAN - LEVEL 2 - QUAD 2 | 100% CD | Feb 17, 2020 | V1 |
| QF422-5A | FOODSERVICE ELECTRICAL PLAN - LEVEL 2 - QUAD 2 | 100% CD | Feb 17, 2020 | V1 |
| QF422-5B | FOODSERVICE ELECTRICAL PLAN - LEVEL 2 - QUAD 2 | 100% CD | Feb 17, 2020 | V1 |
| QF423-1A | FOODSERVICE EQUIPMENT PLAN - LEVEL 2 - QUAD 3 | 100% CD | Feb 17, 2020 | V2 |
| QF423-1B | FOODSERVICE EQUIPMENT SCHEDULE - LEVEL 2 - QUAD 3 | 100% CD | Feb 17, 2020 | V2 |
| QF423-2 | FOODSERVICE UTILITY SCHEDULE - LEVEL 2 - QUAD 3 | 100% CD | Feb 17, 2020 | V1 |
| QF423-3 | FOODSERVICE BC&V PLAN - LEVEL 2 - QUAD 3 | 100% CD | Feb 17, 2020 | V1 |
| QF423-4 | FOODSERVICE PLUMBING PLAN - LEVEL 2 - QUAD 3 | 100% CD | Feb 17, 2020 | V1 |

| | | | | |
|---|---|---|---|---|
| QF423-5 | FOODSERVICE ELECTRICAL PLAN - LEVEL 2 - QUAD 3 | 100% CD | Feb 17, 2020 | V1 |
| QF424-1A | FOODSERVICE EQUIPMENT PLAN - LEVEL 2 - QUAD 4 | 100% CD | Feb 17, 2020 | V1 |
| QF424-1B | FOODSERVICE EQUIPMENT SCHEDULE - LEVEL 2 - QUAD 4 | 100% CD | Feb 17, 2020 | V1 |
| QF424-2A | FOODSERVICE UTILITY SCHEDULE - LEVEL 2 - QUAD 4 | 100% CD | Feb 17, 2020 | V1 |
| QF424-2B | FOODSERVICE UTILITY SCHEDULE - LEVEL 2 - QUAD 4 | 100% CD | Feb 17, 2020 | V1 |
| QF424-3 | FOODSERVICE BC&V PLAN - LEVEL 2 - QUAD 4 | 100% CD | Feb 17, 2020 | V1 |
| QF424-4 | FOODSERVICE PLUMBING PLAN - LEVEL 2 - QUAD 4 | 100% CD | Feb 17, 2020 | V1 |
| QF424-5 | FOODSERVICE ELECTRICAL PLAN - LEVEL 2 - QUAD 4 | 100% CD | Feb 17, 2020 | V1 |
| QF431-1 | FOODSERVICE EQUIPMENT PLAN - LEVEL 3 - QUAD 1 | 100% CD | Feb 17, 2020 | V2 |
| QF431-2 | FOODSERVICE UTILITY SCHEDULE - LEVEL 3 - QUAD 1 | 100% CD | Feb 17, 2020 | V2 |
| QF431-3 | FOODSERVICE BC&V PLAN - LEVEL 3 - QUAD 1 | 100% CD | Feb 17, 2020 | V1 |
| QF431-4 | FOODSERVICE PLUMBING PLAN - LEVEL 3 - QUAD 1 | 100% CD | Feb 17, 2020 | V1 |
| QF431-5 | FOODSERVICE ELECTRICAL PLAN - LEVEL 3 - QUAD 1 | 100% CD | Feb 17, 2020 | V1 |
| QF432-1A | FOODSERVICE EQUIPMENT PLAN - LEVEL 3 - QUAD 2 | 100% CD | Feb 17, 2020 | V1 |
| QF432-1B | FOODSERVICE EQUIPMENT SCHEDULE - LEVEL 3 - QUAD 2 | 100% CD | Feb 17, 2020 | V1 |
| QF432-2 | FOODSERVICE UTILITY SCHEDULE - LEVEL 3 - QUAD 2 | 100% CD | Feb 17, 2020 | V2 |
| QF432-3 | FOODSERVICE BC&V PLAN - LEVEL 3 - QUAD 2 | 100% CD | Feb 17, 2020 | V1 |
| QF432-4 | FOODSERVICE PLUMBING PLAN - LEVEL 3 - QUAD 2 | 100% CD | Feb 17, 2020 | V1 |
| QF432-5 | FOODSERVICE ELECTRICAL PLAN - LEVEL 3 - QUAD 2 | 100% CD | Feb 17, 2020 | V1 |
| QF441-1 | FOODSERVICE EQUIPMENT PLAN - LEVEL 4 - QUAD 1 | 100% CD | Feb 17, 2020 | V2 |
| QF441-2 | FOODSERVICE UTILITY SCHEDULE - LEVEL 4 - QUAD 1 | 100% CD | Feb 17, 2020 | V2 |
| QF441-3 | FOODSERVICE BC&V PLAN - LEVEL 4 - QUAD 1 | 100% CD | Feb 17, 2020 | V1 |
| QF441-4 | FOODSERVICE PLUMBING PLAN - LEVEL 4 - QUAD 1 | 100% CD | Feb 17, 2020 | V1 |
| QF441-5 | FOODSERVICE ELECTRICAL PLAN - LEVEL 4 - QUAD 1 | 100% CD | Feb 17, 2020 | V1 |
| QF442-1 | FOODSERVICE EQUIPMENT PLAN - LEVEL 4 - QUAD 2 | 100% CD | Feb 17, 2020 | V2 |
| QF442-2 | FOODSERVICE UTILITY SCHEDULE - LEVEL 4 - QUAD 2 | 100% CD | Feb 17, 2020 | V2 |
| QF442-3 | FOODSERVICE BC&V PLAN - LEVEL 4 - QUAD 2 | 100% CD | Feb 17, 2020 | V1 |
| QF442-4 | FOODSERVICE PLUMBING PLAN - LEVEL 4 - QUAD 2 | 100% CD | Feb 17, 2020 | V1 |
| QF442-5 | FOODSERVICE ELECTRICAL PLAN - LEVEL 4 - QUAD 2 | 100% CD | Feb 17, 2020 | V1 |
| QF443-1 | FOODSERVICE EQUIPMENT PLAN - LEVEL 4 - QUAD 3 | 100% CD | Feb 17, 2020 | V2 |
| QF443-2 | FOODSERVICE UTILITY SCHEDULE - LEVEL 4 - QUAD 3 | 100% CD | Feb 17, 2020 | V2 |
| QF443-3 | FOODSERVICE BC&V PLAN - LEVEL 4 - QUAD 3 | 100% CD | Feb 17, 2020 | V1 |

| | | | | |
|---|---|---|---|---|
| QF443-4 | FOODSERVICE PLUMBING PLAN - LEVEL 4 - QUAD 3 | 100% CD | Feb 17, 2020 | V1 |
| QF443-5 | FOODSERVICE ELECTRICAL PLAN - LEVEL 4 - QUAD 3 | 100% CD | Feb 17, 2020 | V1 |
| QF501-1 | FOODSERVICE DETAILS & SECTIONS | 100% CD | Feb 17, 2020 | V2 |
| QF501-2 | FOODSERVICE DETAILS & SECTIONS | 100% CD | Feb 17, 2020 | V2 |
| QF501-3 | FOODSERVICE DETAILS & SECTIONS | 100% CD | Feb 17, 2020 | V2 |
| QF501-4 | FOODSERVICE DETAILS & SECTIONS | 100% CD | Feb 17, 2020 | V2 |
| QF511-1 | FOODSERVICE ELEVATION KEY PLAN - LEVEL 1 QUAD 1 | 100% CD | Feb 17, 2020 | V1 |
| QF511-2 | FOODSERVICE ELEVATIONS - LEVEL 1 QUAD 1 | 100% CD | Feb 17, 2020 | V1 |
| QF512-1 | FOODSERVICE ELEVATION KEY PLAN - LEVEL 1 QUAD 2 | 100% CD | Feb 17, 2020 | V1 |
| QF512-2 | FOODSERVICE ELEVATIONS - LEVEL 1 QUAD 2 | 100% CD | Feb 17, 2020 | V1 |
| QF512-3 | FOODSERVICE ELEVATIONS - LEVEL 1 QUAD 2 | 100% CD | Feb 17, 2020 | V1 |
| QF513-1 | FOODSERVICE ELEVATION KEY PLAN - LEVEL 1 QUAD 3 | 100% CD | Feb 17, 2020 | V1 |
| QF513-2 | FOODSERVICE ELEVATIONS - LEVEL 1 QUAD 3 | 100% CD | Feb 17, 2020 | V1 |
| QF513-3 | FOODSERVICE ELEVATIONS - LEVEL 1 QUAD 3 | 100% CD | Feb 17, 2020 | V1 |
| QF521-1 | FOODSERVICE ELEVATION KEY PLAN - LEVEL 2 QUAD 1 | 100% CD | Feb 17, 2020 | V1 |
| QF521-2 | FOODSERVICE ELEVATIONS - LEVEL 2 QUAD 1 | 100% CD | Feb 17, 2020 | V1 |
| QF522-1A | FOODSERVICE ELEVATION KEY PLAN - LEVEL 2 QUAD 2 | 100% CD | Feb 17, 2020 | V1 |
| QF522-1B | FOODSERVICE ELEVATION KEY PLAN - LEVEL 2 QUAD 2 | 100% CD | Feb 17, 2020 | V1 |
| QF522-2 | FOODSERVICE ELEVATIONS - LEVEL 2 QUAD 2 | 100% CD | Feb 17, 2020 | V1 |
| QF522-3 | FOODSERVICE ELEVATIONS - LEVEL 2 QUAD 2 | 100% CD | Feb 17, 2020 | V1 |
| QF523-1 | FOODSERVICE ELEVATION KEY PLAN - LEVEL 2 QUAD 3 | 100% CD | Feb 17, 2020 | V1 |
| QF523-2 | FOODSERVICE ELEVATIONS - LEVEL 2 QUAD 3 | 100% CD | Feb 17, 2020 | V1 |
| QF524-1A | FOODSERVICE ELEVATION KEY PLAN - LEVEL 2 QUAD 4 | 100% CD | Feb 17, 2020 | V1 |
| QF524-1B | FOODSERVICE ELEVATION KEY PLAN - LEVEL 2 QUAD 4 | 100% CD | Feb 17, 2020 | V1 |
| QF524-2 | FOODSERVICE ELEVATIONS - LEVEL 2 QUAD 4 | 100% CD | Feb 17, 2020 | V1 |
| QF524-3 | FOODSERVICE ELEVATIONS - LEVEL 2 QUAD 4 | 100% CD | Feb 17, 2020 | V1 |
| QF531-1 | FOODSERVICE ELEVATION KEY PLAN - LEVEL 3 QUAD 1 | 100% CD | Feb 17, 2020 | V1 |
| QF531-2 | FOODSERVICE ELEVATIONS - LEVEL 3 QUAD 1 | 100% CD | Feb 17, 2020 | V1 |
| QF532-1 | FOODSERVICE ELEVATION KEY PLAN - LEVEL 3 QUAD 2 | 100% CD | Feb 17, 2020 | V1 |
| QF532-2 | FOODSERVICE ELEVATIONS - LEVEL 3 QUAD 2 | 100% CD | Feb 17, 2020 | V1 |
| QF541-1 | FOODSERVICE ELEVATION KEY PLAN - LEVEL 4 QUAD 1 | 100% CD | Feb 17, 2020 | V1 |
| QF541-2 | FOODSERVICE ELEVATIONS - LEVEL 4 QUAD 1 | 100% CD | Feb 17, 2020 | V1 |
| QF542-1 | FOODSERVICE ELEVATION KEY PLAN - LEVEL 4 QUAD 2 | 100% CD | Feb 17, 2020 | V1 |
| QF542-2 | FOODSERVICE ELEVATIONS - LEVEL 4 QUAD 1 | 100% CD | Feb 17, 2020 | V1 |
| QF700-1 | FOODSERVICE WALK-IN REFRIGERATOR DETAILS | 100% CD | Feb 17, 2020 | V2 |
| QF700-2 | FOODSERVICE WALK-IN REFRIGERATOR DETAILS | 100% CD | Feb 17, 2020 | V2 |

| | | | | |
|---|---|---|---|---|
| QF700-3 | FOODSERVICE WALK-IN REFRIGERATOR DETAILS | 100% CD | Feb 17, 2020 | V2 |
| QF700-4 | FOODSERVICE WALK-IN REFRIGERATOR DETAILS | 100% CD | Feb 17, 2020 | V2 |
| QF702-1 | FOOD SERVICE EXHAUST HOODS MAKE-UP AIR PLANNING GUIDE | 100% CD | Feb 17, 2020 | V2 |
| QF702-10 | FOODSERVICE EXHAUST HOOD DETAILS | 100% CD | Feb 17, 2020 | V2 |
| QF702-11 | FOODSERVICE EXHAUST HOOD DETAILS | 100% CD | Feb 17, 2020 | V2 |
| QF702-12 | FOODSERVICE EXHAUST HOOD DETAILS | 100% CD | Feb 17, 2020 | V2 |
| QF702-13 | FOODSERVICE EXHAUST HOOD DETAILS | 100% CD | Feb 17, 2020 | V2 |
| QF702-14 | FOODSERVICE EXHAUST HOOD DETAILS | 100% CD | Feb 17, 2020 | V2 |
| QF702-15 | FOODSERVICE EXHAUST HOOD DETAILS | 100% CD | Feb 17, 2020 | V2 |
| QF702-16 | FOODSERVICE EXHAUST HOOD DETAILS | 100% CD | Feb 17, 2020 | V2 |
| QF702-17 | FOODSERVICE EXHAUST HOOD DETAILS | 100% CD | Feb 17, 2020 | V2 |
| QF702-2 | FOODSERVICE EXHAUST HOOD DETAILS | 100% CD | Feb 17, 2020 | V2 |
| QF702-3 | FOODSERVICE EXHAUST HOOD DETAILS | 100% CD | Feb 17, 2020 | V2 |
| QF702-4 | FOODSERVICE EXHAUST HOOD DETAILS | 100% CD | Feb 17, 2020 | V2 |
| QF702-5 | FOODSERVICE EXHAUST HOOD DETAILS | 100% CD | Feb 17, 2020 | V2 |
| QF702-6 | FOODSERVICE EXHAUST HOOD DETAILS | 100% CD | Feb 17, 2020 | V2 |
| QF702-7 | FOODSERVICE EXHAUST HOOD DETAILS | 100% CD | Feb 17, 2020 | V2 |
| QF702-8 | FOODSERVICE EXHAUST HOOD DETAILS | 100% CD | Feb 17, 2020 | V2 |
| QF702-9 | FOODSERVICE EXHAUST HOOD DETAILS | 100% CD | Feb 17, 2020 | V2 |
| S00-00 | COVER SHEET | ASI-004 | May 11, 2020 | V7 |
| S00-01 | GENERAL STRUCTURAL NOTES | 100% CD | Feb 17, 2020 | V5 |
| S00-02 | GENERAL STRUCTURAL NOTES | ASI-004 | May 11, 2020 | V6 |
| S00-03 | STRUCTURAL SYMBOLS AND NOTATIONS | ASI-002 | Apr 17, 2020 | V6 |
| S00-11 | CONCRETE STRENGTHS AND COVER REQUIREMENTS | ASI-004 | May 11, 2020 | V6 |
| S00-12 | REINFORCEMENT BAR DETAILING AND DEVELOPMENT SCHEDULES | 100% CD | Feb 17, 2020 | V5 |
| S01-01 | LOAD KEY PLAN | 100% CD | Feb 17, 2020 | V4 |
| S01-02 | LOAD KEY PLAN | 100% CD | Feb 17, 2020 | V4 |
| S01-03 | RIGGING LOAD DIAGRAM | 100% CD | Feb 17, 2020 | V4 |
| S01-04 | WIND LOAD KEY PLAN - ROOF UPLIFT AND WALL | 100% CD | Feb 17, 2020 | V4 |
| S01-11 | TRUSS ERECTION SEQUENCE | 100% CD | Feb 17, 2020 | V2 |
| S01-12 | TRUSS ERECTION SEQUENCE | 100% CD | Feb 17, 2020 | V1 |
| S02-01 | STRUCTURAL GRID LAYOUT | ASI-002 | Apr 17, 2020 | V4 |
| S10-10 | EVENT LEVEL - OVERALL FLOOR PLAN | 100% CD | Feb 17, 2020 | V5 |
| S10-10S | EVENT LEVEL - SLAB-ON-GRADE PLAN | 100% CD | Feb 17, 2020 | V1 |
| S10-11 | EVENT LEVEL FLOOR PLAN - QUAD 1 | ASI-004 | May 11, 2020 | V6 |
| S10-12 | EVENT LEVEL FLOOR PLAN - QUAD 2 | ASI-004 | May 11, 2020 | V6 |
| S10-13 | EVENT LEVEL FLOOR PLAN - QUAD 3 | ASI-004 | May 11, 2020 | V7 |
| S10-14 | EVENT LEVEL FLOOR PLAN - QUAD 4 | ASI-004 | May 11, 2020 | V7 |
| S10-20 | CONCOURSE LEVEL - OVERALL FLOOR PLAN | 100% CD | Feb 17, 2020 | V3 |
| S10-21 | CONCOURSE LEVEL FLOOR PLAN - QUAD 1 | ASI-004 | May 11, 2020 | V5 |
| S10-22 | CONCOURSE LEVEL FLOOR PLAN - QUAD 2 | ASI-004 | May 11, 2020 | V5 |
| S10-23 | CONCOURSE LEVEL FLOOR PLAN - QUAD 3 | ASI-004 | May 11, 2020 | V5 |

| | | | | |
|---|---|---|---|---|
| S10-24 | CONCOURSE LEVEL FLOOR PLAN - QUAD 4 | ASI-004 | May 11, 2020 | V5 |
| S10-30 | SUITE LEVEL - OVERALL FLOOR PLAN | 100% CD | Feb 17, 2020 | V3 |
| S10-31 | SUITE LEVEL FLOOR PLAN - QUAD 1 | ASI-004 | May 11, 2020 | V5 |
| S10-32 | SUITE LEVEL FLOOR PLAN - QUAD 2 | ASI-004 | May 11, 2020 | V5 |
| S10-33 | SUITE LEVEL FLOOR PLAN - QUAD 3 | ASI-004 | May 11, 2020 | V5 |
| S10-34 | SUITE LEVEL FLOOR PLAN - QUAD 4 | ASI-004 | May 11, 2020 | V5 |
| S10-40 | OVERLOOK LEVEL - OVERALL FLOOR PLAN | 100% CD | Feb 17, 2020 | V3 |
| S10-40A | UPPER BOWL FRAMING PLAN | ASI-002 | Apr 17, 2020 | V3 |
| S10-41 | OVERLOOK LEVEL FLOOR PLAN - QUAD 1 | ASI-004 | May 11, 2020 | V5 |
| S10-42 | OVERLOOK LEVEL FLOOR PLAN - QUAD 2 | ASI-004 | May 11, 2020 | V5 |
| S10-43 | OVERLOOK LEVEL FLOOR PLAN - QUAD 3 | ASI-004 | May 11, 2020 | V5 |
| S10-44 | OVERLOOK LEVEL FLOOR PLAN - QUAD 4 | ASI-004 | May 11, 2020 | V5 |
| S10-50 | CATWALK LEVEL - OVERALL FLOOR PLAN | 100% CD | Feb 17, 2020 | V3 |
| S10-51 | CATWALK LEVEL FLOOR PLAN - QUAD 1 | ASI-004 | May 11, 2020 | V5 |
| S10-52 | CATWALK LEVEL FLOOR PLAN - QUAD 2 | ASI-004 | May 11, 2020 | V5 |
| S10-53 | CATWALK LEVEL FLOOR PLAN - QUAD 3 | ASI-004 | May 11, 2020 | V5 |
| S10-54 | CATWALK LEVEL FLOOR PLAN - QUAD 4 | ASI-004 | May 11, 2020 | V5 |
| S10-60 | ROOF LEVEL - OVERALL FLOOR PLAN | 100% CD | Feb 17, 2020 | V3 |
| S10-61 | ROOF LEVEL FLOOR PLAN - QUAD 1 | ASI-002 | Apr 17, 2020 | V4 |
| S10-62 | ROOF LEVEL FLOOR PLAN - QUAD 2 | ASI-002 | Apr 17, 2020 | V4 |
| S10-63 | ROOF LEVEL FLOOR PLAN - QUAD 3 | ASI-004 | May 11, 2020 | V5 |
| S10-64 | ROOF LEVEL FLOOR PLAN - QUAD 4 | ASI-004 | May 11, 2020 | V5 |
| S20-01 | EXTERIOR ELEVATIONS - NORTH | ASI-004 | May 11, 2020 | V4 |
| S20-02 | EXTERIOR ELEVATIONS - NORTH | ASI-004 | May 11, 2020 | V5 |
| S20-03 | EXTERIOR ELEVATIONS - SOUTH | ASI-002 | Apr 17, 2020 | V4 |
| S20-04 | EXTERIOR ELEVATIONS - SOUTH | ASI-002 | Apr 17, 2020 | V4 |
| S20-05 | EXTERIOR ELEVATIONS - EAST | 100% CD | Feb 17, 2020 | V3 |
| S20-06 | EXTERIOR ELEVATIONS - EAST | ASI-002 | Apr 17, 2020 | V3 |
| S20-07 | EXTERIOR ELEVATIONS - WEST | ASI-004 | May 11, 2020 | V3 |
| S20-08 | EXTERIOR ELEVATIONS - WEST | ASI-002 | Apr 17, 2020 | V3 |
| S20-09 | EXTERIOR WALL ELEVATIONS | 100% CD | Feb 17, 2020 | V2 |
| S20-11 | BUILDING SECTIONS | 100% CD | Feb 17, 2020 | V2 |
| S20-21 | WALL SECTIONS | ASI-002 | Apr 17, 2020 | V3 |
| S21-01 | ISOMETRIC VIEWS | 100% CD | Feb 17, 2020 | V3 |
| S31-01 | RAKER FRAME ELEVATIONS | 100% CD | Feb 17, 2020 | V4 |
| S31-02 | RAKER FRAME ELEVATIONS | 100% CD | Feb 17, 2020 | V4 |
| S31-03 | RAKER FRAME ELEVATIONS | 100% CD | Feb 17, 2020 | V4 |
| S31-04 | RAKER FRAME ELEVATIONS | ASI-004 | May 11, 2020 | V6 |
| S31-05 | RAKER FRAME ELEVATIONS | ASI-004 | May 11, 2020 | V6 |
| S31-06 | RAKER FRAME ELEVATIONS | ASI-004 | May 11, 2020 | V6 |
| S31-07 | RAKER FRAME ELEVATIONS | ASI-004 | May 11, 2020 | V6 |
| S31-08 | RAKER FRAME ELEVATIONS | ASI-004 | May 11, 2020 | V6 |
| S31-09 | RAKER FRAME ELEVATIONS | ASI-002 | Apr 17, 2020 | V5 |
| S31-10 | RAKER FRAME ELEVATIONS | ASI-002 | Apr 17, 2020 | V5 |

| | | | | |
|---|---|---|---|---|
| S31-11 | RAKER FRAME ELEVATIONS | 100% CD | Feb 17, 2020 | V4 |
| S31-12 | RAKER FRAME ELEVATIONS | 100% CD | Feb 17, 2020 | V4 |
| S32-01 | TRUSS ELEVATIONS | 100% CD | Feb 17, 2020 | V3 |
| S32-02 | TRUSS ELEVATIONS | 100% CD | Feb 17, 2020 | V3 |
| S32-03 | TRUSS ELEVATIONS | 100% CD | Feb 17, 2020 | V3 |
| S33-01 | BRACED FRAME ELEVATIONS | 100% CD | Feb 17, 2020 | V4 |
| S33-02 | BRACED FRAME ELEVATIONS | 100% CD | Feb 17, 2020 | V4 |
| S33-03 | BRACED FRAME ELEVATIONS | ASI-004 | May 11, 2020 | V5 |
| S33-04 | BRACED FRAME ELEVATIONS | 100% CD | Feb 17, 2020 | V3 |
| S40-01 | FOUNDATION DETAILS | 100% CD | Feb 17, 2020 | V5 |
| S40-02 | FOUNDATION DETAILS | 100% CD | Feb 17, 2020 | V4 |
| S40-03 | FOUNDATION DETAILS | 100% CD | Feb 17, 2020 | V4 |
| S40-04 | FOUNDATION DETAILS | ASI-002 | Apr 17, 2020 | V5 |
| S40-11 | ICE SLAB PLAN AND DETAILS | ASI-002 | Apr 17, 2020 | V6 |
| S40-12 | FOUNDATION SECTIONS AND DETAILS | ASI-004 | May 11, 2020 | V6 |
| S41-01 | TYPICAL STEEL FRAMING DETAILS | ASI-002 | Apr 17, 2020 | V4 |
| S41-02 | TYPICAL STEEL FRAMING DETAILS | ASI-002 | Apr 17, 2020 | V4 |
| S41-03 | TYPICAL STEEL FRAMING DETAILS | 100% CD | Feb 17, 2020 | V3 |
| S41-04 | TYPICAL STEEL FRAMING DETAILS | ASI-004 | May 11, 2020 | V3 |
| S41-11 | STEEL FRAMING SECTIONS & DETAILS | ASI-002 | Apr 17, 2020 | V3 |
| S41-12 | STEEL FRAMING SECTIONS & DETAILS | ASI-004 | May 11, 2020 | V4 |
| S41-13 | STEEL FRAMING SECTIONS & DETAILS | ASI-002 | Apr 17, 2020 | V2 |
| S41-14 | STEEL FRAMING SECTIONS & DETAILS | ASI-004 | May 11, 2020 | V2 |
| S41-21 | CATWALK SYSTEM DETAILS | ASI-002 | Apr 17, 2020 | V3 |
| S41-31 | STEEL RAKER FRAMING SECTIONS & DETAILS | ASI-004 | May 11, 2020 | V3 |
| S41-32 | STEEL RAKER FRAMING SECTIONS & DETAILS | ASI-004 | May 11, 2020 | V4 |
| S42-01 | TRUSS DETAILS | 100% CD | Feb 17, 2020 | V3 |
| S42-02 | TRUSS DETAILS | 100% CD | Feb 17, 2020 | V3 |
| S42-03 | TRUSS DETAILS | 100% CD | Feb 17, 2020 | V2 |
| S42-04 | TRUSS DETAILS | ASI-004 | May 11, 2020 | V4 |
| S43-01 | BRACED FRAME SECTIONS AND DETAILS | ASI-002 | Apr 17, 2020 | V3 |
| S43-02 | BRACED FRAME SECTIONS AND DETAILS | ASI-002 | Apr 17, 2020 | V4 |
| S44-01 | COLUMN DETAILS | ASI-004 | May 11, 2020 | V6 |
| S45-01 | CLADDING SUPPORT DETAILS | ASI-004 | May 11, 2020 | V3 |
| S45-02 | CLADDING SUPPORT DETAILS | ASI-002 | Apr 17, 2020 | V3 |
| S45-03 | CLADDING SUPPORT DETAILS | ASI-004 | May 11, 2020 | V3 |
| S45-04 | CLADDING SUPPORT DETAILS | ASI-002 | Apr 17, 2020 | V2 |
| S50-01 | TYPICAL CONCRETE FRAMING DETAILS | 100% CD | Feb 17, 2020 | V3 |
| S51-01 | PRECAST STADIA DETAILS | ASI-004 | May 11, 2020 | V4 |
| S51-02 | PRECAST STADIA DETAILS | ASI-004 | May 11, 2020 | V4 |
| S51-03 | PRECAST DETAILS | 100% CD | Feb 17, 2020 | V3 |
| S60-01 | VERTICAL CIRCULATION - STAIRS | ASI-002 | Apr 17, 2020 | V3 |
| S60-02 | VERTICAL CIRCULATION - STAIRS | 100% CD | Feb 17, 2020 | V2 |
| S60-03 | VERTICAL CIRCULATION - STAIRS | ASI-002 | Apr 17, 2020 | V2 |

| | | | | |
|---|---|---|---|---|
| S60-04 | VERTICAL CIRCULATION - STAIRS | ASI-002 | Apr 17, 2020 | V2 |
| S61-01 | VERTICAL CIRCULATION - ELEVATORS | 100% CD | Feb 17, 2020 | V2 |
| S61-02 | VERTICAL CIRCULATION - ELEVATORS | ASI-004 | May 11, 2020 | V3 |
| S61-03 | VERTICAL CIRCULATION - ELEVATORS | ASI-002 | Apr 17, 2020 | V3 |
| S62-01 | VERTICAL CIRCULATION - MONUMENTAL STAIR | 100% CD | Feb 17, 2020 | V1 |
| S63-01 | MECHANICAL YARD - COOLING TOWER SUPPORT | ASI-004 | May 11, 2020 | V2 |
| S70-01 | COLUMN SCHEDULE | ASI-002 | Apr 17, 2020 | V5 |
| S70-02 | COLUMN SCHEDULE | ASI-002 | Apr 17, 2020 | V5 |
| S70-03 | COLUMN SCHEDULE | ASI-002 | Apr 17, 2020 | V5 |
| S80-01 | CMU SECTIONS & DETAILS | 100% CD | Feb 17, 2020 | V3 |
| S80-02 | CMU SECTIONS & DETAILS | 100% CD | Feb 17, 2020 | V1 |
| S80-11 | EVENT LEVEL - CMU LOCATION PLAN | ASI-002 | Apr 17, 2020 | V2 |

Arena Specifications

| Document Number and Description | Issuance | Date | Version |
|---|---|---|---|
| 00000 - Specification Cover Sheet.pdf | 100% CD | Feb 17, 2020 | V5 |
| 00001 - Table of Contents.pdf | 100% CD | Feb 17, 2020 | V5 |
| 003132 - Geotechnical Data.pdf | 100% CD | Feb 17, 2020 | V1 |
| 011000 - Summary.pdf | 100% CD | Feb 17, 2020 | V2 |
| 012300 - Alternates.pdf | 100% CD | Feb 17, 2020 | V1 |
| 012500 - Substitution Procedures.pdf | 100% CD | Feb 17, 2020 | V2 |
| 012600 - Contract Modification Procedures.pdf | 100% CD | Feb 17, 2020 | V2 |
| 012900 - Payment Procedures.pdf | 100% DD | Oct 21, 2019 | V1 |
| 013100 - Management And Coordination.pdf | 100% CD | Feb 17, 2020 | V2 |
| 013200 - Construction Progress Documentation.pdf | 100% CD | Feb 17, 2020 | V2 |
| 013233 - Photographic Documentation.pdf | 100% DD | Oct 21, 2019 | V1 |
| 013300 - Submittal Procedures.pdf | 100% CD | Feb 17, 2020 | V2 |
| 014000 - Quality Requirements.pdf | 100% CD | Feb 17, 2020 | V2 |
| 014200 - References.pdf | 100% CD | Feb 17, 2020 | V2 |
| 014529 - Structural Testing And Inspections.pdf | 100% CD | Feb 17, 2020 | V5 |
| 015000 - Temporary Facilities And Controls.pdf | 100% CD | Feb 17, 2020 | V2 |
| 016000 - Product Requirements.pdf | 100% CD | Feb 17, 2020 | V2 |
| 017300 - Execution.pdf | 100% CD | Feb 17, 2020 | V2 |
| 017419 - Construction Waste Management And Disposal.pdf | 100% CD | Feb 17, 2020 | V2 |
| 017700 - Closeout Procedures.pdf | 100% CD | Feb 17, 2020 | V2 |
| 017823 - Operation And Maintenance Data.pdf | 100% CD | Feb 17, 2020 | V2 |
| 017839 - Record Documents.pdf | 100% CD | Feb 17, 2020 | V2 |
| 017900 - Demonstration And Training.pdf | 100% CD | Feb 17, 2020 | V2 |
| 018113.14 - Sustainable Design Requirements Leed V B.pdf | 100% CD | Feb 17, 2020 | V2 |
| 019113 - General Commissioning Requirements.pdf | 100% CD | Feb 17, 2020 | V2 |
| 02100 - Clearing.pdf | 100% CD | Feb 17, 2020 | V2 |
| 02200 - Earthwork.pdf | 100% CD | Feb 17, 2020 | V2 |
| 02270 - Erosion And Sedimentation Control.pdf | 100% CD | Feb 17, 2020 | V2 |

| | | | |
|---|---|---|---|
| 02400 - Storm Drainage.pdf | 100% CD | Feb 17, 2020 | V2 |
| 02485 - Grassing.pdf | 100% CD | Feb 17, 2020 | V2 |
| 02550 - Water Distribution System.pdf | 100% CD | Feb 17, 2020 | V2 |
| 02554 - Wastewater Collection System.pdf | 100% CD | Feb 17, 2020 | V2 |
| 02600 - Pavement.pdf | 100% CD | Feb 17, 2020 | V2 |
| 031000 - Concrete Forming And Accessories.pdf | 100% CD | Feb 17, 2020 | V5 |
| 032000 - Concrete Reinforcing.pdf | 100% CD | Feb 17, 2020 | V5 |
| 033000 - Cast in place Concrete.pdf | 100% CD | Feb 17, 2020 | V5 |
| 03300 – Cast-in-place Concrete.pdf | 100% DD | Oct 21, 2019 | V1 |
| 033543 - Polished Concrete Finishing.pdf | 100% CD | Feb 17, 2020 | V2 |
| 034100 - Structural Precast Concrete.pdf | ASI-004 | May 11, 2020 | V4 |
| 034123 - Precast Concrete Stairs.pdf | 100% CD | Feb 17, 2020 | V3 |
| 034134 - Precast Pretensioned Concrete Seating Units.pdf | 100% CD | Feb 17, 2020 | V3 |
| 034500 - Precast Architectural Concrete.pdf | 100% DD | Oct 21, 2019 | V1 |
| 035416 - Hydraulic Cement Underlayment.pdf | 100% CD | Feb 17, 2020 | V2 |
| 042000 - Unit Masonry.pdf | 100% CD | Feb 17, 2020 | V2 |
| 042213 - Structural Reinforced Concrete Unit Masonry.pdf | 100% CD | Feb 17, 2020 | V3 |
| 047200 - Cast Stone Masonry.pdf | 100% CD | Feb 17, 2020 | V1 |
| 051200 - Structural Steel Framing.pdf | 100% CD | Feb 17, 2020 | V3 |
| 051213 - Architecturally Exposed Structural Steel Framing.pdf | Structural Steel Bid Package | Dec 19, 2019 | V1 |
| 052123 - Steel Joists And Joist Girders.pdf | 100% CD | Feb 17, 2020 | V3 |
| 053113 - Steel Floor Decking.pdf | 100% CD | Feb 17, 2020 | V3 |
| 053123 - Steel Roof Decking.pdf | 100% CD | Feb 17, 2020 | V3 |
| 054000 - Cold formed Metal Framing.pdf | 100% CD | Feb 17, 2020 | V3 |
| 055000 - Metal Fabrications.pdf | 100% CD | Feb 17, 2020 | V2 |
| 055100 - Metal Stairs.pdf | 100% CD | Feb 17, 2020 | V1 |
| 055113 - Metal Pan Stairs.pdf | 100% DD | Oct 21, 2019 | V1 |
| 055119 - Metal Grating Stairs.pdf | 100% CD | Feb 17, 2020 | V2 |
| 055213 - Pipe And Tube Railings.pdf | 100% DD | Oct 21, 2019 | V1 |
| 057300 - Decorative Metal Railings.pdf | 100% CD | Feb 17, 2020 | V1 |
| 057313 - Glazed Decorative Metal Railings.pdf | 100% CD | Feb 17, 2020 | V2 |
| 061053 - Miscellaneous Rough Carpentry.pdf | 100% CD | Feb 17, 2020 | V2 |
| 061600 - Sheathing.pdf | 100% CD | Feb 17, 2020 | V2 |
| 064116 – Plastic laminate faced Architectural Cabinets.pdf | 100% CD | Feb 17, 2020 | V2 |
| 064216 - Flush Wood Paneling.pdf | 100% CD | Feb 17, 2020 | V2 |
| 066400 - Plastic Paneling.pdf | 100% CD | Feb 17, 2020 | V2 |
| 071113 - Bituminous Dampproofing.pdf | 100% CD | Feb 17, 2020 | V2 |
| 071616 - Crystalline Waterproofing.pdf | 100% CD | Feb 17, 2020 | V1 |
| 071700 - Bentonite Waterproofing.pdf | 100% CD | Feb 17, 2020 | V1 |
| 072100 - Thermal Insulation.pdf | 100% CD | Feb 17, 2020 | V1 |
| 072119 – Foamed in place Insulation.pdf | 100% CD | Feb 17, 2020 | V2 |
| 072419 – Water drainage Exterior Insulation And Finish.pdf | 100% CD | Feb 17, 2020 | V1 |
| 072726 – Fluid applied Membrane Air Barriers.pdf | 100% CD | Feb 17, 2020 | V2 |
| 074213.13 - Formed Metal Wall Panels.pdf | 100% CD | Feb 17, 2020 | V2 |

| | | | |
|---|---|---|---|
| 074213.23 - Metal Composite Material Wall Panels.pdf | 100% CD | Feb 17, 2020 | V2 |
| 074293 - Soffit Panels.pdf | 100% CD | Feb 17, 2020 | V2 |
| 075423 – Thermoplastic polyolefin Tpo Roofing.pdf | 100% CD | Feb 17, 2020 | V2 |
| 075556 – Fluid applied Protected Membrane Roofing.pdf | 100% CD | Feb 17, 2020 | V1 |
| 076200 - Sheet Metal Flashing And Trim.pdf | 100% CD | Feb 17, 2020 | V2 |
| 077200 - Roof Accessories.pdf | 100% CD | Feb 17, 2020 | V2 |
| 078100 - Applied Fireproofing.pdf | 100% CD | Feb 17, 2020 | V2 |
| 078123 - Intumescent Fireproofing.pdf | 100% CD | Feb 17, 2020 | V2 |
| 078413 - Penetration Firestopping.pdf | 100% CD | Feb 17, 2020 | V2 |
| 078443 - Joint Firestopping.pdf | 100% CD | Feb 17, 2020 | V2 |
| 079200 - Joint Sealants.pdf | 100% CD | Feb 17, 2020 | V1 |
| 079219 - Acoustical Joint Sealants.pdf | 100% CD | Feb 17, 2020 | V2 |
| 081113 - Hollow Metal Doors And Frames.pdf | 100% CD | Feb 17, 2020 | V2 |
| 081416 - Flush Wood Doors.pdf | 100% CD | Feb 17, 2020 | V2 |
| 083113 - Access Doors And Frames.pdf | 100% CD | Feb 17, 2020 | V2 |
| 083323 - Overhead Coiling Doors.pdf | 100% CD | Feb 17, 2020 | V2 |
| 084113 - Aluminum framed Entrances and Storefronts.pdf | 100% CD | Feb 17, 2020 | V1 |
| 084126 - All glass Entrances And Storefronts.pdf | 100% CD | Feb 17, 2020 | V1 |
| 084213 - Aluminum framed Entrances.pdf | 100% DD | Oct 21, 2019 | V1 |
| 084413 - Glazed Aluminum Curtain Walls.pdf | 100% CD | Feb 17, 2020 | V2 |
| 087100 - Door Hardware.pdf | Amendment 3 | Apr 8, 2020 | V1 |
| 088000 - Glazing.pdf | 100% CD | Feb 17, 2020 | V2 |
| 088300 - Mirrors.pdf | 100% CD | Feb 17, 2020 | V2 |
| 089119 - Fixed Louvers.pdf | 100% CD | Feb 17, 2020 | V2 |
| 092116.23 - Gypsum Board Shaft Wall Assemblies.pdf | 100% CD | Feb 17, 2020 | V2 |
| 092216 - Nonstructural Metal Framing.pdf | 100% CD | Feb 17, 2020 | V2 |
| 092900 - Gypsum Board.pdf | 100% CD | Feb 17, 2020 | V2 |
| 093013 - Ceramic Tiling.pdf | 100% CD | Feb 17, 2020 | V2 |
| 095113 - Acoustical Panel Ceilings.pdf | 100% CD | Feb 17, 2020 | V2 |
| 096513 - Resilient Base And Accessories.pdf | 100% CD | Feb 17, 2020 | V2 |
| 096519 - Resilient Tile Flooring.pdf | 100% CD | Feb 17, 2020 | V2 |
| 096566 - Resilient Athletic Flooring.pdf | 100% CD | Feb 17, 2020 | V2 |
| 096623 - Resinous Matrix Terrazzo Flooring.pdf | 100% CD | Feb 17, 2020 | V1 |
| 096723 - Resinous Flooring.pdf | 100% CD | Feb 17, 2020 | V1 |
| 096813 - Tile Carpeting.pdf | 100% CD | Feb 17, 2020 | V2 |
| 097200 - Wall Coverings.pdf | 100% CD | Feb 17, 2020 | V2 |
| 097723 - Fabric wrapped Panels.pdf | 100% DD | Oct 21, 2019 | V1 |
| 098433 - Sound absorbing Wall Units.pdf | 100% CD | Feb 17, 2020 | V2 |
| 099123 - Interior Painting.pdf | 100% CD | Feb 17, 2020 | V2 |
| 099600 - High-performance Coatings.pdf | 100% CD | Feb 17, 2020 | V2 |
| 101100 - Visual Display Units.pdf | 100% DD | Oct 21, 2019 | V1 |
| 101423 - Panel Signage.pdf | 100% CD | Feb 17, 2020 | V2 |
| 102113.13 - Metal Toilet Compartments.pdf | 100% DD | Oct 21, 2019 | V1 |
| 102113.15 - Stainless-steel Toilet Compartments.pdf | 100% DD | Oct 21, 2019 | V1 |

| | | | |
|---|---|---|---|
| 102113.19 - Plastic Toilet Compartments.pdf | 100% CD | Feb 17, 2020 | V1 |
| 102239 - Folding Panel Partitions.pdf | 100% CD | Feb 17, 2020 | V2 |
| 102600 - Wall And Door Protection.pdf | 100% CD | Feb 17, 2020 | V2 |
| 102800 - Toilet Bath And Laundry Accessories.pdf | 100% CD | Feb 17, 2020 | V2 |
| 104413 - Fire Protection Cabinets.pdf | 100% CD | Feb 17, 2020 | V2 |
| 104416 - Fire Extinguishers.pdf | 100% CD | Feb 17, 2020 | V2 |
| 111313 - Loading Dock Bumpers.pdf | 100% CD | Feb 17, 2020 | V2 |
| 111316 - Loading Dock Seals And Shelters.pdf | 100% CD | Feb 17, 2020 | V2 |
| 111319 - Stationary Loading Dock Equipment.pdf | 100% CD | Feb 17, 2020 | V2 |
| 112423 - Window Washing Equipment.pdf | 100% CD | Feb 17, 2020 | V2 |
| 114000 - Foodservice Equipment.pdf | 100% CD | Feb 17, 2020 | V2 |
| 116123 - Folding And Portable Stages.pdf | 100% CD | Feb 17, 2020 | V2 |
| 116133 - Arena Rigging Systems.pdf | 100% CD | Feb 17, 2020 | V1 |
| 116143 - House Reduction Curtains.pdf | 100% CD | Feb 17, 2020 | V2 |
| 116145 - Blackout And Vomitory Curtains.pdf | 100% CD | Feb 17, 2020 | V2 |
| 116147 - Half House Curtains.pdf | 100% CD | Feb 17, 2020 | V2 |
| 116310 - Led Display And Scoring Systems.pdf | 100% CD | Feb 17, 2020 | V2 |
| 116350 - Video Production System.pdf | 100% CD | Feb 17, 2020 | V2 |
| 122413 - Roller Window Shades.pdf | 100% CD | Feb 17, 2020 | V2 |
| 123661.16 - Solid Surfacing Countertops.pdf | 100% CD | Feb 17, 2020 | V2 |
| 123661.19 - Quartz Agglomerate Countertops.pdf | 100% CD | Feb 17, 2020 | V2 |
| 124816 - Entrance Floor Grilles.pdf | 100% CD | Feb 17, 2020 | V2 |
| 127100 - Telescopic Platforms.pdf | 100% CD | Feb 17, 2020 | V2 |
| 127200 - Telescopic Platform Seating.pdf | 100% CD | Feb 17, 2020 | V2 |
| 127300 - Fixed Arena Seating.pdf | 100% CD | Feb 17, 2020 | V2 |
| 127400 - Portable Folding Chairs.pdf | 100% CD | Feb 17, 2020 | V2 |
| 127500 - Moveable Riser Platforms.pdf | 100% CD | Feb 17, 2020 | V2 |
| 131061 - Ice Rink Refrigeration And Piping.pdf | 100% CD | Feb 17, 2020 | V2 |
| 131062 - Ice Rink Floor.pdf | 100% CD | Feb 17, 2020 | V2 |
| 131063 - Ice Rink Insulation.pdf | 100% CD | Feb 17, 2020 | V2 |
| 131064 - Ice Conditioning Equipment.pdf | 100% CD | Feb 17, 2020 | V2 |
| 132000 - Aluminum Frame Dasher Board System.pdf | 100% CD | Feb 17, 2020 | V1 |
| 142123.16 - Machine Roomless Electric Traction Passeng.pdf | 100% CD | Feb 17, 2020 | V2 |
| 143100 - Escalators.pdf | 100% CD | Feb 17, 2020 | V2 |
| 210500 - Common Work Results For Fire Suppression.pdf | 100% CD | Feb 17, 2020 | V2 |
| 210800 - Commissioning Of Fire Suppression System.pdf | 100% CD | Feb 17, 2020 | V2 |
| 210900 - Fire Suppression System Automation And Automat.pdf | 100% CD | Feb 17, 2020 | V2 |
| 211300 - Fire Suppression Sprinkler Systems.pdf | 100% CD | Feb 17, 2020 | V2 |
| 211319 - Preaction Suppression Systems.pdf | 100% CD | Feb 17, 2020 | V2 |
| 212200 - Clean Agent Fire Extinguishing Systems.pdf | 100% CD | Feb 17, 2020 | V2 |
| 219000 - Fire Suppression System Closeout.pdf | 100% CD | Feb 17, 2020 | V2 |
| 220500 - Common Work Results For Plumbing.pdf | 100% CD | Feb 17, 2020 | V2 |
| 220700 - Plumbing Insulation.pdf | 100% CD | Feb 17, 2020 | V2 |
| 220800 - Commissioning Of Plumbing.pdf | 100% CD | Feb 17, 2020 | V2 |

| | | | |
|---|---|---|---|
| 220900 - Plumbing Automation And Automatic Temperature.pdf | 100% CD | Feb 17, 2020 | V2 |
| 221000 - Plumbing Piping.pdf | 100% CD | Feb 17, 2020 | V2 |
| 221123 - Domestic Water Booster.pdf | 100% CD | Feb 17, 2020 | V2 |
| 222123 - Natural Gas Systems.pdf | 100% CD | Feb 17, 2020 | V2 |
| 223000 - Plumbing Equipment.pdf | 100% CD | Feb 17, 2020 | V2 |
| 224000 - Plumbing Fixtures.pdf | 100% CD | Feb 17, 2020 | V2 |
| 226317 - Carbon dioxide Systems.pdf | 100% CD | Feb 17, 2020 | V1 |
| 229000 - Plumbing Closeout.pdf | 100% CD | Feb 17, 2020 | V2 |
| 230501 - Mechanical And Electrical Coordination.pdf | 100% CD | Feb 17, 2020 | V2 |
| 230501_revised_1854 - Mechanical And Electrical Coordinatio.pdf | 100% DD | Oct 21, 2019 | V1 |
| 230501_revised_2094 - Mechanical And Electrical Coordinatio.pdf | 100% CD | Feb 17, 2020 | V1 |
| 230502 - Basic Mechanical Requirements.pdf | 100% CD | Feb 17, 2020 | V2 |
| 230503 - Basic Mechanical Materials And Methods.pdf | 100% CD | Feb 17, 2020 | V2 |
| 230513 - Motors And Starters.pdf | 100% CD | Feb 17, 2020 | V2 |
| 230521 - Pipe And Pipe Fittings.pdf | 100% CD | Feb 17, 2020 | V2 |
| 230522 - Piping Accessories.pdf | 100% CD | Feb 17, 2020 | V2 |
| 230523 - Valves.pdf | 100% CD | Feb 17, 2020 | V2 |
| 230529 - Pipe Supports And Anchors.pdf | 100% CD | Feb 17, 2020 | V2 |
| 230530 - Electronic Speed Controllers.pdf | 100% CD | Feb 17, 2020 | V2 |
| 230548 - Vibration Control.pdf | 100% CD | Feb 17, 2020 | V2 |
| 230549 - Seismic Restraints.pdf | RFI 104 | Apr 20, 2020 | V1 |
| 230549 - Seismic Restraints.pdf | 100% DD | Oct 21, 2019 | V1 |
| 230553 - Mechanical Identification.pdf | 100% CD | Feb 17, 2020 | V2 |
| 230593 - Testadjustbalance.pdf | 100% CD | Feb 17, 2020 | V2 |
| 230700 - Mechanical Insulation.pdf | 100% CD | Feb 17, 2020 | V2 |
| 230800 - Building Mechanical System Commissioning.pdf | 100% CD | Feb 17, 2020 | V2 |
| 230801 - Commissioning Agent Requirements.pdf | 100% CD | Feb 17, 2020 | V2 |
| 230900 - Building Automation And Automatic Temperature.pdf | ASI-001 | Apr 13, 2020 | V3 |
| 230902 - Life Safety Systems.pdf | 100% CD | Feb 17, 2020 | V2 |
| 230903_revised_2372 - Smoke Management.pdf | 100% DD | Oct 21, 2019 | V1 |
| 230903 - Smoke Management.pdf | 100% CD | Feb 17, 2020 | V2 |
| 232113 - Hydronic Piping.pdf | 100% CD | Feb 17, 2020 | V2 |
| 232123 - Hvac Pumps.pdf | 100% CD | Feb 17, 2020 | V2 |
| 232124 - Variable Speed Pumping System.pdf | 100% CD | Feb 17, 2020 | V2 |
| 232300 - Refrigerant Piping.pdf | 100% CD | Feb 17, 2020 | V2 |
| 232513 - Hvac System Chemical Treatment.pdf | 100% CD | Feb 17, 2020 | V2 |
| 232516 - Condenser Water Treating System.pdf | 100% CD | Feb 17, 2020 | V2 |
| 232600 - Energy And Water Metering Devices.pdf | 100% CD | Feb 17, 2020 | V2 |
| 233113 - Ductwork.pdf | 100% CD | Feb 17, 2020 | V2 |
| 233117 - Fabric Ductwork.pdf | 100% CD | Feb 17, 2020 | V2 |
| 233300 - Ductwork Accessories.pdf | 100% CD | Feb 17, 2020 | V2 |
| 233400 - Fans.pdf | 100% CD | Feb 17, 2020 | V2 |
| 233600 - Air Terminal Units.pdf | 100% CD | Feb 17, 2020 | V2 |
| 233700 - Air Inlets And Outlets.pdf | 100% CD | Feb 17, 2020 | V2 |

| | | | |
|---|---|---|---|
| 234000 - Air Cleaning.pdf | 100% CD | Feb 17, 2020 | V2 |
| 235100 - Flue Systems.pdf | 100% CD | Feb 17, 2020 | V2 |
| 235200 - Boilers.pdf | 100% CD | Feb 17, 2020 | V2 |
| 235700 - Heat Exchangers.pdf | 100% CD | Feb 17, 2020 | V2 |
| 236416 - Centrifugal Water Chillers.pdf | 100% CD | Feb 17, 2020 | V2 |
| 236500 - Cooling Towers.pdf | 100% CD | Feb 17, 2020 | V2 |
| 237313 - Air Handling Units With Coil.pdf | 100% CD | Feb 17, 2020 | V1 |
| 237325 - Desiccant Air Handling Units With Coils.pdf | 100% DD | Oct 21, 2019 | V1 |
| 237500 - Outdoor Air Handling Units With Coils.pdf | 100% DD | Oct 21, 2019 | V1 |
| 238219 - Fan Coil Units.pdf | 100% CD | Feb 17, 2020 | V2 |
| 239000 - Closeout.pdf | 100% CD | Feb 17, 2020 | V2 |
| 260502 - Electrical Requirements.pdf | 100% CD | Feb 17, 2020 | V2 |
| 260503 - Testing.pdf | 100% CD | Feb 17, 2020 | V2 |
| 260505 - Manufacturers.pdf | 100% CD | Feb 17, 2020 | V2 |
| 260506 - Basic Material And Methods.pdf | 100% CD | Feb 17, 2020 | V2 |
| 260507 - Food Service Equipment Wiring.pdf | 100% CD | Feb 17, 2020 | V2 |
| 260519 - Electrical Power Conductors And Cables.pdf | 100% CD | Feb 17, 2020 | V2 |
| 260526 - Grounding And Bonding.pdf | 100% CD | Feb 17, 2020 | V2 |
| 260529 - Hangers And Supports.pdf | 100% CD | Feb 17, 2020 | V2 |
| 260533 - Raceways And Boxes.pdf | 100% CD | Feb 17, 2020 | V2 |
| 260553 - Identification.pdf | 100% CD | Feb 17, 2020 | V2 |
| 260943 - Lighting Control System.pdf | 100% CD | Feb 17, 2020 | V2 |
| 262213 - Low voltage Distribution Transformers.pdf | 100% CD | Feb 17, 2020 | V2 |
| 262413 - Distribution Switchboards.pdf | 100% CD | Feb 17, 2020 | V2 |
| 262416 - Panelboards.pdf | 100% CD | Feb 17, 2020 | V2 |
| 262726 - Wiring Devices.pdf | 100% CD | Feb 17, 2020 | V2 |
| 262816 - Enclosed Switches Fuses And Circuit Breakers.pdf | 100% CD | Feb 17, 2020 | V2 |
| 262817 - Company Switches.pdf | 100% CD | Feb 17, 2020 | V2 |
| 262913 - Enclosed Motor Controllers.pdf | 100% CD | Feb 17, 2020 | V2 |
| 263213 - Diesel engine Driven Generator Sets.pdf | 100% CD | Feb 17, 2020 | V2 |
| 263353 - Static Uninterruptible Power Supply.pdf | 100% CD | Feb 17, 2020 | V2 |
| 263623 - Automatic Transfer Switches.pdf | 100% CD | Feb 17, 2020 | V2 |
| 264113 - Lightning Protection For Structures.pdf | 100% CD | Feb 17, 2020 | V2 |
| 264314 - Surge Protective Device Spd.pdf | 100% CD | Feb 17, 2020 | V2 |
| 265113 - Lighting Fixtures.pdf | 100% CD | Feb 17, 2020 | V2 |
| 265210 - Emergency Lighting Inverter.pdf | 100% DD | Oct 21, 2019 | V1 |
| 265613 - Poles And Standards.pdf | 100% CD | Feb 17, 2020 | V2 |
| 265671 - Led Arena Lighting Fixtures.pdf | 100% CD | Feb 17, 2020 | V2 |
| 269000 - Closeout.pdf | 100% CD | Feb 17, 2020 | V2 |
| 270100 - General Requirements For Communications Systems.pdf | 100% CD | Feb 17, 2020 | V2 |
| 270510 - Firestopping For Communications Systems.pdf | 100% CD | Feb 17, 2020 | V2 |
| 270526 - Grounding Bonding For Communications Systems.pdf | 100% CD | Feb 17, 2020 | V2 |
| 270528 - Pathways For Communications Systems.pdf | 100% CD | Feb 17, 2020 | V2 |
| 270553 - Administration Labeling.pdf | 100% CD | Feb 17, 2020 | V2 |

| | | | |
|---|---|---|---|
| 270800 - Communications Commissioning.pdf | 100% CD | Feb 17, 2020 | V2 |
| 271100 - Equipment Room Components.pdf | 100% CD | Feb 17, 2020 | V2 |
| 271119 - Communication System Termination Blocks Patch.pdf | 100% CD | Feb 17, 2020 | V2 |
| 271123 - Communication Cable Management Telecom Room La.pdf | 100% CD | Feb 17, 2020 | V2 |
| 271126 - Communications Rack Mounted Power Distribution.pdf | ASI-006 | Jun 3, 2020 | V2 |
| 271300 - Communications Backbone Cabling.pdf | 100% DD | Oct 21, 2019 | V1 |
| 271300 - Copper Backbone Cabling.pdf | 100% CD | Feb 17, 2020 | V1 |
| 271323 - Communications Optical Fiber Backbone Cabling.pdf | 100% CD | Feb 17, 2020 | V2 |
| 271500 - Copper Horizontal Cabling.pdf | 100% CD | Feb 17, 2020 | V2 |
| 271543 - Communication Faceplates Connectors.pdf | 100% CD | Feb 17, 2020 | V2 |
| 272000 - Acceptable Manufacturers.pdf | 100% CD | Feb 17, 2020 | V2 |
| 274000 - Audio Visual Systems General.pdf | ASI-006 | Jun 3, 2020 | V3 |
| 274116 - Integrated Audio video Systems Equipment.pdf | 100% CD | Feb 17, 2020 | V2 |
| 276000 - Broadcast Cabling System.pdf | 100% CD | Feb 17, 2020 | V2 |
| 281000 - Ip Video Surveillance System.pdf | ASI-006 | Jun 3, 2020 | V3 |
| 282000 - Security Access Control Systems.pdf | ASI-006 | Jun 3, 2020 | V2 |
| 282000 - Security Access Control Systems.pdf | ASI-006 | Jun 3, 2020 | V1 |
| 283000 - Intercom Emergency Call System.pdf | 100% CD | Feb 17, 2020 | V1 |
| 283100 - Addressable Fire Alarm System.pdf | 100% CD | Feb 17, 2020 | V2 |
| 284000 - Intercom System.pdf | 100% DD | Oct 21, 2019 | V1 |
| 285000 - Area Of Rescue Assistance System.pdf | 100% CD | Feb 17, 2020 | V2 |
| 285320 - Emergency Responder Radio System.pdf | 100% CD | Feb 17, 2020 | V2 |
| 312300 - Excavation And Fill.pdf | 100% CD | Feb 17, 2020 | V5 |
| 316316 - Auger Cast Grout Piles.pdf | 100% CD | Feb 17, 2020 | V5 |
| 321813 fl - Synthetic Turf System.pdf | RFI 188 | Jun 4, 2020 | V1 |

Canal Wall Drawings

| Document Number | Description | Issuance | Date | Version |
|---|---|---|---|---|
| B001 | BORING LOGS | Canal Wall Drawings | Feb 14, 2020 | V1 |
| C101 | LAYOUT PLAN | Canal Wall Drawings | Feb 14, 2020 | V1 |
| C201 | PILE PLAN | Canal Wall Drawings | Feb 14, 2020 | V1 |
| C202 | PILE PLAN | Canal Wall Drawings | Feb 14, 2020 | V1 |
| C203 | PILE PLAN | Canal Wall Drawings | Feb 14, 2020 | V1 |
| C301 | GRADING PLAN AND SEQUENCING | Canal Wall Drawings | Feb 14, 2020 | V1 |
| C501 | SECTIONS AND DETAILS | Canal Wall Drawings | Feb 14, 2020 | V1 |
| C502 | SECTIONS AND DETAILS | Canal Wall Drawings | Feb 14, 2020 | V1 |
| C503 | SECTIONS AND DETAILS | Canal Wall Drawings | Feb 14, 2020 | V1 |

| | | | | |
|---|---|---|---|---|
| C504 | SECTIONS AND DETAILS | Canal Wall Drawings | Feb 14, 2020 | V1 |
| C505 | SECTIONS AND DETAILS | Canal Wall Drawings | Feb 14, 2020 | V1 |
| C506 | SECTIONS AND DETAILS | Canal Wall Drawings | Feb 14, 2020 | V1 |
| EC001 | ESPC DETAILS | Canal Wall Drawings | Feb 14, 2020 | V1 |
| EC002 | ESPC DETAILS | Canal Wall Drawings | Feb 14, 2020 | V1 |
| EC003 | ESPC DETAILS | Canal Wall Drawings | Feb 14, 2020 | V1 |
| EC004 | ESPC DETAILS | Canal Wall Drawings | Feb 14, 2020 | V1 |
| EC101 | INITIAL ESPC PLAN | Canal Wall Drawings | Feb 14, 2020 | V1 |
| EC102 | INTERMEDIATE ESPC PLAN | Canal Wall Drawings | Feb 14, 2020 | V1 |
| EC103 | DINAL ESPC PLAN | Canal Wall Drawings | Feb 14, 2020 | V1 |
| EC501 | ESPC DETAILS | Canal Wall Drawings | Feb 14, 2020 | V1 |
| EC502 | ESPC DETAILS | Canal Wall Drawings | Feb 14, 2020 | V1 |
| EC503 | ESPC DETAILS | Canal Wall Drawings | Feb 14, 2020 | V1 |
| EC504 | ESPC DETAILS | Canal Wall Drawings | Feb 14, 2020 | V1 |
| G100 | COVER | Canal Wall Drawings | Feb 14, 2020 | V1 |
| G101 | GENERAL NOTES & LEGEND | Canal Wall Drawings | Feb 14, 2020 | V1 |
| G102 | PROJECT MAP | Canal Wall Drawings | Feb 14, 2020 | V1 |
| V101 | EXISTING CONDITIONS & DEMOLITION PLAN | Canal Wall Drawings | Feb 14, 2020 | V1 |
| V102 | USGS TOPOGRAPHIC MAP | Canal Wall Drawings | Feb 14, 2020 | V1 |

Stiles Avenue Drawings

| Document Number | Description | Issuance | Date | Version |
|---|---|---|---|---|
| *Title Page | | Stiles Avenue Drawings | Apr 3, 2020 | V1 |
| 02 | CONSTRUCTION NOTES AND LEGENDS | Stiles Avenue Drawings | Apr 3, 2020 | V1 |
| 03 | PROJECT MAP | Stiles Avenue Drawings | Apr 3, 2020 | V1 |
| 04 | EXISTING CONDITIONS PLAN | Stiles Avenue Drawings | Apr 3, 2020 | V1 |
| 05 | EXISTING CONDITIONS PLAN | Stiles Avenue Drawings | Apr 3, 2020 | V1 |
| 06 | DEMOLITION PLAN | Stiles Avenue Drawings | Apr 3, 2020 | V1 |
| 07 | DEMOLITION PLAN | Stiles Avenue Drawings | Apr 3, 2020 | V1 |
| 08 | LAYOUT AND TRAFFIC MARKING PLAN | Stiles Avenue Drawings | Apr 3, 2020 | V1 |

| | | | | |
|---|---|---|---|---|
| 09 | LAYOUT AND TRAFFIC MARKING PLAN | Stiles Avenue Drawings | Apr 3, 2020 | V1 |
| 10 | PAVING, GRADING AND DRAINAGE PLAN AND ROAD PROFILE | Stiles Avenue Drawings | Apr 3, 2020 | V1 |
| 11 | PAVING, GRADING AND DRAINAGE PLAN AND ROAD PROFILE | Stiles Avenue Drawings | Apr 3, 2020 | V1 |
| 12 | PAVING, GRADING AND DRAINAGE PLAN AND ROAD PROFILE | Stiles Avenue Drawings | Apr 3, 2020 | V1 |
| 13 | PAVING, GRADING AND DRAINAGE PLAN | Stiles Avenue Drawings | Apr 3, 2020 | V1 |
| 14 | UTILITY RELOACTION PLAN AND PROFILE | Stiles Avenue Drawings | Apr 3, 2020 | V1 |
| 15 | UTILITY RELOACTION PLAN AND PROFILE | Stiles Avenue Drawings | Apr 3, 2020 | V1 |
| 16 | UTILITY RELOACTION PLAN AND PROFILE | Stiles Avenue Drawings | Apr 3, 2020 | V1 |
| 17 | WATER MAIN AND STORM DRAINAGE PROFILES | Stiles Avenue Drawings | Apr 3, 2020 | V1 |
| 18 | SEWER PROFILE AND CONSTRUCTION DETAILS | Stiles Avenue Drawings | Apr 3, 2020 | V1 |
| 19 | CONSTRUCTION DETAILS | Stiles Avenue Drawings | Apr 3, 2020 | V1 |
| 20 | CONSTRUCTION DETAILS | Stiles Avenue Drawings | Apr 3, 2020 | V1 |
| 21 | CONSTRUCTION DETAILS | Stiles Avenue Drawings | Apr 3, 2020 | V1 |
| 22 | CONSTRUCTION DETAILS | Stiles Avenue Drawings | Apr 3, 2020 | V1 |
| 23 | CONSTRUCTION DETAILS | Stiles Avenue Drawings | Apr 3, 2020 | V1 |
| 24 | D.O.T CONSTRUCTION DETAILS | Stiles Avenue Drawings | Apr 3, 2020 | V1 |
| 25 | D.O.T CONSTRUCTION DETAILS | Stiles Avenue Drawings | Apr 3, 2020 | V1 |
| 26 | D.O.T CONSTRUCTION DETAILS | Stiles Avenue Drawings | Apr 3, 2020 | V1 |
| 27 | EROSION & SEDIMENT CONTROL NOTES | Stiles Avenue Drawings | Apr 3, 2020 | V1 |
| 28 | EROSION & SEDIMENT CONTROL NOTES | Stiles Avenue Drawings | Apr 3, 2020 | V1 |
| 29 | EROSION & SEDIMENT CONTROL PLAN – INITIAL PHASE | Stiles Avenue Drawings | Apr 3, 2020 | V1 |
| 30 | EROSION & SEDIMENT CONTROL PLAN – INITIAL PHASE | Stiles Avenue Drawings | Apr 3, 2020 | V1 |
| 31 | EROSION & SEDIMENT CONTROL PLAN – INTERMEDIATE PHASE | Stiles Avenue Drawings | Apr 3, 2020 | V1 |
| 32 | EROSION & SEDIMENT CONTROL PLAN – INTERMEDIATE PHASE | Stiles Avenue Drawings | Apr 3, 2020 | V1 |
| 33 | EROSION & SEDIMENT CONTROL PLAN – FINAL PHASE | Stiles Avenue Drawings | Apr 3, 2020 | V1 |
| 34 | EROSION & SEDIMENT CONTROL PLAN – FINAL PHASE | Stiles Avenue Drawings | Apr 3, 2020 | V1 |
| 35 | EROSION & SEDIMENT CONTROL DETAILS | Stiles Avenue Drawings | Apr 3, 2020 | V1 |

Pump Station and Off-Site Force Main Drawings

| Document Number | Description | Issuance | Date | Version |
|---|---|---|---|---|
| *Title Sheet | COVER SHEET, VICINITY MAPAND SCHEDULE OF DRAWINGS | Pump Station_ Off Site Force Main Drawings | Apr 14, 2020 | V1 |
| 02 | PROJECT MAP, LEGEND & GENERAL NOTES | Pump Station_ Off Site Force Main Drawings | Apr 14, 2020 | V1 |
| 03 | 8" FM PLAN & PROFILE | Pump Station_ Off Site Force Main Drawings | Apr 14, 2020 | V1 |
| 04 | 8" FM PLAN & PROFILE | Pump Station_ Off Site Force Main Drawings | Apr 14, 2020 | V1 |

| | | | | |
|---|---|---|---|---|
| 05 | 8" FM PLAN & PROFILE | Pump Station_ Off Site Force Main Drawings | Apr 14, 2020 | V1 |
| 06 | 8" FM PLAN & PROFILE | Pump Station_ Off Site Force Main Drawings | Apr 14, 2020 | V1 |
| 07 | CONNECTION AT EX. LIFT STATION | Pump Station_ Off Site Force Main Drawings | Apr 14, 2020 | V1 |
| 08 | CONNECTION AT PROPOSED LIFT STATION | Pump Station_ Off Site Force Main Drawings | Apr 14, 2020 | V1 |
| 09 | LIFT STATION PLAN AND SECTION | Pump Station_ Off Site Force Main Drawings | Apr 14, 2020 | V1 |
| 10 | CONSTRUCTION DETAILS | Pump Station_ Off Site Force Main Drawings | Apr 14, 2020 | V1 |
| 11 | CONSTRUCTION DETAILS | Pump Station_ Off Site Force Main Drawings | Apr 14, 2020 | V1 |
| 12 | CONSTRUCTION DETAILS | Pump Station_ Off Site Force Main Drawings | Apr 14, 2020 | V1 |
| 13 | EROSION & SEDIMENT CONTROL NOTES | Pump Station_ Off Site Force Main Drawings | Apr 14, 2020 | V1 |
| 14 | EROSION & SEDIMENT CONTROL NOTES | Pump Station_ Off Site Force Main Drawings | Apr 14, 2020 | V1 |

*Section 05*

# *Clarifications and Qualifications*

AECOM HUNT

*in association with*

Brownstone Construction Group
Pat Mathis Construction Company
A. Riley Consultants

## General –

1. Notwithstanding any provisions of the Construction Manager-at-Risk Agreement to the contrary, the total amount to be paid to AECOM Hunt for the performance of the Contract shall be a stipulated lump sum of $12,770,427 (which includes Pre-Construction Services Amount, the Staff costs/General Conditions Amount, and construction contingency).

2. This Guaranteed Maximum Price (GMP) was generated using the Construction Documents issued on February 17th, 2020, Stiles Avenue documents issued April 3, 2020, Savannah Arena Bulkhead documents issued February 12th, 2020, and Force Main documents issued April 14, 2020. The Future Parking Garage along the North face of the arena is excluded. Refer to Section 8 for the drawing, specification, and supplemental information log.

3. In the event of a discrepancy between these clarifications and any other document, these clarifications shall prevail.

4. The GMP is not a line-by-line guarantee of costs. The GMP includes adjustment for Subcontractor pricing, which may affect the detailed unit pricing displayed in our estimate report. The individual unit price amounts should not be used for budgetary purposes until their adjusted value has been verified with AECOM Hunt.

5. Any accepted value analysis items or value engineering items shall be incorporated in the construction documents or otherwise memorialized in a form agreed upon between AECOM Hunt and Owner in order to allow the construction to progress in accordance with the GMP Project Schedule.

6. The GMP excludes union wage rates and fringe benefits, Davis Bacon or any other prevailing wage rates.

7. The GMP excludes costs for building permits, plan review fees, impact fees, and metering fees.

8. The GMP includes special provisions and housekeeping as it relates to COVID-19 or Coronavirus as outlined in the "Coronavirus Disease 2019 & Workplace Preparedness Plan for Construction Projects" dated March 12, 2020. The GMP excludes any delays, work stoppages, quarantines, and all other unforeseen impacts as it relates to COVID-19.

9. Construction Manager shall not be responsible for the functionality, sight lines, layout, massing, positioning of suites and vertical and horizontal layout of all aspects of the program. Architect is the responsible designer for the facility and any issue that may arise during construction or after construction that involves the aforementioned items shall be the sole responsibility of Architect and the Owner.

10. It is assumed that all conditions for accessibility per local, state, and federal requirements are reflected in the Documents. Construction Manager shall not be responsible for changes to design or work to comply with local, state, or federal requirements regarding ADA compliance.

11. It is assumed that all requirements by local, state, and federal jurisdictions are reflected in the documents. This GMP relies on the drawings and specifications being code compliant. If not, the Owner shall be responsible for all costs to make design code compliant.

12. The GMP is based on the qualifications and assumptions that all elements of the work containing performance specifications and/or delegated design elements can be achieved as indicated in the Documents. The GMP assumes that all portion of the Work upon which such elements rely are sufficient to support installation and performance of such elements without modification. The GMP includes delegated design services only to the extent that such work is explicitly identified on the Contract Documents. AECOM Hunt is not responsible for the adequacy of any performance and design criteria. Neither AECOM Hunt nor its subcontractors shall be considered the Architect or Engineer of Record for any work.

    a. Including Exterior Framing (Specification 05 40 00)
    b. Including Curtainwall (Specification 08 44 13)
    c. Including Metal Stairs (Specification 05 51 00)
    d. Including Decorative Metal Railing (Specification 05 73 00)
    e. Including Glazed Decorative Metal Railings (Specification 05 73 00)
    f. Including Ice Rink Refrigeration and Piping (Specification 13 10 61)
    g. Including Fire Suppression Sprinkler Systems (Specification 21 13 00)
    h. Including Addressable Fire Alarm System (Specification 28 31 00)

13. The Management General Conditions and Non-Management General Conditions include items for AECOM Hunt to conduct business at the site. This includes office set-up, office staff salary, and other similar items. For accounting purposes only, the General Conditions have been split between subjobs (Sitework, Stiles Avenue, Force Main, and Canal Wall), but these are not line-by-line guarantee of costs. In the unlikely event a subjob is not authorized or is completed by others, the General Conditions within the GMP shall be revisited and adjusted appropriately through the change order process.

14. The GMP excludes General Conditions for the Owner's separate contractors, FFE, and consultants.

15. The construction schedule is based on a start of December 2019 with a substantial completion of December 20, 2021.

16. GMP is based generally on normal working hours, 7 AM to 3:30 PM Monday through Friday.

17. Sales tax is included

18. Subcontractor bonding is included

19. CM Payment/Performance Bond is included

20. General liability insurance is included.

21. In accordance with the Agreement, Builders Risk Property Insurance is excluded and shall be provided by Owner. Owner has procured and shall maintain "all-risk" Builder's Risk for the full duration of the project.

22. Railroad Protective Insurance is excluded. Any special provisions including but not limited to standby or railroad monitoring by separate entities is excluded.

23. The GMP excludes all utility fees and/or charges for permanent service installation or relocation, including but not limited to fees and/or charges from utility companies, railroad, City of Savannah, etc.

24. Estimate does not include tap/connection fees or service initial fees from any utility providers.

25. We have excluded owner related project soft costs such as:

    a. Owner's Contingency other than as noted below the line on the GMP Amendment estimate cover page. Said contingency excludes all allowable AECOM Hunt mark ups which shall be applied as contingency utilized.
    b. Financing
    c. A/E and other consultant fees
    d. Owner project management and administration costs
    e. Commissioning Agent Services
    f. Moving expenses
    g. Advertising expenses
    h. Utility Consumption

26. AECOM Hunt shall be provided CAD/Revit files at no cost to distribute to subcontractors for shop drawing and coordination drawing preparation without fees.

27. Material Testing is excluded.

28. The GMP assumes prompt response by the Owner's consultants including testing consultants within 48 hours (or otherwise required) of receipt of notice from Hunt in order to maintain the Project Schedule. Any delays caused by non-responsiveness of these consultants will be at the Owner's expense.

29. The GMP excludes any costs for a Commissioning Agent or Third-Party Inspections.

30. The GMP includes the use of BIM 360 for Requests for Information (RFIs) and Submittals.

31. The GMP includes the use of BIM 360 for field use for QA/QC and Punch List by the entire Project Team, including but not limited to A/E.

32. Any design team and/or third party testing agency observations requiring remediation/rework and other field inspection reports shall be issued and be inclusive of all comment and/or direction from the Owner and its design team on a bi-weekly basis in BIM 360. Such lists shall be coordinated and formally issued to the CM through a single entity.

33. The GMP includes the use of the Hunt Project Management Software, CMiC and Textura. CMiC will be used for Cost i.e. Subcontracts, Change Orders, etc. communicate with Textura. Textura will be used for accounting and the monthly payment applications.

34. The GMP excludes any guarantee for any type of LEED certification for the Savannah Arena, Stiles Avenue, Force Main, and/or Savannah Arena Bulkhead projects. The GMP includes

provisions for AECOM Hunt to assist in the preparation of the Construction and Demolition Waste Management Planning, Construction and Demolition Waste Management, and Construction Indoor Air Quality Management Plan.

35. The parking garage and arena lobbies shown within the garage are excluded.

36. The GMP does not include future tariffs, governmental fees or taxes, or changes in law to the extent any such events increase the cost or time of the performance of the Work, Construction Manager shall be entitled to a Change Order equitably adjusting the Contract Sum and Contract Time accordingly.

37. The GMP excludes any facility permanent fall protection and any associated provisions (embeds, anchor bolts, pockets, etc.).

38. The GMP excludes all mercantile equipment. All mercantile equipment shall be owner provided and owner installed including but not limited to point of sale, washers, and dryers.

39. The GMP excludes all Furniture, Fixtures, and Equipment (FF&E) that are to be Owner Furnished and/or Owner Furnished Owner Installed. Reference Section 06 of the GMP for responsibility matrix.

40. FF&E Contractors working directly for the owner will provide their own hoisting, clean-up, trash removal, and dumpsters for their items of work.

41. Blocking, sleeving, or similar rough-in requirements for Owner-furnished items is excluded unless specifically shown on the Contract Documents.

42. The GMP excludes final clean. GMP includes a construction clean or “broom sweep” clean for final clean to be completed by others.

43. The GMP requires Submittals as required by the Contract Documents to be returned within 10 working days from submission.

44. The GMP requires Requests for Information (RFIs) to be returned within 5 working days from submission.

45. The GMP assumes no hazardous materials are present on the site in any form that may require special handling, disposal, recovery, or cost considerations. There have been no costs included for remediation of or haul off of any soils materials that may contain hazardous materials.

46. The GMP does not include funds for unforeseen site conditions beyond the identified Owner controlled Allowance. The GMP excludes the removal of unidentified or unknown structures below grade.

47. Off-site utility demolition and/or relocation has not been included.

48. The GMP includes the following Owner Allowances to be used only at Owner Direction and Approval, and all values are NOT guaranteed by AECOM Hunt and if costs exceed Owner

Allowances than AECOM Hunt shall only perform work in excess of Owner Allowance following receipt of Owner Change Order (OCO) or other acceptable contract vehicle:

| | | |
|---|---|---|
| a. | Branding, Graphics, and Wayfinding Signage | $1,350,000 |
| b. | Sitework Allowance | $ 50,000 |
| c. | Unforeseen Underground Obstructions | $ 100,000 |
| d. | Fountains | $ 250,000 |
| e. | Stiles, Force Main, Canal Development (HGB) | $ 700,000 |

49. The GMP incorporates the project information including but not limited to all associated costs contained in the following Potential Change Items (PCIs) document:

| | | |
|---|---|---|
| a. | PCI 00033 – SA – Q2 Unforeseen Buried Drums, Tires, etc. | $103,330 |
| b. | PCI 00036 – SA – Unforeseen Concrete Washout along Canal | $32,896 |
| c. | PCI 00046 – SA – CCD 01 – Site Utilities and Stiles Work Rev | $106,165 |
| d. | PCI 00047 – SA 31A – Quad 3 Unforeseen Unground Tank Discovery | $41,591 |
| e. | PCI 00057 – SA – ASI 002 – Structural Revisions | $64,189 |
| f. | PCI 00059 – SA – ASI 004 – Structural Coordination | $67,168 |
| g. | PCI 00065 – SA – ASI 009 – Structural Steel RFI SSK Inclusions | $84,046 |
| h. | PCI 00078 – SA – RFI 00234 – Revised Box Truss Framing to WF | $60,000 |
| i. | PCI 00080 – SA – ASI 006 – AV and LV Changes | $20,304 |

50. For changes in the Work, in addition to mark ups by Subcontractors, the following mark ups shall be applied by AECOM Hunt (AECOM Hunt reserves the right to waive mark ups or adjust appropriately on a case by case basis with mutual agreement by Owner):

a. General Conditions (GCs) 2.5%
b. Insurance 0.7%
c. CM Payment and Performance Bonds 0.8%
d. Fee 2.75%

## Division 3 –Concrete

3.1. The GMP includes precast structure for the lower bowl seating area in lieu of structural steel.

3.2. The GMP excludes any architectural colored concrete in building structure.

3.3. The GMP excludes concrete encased columns.

## Division 4 – Masonry

4.1. CMU walls are carried as 8'-0" elevation and metal studs/gyp to structure above on Event Level as shown on the Contract Documents.

4.2. The GMP excludes all radius block as none shown on the contract documents.

4.3. The GMP includes the use of Belden Mayo Blend Norman Blend for all brick. The GMP includes a mock-up for Belden Mayo Blend Normal Blend as well as a separate mock-up of a Cherokee brick. Final selection shall be following review of said mock-ups, and the GMP shall be adjusted appropriately through the change order process.

## Division 5 – Steel

5.1. The GMP includes a subcontract for connection design with Walter P Moore dba MXE Consultants for accounting purposes only. Walter P Moore and Perkins & Will shall coordinate their services together as if steel connection engineering is being performed as part of overall arena design services. AECOM Hunt shall not be held responsible or liable for structural steel connection design and engineering. The GMP excludes note B.1 on S00-01 which is contrary to previous statement.

5.2. The GMP excludes LOD400 Modeling

5.3. The GMP excludes handrailing at the dock area. All handrail shown on Parking Garage contract documents shall be in included within future Parking Garage amendment.

5.4. Structural Steel will come to the job site with shop primer only, any finish painting of steel will be done in the field and is included in division 9 painting scope of work.

5.5. It is agreed and understood that the paint system on the Structural Steel will require touch-up at connections and areas damaged in the erection process. These areas will be field painted and the field painting will potentially have a different sheen and shading than the shop applied coat.

5.6. The GMP includes RFI 00234 which changes (7) joist bays to WF framing with HSS bracing between the beams similar to the permanent braced bays. Said temporary bracing connections shall be designed such that after erection each end of diagonal brace is released and remain in place with no axial load in final condition.

5.7. The GMP includes NOMMA 3 welds at all handrails and guardrails.

5.8. The GMP excludes carts or storage racks for removable railings.

5.9. The GMP assumes all removable rails are attached by use of Halfen Channels (31/A42-22) not internal sleeves and plates.

5.10. The GMP includes Architecturally Exposed Structural Steel (AESS) as noted on the Contract Documents including but not limited to S33-02 Note 1. AESS category to be applied to said notes and I.D. shall be AESS C Custom Elements.

5.11. The GMP excludes S00-02 Part XIII – Miscellaneous, Note I Elevator Guide Rail Supports, 1. "The General Contractor shall provide intermediate guide rail supports for elevator cab rails and

counterweight rails wherever the floor to floor height exceeds 12'-2"" unless specifically located and noted on the Contract Documents.

## Division 6 – Woods and Plastics

6.1. Wood lockers are included for home locker and coaches' lockers.

6.2. The GMP Excludes any fire rated special provisions or Fire Testing of Millwork assemblies.

## Division 7 – Thermal & Moisture Protection

7.1. Applied fireproofing shall only be applied as specifically indicated on ASI 07 dated June 30th, 2020. All other general references on the contract documents which state "applied fireproofing" if or as required shall be considered null and void.

7.2. The GMP excludes any touch up of applied fireproofing following any work direct for the Owner, agents of the Owner, and/or others not subcontracted through AECOM Hunt.

7.3. The GMP assumes caulking as JS-1 Urethane, M, P, 50, T, NT as specified for horizontal traffic systems as specified. It is assumed and understood specified products shall meet all traffic requirements including but not limited to "high heel" point load traffic.

## Division 8 – Doors Frames and Hardware

8.1. The GMP excludes Door Hardware Inspection Agency to perform including but not limited to Fire-Rated Door Inspections and Egress Door Inspections.

8.2. The GMP excludes "Architectural Hardware Consultant (AHC)" as noted in Door Hardware Specification 08 71 00.

8.3. The GMP includes the type of glass as specified:
   a. GL-1: 1 1/16" "clear" insulated AGC Select Clear 23
   b. GL-1 Tempered: 1 1/16" "clear" insulated AGC Select Clear 23

## Division 9 – Finishes

9.1. A sealer is included for the precast seating bowl. Base or other flooring materials are excluded from the seating bowl.

9.2. The GMP includes Level 5 Drywall Finish as indicated on contract documents at VG-01 locations specifically at the North Club Wall (Room 21.12) and outside of East and West Stairs. All other areas are assumed to be Level 4 Drywall Finish or less as specified on Contract Documents.

9.3. The GMP includes Polished Concrete without any special provisions for crack suppression. Superficial or non-structural cracks will be visible without any special treatment or cover up following said work.

9.4. The GMP excludes moisture mitigation membranes to address high vapor transmission from concrete floors to achieve floor manufacturers and adhesive requirements.

9.5. The GMP excludes Tile TW-01 which has been removed from the project.

## Division 10 – Miscellaneous Specialties

10.1. Metal lockers are included at staff/employee locker rooms.

10.2. Signage and branding owner allowances have been carried for the following signage packages:

a. Branding & Graphics
b. Concession Identification and Branding Signage
c. Code and Wayfinding

10.3 Static menu board graphics and signage excluded beyond the identified Owner controlled Allowance.

10.4 Exterior Marquee signage excluded.

10.5 The GMP excludes toilet paper dispensers and paper products.

10.6 The GMP includes floor mounted toilet partitions. Miscellaneous OH support steel or associated blocking is excluded.

10.7 The GMP includes fifty (50) 4' long surface mounted metal corner guards to be installed as located by Owner's and Designer's discretion.

10.8 The GMP excludes soap dispensers.

## Division 11 – Equipment

11.1. We exclude window washing equipment.

11.2. The GMP excludes specification 11 61 33 Arena Rigging Systems in its entirety. Exclude rigging grid cable net mesh platforms.

11.3. We exclude portable camera platforms.

11.4. We exclude POS equipment.

11.5. LED Scoreboard Display and Scoring System is included:

a. Primary Center hung main sides and ends
b. Center hung hoist way
c. LED Ribbon boards display North and South
d. Center hung scrim and channel lettering
e. Display Control System
f. Scoring & Timing System
g. Locker room clocks
h. Shot/Game clocks

11.6. The GMP excludes posted BP#11C alternates as noted in Specification 116310 LED Display and Scoring System.

a. Alternate C Extended Warranty
b. Alternate D Health Check

11.7. The GMP does not include concrete pads for food service equipment.

11.8. The GMP does not include Static Signage or Graphics other than included in Signage and Branding Owner Allowance.

11.9. The GMP excludes ticket window displays other than IPTV as shown on the contract documents.

11.10. The GMP requires a model change on Item #H11Meiko model specified which has been discontinued, and the GMP includes Meiko DV 80.2 in its stead.

11.11. The GMP includes 60 Qt. mixer Hobart HL600C-1STD for Item #B21.1. Specification do not have a model number or manufacturer's name.

## Division 12 – Furnishings

12.1. Retractables and platforms for a basketball setup is included in accordance with the contract documents.

12.2. A basketball scorer's table, shots clocks, basketball hoops, and other basketball equipment are excluded.

12.3. The GMP excludes FF&E of Owner Furnished and Owner Furnished/Owner Installed refer to Section 7.

12.4. The GMP excludes the House Reduction Curtain or any provisions for a future installation by others.

12.5. The GMP excludes carts or storage racks for removable railings

## Division 13 – Special Construction

13.1. The stage, stage rigging, and stage equipment is excluded.

13.2. An Exterior Plaza or Marquee display is excluded.

13.3. The GMP includes a design build new ice rink and mechanical room ice package complete with Crystaplex Series 6A Aluminum prefabricated dasher board system.

## Division 14 – Conveying Equipment

14.1. Elevator cabs are assumed to be manufacturer standard finishes.

14.2. Provisions for televisions and speakers at elevators are excluded.

## Division 21 – Fire Protection

21.1. The GMP includes pre-action systems for the following rooms: Head In (11.04), Main IT (11.08), AV (11.25), and DAS Cell (12.04).

21.2. We assume a dry pipe system at the loading dock area. No other dry pipe systems are included.

21.3. The GMP is based on complete fire protection system based on (National Fire Protection Association) NFPA 13 and various applicable NFPA standards and any state and/or local amendments and supplements.

21.4. We assume the building will not be required to meet any FM Global insurance requirements for the fire suppression systems.

21.5. We have not included any chemical agent systems in this budget as no areas have currently been identified to require these special systems.

21.6. We assume concealed heads in all areas with ceilings and upright heads where no ceilings are present.

21.7. The GMP excludes sprinklers above the seating bowl area and ice floor.

## Division 22 – Plumbing

22.1. We have included underground and aboveground sanitary waste and vent piping as PVC.

22.2. We have included underground and aboveground storm piping as PVC.

22.3. For areas where PVC piping is routed through return air plenums we have allowed for fire wrap of the piping.

## Division 23 – HVAC

23.1. We exclude any glycol for the CHW or HW building systems.

23.2. We have not included any stair pressurization systems.

23.3. We have assumed that all ductwork in locker room or 'wet' areas will be of aluminum or stainless-steel material and not galvanized.

23.4. The GMP is based on Trane Equipment and Controls.

## Division 26 Electrical

26.1. A lightning protection system is included.

26.2. The GMP includes exterior lighting pursuant the fixtures as shown on the EL series of documents.

26.3. The GMP excludes electrical permit as we have been instructed the electrical shall fall under the building permit.

## Division 27 Communication

27.1. A DAS System for Public Safety is included.

27.2. Pathways (cable Tray) for a future carrier DAS system is included.

27.3. DAS cabling, hardware, devices, and head end equipment is excluded.

27.4. Pathways and Cabling for the Wi-Fi system is included.

27.5. Wi-Fi devices (provided by others) installation for (13) locations as indicated on the contract documents is included.

27.6. Active wireless electronics and wireless devices are excluded

27.7. Network electronics for voice/data are excluded.

27.8. Incoming Internet and Communications services are excluded.

## Division 28 Security

28.1. Area of Rescue assistance is included based on local codes, and products manufacturer recommendation.

28.2. Pedestals or bollards are excluded.

28.3. Ticketmaster programming is excluded.

28.4. Gate operating systems are excluded.

## Division 31 – Earthwork

31.1. We exclude any rock excavation.

31.2. We exclude any contaminated soils and existing materials demolished on site.

31.3. We include import of fill materials as identified and designated in the contract documents.

31.4. For the deep foundations, we include drilled displacement piles.

## Division 32 – Site Improvements

32.1. We include unit pavers set on concrete.

## Division 33 –Utilities

33.1 The GMP assumes the use of excavated material from trenched or associated excavation may be used for appropriate back fill within said excavation.

## Stiles Avenue

SA.1 Due to adjacent Gwinnett Street closure by others, AECOM Hunt has included maintenance of two-way traffic with flagmen to allow a single lane closure to perform work associated with contract documents. Any additional measures for traffic control has been excluded.

SA.2 Traffic Signal work has been excluded.

## Force Main

FM.1 Rail flagmen are excluded.

FM.2 Encampments are located within the limits of the Force Main scope of work. Relocation of aforementioned and/or security while performing the work has been excluded.

## Savannah Arena Bulkhead

SAB.1 The GMP excludes coordination and/or participation with Army Corps of Engineers including but not limited to any references in the Contract Documents to the like of "in accordance with standard Army Corps of Engineer" details not shown on the contract documents.

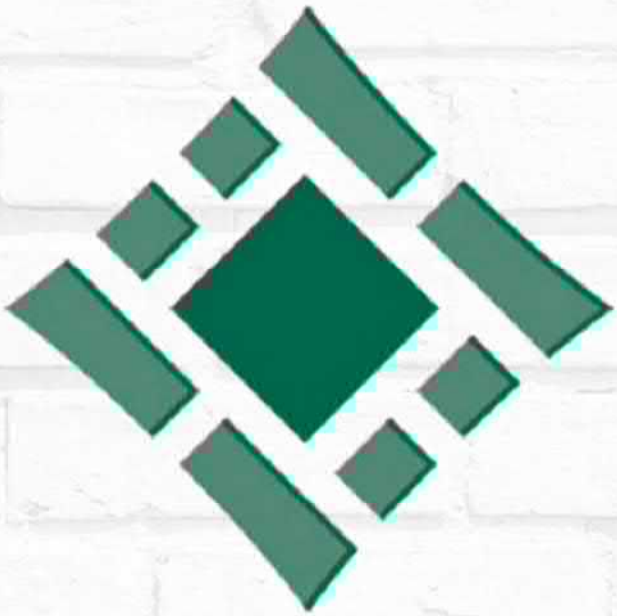

*Section 06*

# *Responsibility Matrix*

AECOM HUNT

*in association with*

**Brownstone Construction Group**
**Pat Mathis Construction Company**
**A. Riley Consultants**

AECOM HUNT
in association with
Brownstone Construction Group
Pat Mathis Construction Company
A. Riley Consultants

**Savannah Arena**
**Responsibility Matrix**
7/9/2020

| | Item of Work | AECOM Hunt (or via Subs) | Owner |
|---|---|---|---|
| **I.** | **Soft Costs** | | |
| | Design Consultants and Fees | | X |
| | Design Peer Reviews | | X |
| | Delegated Design Costs (as identified in final specifications and GMP) | X | |
| | Geotechnical Consultant | | X |
| | Geotechnical Report | | X |
| | Support-Of-Excavation Design | | X |
| | Environmental Impact Studies | | X |
| | Soil Testing | | X |
| | Traffic Studies | | X |
| | Code Consultant | | X |
| | Existing Property and Land Surveys | | X |
| | Storm Water Retention Plan | | X |
| | Food Service Operator Review | | X |
| | Third Party Commissioning Agent | | X |
| | Third Party Material Testing | | X |
| | Third Party Field Testing and Inspections | | X |
| | Siesmic Monitoring | | X |
| | Air Quality and Noise Level Monitoring | | X |
| | | | |
| **II.** | **Permits** | | |
| | Permit Expediting Agent - Building Permit/Filing/TCO/Operating Permits | | X |
| | Permit Expediting Agent - Work Permits for Trades/General Conditions | X | |
| | Fees - Building Permit/TCO | | X |
| | Fees - Standard Work Permits for Trades and General Conditions | X | |
| | Fees - After Hours Work Permits | | X |
| | Fees - Facility, Equipment $ Systems Operating Permits | | X |
| | Fees - Jobsite Office Permits | X | |
| | Permit Plan Check Cost | | X |
| | Crane Permits | X | |
| | FAA Permits | | X |
| | | | |
| **III.** | **General Conditions and General Site Requirements** | | |
| | MWBE Coordinator | X | |
| | Owner & Design Team Field Office (set-up, rental, removal) | X | |
| | Owner & Design Team Field Office - equipment, phone service, internet, etc | | X |
| | Utility Consumption - Jobsite Offices (Owner, Arch, CM) | X | |
| | Primary Construction Sign | | X |
| | Parking Cost for Workmen (Sub cost) | X | |
| | Surveying - Baseline Control, Workpoints | X | |
| | Surveying - Final As-Built | X | |
| | Site Security / Watchmen | X | |
| | Construction Progress Clean-up | X | |

AECOM HUNT
in association with
Brownstone Construction Group
Pat Mathis Construction Company
A. Riley Consultants

**Savannah Arena**
**Responsibility Matrix**
7/9/2020

| | Item of Work | AECOM Hunt (or via Subs) | Owner |
|---|---|---|---|
| | Final Construction Clean (All Areas) | X | |
| | Fine Cleaning, Polishing, Etc | | X |
| | Utilities - Final Connections, Taps, Tie-ins, Permits, Meters | | X |
| | Utility Demand and/or Impact Fees | | X |
| | Utility Consumption Costs through Substantial Completion | | X |
| | Project Management Software (Hunt Standards) | X | |
| | Project Webcam System | | X |
| | Snow Removal - within project limits | X | |
| | Snow Removal - outside project limits | | X |
| | Onsite Medic (if required) | | X |
| | | | |
| **IV.** | **Insurance Costs** | | |
| | General Liability | X | |
| | Automobile Liability | X | |
| | Workers Compensation | X | |
| | Builder's Risk Insurance | | X |
| | Property Insurance | | X |
| | Railroad Liability | | X |
| | Pollution Liability | | X |
| | Deductibles for Insurance Provided by Owner | | X |
| | Owner's Protective Professional Indemnity | | X |
| | | | |
| **V.** | **Site Costs** | | |
| | Off Site Improvements | | X |
| | Site Improvements (Unless Specifically Noted) | | X |
| | Demolition existing structures | X | |
| | Utility Relocations (as shown on drawings) | X | |
| | Public Roadway Work (as shown on drawings) | X | |
| | Traffic Signals | | X |
| | Lightposts (public roadways) | | X |
| | Signage (public roadways) | | X |
| | Bus Shelters if applicable | | X |
| | Parking Meters | | X |
| | Cost for Easments | | X |
| | Parking Garages | | X |
| | | | |
| **VI.** | **Environmental Costs** | | |
| | Hazardous Waste, Regulated Material Removal | | X |
| | Asbestos Abatement | | X |
| | Environmental consultant & monitor (Pre-con & construction phase) | | X |
| | Testing of Regulated (or potentially regulated) Materials | | X |
| | | | |
| **VII.** | **Furniture, Fixtures, & Equipment** | | |

AECOM HUNT
in association with
Brownstone Construction Group
Pat Mathis Construction Company
A. Riley Consultants

**Savannah Arena**
**Responsibility Matrix**
7/9/2020

| | Item of Work | AECOM Hunt (or via Subs) | Owner |
|---|---|---|---|
| | Refer to FF&E Matrix | | |
| | | | |
| **VIII.** | **Food Service Areas** | | |
| | Health Department Filings and Filing Fees | | X |
| | Health Department Permits | | X |
| | Expediting Agent - Health Department Approval Process | | X |
| | Health Department Inspections | | X |
| | Sanitization of all Food Service Areas | | X |
| | | | |
| **IX.** | **Technology** | | |
| | Portable Sound Equipment | | X |
| | Special Systems (LAN, POS, Ticketing) | | X |
| | Video Replay Systems (Video Production) | | X |
| | Video Coaching Systems | | X |
| | Hook-up Costs and Fees for Services (television, satellite, telephone, internet) | | X |
| | IPTV Installation | X | |
| | Player Tracking System | | X |
| | | | |
| **X.** | **LEED** | | |
| | Filing Fees | | X |
| | LEED Consultant / Champion with Green Building Council | | X |
| | LEED Point Tracking | | X |
| | Energy Model | | X |
| | Construction Waste Management | | X |
| | LEED Submittals (as outlined in final specifications) | | X |
| | | | |
| **XI.** | **Misc Project Requirements** | | |
| | Field Samples/Field Mock-ups (as indicated in final Specifications and GMP) | X | |
| | Offsite Suite Mock-ups | | X |
| | Offsite Costs for Power Company (Vault Design/Construction and Related Costs) | | X |
| | Facility Reconfiguation for Events not specifically defined in the GMP Documents | | X |
| | Offsite Sales Offices | | X |
| | Final / permanent keying of locksets | X | |
| | Emergency Generator Fuel - Testing and Initial Fill | X | |

*Section 07*

# *FFE Responsibility Matrix*

AECOM HUNT

*in association with*

**Brownstone Construction Group**
**Pat Mathis Construction Company**
**A. Riley Consultants**

SAVANNAH
savannahga.gov

# Savannah Area
## FF&E Scope, Procurement, and Budget

Latest Update: 2020-07-09

| Item ID | Category | Procurement Group | OVG | COS | DESCRIPTION | Contractor Furnished / Contractor Installed (CFCI) | Owner Furnished / Contractor Installed (OFCI) | Owner Furnished / Owner Installed (OFOI) | Infrastructure Required (Power / Data / Mech / Struct / Wall / Other) P | D | M | S | W | O | Infrastructure Incorporated | Item Specified | Priority 1 - critical 2 - important 3 - optional 4 - not needed | Notes/Comments |
|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|
| 012 | Concession | Branding & Graphics | | | Signage & Graphics (Allowance Only) | x | | | x | | | | x | | | | | |
| 027 | Video Systems | Branding & Graphics | x | | Basket Stanchion Displays (other than clocks) | | | x | x | x | | x | | | | | 3 | SPONSORSHIP SCOPE |
| 087 | Box Office | Branding & Graphics | | | Box Office Signage | | | x | x | x | | | | | | | 1 | Part of "Building Identification Signage - Interior" |
| 185 | Other - Signage | Branding & Graphics | | | Building Identification Signage - Exterior Building Mounted (Allowance Only) | x | | | x | x | | x | | | | | 1 | SPONSORSHIP SCOPE |
| 186 | Other - Signage | Branding & Graphics | | | Building Identification Signage - Interior (Allowance Only) | x | | | x | x | | x | | | | | 1 | |
| 187 | Other - Signage | Branding & Graphics | | | Building Identification Signage - Marquee (Allowance Only) | x | | | x | x | | x | | | | | 1 | See also "Exterior Video Board" |
| 188 | Other - Signage | Branding & Graphics | | | Site Directional Signage (Allowance Only) | x | | | | | | | | | | | 1 | |
| 190 | Other - Site | Branding & Graphics | | | Banner Poles | | | x | | | | | | | | | 1 | |
| 090 | FF&E - Other | Building | | | Acoustical Treatments (Excludes Lapendary Panels as none shown) | x | | | | | | | | | | | 3 | In base scope |
| 091 | FF&E - Other | Building | | | Circus Inserts | x | | | | | x | | | | | | | In base scope - Event layout to be confirmed |
| 109 | FF&E - Other | Building | | | Window Treatments (Excludes Blinds at offices) | x | | | | | | | | | | | 1 | Verify specfic locations |
| 132 | FF&E - Other | Building | | | Operable Partitions | x | | | | | | x | x | | | | 1 | |
| 136 | FF&E - Other | Building | | | Wall Pads | | | x | | | | | x | | | | 1 | Sensory room? |
| 159 | FF&E - Other | Building | | | Suite Millwork | x | | | | | | | | | | | 1 | |
| 161 | Operations | Computers | | | Computers/workstations | | | x | | | | | | | | | 1 | |
| 163 | Operations | Computers | | | Misc Software (Accounting, Maint, Operations, etc.) | | | x | | | | | | | | | 1 | Is there an OVG standard? |
| 164 | Operations | Computers | | | Large format printer | | | x | x | x | | | | | | | 1 | |
| 168 | Operations | Computers | | | Servers, switches | | | x | x | x | | | | | | | 1 | |
| 169 | Operations | Computers | | | Inventory System (arena operations) | | | x | | | | | | | | | 2 | Is there an OVG standard? Subscritpion? |
| 019 | Video Systems | Event | | | Ice Mapping/Projectors | | | x | x | x | | | | | | | 3 | Future - verify power & data available in catwalks |
| 025 | Video Systems | Event | x | | Courtside Scorer's tables | | | x | x | x | | | | | | | 3 | Wall mounted power & data boxes at sidelines. Project does not need LED displays on tables |
| 065 | Seating | Event | | | Telescopic & Removable Platforms | x | | | | | | | | | | | 1 | |
| 070 | Event Production | Event | x | | Portable Stage | | | x | | | | | | | | | 1 | 40 x 60 (no extensions), includes rails & steps |
| 071 | Event Production | Event | x | | Portable Stage Ramp | | | x | | | | | | | | | 1 | |
| 072 | Other - ADA | Event | x | | Portable Stage ADA Lift | | | x | | | | | | | | | 1 | price from phone call |
| 073 | Event Production | Event | x | | Spotlights | | | x | x | x | | | | | | | 1 | Data needed for robotic lights |
| 074 | Event Production | Event | x | | Security Barriers - Bike Racks | | | x | | | | | | | | | 1 | 8' long each - 1000' total used for budget |
| 075 | Event Production | Event | x | | Security Barriers - Blow-through | | | x | | | | | | | | | 1 | 40" each - 150' total used for budget |
| 076 | Event Production | Event | x | | Strobe Lights | | | x | x | x | | | | | | | 3 | Power & data should be available in catwalk |
| 077 | Event Production | Event | x | | Strobe Lights-Control System | | | x | x | x | | | | | | | 3 | Power & data should be available in catwalk |
| 078 | Event Production | Event | x | | Theatrical Lighting | | | x | x | x | | | | | | | 1 | Need is dependent on SCC. This was not inlcuded in any RFPs or programming |
| 082 | Ice Floor | Event | x | | Zamboni | | | x | | | | | | | | | 1 | 1 new, 1 used (from MLK Arena) |
| 099 | FF&E - Other | Event | x | | Basketball Floor | | | x | x | x | | | | | | | 1 | Includes storage carts |
| 100 | FF&E - Other | Event | x | | Basketball Goals | | | x | x | x | | | | | | | 1 | Requires floor box. Need tie-downs in conc slab. |
| 104 | FF&E - Other | Event | x | | Turnstiles/Entry Point Ticket Control | | | x | | | | | | | | | 2 | Turnstyles may be needed for certain events - further discussion needed |
| 107 | FF&E - Other | Event | | | Black Out Curtains/Track | x | | | | | | | | | | | 1 | |
| 108 | FF&E - Other | Event | | | Bowl Reduction Curtains Excluding Half House Curtain | | | | | | | | | | | | 1 | |
| 111 | FF&E - Other | Event | | x | Concierge Stations (portable) | | | x | | | | | | | | | 1 | |
| 125 | FF&E - Other | Event | x | x | Metal Detectors (walk through) | | | x | x | | | | | | | | 1 | Need Infrastructure! |
| 128 | FF&E - Other | Event | | x | Two Way Radio Communications (walkie-talkies) | | | x | | | | | | | | | 1 | |
| 129 | FF&E - Other | Event | | | Easels | | | x | | | | | | | | | 1 | |
| 130 | FF&E - Other | Event | | | Flags - Indoor | | | x | x | | | | | | | | 1 | Power for lighting? |
| 131 | FF&E - Other | Event | | | Flags - Outdoor | | | x | x | | | | | | | | 1 | See also flag poles |
| 135 | FF&E - Other | Event | | | Visual Display Boards (dry erase boards) | | | x | | | | | x | | | | 3 | |
| 001 | Concession | Food Service Equip | | | Coolers and Freezers | x | | | x | x | x | | | | | | 1 | in food service base scope docs |
| 002 | Concession | Food Service Equip | | | Food Service Equipment - Commissary, Kitchen | x | | | x | x | x | | | | | | 1 | in food service base scope docs |
| 003 | Concession | Food Service Equip | | | Food Service Equipment - Concessions | x | | | x | x | x | | | | | | 1 | in food service base scope docs |
| 004 | Concession | Food Service Equip | x | | Foodservice Computers | | | x | x | x | | | | | | | 1 | computer included in main "Computers/workstations" item |
| 005 | Concession | Food Service Equip | x | | Foodservice Currency Counters, Safes, Money Trays | | | x | x | x | | | | | | | 1 | |
| 006 | Concession | Food Service Equip | | | Ice Makers (Non-Foodservice/Non-Suite Areas) | | | x | x | x | x | | | | | | 1 | Verify floor drains provided |
| 008 | Concession | Food Service Equip | x | | Points of Sale (POS) Equipment (Concessions) | | | x | x | x | | | | | | | 1 | |
| 009 | Concession | Food Service Equip | x | | Soda System/CO2 equipment | | | x | x | x | x | | | x | | | 1 | by vendor |
| 011 | Concession | Food Service Equip | | | Menu Boards - Head End System - Through IPTV Only | X | | | x | x | | | | | | | 1 | server included as one of 3 servers |
| 013 | Concession | Food Service Equip | x | | Food Service Serviceware/Smallwares | | | x | | | | | | | | | 1 | |
| 014 | Concession | Food Service Equip | x | | Portable Foodservice Carts/Kiosks | | | x | x | x | | | | | | | 1 | SPONSORSHIP SCOPE |
| 158 | FF&E - Other | Food Service Equip | | | Suite Kitchen Equipment | | | x | | | | | | | | | 1 | in food service base scope docs |
| 160 | FF&E - Other | Food Service Equip | | | Suite Serving Equipment | | | x | | | | | | | | | 1 | |
| 059 | Seating | Furniture | x | | Cupholders (material/installation) | x | | | | | | | | | | | 1 | Critical in premium areas, needs discussion/mockup |
| 060 | Seating | Furniture | x | | Seating Fixed-Club & Suite Seating | x | | | | | | | | | | | 1 | |

SAVANNAH savannahga.gov

# Savannah Area
## FF&E Scope, Procurement, and Budget

Latest Update: 2020-07-09

| Item ID | Category | Procurement Group | O V G | C o S | DESCRIPTION | Contractor Furnished / Contractor Installed (CFCI) | Owner Furnished / Contractor Installed (OFCI) | Owner Furnished / Owner Installed (OFOI) | Infrastructure Required (Power / Data / Mech / Struct / Wall / Other) P | D | M | S | W | O | Infrastructure Incorporated | Item Specified | Priority 1 - critical 2 - important 3 - optional 4 - not needed | Notes/Comments |
|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|
| 061 | Seating | Furniture | x | | Removable Seating at Suites ADA Removable Fixed Seats Only | x | | | | | | | | | | | 1 | |
| 062 | Seating | Furniture | x | | Seating Fixed-General Seating | x | | | | | | | | | | | 1 | |
| 063 | Seating | Furniture | x | | Seating-Courtside (Loose) | | | x | | | | | | | | | 1 | |
| 064 | Seating | Furniture | x | | Seating-Suites Loose Chair Seating & Fixed Tables | | | x | | | | | | | | | 1 | |
| 066 | Seating | Furniture | x | | ADA - Fixed | x | | | | | | | | | | | 1 | Inlcuded with nearby seating |
| 067 | Seating | Furniture | x | | ADA - Portable | | | x | | | | | | | | | 1 | Inlcuded with nearby seating |
| 086 | FF&E - Other | Furniture | | | Administrative - Box Office | | | x | | | | | | | | | 1 | |
| 103 | FF&E - Other | Furniture | | | Administrative- Executive | | | x | | | | | | | | | 1 | |
| 112 | FF&E - Other | Furniture | | | Administrative - Operations | | | x | | | | | | | | | 1 | |
| 113 | FF&E - Other | Furniture | x | | Administrative - Security | | | x | | | | | | | | | 1 | |
| 114 | FF&E - Other | Furniture | x | | Administrative - Conference Rooms | | | x | | | | | | | | | 1 | |
| 115 | FF&E - Other | Furniture | | | Press Box | | | x | | | | | | | | | 1 | |
| 116 | FF&E - Other | Furniture | | | Employee Catering Room | | | x | | | | | | | | | 1 | |
| 117 | FF&E - Other | Furniture | | | Scoreboard Control Room | | | x | x | x | | | | | | | 1 | May not need power/data - against a wall |
| 118 | FF&E - Other | Furniture | | | North Club Lounge - Bar Stools (Bistro) | | | x | | | | | | | | | 1 | |
| 119 | FF&E - Other | Furniture | | | North Club Lounge - High Top Table (Bistro) | | | x | | | | | | | | | 1 | |
| 120 | FF&E - Other | Furniture | | | North Club Lounge - Lounge Chair | | | x | | | | | | | | | 1 | ? |
| 121 | FF&E - Other | Furniture | | | North Club Lounge - Table, Dining | | | x | | | | | | | | | 1 | |
| 122 | FF&E - Other | Furniture | | | North Club Lounge - Chair, Dining | | | x | | | | | | | | | 1 | |
| 123 | FF&E - Other | Furniture | | | North Club Lounge-Table, Dining (4 Person) | | | x | | | | | | | | | 2 | |
| 124 | FF&E - Other | Furniture | | | Concourse Bar-Bar Stools (Bistro) | | | x | | | | | | | | | 2 | |
| 133 | FF&E - Other | Furniture | | | Loge - Exec Task Chairs | | | x | | | | | | | | | 1 | Future? |
| 134 | FF&E - Other | Furniture | | | Loge-Bar Stools (Bistro) | | | x | | | | | | | | | 1 | |
| 150 | FF&E - Other | Furniture | | | Suite - Chairs | | | x | | | | | | | | | 1 | |
| 153 | FF&E - Other | Furniture | | | Suite - Bar Stools (Bistro) | | | x | | | | | | | | | 1 | |
| 154 | FF&E - Other | Furniture | | | Suite- High Top Table (Bistro)/Moveable | | | x | | | | | | | | | 1 | |
| 157 | FF&E - Other | Furniture | | | Suite - Coffee Table (Occasional) | | | x | | | | | | | | | 1 | |
| 170 | FF&E - Other | Furniture | | x | Suite - Lounge Chair | | | x | | | | | | | | | 1 | |
| | FF&E - Other | Furniture | | | Overlook Level-Bar Stools (Bistro) | | | x | | | | | | | | | 1 | |
| | FF&E - Other | Furniture | | | Overlook Level-High Top Table (Bistro) | | | x | | | | | | | | | 1 | |
| | FF&E - Other | Furniture | | | East Club (Allowance) | | | x | | | | | | | | | 1 | |
| 079 | Ice Floor | Ice Floor | | | Dasher system | x | | | | | | x | | | | | 1 | |
| 080 | Ice Floor | Ice Floor | | | Ramps-Transition from service level to ice floor (cover) over Ice Dam | | | x | | | | | | | | | 1 | Built by in-house maint |
| 081 | Ice Floor | Ice Floor | | | Ice Floor Cover | x | | | | | | | | | | | 1 | |
| 028 | Video Production | Low Voltage | | | Video Projectors and Screens (conf rooms, etc.) | x | | | x | x | | | | | | | 1 | Need to identify spaces with permanenet projectors and screens |
| 029 | Audio Systems | Low Voltage | | | Assisted Listening Devices | x | | | x | x | | | | | | | 1 | Should be a part of the CFCI audio system |
| 031 | Audio Systems | Low Voltage | | | Audio System (portable, non-arena) | | | x | | | | | | | | | 2 | Project should include 1 or 2 portable lecterns and portable speakers |
| 032 | Audio Systems | Low Voltage | | | Audio System-Clubs, Restaurants, VIP Lounges | x | | | x | x | | | | | | | 1 | Should be a part of the CFCI audio system |
| ~~033~~ | ~~Audio Systems~~ | ~~Low Voltage~~ | | | ~~Audio System-Concourses, Restrooms, Lobbies~~ | | | x | x | x | | | | | | | 1 | Should be a part of the CFCI audio system |
| 034 | Audio Systems | Low Voltage | | | Audio System-Main Bowl | x | | | x | x | | | | | | | 1 | Should be a part of the CFCI audio system |
| 035 | Audio Systems | Low Voltage | | | Audio System-Away Team Locker Rooms/Weight Rooms | x | | | x | x | | | | | | | 1 | Should be a part of the CFCI audio system |
| 036 | Audio Systems | Low Voltage | | | Audio-Control Systems | x | | | x | x | | | | | | | 1 | Should be a part of the CFCI audio system |
| 037 | Broadcast | Low Voltage | | | Broadcast Cabling | x | | | x | x | | | | x | | | 1 | Power & Network Data to camera locations, plus conduit only for broadcast cabling |
| 038 | Broadcast | Low Voltage | | | Broadcast Camera (underside of scoreboard) | | | x | x | x | | | | | | | 3 | can be incuded with CCTV |
| 039 | Broadcast | Low Voltage | | | Broadcast Camera Equipment-Camera Seats, Platforms, Carts | | | x | | | | | | | | | 3 | |
| 040 | Broadcast | Low Voltage | | | Broadcast Cameras | | | x | | | | | | | | | 3 | |
| 041 | Security | Low Voltage | | | CCTV Cameras | x | | | | x | | | | | | | 1 | No power required if powered by IP |
| 043 | Security | Low Voltage | | | Security & Controlled Access Systems | x | | | x | x | | | | | | | 1 | |
| 044 | Security | Low Voltage | | | Security Cameras | x | | | | x | | | | | | | 1 | No power required if powered by IP |
| 045 | Security | Low Voltage | x | | Security Devices-Others | | | x | | | | | | | | | 2 | Needs definition and scope |
| 046 | Security | Low Voltage | | | Security Head End Equip. | x | | | x | x | | | | | | | 1 | |
| 048 | DAS | Low Voltage | x | | Distributed Antenna System - Public Safety | | | x | x | x | | | | | | | 1 | Need coordination with local first responders |
| 049 | DAS | Low Voltage | x | | Distributed Antenna System - Other | | | x | x | x | | | | | | | 1 | public DAS or wifi |
| 050 | Wi-Fi | Low Voltage | | | Wireless Data System - Equipment | | | x | x | x | | | | | | | 1 | public DAS or wifi |
| 051 | Wi-Fi | Low Voltage | | | Wireless Data System - Infrastructure | x | | | x | x | | | | | | | 1 | public DAS or wifi |
| 052 | IPTV | Low Voltage | | | Distributed Television Systems - IPTV | x | | | | x | | | | | | | 1 | |
| 053 | Network Cabling | Low Voltage | | | Data System (Cable Plant/Wiring) | x | | | x | x | | | | | | | 1 | |
| 054 | Network Cabling | Low Voltage | | | Data System-Hubs, Routers, | x | | | x | x | | | | | | | 1 | |
| 055 | Network Cabling | Low Voltage | | x | Telephone System-VOIP, Switchers, Routers | | | x | x | x | | | | | | | 1 | |
| 085 | Box Office | Low Voltage | | | Box Office Ticket Window Communication System/Equipment | | | x | x | x | | | | | | | 1 | Need to discuss type, communications, etc. - NEED PANIC ALARMS |
| 126 | FF&E - Other | Low Voltage | | x | Telephone System-Hand Sets, Consoles | | | x | x | x | | | | | | | 1 | |

SAVANNAH savannahga.gov

# Savannah Area
## FF&E Scope, Procurement, and Budget

Latest Update: 2020-07-09

| Item ID | Category | Procurement Group | OVG | COS | DESCRIPTION | Contractor Furnished / Contractor Installed (CFCI) | Owner Furnished / Contractor Installed (OFCI) | Owner Furnished / Owner Installed (OFOI) | Infrastructure Required (Power / Data / Mech / Struct / Wall / Other) P | D | M | S | W | O | Infrastructure Incorporated | Item Specified | Priority 1 - critical 2 - important 3 - optional 4 - not needed | Notes/Comments |
|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|
| 127 | FF&E - Other | Low Voltage | | | TTY Units (hearing or speech impaired devices) | | | x | x | x | | | | | | | 1 | with audio systems |
| 094 | FF&E - Other | Maintenance | | x | Entrance Mats - Portable (loose) | | | x | | | | | | | | | 2 | |
| 095 | FF&E - Other | Maintenance | | x | Entrance Mats - Recessed | | | x | | | | x | | | | | 1 | Coordinate clab recesses |
| 096 | FF&E - Other | Maintenance | | x | Loading Dock Levelers & Bumpers | x | | | x | | | | | | | | 1 | verify spec and slab recess |
| 097 | FF&E - Other | Maintenance | | x | Plans (Blue Print Storage System in maintenance) | | | x | | | | | | | | | 1 | Rack? |
| 106 | FF&E - Other | Maintenance | | x | Cable Crossover Ramps | | | x | | | | | | | | | 1 | |
| 137 | FF&E - Other | Maintenance | | | Janitorial Closet Shelving, Handle Holders, | | | x | | | | | x | | | | 1 | Infrastrucure? Backing? |
| 138 | FF&E - Other | Maintenance | | | Floor sweep (Ride-on) | | | x | | | | | | | | | 1 | |
| | FF&E - Other | Maintenance | | | Floor sweep (Puch) | | | x | | | | | | | | | 1 | |
| 141 | FF&E - Other | Maintenance | | x | Trash Transportation Carts | | | x | | | | | | | | | 1 | |
| 142 | FF&E - Other | Maintenance | | x | Washer & Dryer - Building Laundry Room (Residential Grade) | | | x | x | | x | | | | | | 1 | Consider dryer venting routes |
| 143 | FF&E - Other | Maintenance | | x | Washer & Dryer - Locker Room Area (Commerical Grade) | | | x | x | | x | | | | | | 1 | Consider dryer venting routes |
| 144 | FF&E - Other | Maintenance | | | Detergent Dispensers | | | x | | | | | x | | | | 1 | |
| 145 | FF&E - Other | Maintenance | | | Laundry Room Millwork | x | | | | | | | | | | | 1 | |
| 162 | FF&E - Other | Maintenance | | x | Pick Up Truck | | | x | | | | | | | | | 1 | |
| | Operating Budget | Maintenance | | | Utility Carts | | | x | | | | | | | | | 1 | |
| | Operating Budget | Maintenance | | | Pallet Jacks | | | x | | | | | | | | | 1 | |
| | Operating Budget | Maintenance | | | Hand Trucks | | | x | | | | | | | | | 1 | |
| 166 | Operating Budget | Maintenance | | | Golf Carts | | | x | | | | | | | | | 1 | |
| 167 | Operating Budget | Maintenance | | | Fork Lifts | | | x | | | | | | | | | 1 | Propane storage? |
| 171 | Operating Budget | Maintenance | | x | Maintenance/Engineer Tools & Equipment | | | x | | | | | | | | | 1 | |
| 178 | Operating Budget | Maintenance | | x | Can Crusher | | | x | | | | | | | | | 3 | Need cut sheets |
| 179 | Operating Budget | Maintenance | | x | Card Board Baler | | | x | | | | | | | | | 3 | Need cut sheets |
| 180 | Operating Budget | Maintenance | | x | Recycling Equipment/Bins | | | x | | | | | | | | | 1 | |
| 181 | Operating Budget | Maintenance | | x | Waste Compactors | | | x | x | | x | | | | | | 1 | Need cut sheets |
| 182 | Operating Budget | Maintenance | | x | Trash Cans - Interior | | | x | | | | | | | | | 1 | |
| 184 | Operating Budget | Maintenance | | x | Waste Transport Equipment | | | x | | | | | | | | | 1 | |
| 147 | FF&E - Other | Medical | | | Automatic Defibrillators | | | x | | | | | | | | | 1 | Coordinate locations (may not want these out in the open) |
| 152 | FF&E - Other | Medical | | | Wheelchairs, Back Boards | | | x | | | | | | | | | 1 | 2 WC, 2 backboards |
| 177 | Operating Budget | Medical | x | x | Medical Equipment/Supplies | | | x | | | | | | | | | 2 | Cainet and supplies |
| 093 | FF&E - Other | Operations | x | | Biometric Time Clocks | | | x | x | | | | | | | | 1 | |
| 151 | FF&E - Other | Operations | | | Refrigerators, Ice Maker (First Aid) | | | x | x | | x | | | | | | 1 | Will ice bin should be sufficient? |
| 068 | Event Production | Safety | | x | Fall Arrest System/Rigging (lanyards, loose equipment) | | | x | | | | x | | | | | 1 | Struct capacity in place, JLL pursuing pricing |
| 069 | Event Production | Safety | | x | Fall Arrest System/Rigging-System | | | x | | | | x | | | | | 1 | Struct capacity in place, JLL pursuing pricing |
| 017 | Video Systems | Scoreboard | | | Exterior Video Board | | | x | x | x | | | | | | | 1 | Part of Exterior Marquee |
| 018 | Video Systems | Scoreboard | | | Game Clocks Displays | x | | | x | x | | | | | | | 1 | included with Scoreboard |
| 021 | Video Systems | Scoreboard | | | Ribbon Boards | x | | | x | x | | | | | | | 1 | verify loads on seating precast, verify conduit openings in seating precast |
| 022 | Video Systems | Scoreboard | | | Scoreboard (center hung) | x | | | x | x | | x | | | | | 1 | |
| 023 | Video Systems | Scoreboard | | | Scoreboard Hoist | x | | | x | | | | | | | | 1 | |
| 030 | Audio Systems | Scoreboard | | | Assisted Viewing System (closed caption, pager system) | x | | | x | x | | | | | | | 1 | |
| 042 | Security | Security | x | | Hand Wand Metal Detectors | | | x | x | | | | | x | | | 1 | Charging wall/stations needed? For tix scanners too |
| 047 | Security | Signage | | | Security Signage | | | x | | | | | | | | | 2 | Temp signs in plaza and other entries |
| 189 | Other - Signage | Signage | | | Way Finding & Code-Required Graphics (Arena) - Owner Allowance Only | x | | | | | | | | | | | 1 | In base scope |
| 191 | Other - Site | Site Furniture | | x | Bollard Bench, Bench 1, Bench 2 | x | | | | | | | | | | | 1 | |
| 192 | Other - Site | Site Furniture | | x | Bench 3 | x | | | | | | | | | | | 1 | |
| 193 | Other - Site | Site Furniture | | x | Bicycle Racks | x | | | | | | | | | | | 1 | |
| 194 | Other - Site | Site Furniture | | x | Flag Poles - None Shown | | | x | x | | | | | | | | 1 | Power for lighting? |
| 195 | Other - Site | Site Furniture | | x | Trash Cans-Site | x | | | | | | | | | | | 1 | |
| 024 | Video Systems | Sponsorship | | | Vomitory Displays | | | x | x | x | | | | | | | 3 | Future - verify power & data will be available |
| 056 | Advertising | Sponsorship | | | Advertising Graphics-LED Displays | | | x | x | x | | | | | | | 1 | Future by OVG |
| 057 | Advertising | Sponsorship | | | Advertising Panels | | | x | x | x | | | | | | | 1 | Future by OVG |
| 058 | Advertising | Sponsorship | | | Digital Advertising System | | | x | x | x | | | | | | | 1 | Future by OVG |
| 105 | FF&E - Other | Sponsorship | | | ATMs | | | x | x | x | | | | | | | 2 | Only need power/data - future bank sponsor will provide ATMs in future |
| 098 | FF&E - Other | Staff | | | Portable Metal Lockers | | | x | | | | | | | | | 1 | |
| 101 | FF&E - Other | Staff | | | Locker Room Benches (staff / employees) | x | | | | | | | | | | | 1 | |
| 102 | FF&E - Other | Staff | | | Lockers (staff / employees) | x | | | | | | | | | | | 1 | |
| 174 | Operating Budget | Staff | | | Time/Attendance System | | | x | | | | | | | | | 1 | cloud based |
| 175 | Operating Budget | Staff | x | x | Uniforms-Event Staff | | | x | | | | | | | | | 1 | t-shirts assumed |
| 176 | Operating Budget | Staff | x | x | Uniforms-Maintenance/Engineering | | | x | | | | | | | | | 1 | Varying styles, 3 per employee |
| 139 | FF&E - Other | Storage | | | Storage Shelving | | | x | | | | | x | | | | 1 | |
| 140 | FF&E - Other | Storage | | | Mobile Storage Shelving Systems | | | x | | | | | | | | | 1 | |

SAVANNAH
savannahga.gov

# Savannah Area
## FF&E Scope, Procurement, and Budget

Latest Update: 2020-07-09

| Item ID | Category | Procurement Group | O V G | C o S | DESCRIPTION | Contractor Furnished / Contractor Installed (CFCI) | Owner Furnished / Contractor Installed (OFCI) | Owner Furnished / Owner Installed (OFOI) | Infrastructure Required (Power / Data / Mech / Struct / Wall / Other) | | | | | | Infrastructure Incorporated | Item Specified | Priority 1 - critical 2 - important 3 - optional 4 - not needed | Notes/Comments |
|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|
| | | | | | | | | | P | D | M | S | W | O | | | | |
| 146 | FF&E - Other | Storage | | | Laundry Room Shelving | | | x | | | | | x | | | | 1 | |
| 155 | FF&E - Other | TBD | | | Suite Artwork/Decorations | | | x | x | | | | x | | | | 1 | Art lighting? Wall blocking? |
| 083 | Box Office | Ticketing | | x | Box Office Vault/Safe (standalone unit) | | | x | | | | | | | | | 1 | Need cut sheet |
| 084 | Box Office | Ticketing | | | Box Office Equipment, Computers, Printers, etc. | | | x | x | x | | | | | | | 1 | By TicketMaster |
| 088 | Box Office | Ticketing | | | Box Office Ticket Window Covers (blinds, shades) | | | x | | | | | | | | | 1 | By TicketMaster |
| 089 | Box Office | Ticketing | | | Box Office Currency/Money Counters | | | x | x | | | | | | | | 1 | By TicketMaster |
| 092 | FF&E - Other | Ticketing | | | Transaction Windows with Electronic Speak-Thru - RFI Submitted | X | | | x | | | | | | | | 1 | Need to discuss windows. This is old school |
| 156 | FF&E - Other | Ticketing | | | Suite Entry Ticketing System | | | x | | | | | | | | | 1 | Vendor supplied - NO COST TO PROJECT |
| ~~010~~ | ~~Concession~~ | ~~TVs & Mounts~~ | ~~x~~ | | ~~Menu Boards - Digital - TVS only~~ | | | x | x | x | | | | | | | 1 | |
| 015 | Video Systems | TVs & Mounts | x | | Television Displays | x | | | x | x | | | | | | | 1 | All TVs and Mounts in one price |
| 016 | Video Systems | TVs & Mounts | x | | Television Mounts | x | | | | | | | x | | | | 1 | |
| 020 | Video Systems | TVs & Mounts | | | Lobby / Public Area Large Video Displays - None Shown | | | | | | | | | | | | 2 | |
| 026 | Box Office | TVs & Mounts | | | Ticket Window Displays - Add Alternate for TVS | | | | | | | | | | | | 1 | |
| | | | | | | | | | | | | | | | | | | |

*Section 08*

# *Schedule and Logistics*

AECOM HUNT

*in association with*

Brownstone Construction Group
Pat Mathis Construction Company
A. Riley Consultants

Project: Savannah Arena | **Update - 08-Jul-20** | Date: 09-Jul-20 Time: 11:57

| Activity ID | Activity Name | Original Duration | Remaining Duration | Start | Finish |
|---|---|---|---|---|---|
| **Savannah Arena** | | 927 | 408 | 19-Jun-18 A | 16-Feb-22 |
| **Project Milestones / Preconstruction** | | 927 | 380 | 19-Jun-18 A | 16-Feb-22 |
| A1110 | Interviews with Shortlisted Companies | 0 | 0 | 19-Jun-18 A | |
| A1010 | Award and City Council Approval | 31 | 0 | 20-Jun-18 A | 02-Aug-18 A |
| A1020 | Design Kick-off Meeting | 1 | 0 | 03-Jul-18 A | 03-Jul-18 A |
| A1120 | Contract Award Date | 0 | 0 | | 07-Sep-18 A |
| A1770 | Design Start | 0 | 0 | 15-Feb-19 A | |
| A1760 | Ground Breaking | 0 | 0 | 13-Sep-19 A | |
| A1440 | 100% CD's Complete | 0 | 0 | | 17-Feb-20 A |
| DICMILE1000 | Start Erecting Steel | 0 | 0 | 17-Aug-20 | |
| DICMILE1010 | Start Steel Erection Crane 1 | 0 | 0 | 17-Aug-20 | |
| DICMILE1040 | Start Receiving Steel | 0 | 0 | 17-Aug-20 | |
| DICMILE1050 | Start Steel Erection Crane 2 | 0 | 0 | 14-Dec-20 | |
| DICMILE1030 | Finish Erecting Steel | 0 | 0 | | 10-Mar-21 |
| A1050 | Substantial Completion | 0 | 0 | | 20-Dec-21* |
| A3080 | Closeout | 40 | 40 | 21-Dec-21 | 16-Feb-22 |
| A3320 | Final Completion | 0 | 0 | | 16-Feb-22 |
| **COVID-19 Delays** | | 5 | 0 | 02-Apr-20 A | 03-Apr-20 A |
| CVD-19-1000 | Potential Delay - Site Utilities Permit | 5 | 0 | 02-Apr-20 A | 03-Apr-20 A |
| **Design Schedule - JLL** | | 421 | 60 | 10-Jul-18 A | 30-Sep-20 |
| 1 Project Kick-Off | | 1 | 0 | 10-Jul-18 A | 10-Jul-18 A |
| DES-1000 | Project Kick-Off | 1 | 0 | 10-Jul-18 A | 10-Jul-18 A |
| 2 Design - Arena & Site | | 332 | 0 | 10-Jul-18 A | 22-May-20 A |
| DES-2000 | 2.1 Predesign | 153 | 0 | 10-Jul-18 A | 15-Feb-19 A |
| DES-2010 | 2.2 Design Contract Approval | 1 | 0 | 15-Feb-19 A | 15-Feb-19 A |
| DES-2020 | 2.3.1 Survey | 25 | 0 | 18-Feb-19 A | 22-Mar-19 A |
| DES-2030 | 2.3.2 Geotech | 25 | 0 | 18-Feb-19 A | 22-Mar-19 A |
| DES-2040 | 2.4 Schematic Design | 69 | 0 | 18-Feb-19 A | 19-May-19 A |
| DES-2080 | 2.8 Early Release Package - Site Demolition Permit/Bid Submittal | 30 | 0 | 26-Mar-19 A | 08-Jul-19 A |
| DES-2090 | 2.9 Early Release Package - Site Design Permit/Bid Submittal | 29 | 0 | 16-May-19 A | 08-Jul-19 A |
| DES-2050 | 2.5 Review / Approval (Schematic Design) | 20 | 0 | 20-May-19 A | 16-Jul-19 A |
| DES-2140 | Schematic Design Estimate & Review | 30 | 0 | 20-May-19 A | 08-Jul-19 A |
| DES-2060 | 2.6 Design Development | 63 | 0 | 09-Jul-19 A | 21-Oct-19 A |
| DES-2100 | 2.10 Early Release Package - Foundations Design Permit/Bid Set | 74 | 0 | 09-Jul-19 A | 21-Oct-19 A |
| DES-7180 | Early Release Package - Elevator Design Permit/Bid Submittal | 74 | 0 | 09-Jul-19 A | 21-Oct-19 A |
| DES-2150 | Building Grid & Columns Established | 1 | 0 | 07-Aug-19 A | 07-Aug-19 A |
| DES-2070 | 2.7 Review / Approval (Design Development) | 20 | 0 | 22-Oct-19 A | 18-Dec-19 A |
| DES-2110 | 2.11 Early Release Package - Structure Design Permit/Bid Set | 41 | 0 | 22-Oct-19 A | 19-Dec-19 A |
| DES-2130 | 100% CDs | 80 | 0 | 22-Oct-19 A | 17-Feb-20 A |
| DES-7190 | Design Development Estimate & Review | 20 | 0 | 22-Oct-19 A | 18-Dec-19 A |
| DES-7210 | Steel Initial Procurement Package (Does not Include Connections) | 25 | 0 | 14-Nov-19 A | 19-Dec-19 A |
| DES-7220 | Steel Connections Finalized | 20 | 0 | 20-Dec-19 A | 27-Mar-20 A |
| DES-2160 | Typical Connection Design | 0 | 0 | | 27-Mar-20 A |
| DES-2180 | Steel Connection Design Delivery - Quad 1, up to 3rd Level | 0 | 0 | | 27-Mar-20 A |
| DES-2190 | Steel Connection Design Delivery - Quad 2, up to 3rd Level | 0 | 0 | | 03-Apr-20 A |
| DES-2200 | Steel Connection Design Delivery - Quad 3, up to 3rd Level | 0 | 0 | | 10-Apr-20 A |
| DES-2210 | Steel Connection Design Delivery - Quad 4, up to 3rd Level | 0 | 0 | | 17-Apr-20 A |
| DES-2220 | Steel Connection Design Delivery - Quad 1, Balance | 0 | 0 | | 24-Apr-20 A |
| DES-2230 | Steel Connection Design Delivery - Quad 2, Balance | 0 | 0 | | 01-May-20 A |
| DES-2240 | Steel Connection Design Delivery - Quad 3, Balance | 0 | 0 | | 08-May-20 A |
| DES-2250 | Steel Connection Design Delivery - Quad 4, Balance | 0 | 0 | | 15-May-20 A |
| DES-2170 | Steel Connections Finalized (within 60D of TCD) 5/22 | 0 | 0 | | 22-May-20 A |
| DES-2260 | Steel Connection Design Delivery - Roof | 0 | 0 | | 22-May-20 A |
| 3 Design - Off-Site - Stiles | | 220 | 0 | 18-Feb-19 A | 06-Apr-20 A |
| DES-3000 | Design - Stiles | 177 | 0 | 18-Feb-19 A | 06-Apr-20 A |
| DES-3010 | Permit/Bid Set - Stiles | 1 | 0 | 06-Apr-20 A | 06-Apr-20 A |
| DES-3020 | Conformed Construction Documents - Stiles | 0 | 0 | | 06-Apr-20 A |
| 4 Design - Off-Site - Canal & Stormwater | | 236 | 0 | 18-Feb-19 A | 16-Apr-20 A |
| DES-4000 | Design - Canal & Stormwater | 177 | 0 | 18-Feb-19 A | 16-Apr-20 A |
| DES-4010 | Permit/Bid Set - Canal & Stormwater | 1 | 0 | 16-Apr-20 A | 16-Apr-20 A |
| DES-4020 | Conformed Construction Documents - Canal & Stormwater | 0 | 0 | | 16-Apr-20 A |
| 5 Design - Off-Site - Force Main / Lift Station | | 221 | 0 | 18-Feb-19 A | 14-Apr-20 A |
| DES-5000 | Design - Force Main / Lift Station | 177 | 0 | 18-Feb-19 A | 14-Apr-20 A |
| DES-5010 | Permit/Bid Set - Force Main / Lift Station | 1 | 0 | 14-Apr-20 A | 14-Apr-20 A |
| DES-5020 | Conformed Construction Documents - Force Main / Lift Station | 0 | 0 | | 14-Apr-20 A |
| 6 Entitlements | | 189 | 0 | 18-Feb-19 A | 06-Jun-19 A |
| DES-6000 | 6.1.1 Traffic Analysis | 30 | 0 | 18-Feb-19 A | 29-Mar-19 A |
| DES-6010 | 6.1.2 Form-1 from City of Savannah to Regional Commission | 0 | 0 | | 29-Mar-19 A |
| DES-6020 | 6.1.3 Review Process | 35 | 0 | 01-Apr-19 A | 17-May-19 A |

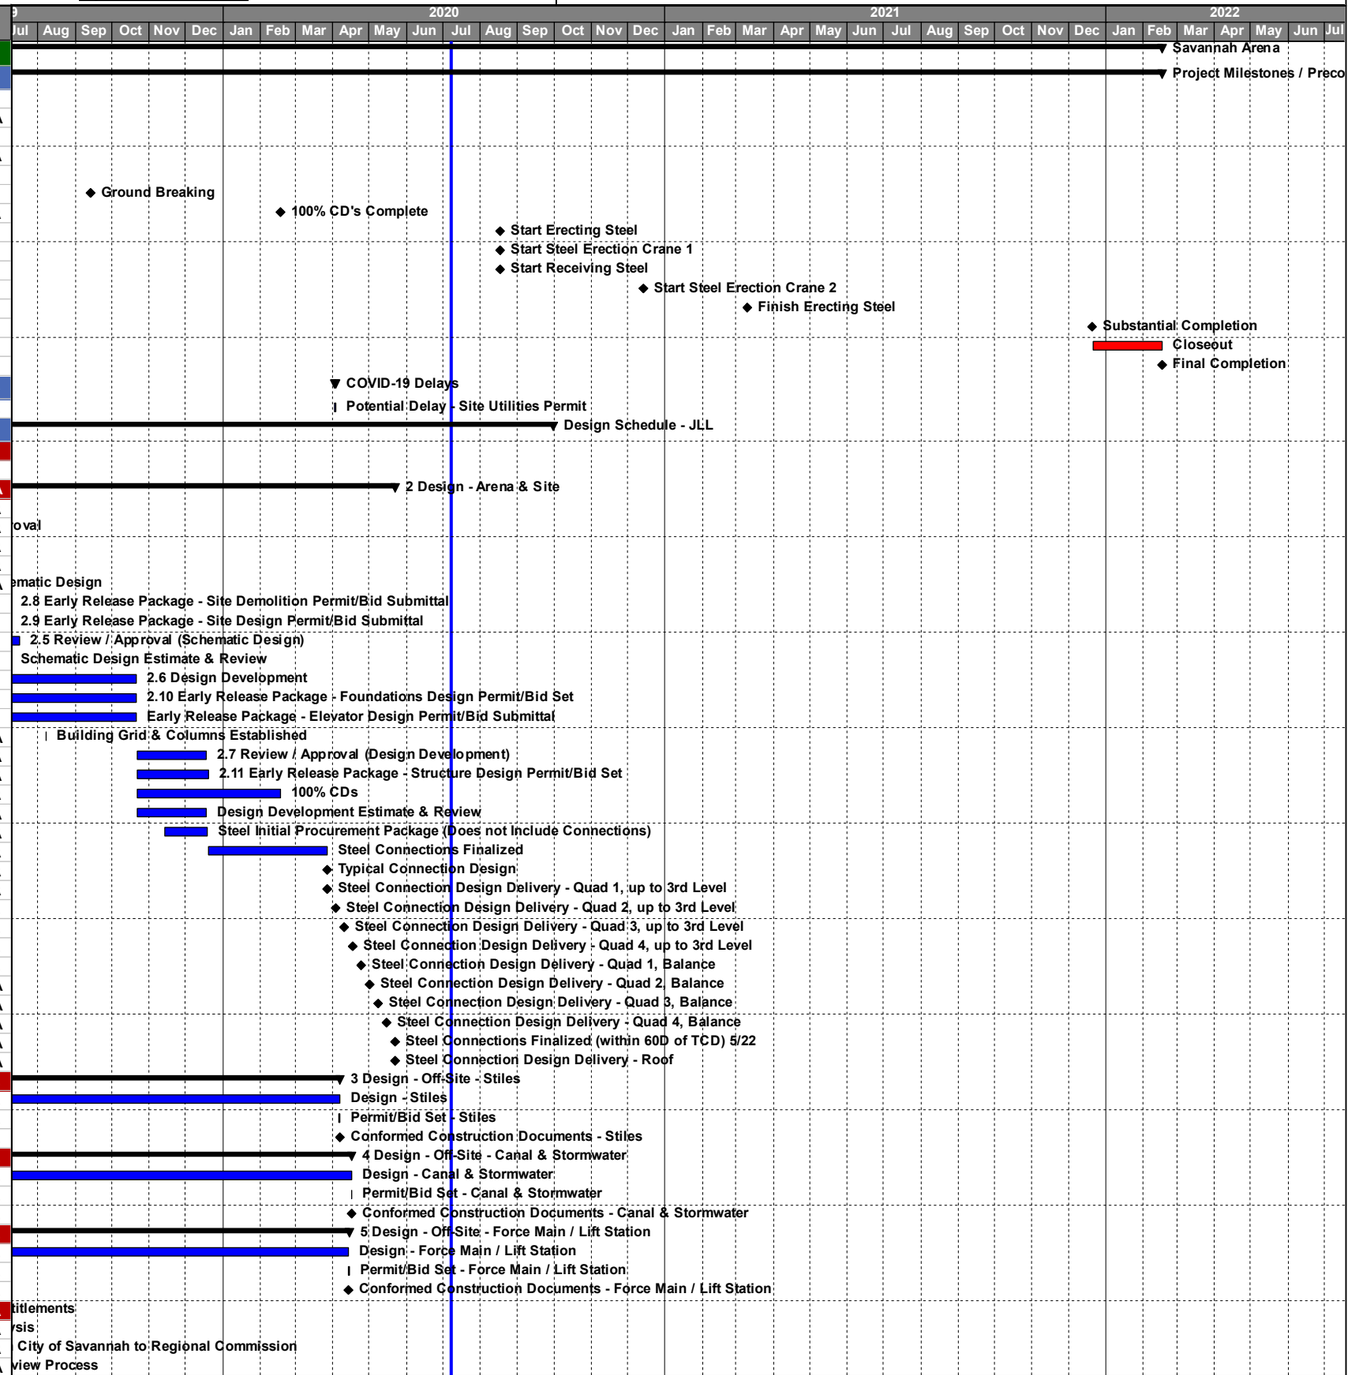


Remaining Level of Effort | Remainin...
Actual Level of Effort | Critical R...
Actual Work | Milestone

**Savannah Arena**
**Current Data Date: 08-Jul-20**



AECOM HUNT
in association with
Brownstone Construction Group
Pat Mathis Construction Company
A. Riley Consultants

| Activity ID | Activity Name | Original Duration | Remaining Duration | Start | Finish |
|---|---|---|---|---|---|
| DES-6040 | 6.2.1 Submit Application (Deadline for Next MPC Meeting) | 1 | 0 | 02-Apr-19 A | 02-Apr-19 A |
| DES-6050 | 6.2.2 Metropolitan Planning Commission Meeting | 1 | 0 | 23-Apr-19 A | 23-Apr-19 A |
| DES-6030 | 6.1.4 Notice of Decision | 0 | 0 | | 17-May-19 A |
| DES-6060 | 6.2.3 City Council Meeting (Zoning Hearing) | 1 | 0 | 23-May-19 A | 23-May-19 A |
| DES-6070 | 6.2.4 City Council Meeting (First & Second Reading - Request) | 0 | 0 | 06-Jun-19 A | 06-Jun-19 A |
| 7 Permitting | | 313 | 60 | 09-Jul-19 A | 30-Sep-20 |
| Arena / Site | | 247 | 0 | 09-Jul-19 A | 22-Jun-20 A |
| Site Development Permit | | 85 | 0 | 09-Jul-19 A | 19-Sep-19 A |
| DES-7000 | 7.1.1.1 Attend Site Plan Review (SPR) | 1 | 0 | 09-Jul-19 A | 09-Jul-19 A |
| DES-7010 | 7.1.1.2 Submit Application | 1 | 0 | 23-Jul-19 A | 23-Jul-19 A |
| DES-7020 | 7.1.1.3 Review Process | 20 | 0 | 23-Jul-19 A | 03-Sep-19 A |
| DES-7200 | Stormwater Polution Prevention Plan - NOI | 40 | 0 | 26-Aug-19 A | 26-Aug-19 A |
| DES-7030 | 7.1.1.4 Site Development Plan Approval Issued | 0 | 0 | | 03-Sep-19 A |
| DES-7060 | 7.1.1.7 Site Permit Issued | 0 | 0 | | 10-Sep-19 A |
| DES-7050 | 7.1.1.6 Release Hold on Building Permit | 0 | 0 | | 10-Sep-19 A |
| DES-7040 | 7.1.1.5 Preconstruction Meeting | 1 | 0 | 19-Sep-19 A | 19-Sep-19 A |
| Foundations Permit | | 38 | 0 | 20-Dec-19 A | 25-Feb-20 A |
| DES-7070 | 7.1.2.1 Submit Application - Deep Foundations | 1 | 0 | 20-Dec-19 A | 06-Jan-20 A |
| DES-7080 | 7.1.2.2 Review Process - Deep Foundations | 20 | 0 | 07-Jan-20 A | 25-Feb-20 A |
| DES-7090 | 7.1.2.3 Foundations Permit Issued - Deep Foundations | 0 | 0 | | 25-Feb-20 A |
| Building Permit | | 94 | 0 | 13-Feb-20 A | 22-Jun-20 A |
| DES-7170 | Review Process - Site Utilities Permit | 20 | 0 | 13-Feb-20 A | 03-Apr-20 A |
| DES-7100 | 7.1.3.1 Submit Application - Building Permit | 0 | 0 | 03-Mar-20 A | 03-Mar-20 A |
| DES-7110 | 7.1.3.2 Review Process - Building Permit | 40 | 0 | 03-Mar-20 A | 22-Jun-20 A |
| DES-7230 | Site Utilities Permit Issued | 0 | 0 | | 03-Apr-20 A |
| DES-7240 | Full Arena Site Permit Issued | 0 | 0 | | 22-May-20 A |
| DES-7120 | 7.1.3.3 Building Permit Issued | 0 | 0 | | 22-Jun-20 A |
| Off-Site | | 60 | 60 | 08-Jul-20 | 30-Sep-20 |
| Stiles Ave | | 60 | 60 | 08-Jul-20 | 30-Sep-20 |
| DES-7130 | 7.2.1.1 City Work in Right of Way Permit | 60 | 60 | 08-Jul-20 | 30-Sep-20 |
| DES-7140 | 7.2.1.2 GDOT Right of Way/Permit | 60 | 60 | 08-Jul-20 | 30-Sep-20 |
| Force Main / Lift Station | | 60 | 60 | 08-Jul-20 | 30-Sep-20 |
| DES-7150 | 7.2.2.1 Right of Way Work Permit | 40 | 40 | 08-Jul-20 | 01-Sep-20 |
| DES-7160 | 7.2.2.2 GA Department of Public Health Permit | 20 | 20 | 02-Sep-20 | 30-Sep-20 |
| GMP | | 48 | 27 | 28-May-20 A | 13-Aug-20 |
| A3660 | Prepare & Submit GMP | 20 | 3 | 28-May-20 A | 10-Jul-20 |
| A3680 | Review & Approve GMP | 24 | 24 | 13-Jul-20 | 13-Aug-20 |
| A4950 | GMP Execution | 0 | 0 | | 13-Aug-20 |
| Bid Packages (Bid / Award) | | 233 | 0 | 07-Nov-19 A | 08-Jul-20 |
| Group #1 | | 156 | 0 | 07-Nov-19 A | 05-Jun-20 A |
| A3480 | Bid/Award/Execute Subcontract - 02D Demolition | 40 | 0 | 07-Nov-19 A | 19-Dec-19 A |
| A3380 | Bid/Award/Execute Subcontract - 31A Site Work | 40 | 0 | 06-Dec-19 A | 07-Feb-20 A |
| A5560 | Bid/Award/Execute Subcontract - 31A Utilities | 10 | 0 | 06-Dec-19 A | 07-Feb-20 A |
| A3370 | Bid/Award/Execute Subcontract - 31B Foundations - Piles | 20 | 0 | 30-Dec-19 A | 07-Feb-20 A |
| A3390 | Bid/Award/Execute Subcontract - 05A Structural Steel | 45 | 0 | 09-Jan-20 A | 07-Apr-20 A |
| A5220 | Bid/Award/Execute Subcontract - 03A Concrete | 20 | 0 | 17-Jan-20 A | 20-Mar-20 A |
| A3590 | Bid/Award/LOA Approved - 14A Elevators & Escalators | 26 | 0 | 24-Jan-20 A | 05-Jun-20 A |
| DICMILE1020 | Notice to Proceed | 0 | 0 | 13-Mar-20 A | |
| DICMILE1060 | Receipt of Contract | 0 | 0 | 16-Mar-20 A | |
| Group #2 | | 82 | 0 | 26-Feb-20 A | 08-Jul-20 |
| A3450 | Bid/Award/LOA Approved - 07B Curtainwall/Glass | 50 | 0 | 26-Feb-20 A | 22-May-20 A |
| A11540 | Bid/Award/LOA Approved - 07E Metal Panels | 50 | 0 | 26-Feb-20 A | 28-May-20 A |
| A11550 | Bid/Award/LOA Approved - 09A Framing & Sheathing | 50 | 0 | 27-Feb-20 A | 05-Jun-20 A |
| A3420 | Bid/Award/LOA Approved - 22A Plumbing | 50 | 0 | 05-Mar-20 A | 07-Jul-20 A |
| A3440 | Bid/Award/LOA Approved - 21A Fire Protection | 50 | 0 | 09-Mar-20 A | 05-Jun-20 A |
| A3410 | Bid/Award/LOA Approved - 23A Mechanical | 15 | 0 | 20-Mar-20 A | 10-Jun-20 A |
| A3430 | Bid/Award/LOA Approved - 26B Electrical | 19 | 0 | 23-Mar-20 A | 08-Jul-20 |
| A3400 | Bid/Award/LOA Approved - 07A Roofing | 33 | 0 | 30-Mar-20 A | 10-Jun-20 A |
| A3460 | Bid/Award/LOA Approved - 05D Misc Metals | 18 | 0 | 29-May-20 A | 08-Jul-20 |
| Group #3 | | 80 | 0 | 04-Mar-20 A | 08-Jul-20 |
| A3490 | Bid/Award/LOA Approved - 03C Precast | 40 | 0 | 04-Mar-20 A | 20-May-20 A |
| A3510 | Bid/Award/LOA Approved - 07D Spray Fireproofing | 40 | 0 | 04-Mar-20 A | 08-Jul-20 |
| A3520 | Bid/Award/LOA Approved - 04A Masonry | 40 | 0 | 04-Mar-20 A | 04-Jun-20 A |
| A3500 | Bid/Award/LOA Approved 11B Food Service Equipment | 40 | 0 | 20-Mar-20 A | 04-Jun-20 A |
| A3540 | Bid/Award/LOA Approved - 11C Scoreboards & Video Boards | 40 | 0 | 23-Mar-20 A | 08-Jul-20 |
| A3560 | Bid/Award/LOA Approved - 13A Ice Rink System | 41 | 0 | 23-Mar-20 A | 08-Jul-20 |
| A3570 | Bid/Award/LOA Approved - 26D Sports Lighting | 40 | 0 | 23-Mar-20 A | 08-Jul-20 |
| A3550 | Bid/Award/LOA Approved - 07C Joint Sealants | 40 | 0 | 27-Mar-20 A | 08-Jul-20 |
| A5120 | Bid/Award/LOA Approved - 27A Low Voltage & Security Systems | 40 | 0 | 05-Apr-20 A | 08-Jul-20 |

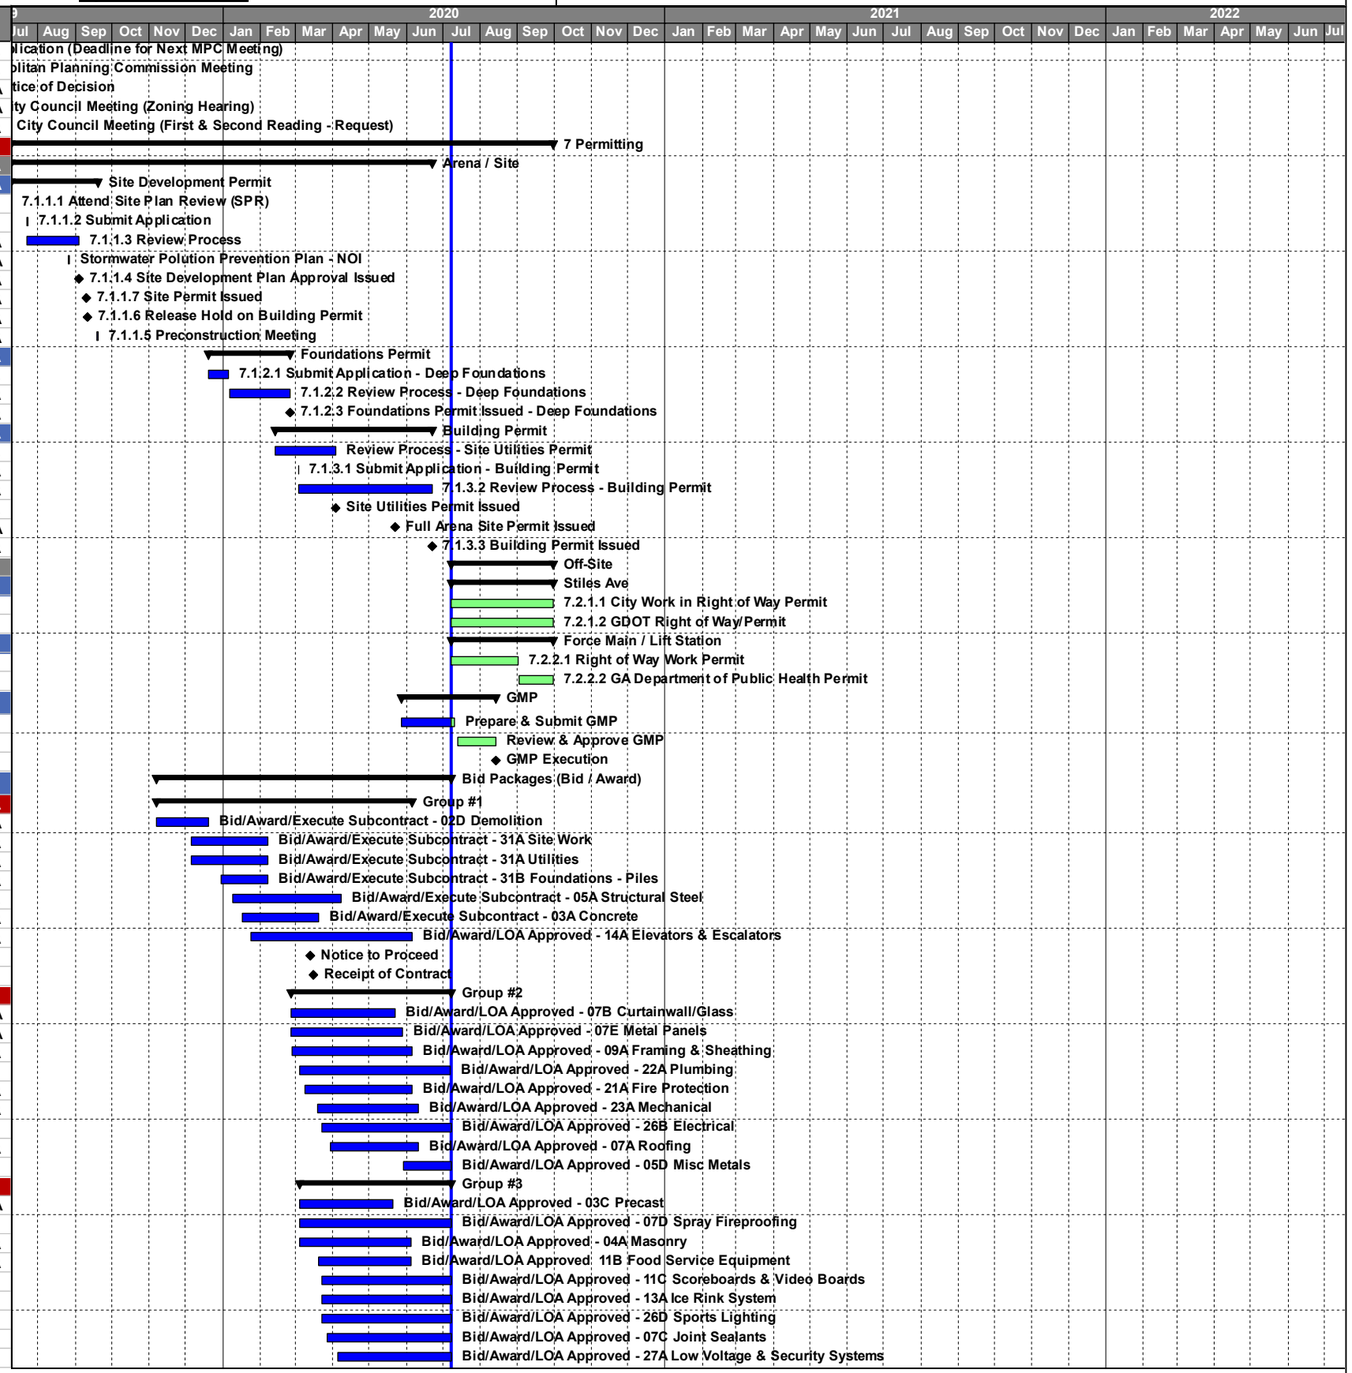

| Activity ID | Activity Name | Original Duration | Remaining Duration | Start | Finish |
|---|---|---|---|---|---|
| A3580 | Bid/Award/LOA Approved - 06A Architectural Woodwork | 40 | 0 | 13-Apr-20 A | 08-Jul-20 |
| A3650 | Bid/Award/LOA Approved - 09C Tile | 40 | 0 | 13-Apr-20 A | 08-Jul-20 |
| A3670 | Bid/Award/LOA Approved - 09D Carpet & Resilient Flooring | 40 | 0 | 13-Apr-20 A | 08-Jul-20 |
| A4880 | Bid/Award/LOA Approved - 09F Polished Concrete | 40 | 0 | 13-Apr-20 A | 08-Jul-20 |
| A4890 | Bid/Award/LOA Approved - 10A Specialties | 40 | 0 | 13-Apr-20 A | 08-Jul-20 |
| A4875 | Bid/Award/LOA Approved - 09E Resinous Flooring | 40 | 0 | 13-Apr-20 A | 08-Jul-20 |
| A4900 | Bid/Award/LOA Approved - 08B Overhead Doors | 41 | 0 | 20-Apr-20 A | 08-Jul-20 |
| A4910 | Bid/Award/LOA Approved - 08C Doors, Frames & Hardware | 29 | 0 | 25-Apr-20 A | 08-Jul-20 |
| A4920 | Bid/Award/LOA Approved - 09B Interior Drywall & Ceilings | 31 | 0 | 27-Apr-20 A | 08-Jul-20 |
| A4930 | Bid/Award/LOA Approved - 09G Painting & Wallcovering | 31 | 0 | 27-Apr-20 A | 08-Jul-20 |
| A4960 | Bid/Award/LOA Approved - 05C Metal Railing | 32 | 0 | 12-May-20 A | 08-Jul-20 |
| A4970 | Bid/Award/LOA Approved - 12C Seating | 36 | 0 | 12-May-20 A | 08-Jul-20 |
| A4940 | Bid/Award/LOA Approved - 12A Blackout/House Curtain | 28 | 0 | 14-May-20 A | 08-Jul-20 |
| **Long Lead Items** | | 252 | 164 | 10-Feb-20 A | 02-Mar-21 |
| **03A - Foundations** | | 68 | 5 | 23-Mar-20 A | 14-Jul-20 |
| A5690 | Prepare Submittal | 5 | 3 | 23-Mar-20 A | 10-Jul-20 |
| A5700 | Submittal Initial Review Time | 10 | 5 | 07-Apr-20 A | 14-Jul-20 |
| A5740 | Fabricate & Deliver | 5 | 0 | 27-Apr-20 A | 01-May-20 A |
| A5730 | Approval of Submittal | 0 | 0 | | 14-Jul-20 |
| **03B - Concrete Flatwork/Superstructure** | | 143 | 80 | 23-Mar-20 A | 28-Oct-20 |
| A5750 | Prepare Submittal | 10 | 5 | 23-Mar-20 A | 14-Jul-20 |
| A5760 | Submittal Initial Review Time | 15 | 10 | 07-Apr-20 A | 21-Jul-20 |
| A5770 | Revise for Resubmittal | 5 | 5 | 22-Jul-20 | 28-Jul-20 |
| A5780 | Resubmittal Review Time | 15 | 15 | 29-Jul-20 | 18-Aug-20 |
| A5790 | Approval of Submittal | 0 | 0 | | 18-Aug-20 |
| A5800 | Fabricate & Deliver | 50 | 50 | 19-Aug-20 | 28-Oct-20 |
| **03C - Structural Precast Stadia** | | 134 | 105 | 21-May-20 A | 04-Dec-20 |
| A5810 | Prepare Submittal | 60 | 57 | 21-May-20 A | 25-Sep-20 |
| A5820 | Submittal Initial Review Time | 60 | 60 | 08-Jul-20 | 30-Sep-20 |
| A5830 | Revise for Resubmittal | 5 | 5 | 01-Oct-20 | 07-Oct-20 |
| A5840 | Resubmittal Review Time | 15 | 15 | 08-Oct-20 | 28-Oct-20 |
| A5850 | Approval of Submittal | 0 | 0 | | 08-Oct-20 |
| A5860 | Fabricate & Deliver | 40 | 40 | 08-Oct-20 | 04-Dec-20 |
| **04A - Masonry** | | 95 | 95 | 08-Jul-20 | 18-Nov-20 |
| A7130 | Prepare Submittal | 10 | 10 | 08-Jul-20 | 21-Jul-20 |
| A7140 | Submittal Initial Review Time | 15 | 15 | 22-Jul-20 | 11-Aug-20 |
| A7150 | Revise for Resubmittal | 5 | 5 | 12-Aug-20 | 18-Aug-20 |
| A7160 | Resubmittal Review Time | 15 | 15 | 19-Aug-20 | 09-Sep-20 |
| A7170 | Approval of Submittal | 0 | 0 | | 09-Sep-20 |
| A7180 | Fabricate & Deliver | 50 | 50 | 10-Sep-20 | 18-Nov-20 |
| **05A - Structural Steel** | | 243 | 164 | 17-Mar-20 A | 02-Mar-21 |
| A7070 | Prepare Submittal | 20 | 0 | 17-Mar-20 A | 24-Jun-20 A |
| DICMILE1070 | Advance Bill of Material (ABM) Project | 10 | 0 | 17-Mar-20 A | 30-Mar-20 A |
| A7190 | Mill Order | 60 | 0 | 31-Mar-20 A | 08-Jul-20 |
| DICMILE1080 | Place Material Order (Based Upon Contract Date) | 10 | 0 | 31-Mar-20 A | 13-Apr-20 A |
| DICMILE1090 | Material Production & Shipment | 30 | 0 | 14-Apr-20 A | 01-Jul-20 A |
| **Detailing** | | 138 | 60 | 17-Mar-20 A | 30-Sep-20 |
| **Anchor Bolts & Embeds** | | 20 | 0 | 17-Mar-20 A | 07-Apr-20 A |
| DETANBE-1000 | Out for Approval - Detailing of Anchor Botls & Embeds | 10 | 0 | 17-Mar-20 A | 20-Mar-20 A |
| DETANBE-1010 | Back for Approval - Detailing of Anchor Botls & Embeds | 10 | 0 | 20-Mar-20 A | 07-Apr-20 A |
| **Ground to Level 3 Seq 101 thru 105** | | 45 | 0 | 18-Mar-20 A | 26-May-20 A |
| DETGRNDTOL\ | Out for Approval - Estimated Drawing Count 820 | 35 | 0 | 18-Mar-20 A | 01-May-20 A |
| DETGRNDTOL\ | Back for Approval - Estimated Drawing Count 820 | 10 | 0 | 06-May-20 A | 26-May-20 A |
| **Ground to Level 3 Seq 106 thru 110** | | 18 | 0 | 04-May-20 A | 10-Jun-20 A |
| DETGRNDTOL\ | Out for Approval - Estimated Drawing Count 710 | 10 | 0 | 04-May-20 A | 21-May-20 A |
| DETGRNDTOL\ | Back for Approval - Estimated Drawing Count 710 | 10 | 0 | 26-May-20 A | 10-Jun-20 A |
| **Level 3 to Roof Steel** | | 33 | 4 | 21-May-20 A | 13-Jul-20 |
| DETLVL3TORO | Out for Approval - Estimated Drawing Count 1100 | 15 | 0 | 21-May-20 A | 11-Jun-20 A |
| DETLVL3TORO | Back for Approval - Estimated Drawing Count 1100 | 10 | 0 | 12-Jun-20 A | 17-Jun-20 A |
| DETLVL3TORO | Back for Approval - 201-207 & 401-404 | 10 | 0 | 12-Jun-20 A | 17-Jun-20 A |
| DETLVL3TORO | Back for Approval - Estimated Drawing Count 1100 *RESUBMIT | 2 | 0 | 24-Jun-20 A | 25-Jun-20 A |
| DETLVL3TORO | Back for Approval - 201-207 & 401-404 *RESUBMIT | 10 | 4 | 30-Jun-20 A | 13-Jul-20 |
| **High Roof Seq 301 thru 316** | | 20 | 6 | 12-Jun-20 A | 15-Jul-20 |
| DETHIGHROOF | Out for Approval - Estimated Drawing Count 270 | 10 | 0 | 12-Jun-20 A | 29-Jun-20 A |
| DETHIGHROOF | Back for Approval - Estimated Drawing Count 270 | 10 | 6 | 30-Jun-20 A | 15-Jul-20 |
| **High Roof Seq 317 thru 330** | | 14 | 10 | 01-Jul-20 A | 21-Jul-20 |
| DETHIGHROOF | Out for Approval - Estimated Drawing Count 330 | 7 | 0 | 01-Jul-20 A | 07-Jul-20 A |
| DETHIGHROOF | Back for Approval - Estimated Drawing Count 330 | 10 | 10 | 08-Jul-20 | 21-Jul-20 |
| **Cooling Tower** | | 20 | 13 | 26-Jun-20 A | 24-Jul-20 |
| DETCOOLTWR· | Out for Approval - Estimated Drawing Count 18 | 10 | 3 | 26-Jun-20 A | 10-Jul-20 |

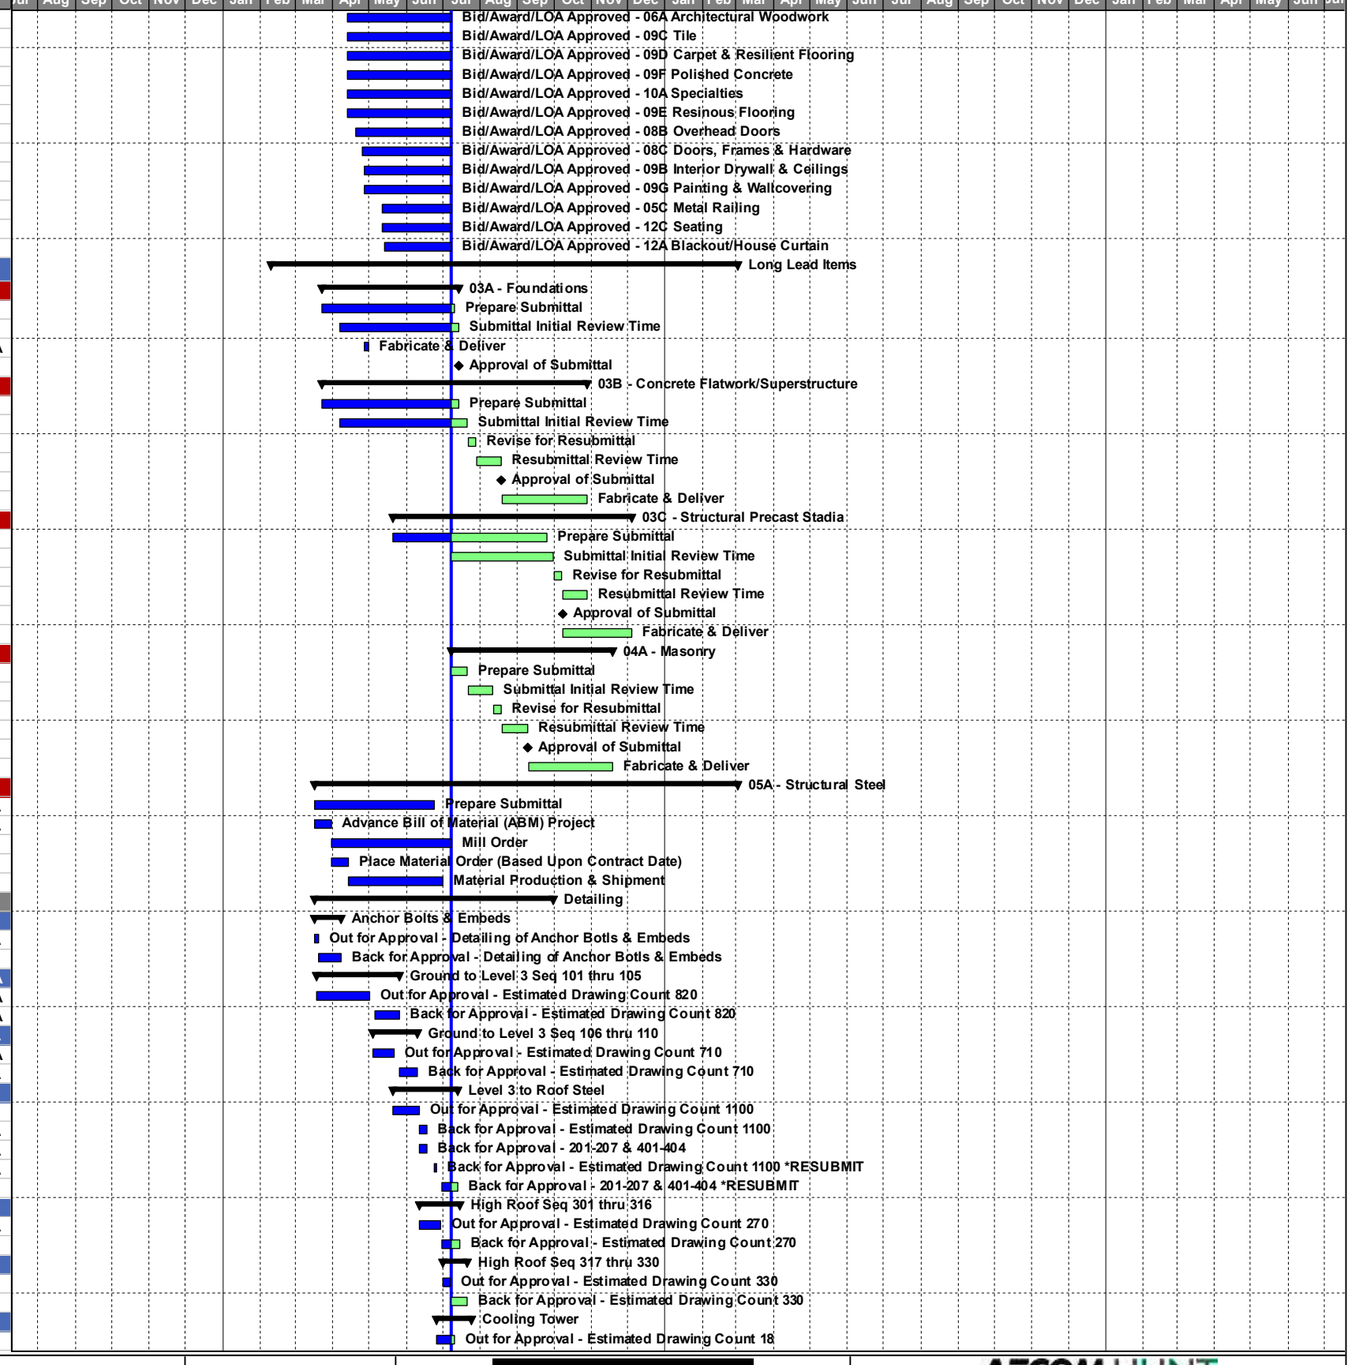

| Activity ID | Activity Name | Original Duration | Remaining Duration | Start | Finish |
|---|---|---|---|---|---|
| DETCOOLTWR· | Back for Approval - Estimated Drawing Count 18 | 10 | 10 | 13-Jul-20 | 24-Jul-20 |
| Fabrication | | 116 | 60 | 17-Apr-20 A | 30-Sep-20 |
| FAB-1000 | Fabricate Anchor Bolts and Embeds | 20 | 0 | 17-Apr-20 A | 14-May-20 A |
| FAB-1010 | Fabrication for Sequences 101 thru 105 | 50 | 21 | 22-Jun-20 A | 05-Aug-20 |
| FAB-1020 | Fabrication for Sequences 106 thru 110 | 50 | 41 | 24-Jun-20 A | 02-Sep-20 |
| FAB-1030 | Fabrication for Sequences 201 thru 207 & 401 thru 404 | 50 | 50 | 14-Jul-20 | 22-Sep-20 |
| FAB-1040 | Fabrication for Sequences 301 thru 316 | 50 | 50 | 16-Jul-20 | 24-Sep-20 |
| FAB-1050 | Fabrication for Sequences 317 thru 330 | 50 | 50 | 22-Jul-20 | 30-Sep-20 |
| FAB-1060 | Fabrication for Cooling Tower | 35 | 35 | 27-Jul-20 | 14-Sep-20 |
| Detailing Deck | | 60 | 0 | 06-May-20 A | 22-Jun-20 A |
| Decking Submittal 101 thru 105 | | 20 | 0 | 06-May-20 A | 22-Jun-20 A |
| DETDECKSUE | Out for Approval - Sequences 101 thru 105 | 20 | 0 | 06-May-20 A | 02-Jun-20 A |
| DETDECKSUE | Back for Approval - Sequences 101 thru 105 | 10 | 0 | 04-Jun-20 A | 22-Jun-20 A |
| Decking Submittal 106 thru 110 | | 25 | 0 | 06-May-20 A | 22-Jun-20 A |
| DETDECKSUE | Out for Approval - Sequences 106 thru 110 | 15 | 0 | 06-May-20 A | 02-Jun-20 A |
| DETDECKSUE | Back for Approval - Sequences 106 thru 110 | 10 | 0 | 04-Jun-20 A | 22-Jun-20 A |
| Decking Submittal 201 thru 207 & 401 thru 404 | | 25 | 0 | 06-May-20 A | 22-Jun-20 A |
| DETDECKSUE | Out for Approval - Sequences 201 thru 207 & 401 thru 404 | 15 | 0 | 06-May-20 A | 02-Jun-20 A |
| DETDECKSUE | Back for Approval - Sequences 201 thru 207 & 401 thru 404 | 10 | 0 | 04-Jun-20 A | 22-Jun-20 A |
| Decking Submittal 301 thru 330 | | 20 | 0 | 06-May-20 A | 02-Jun-20 A |
| DETDECKSUE | Out for Approval - Sequences 301 thru 330 | 20 | 0 | 06-May-20 A | 02-Jun-20 A |
| Procurement | | 137 | 137 | 17-Aug-20 | 02-Mar-21 |
| Receive Steel | | 137 | 137 | 17-Aug-20 | 02-Mar-21 |
| Crane 1 | | 137 | 137 | 17-Aug-20 | 02-Mar-21 |
| CR1RECSTL1( | Receive Steel with Crane 1 - First Tier - Seq 101 | 1 | 1 | 17-Aug-20 | 17-Aug-20 |
| CR1RECSTL1( | Receive Steel with Crane 1 - First Tier - Seq 102 | 1 | 1 | 24-Aug-20 | 24-Aug-20 |
| CR1RECSTL1( | Receive Steel with Crane 1 - First Tier - Seq 103 | 1 | 1 | 01-Sep-20 | 01-Sep-20 |
| CR1RECSTL1( | Receive Steel with Crane 1 - First Tier - Seq 104 | 1 | 1 | 10-Sep-20 | 10-Sep-20 |
| CR1RECSTL1( | Receive Steel with Crane 1 - First Tier - Seq 105 | 1 | 1 | 17-Sep-20 | 17-Sep-20 |
| CR1RECSTL1( | Receive Steel with Crane 1 - First Tier - Seq 106 | 1 | 1 | 23-Sep-20 | 23-Sep-20 |
| CR1RECSTL1( | Receive Steel with Crane 1 - First Tier - Seq 107 | 1 | 1 | 01-Oct-20 | 01-Oct-20 |
| CR1RECSTL1( | Receive Steel with Crane 1 - First Tier - Seq 108 | 1 | 1 | 09-Oct-20 | 09-Oct-20 |
| CR1RECSTL1( | Receive Steel with Crane 1 - First Tier - Seq 109 | 1 | 1 | 16-Oct-20 | 16-Oct-20 |
| CR1RECSTL2( | Receive Steel with Crane 1 - 2nd Tier - Seq 201 | 1 | 1 | 26-Oct-20 | 26-Oct-20 |
| CR1RECSTL3( | Receive Steel with Crane 1 - Roof - Seq 301 | 1 | 1 | 26-Oct-20 | 26-Oct-20 |
| CR1RECSTL3( | Receive Steel with Crane 1 - Roof - Seq 303 | 1 | 1 | 26-Oct-20 | 26-Oct-20 |
| CR1RECSTL3( | Receive Steel with Crane 1 - Roof - Seq 302 | 1 | 1 | 28-Oct-20 | 28-Oct-20 |
| CR1RECSTL3( | Receive Steel with Crane 1 - Roof - Seq 304 | 1 | 1 | 28-Oct-20 | 28-Oct-20 |
| CR1RECSTL2( | Receive Steel with Crane 1 - 2nd Tier - Seq 202 | 1 | 1 | 30-Oct-20 | 30-Oct-20 |
| CR1RECSTL2( | Receive Steel with Crane 1 - 2nd Tier - Seq 204 | 1 | 1 | 06-Nov-20 | 06-Nov-20 |
| CR1RECSTL2( | Receive Steel with Crane 1 - 2nd Tier - Seq 205 | 1 | 1 | 12-Nov-20 | 12-Nov-20 |
| CR1RECSTL3( | Receive Steel with Crane 1 - Roof - Seq 307 | 1 | 1 | 16-Nov-20 | 16-Nov-20 |
| CR1RECSTL3( | Receive Steel with Crane 1 - Roof - Seq 309 | 1 | 1 | 18-Nov-20 | 18-Nov-20 |
| CR1RECSTL3( | Receive Steel with Crane 1 - Roof - Seq 310 | 1 | 1 | 19-Nov-20 | 19-Nov-20 |
| CR1RECSTL3( | Receive Steel with Crane 1 - Roof - Seq 305 | 1 | 1 | 19-Nov-20 | 19-Nov-20 |
| CR1RECSTL3( | Receive Steel with Crane 1 - Roof - Seq 306 | 1 | 1 | 23-Nov-20 | 23-Nov-20 |
| CR1RECSTL3( | Receive Steel with Crane 1 - Roof - Seq 313 | 1 | 1 | 30-Nov-20 | 30-Nov-20 |
| CR1RECSTL3( | Receive Steel with Crane 1 - Roof - Seq 314 | 1 | 1 | 01-Dec-20 | 01-Dec-20 |
| CR1RECSTL3( | Receive Steel with Crane 1 - Roof - Seq 311 | 1 | 1 | 02-Dec-20 | 02-Dec-20 |
| CR1RECSTL3( | Receive Steel with Crane 1 - Roof - Seq 312 | 1 | 1 | 04-Dec-20 | 04-Dec-20 |
| CR1RECSTL3( | Receive Steel with Crane 1 - Roof - Seq 317 | 1 | 1 | 08-Dec-20 | 08-Dec-20 |
| CR1RECSTL3( | Receive Steel with Crane 1 - Roof - Seq 318 | 1 | 1 | 09-Dec-20 | 09-Dec-20 |
| CR1RECSTL3( | Receive Steel with Crane 1 - Roof - Seq 315 | 1 | 1 | 10-Dec-20 | 10-Dec-20 |
| CR1RECSTL3( | Receive Steel with Crane 1 - Roof - Seq 316 | 1 | 1 | 15-Dec-20 | 15-Dec-20 |
| CR1RECSTL3( | Receive Steel with Crane 1 - Roof - Seq 321 | 1 | 1 | 15-Dec-20 | 15-Dec-20 |
| CR1RECSTL3( | Receive Steel with Crane 1 - Roof - Seq 322 | 1 | 1 | 16-Dec-20 | 16-Dec-20 |
| CR1RECSTL3( | Receive Steel with Crane 1 - Roof - Seq 319 | 1 | 1 | 18-Dec-20 | 18-Dec-20 |
| CR1RECSTL3( | Receive Steel with Crane 1 - Roof - Seq 320 | 1 | 1 | 22-Dec-20 | 22-Dec-20 |
| CR1RECSTL3( | Receive Steel with Crane 1 - Roof - Seq 325 | 1 | 1 | 22-Dec-20 | 22-Dec-20 |
| CR1RECSTL3( | Receive Steel with Crane 1 - Roof - Seq 326 | 1 | 1 | 23-Dec-20 | 23-Dec-20 |
| CR1RECSTL3( | Receive Steel with Crane 1 - Roof - Seq 323 | 1 | 1 | 28-Dec-20 | 28-Dec-20 |
| CR1RECSTL3( | Receive Steel with Crane 1 - Roof - Seq 324 | 1 | 1 | 30-Dec-20 | 30-Dec-20 |
| CR1RECSTL3( | Receive Steel with Crane 1 - Roof - Seq 329 | 1 | 1 | 04-Jan-21 | 04-Jan-21 |
| CR1RECSTL3( | Receive Steel with Crane 1 - Roof - Seq 327 | 1 | 1 | 05-Jan-21 | 05-Jan-21 |
| CR1RECSTL3( | Receive Steel with Crane 1 - Roof - Seq 328 | 1 | 1 | 07-Jan-21 | 07-Jan-21 |
| CR1RECSTL11 | Receive Steel with Crane 1 - First Tier - Seq 110 | 1 | 1 | 11-Jan-21 | 11-Jan-21 |
| CR1RECSTL3( | Receive Steel with Crane 1 - Roof - Seq 330 | 1 | 1 | 13-Jan-21 | 13-Jan-21 |
| CR1RECSTL2( | Receive Steel with Crane 1 - 2nd Tier - Seq 206 | 1 | 1 | 19-Jan-21 | 19-Jan-21 |
| CR1RECSTL2( | Receive Steel with Crane 1 - 2nd Tier - Seq 207 | 1 | 1 | 28-Jan-21 | 28-Jan-21 |
| CR1RECSTL4( | Receive Steel with Crane 1 - Quads - Seq 401 | 1 | 1 | 03-Feb-21 | 03-Feb-21 |

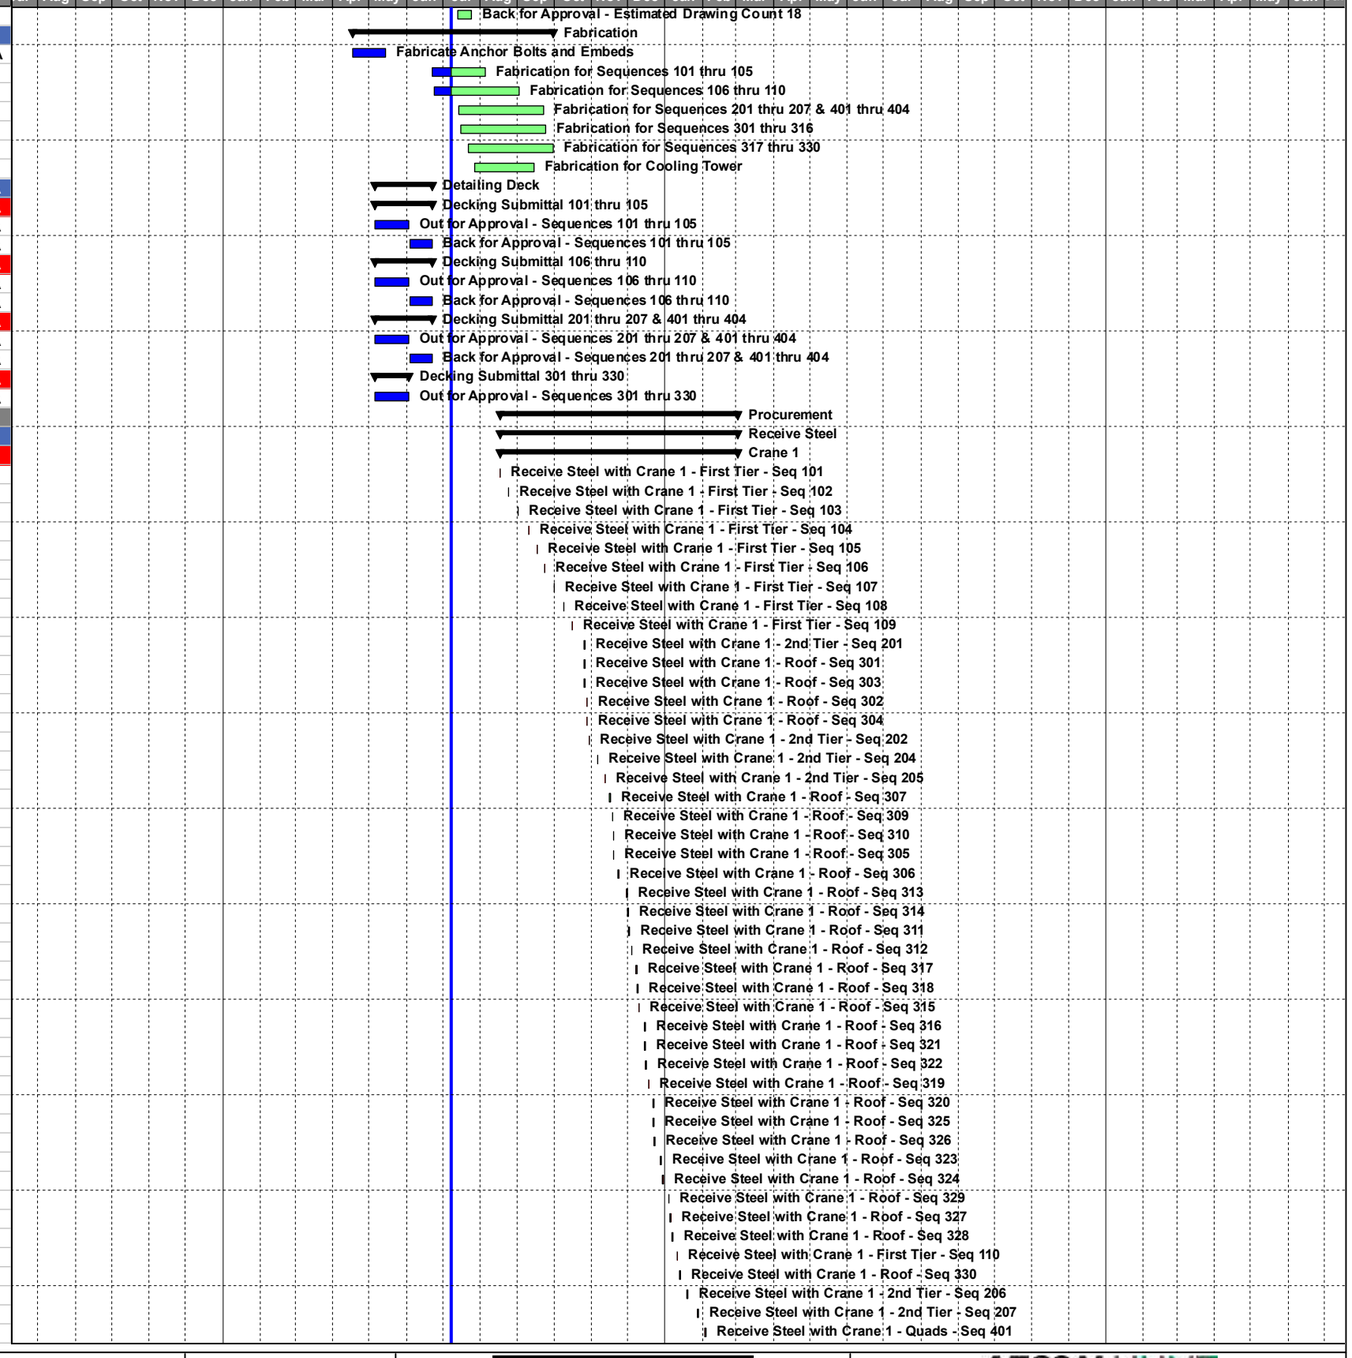

| Activity ID | Activity Name | Original Duration | Remaining Duration | Start | Finish |
|---|---|---|---|---|---|
| CR1RECSTL4( | Receive Steel with Crane 1 - Quads - Seq 404 | 1 | 1 | 04-Feb-21 | 04-Feb-21 |
| CR1RECSTL5( | Receive Steel with Crane 1 - Cooling Tower - Seq 501 | 1 | 1 | 02-Mar-21 | 02-Mar-21 |
| Crane 2 | | 10 | 10 | 14-Dec-20 | 28-Dec-20 |
| CR2RECSTL3( | Receive Steel with Crane 2 - Roof - Seq 308 | 1 | 1 | 14-Dec-20 | 14-Dec-20 |
| CR2RECSTL2( | Receive Steel with Crane 2 - 2nd Tier - Seq 203 | 1 | 1 | 17-Dec-20 | 17-Dec-20 |
| CR2RECSTL4( | Receive Steel with Crane 2 - Quads - Seq 402 | 1 | 1 | 24-Dec-20 | 24-Dec-20 |
| CR2RECSTL4( | Receive Steel with Crane 2 - Quads - Seq 403 | 1 | 1 | 28-Dec-20 | 28-Dec-20 |
| Assemble Steel | | 52 | 52 | 27-Oct-20 | 12-Jan-21 |
| Ground Assembly of Shoring Towers | | 1 | 1 | 14-Dec-20 | 14-Dec-20 |
| Crane 2 | | 1 | 1 | 14-Dec-20 | 14-Dec-20 |
| CR2GRASST3 | Ground Assembly of Shoring Tower E4 with Crane 2 | 1 | 1 | 14-Dec-20 | 14-Dec-20 |
| CR2GRASST3 | Ground Assembly of Shoring Tower E3 with Crane 2 | 1 | 1 | 14-Dec-20 | 14-Dec-20 |
| CR2GRASST3 | Ground Assembly of Shoring Tower E2 with Crane 2 | 1 | 1 | 14-Dec-20 | 14-Dec-20 |
| Ground Assembly of Trusses | | 47 | 47 | 27-Oct-20 | 05-Jan-21 |
| Crane 1 | | 47 | 47 | 27-Oct-20 | 05-Jan-21 |
| CR1GRASST3 | Ground Assembly with Crane 1 - Roof - Seq 301, 303 | 3 | 3 | 27-Oct-20 | 29-Oct-20 |
| CR1GRASST3 | Ground Assembly with Crane 1 - Roof - Seq 302, 304 | 3 | 3 | 29-Oct-20 | 02-Nov-20 |
| CR1GRASST3 | Ground Assembly with Crane 1 - Roof - Seq 307 | 2 | 2 | 17-Nov-20 | 18-Nov-20 |
| CR1GRASST3 | Ground Assembly with Crane 1 - Roof - Seq 309 | 1 | 1 | 19-Nov-20 | 19-Nov-20 |
| CR1GRASST3 | Ground Assembly with Crane 1 - Roof - Seq 310 | 1 | 1 | 20-Nov-20 | 20-Nov-20 |
| CR1GRASST3 | Ground Assembly with Crane 1 - Roof - Seq 313 | 1 | 1 | 01-Dec-20 | 01-Dec-20 |
| CR1GRASST3 | Ground Assembly with Crane 1 - Roof - Seq 314 | 1 | 1 | 02-Dec-20 | 02-Dec-20 |
| CR1GRASST3 | Ground Assembly with Crane 1 - Roof - Seq 317 | 1 | 1 | 09-Dec-20 | 09-Dec-20 |
| CR1GRASST4 | Ground Assembly with Crane 1 - Roof - Seq 318 | 1 | 1 | 10-Dec-20 | 10-Dec-20 |
| CR1GRASST4 | Ground Assembly with Crane 1 - Roof - Seq 321 | 1 | 1 | 16-Dec-20 | 16-Dec-20 |
| CR1GRASST4 | Ground Assembly with Crane 1 - Roof - Seq 322 | 1 | 1 | 17-Dec-20 | 17-Dec-20 |
| CR1GRASST4 | Ground Assembly with Crane 1 - Roof - Seq 325 | 1 | 1 | 23-Dec-20 | 23-Dec-20 |
| CR1GRASST3 | Ground Assembly with Crane 1 - Roof - Seq 326 | 1 | 1 | 24-Dec-20 | 24-Dec-20 |
| CR1GRASST5 | Ground Assembly with Crane 1 - Roof - Seq 329 | 1 | 1 | 05-Jan-21 | 05-Jan-21 |
| Detail Assembly of Trusses | | 49 | 49 | 30-Oct-20 | 12-Jan-21 |
| Crane 1 | | 49 | 49 | 30-Oct-20 | 12-Jan-21 |
| CR1DETASST | Detail Assembly of Trusses with Crane 1 - Roof - Seq 301, 303 | 15 | 15 | 30-Oct-20 | 19-Nov-20 |
| CR1DETASST | Detail Assembly of Trusses with Crane 1 - Roof - Seq 302, 304 | 15 | 15 | 03-Nov-20 | 23-Nov-20 |
| CR1DETASST | Detail Assembly of Trusses with Crane 1 - Roof - Seq 307 | 5 | 5 | 19-Nov-20 | 25-Nov-20 |
| CR1DETASST | Detail Assembly of Trusses with Crane 1 - Roof - Seq 309 | 5 | 5 | 20-Nov-20 | 30-Nov-20 |
| CR1GRASST7 | Detail Assembly of Trusses with Crane 1 - Roof - Seq 310 | 5 | 5 | 23-Nov-20 | 01-Dec-20 |
| CR1GRASST5 | Detail Assembly of Trusses with Crane 1 - Roof - Seq 313 | 5 | 5 | 02-Dec-20 | 08-Dec-20 |
| CR1GRASST5 | Detail Assembly of Trusses with Crane 1 - Roof - Seq 314 | 5 | 5 | 03-Dec-20 | 09-Dec-20 |
| CR1GRASST5 | Detail Assembly of Trusses with Crane 1 - Roof - Seq 317 | 5 | 5 | 10-Dec-20 | 16-Dec-20 |
| CR1GRASST6 | Detail Assembly of Trusses with Crane 1 - Roof - Seq 318 | 5 | 5 | 11-Dec-20 | 17-Dec-20 |
| CR1GRASST6 | Detail Assembly of Trusses with Crane 1 - Roof - Seq 321 | 5 | 5 | 17-Dec-20 | 23-Dec-20 |
| CR1GRASST6 | Detail Assembly of Trusses with Crane 1 - Roof - Seq 322 | 5 | 5 | 18-Dec-20 | 24-Dec-20 |
| CR1GRASST6 | Detail Assembly of Trusses with Crane 1 - Roof - Seq 325 | 5 | 5 | 24-Dec-20 | 31-Dec-20 |
| CR1GRASST6 | Detail Assembly of Trusses with Crane 1 - Roof - Seq 326 | 5 | 5 | 28-Dec-20 | 04-Jan-21 |
| CR1GRASST7 | Detail Assembly of Trusses with Crane 1 - Roof - Seq 329 | 5 | 5 | 06-Jan-21 | 12-Jan-21 |
| 06A - Architectural Woodwork | | 95 | 95 | 14-Aug-20 | 31-Dec-20 |
| A7010 | Prepare Submittal | 10 | 10 | 14-Aug-20 | 27-Aug-20 |
| A7020 | Submittal Initial Review Time | 15 | 15 | 28-Aug-20 | 18-Sep-20 |
| A7030 | Revise for Resubmittal | 5 | 5 | 21-Sep-20 | 25-Sep-20 |
| A7040 | Resubmittal Review Time | 15 | 15 | 28-Sep-20 | 16-Oct-20 |
| A7050 | Approval of Submittal | 0 | 0 | | 16-Oct-20 |
| A7060 | Fabricate & Deliver | 50 | 50 | 19-Oct-20 | 31-Dec-20 |
| 07A - Roofing | | 95 | 95 | 08-Jul-20 | 18-Nov-20 |
| A6950 | Prepare Submittal | 10 | 10 | 08-Jul-20 | 21-Jul-20 |
| A6960 | Submittal Initial Review Time | 15 | 15 | 22-Jul-20 | 11-Aug-20 |
| A6970 | Revise for Resubmittal | 5 | 5 | 12-Aug-20 | 18-Aug-20 |
| A6980 | Resubmittal Review Time | 15 | 15 | 19-Aug-20 | 09-Sep-20 |
| A6990 | Approval of Submittal | 0 | 0 | | 09-Sep-20 |
| A7000 | Fabricate & Deliver | 50 | 50 | 10-Sep-20 | 18-Nov-20 |
| 07B - Exterior Cladding & Curtainwall | | 95 | 95 | 08-Jul-20 | 18-Nov-20 |
| A6890 | Prepare Submittal | 10 | 10 | 08-Jul-20 | 21-Jul-20 |
| A6900 | Submittal Initial Review Time | 15 | 15 | 22-Jul-20 | 11-Aug-20 |
| A6910 | Revise for Resubmittal | 5 | 5 | 12-Aug-20 | 18-Aug-20 |
| A6920 | Resubmittal Review Time | 15 | 15 | 19-Aug-20 | 09-Sep-20 |
| A6930 | Approval of Submittal | 0 | 0 | | 09-Sep-20 |
| A6940 | Fabricate & Deliver | 50 | 50 | 10-Sep-20 | 18-Nov-20 |
| 08A - Storefront & Interior Glass | | 95 | 95 | 08-Jul-20 | 18-Nov-20 |
| A6830 | Prepare Submittal | 10 | 10 | 08-Jul-20 | 21-Jul-20 |
| A6840 | Submittal Initial Review Time | 15 | 15 | 22-Jul-20 | 11-Aug-20 |
| A6850 | Revise for Resubmittal | 5 | 5 | 12-Aug-20 | 18-Aug-20 |

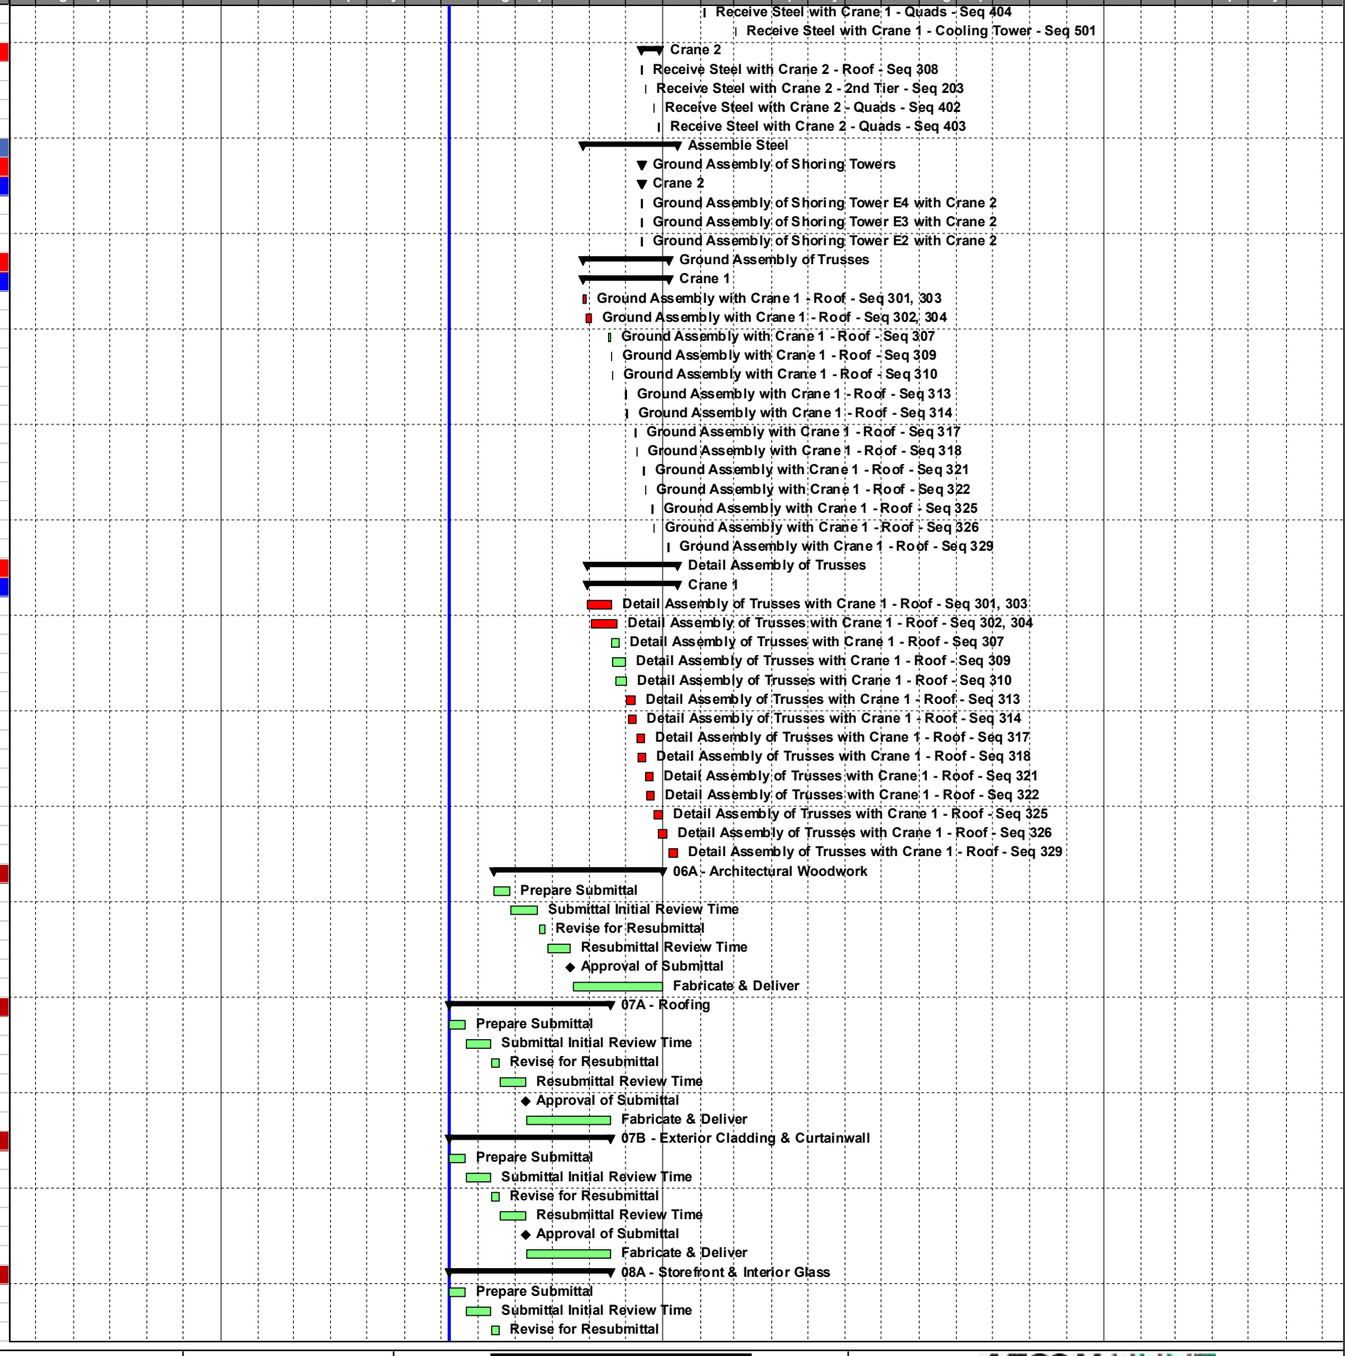

| Activity ID | Activity Name | Original Duration | Remaining Duration | Start | Finish |
|---|---|---|---|---|---|
| A6860 | Resubmittal Review Time | 15 | 15 | 19-Aug-20 | 09-Sep-20 |
| A6870 | Approval of Submittal | 0 | 0 | | 09-Sep-20 |
| A6880 | Fabricate & Deliver | 50 | 50 | 10-Sep-20 | 18-Nov-20 |
| 08B - Overhead Doors | | 95 | 95 | 08-Jul-20 | 18-Nov-20 |
| A6770 | Prepare Submittal | 10 | 10 | 08-Jul-20 | 21-Jul-20 |
| A6780 | Submittal Initial Review Time | 15 | 15 | 22-Jul-20 | 11-Aug-20 |
| A6790 | Revise for Resubmittal | 5 | 5 | 12-Aug-20 | 18-Aug-20 |
| A6800 | Resubmittal Review Time | 15 | 15 | 19-Aug-20 | 09-Sep-20 |
| A6810 | Approval of Submittal | 0 | 0 | | 09-Sep-20 |
| A6820 | Fabricate & Deliver | 50 | 50 | 10-Sep-20 | 18-Nov-20 |
| 08C - Doors & Hardware | | 125 | 125 | 14-Aug-20 | 12-Feb-21 |
| A31870 | Prepare Submittal | 10 | 10 | 14-Aug-20 | 27-Aug-20 |
| A31880 | Submittal Initial Review Time | 15 | 15 | 28-Aug-20 | 18-Sep-20 |
| A31890 | Revise for Resubmittal | 5 | 5 | 21-Sep-20 | 25-Sep-20 |
| A31900 | Resubmittal Review Time | 15 | 15 | 28-Sep-20 | 16-Oct-20 |
| A31910 | Approval of Submittal | 0 | 0 | | 16-Oct-20 |
| A31920 | Fabricate & Deliver - Doors | 80 | 80 | 19-Oct-20 | 12-Feb-21 |
| A31990 | Fabricate & Deliver - Hardware | 45 | 45 | 19-Oct-20 | 22-Dec-20 |
| 09C - Tile | | 115 | 115 | 14-Aug-20 | 29-Jan-21 |
| A31930 | Prepare Submittal | 10 | 10 | 14-Aug-20 | 27-Aug-20 |
| A31940 | Submittal Initial Review Time | 15 | 15 | 28-Aug-20 | 18-Sep-20 |
| A31950 | Revise for Resubmittal | 5 | 5 | 21-Sep-20 | 25-Sep-20 |
| A31960 | Resubmittal Review Time | 15 | 15 | 28-Sep-20 | 16-Oct-20 |
| A31970 | Approval of Submittal | 0 | 0 | | 16-Oct-20 |
| A31980 | Fabricate & Deliver | 70 | 70 | 19-Oct-20 | 29-Jan-21 |
| 10A - Specialties | | 105 | 105 | 08-Jul-20 | 04-Dec-20 |
| Folding Partitions | | 105 | 105 | 08-Jul-20 | 04-Dec-20 |
| A32450 | Prepare Submittal - Folding Partitions | 10 | 10 | 08-Jul-20 | 21-Jul-20 |
| A32460 | Submittal Initial Review Time - Folding Partitions | 15 | 15 | 22-Jul-20 | 11-Aug-20 |
| A32470 | Revise for Resubmittal - Folding Partitions | 5 | 5 | 12-Aug-20 | 18-Aug-20 |
| A32480 | Resubmittal Review Time - Folding Partitions | 15 | 15 | 19-Aug-20 | 09-Sep-20 |
| A32490 | Approval of Submittal - Folding Partitions | 0 | 0 | | 09-Sep-20 |
| A32500 | Fabricate & Deliver - Folding Partitions | 60 | 60 | 10-Sep-20 | 04-Dec-20 |
| Metal Lockers | | 105 | 105 | 08-Jul-20 | 04-Dec-20 |
| A32510 | Prepare Submittal - 2-Tier Metal Lockers | 10 | 10 | 08-Jul-20 | 21-Jul-20 |
| A32520 | Submittal Initial Review Time - 2-Tier Metal Lockers | 15 | 15 | 22-Jul-20 | 11-Aug-20 |
| A32530 | Revise for Resubmittal - 2-Tier Metal Lockers | 5 | 5 | 12-Aug-20 | 18-Aug-20 |
| A32540 | Resubmittal Review Time - 2-Tier Metal Lockers | 15 | 15 | 19-Aug-20 | 09-Sep-20 |
| A32550 | Approval of Submittal - 2-Tier Metal Lockers | 0 | 0 | | 09-Sep-20 |
| A32560 | Fabricate & Deliver - 2-Tier Metal Lockers | 60 | 60 | 10-Sep-20 | 04-Dec-20 |
| Toilet Partitions & Accessories | | 75 | 75 | 08-Jul-20 | 21-Oct-20 |
| A32570 | Prepare Submittal - Toilet Partitions & Accessories | 10 | 10 | 08-Jul-20 | 21-Jul-20 |
| A32580 | Submittal Initial Review Time - Toilet Partitions & Accessories | 15 | 15 | 22-Jul-20 | 11-Aug-20 |
| A32590 | Revise for Resubmittal - Toilet Partitions & Accessories | 5 | 5 | 12-Aug-20 | 18-Aug-20 |
| A32600 | Resubmittal Review Time - Toilet Partitions & Accessories | 15 | 15 | 19-Aug-20 | 09-Sep-20 |
| A32610 | Approval of Submittal - Toilet Partitions & Accessories | 0 | 0 | | 09-Sep-20 |
| A32620 | Fabricate & Deliver - Toilet Partitions & Accessories | 30 | 30 | 10-Sep-20 | 21-Oct-20 |
| 11A - Loading Dock Equipment | | 95 | 95 | 08-Jul-20 | 18-Nov-20 |
| A6710 | Prepare Submittal | 10 | 10 | 08-Jul-20 | 21-Jul-20 |
| A6720 | Submittal Initial Review Time | 15 | 15 | 22-Jul-20 | 11-Aug-20 |
| A6730 | Revise for Resubmittal | 5 | 5 | 12-Aug-20 | 18-Aug-20 |
| A6740 | Resubmittal Review Time | 15 | 15 | 19-Aug-20 | 09-Sep-20 |
| A6750 | Approval of Submittal | 0 | 0 | | 09-Sep-20 |
| A6760 | Fabricate & Deliver | 50 | 50 | 10-Sep-20 | 18-Nov-20 |
| 11B - Food Service Equipment | | 95 | 95 | 14-Aug-20 | 31-Dec-20 |
| A6650 | Prepare Submittal | 10 | 10 | 14-Aug-20 | 27-Aug-20 |
| A6660 | Submittal Initial Review Time | 15 | 15 | 28-Aug-20 | 18-Sep-20 |
| A6670 | Revise for Resubmittal | 5 | 5 | 21-Sep-20 | 25-Sep-20 |
| A6680 | Resubmittal Review Time | 15 | 15 | 28-Sep-20 | 16-Oct-20 |
| A6690 | Approval of Submittal | 0 | 0 | | 16-Oct-20 |
| A6700 | Fabricate & Deliver | 50 | 50 | 19-Oct-20 | 31-Dec-20 |
| 11C - Scoreboards & Video Boards | | 95 | 95 | 14-Aug-20 | 31-Dec-20 |
| A6590 | Prepare Submittal | 10 | 10 | 14-Aug-20 | 27-Aug-20 |
| A6600 | Submittal Initial Review Time | 15 | 15 | 28-Aug-20 | 18-Sep-20 |
| A6610 | Revise for Resubmittal | 5 | 5 | 21-Sep-20 | 25-Sep-20 |
| A6620 | Resubmittal Review Time | 15 | 15 | 28-Sep-20 | 16-Oct-20 |
| A6630 | Approval of Submittal | 0 | 0 | | 16-Oct-20 |
| A6640 | Fabricate & Deliver | 50 | 50 | 19-Oct-20 | 31-Dec-20 |
| 12A - Arena Curtains | | 75 | 75 | 14-Aug-20 | 01-Dec-20 |
| A32010 | Prepare Submittal | 10 | 10 | 14-Aug-20 | 27-Aug-20 |

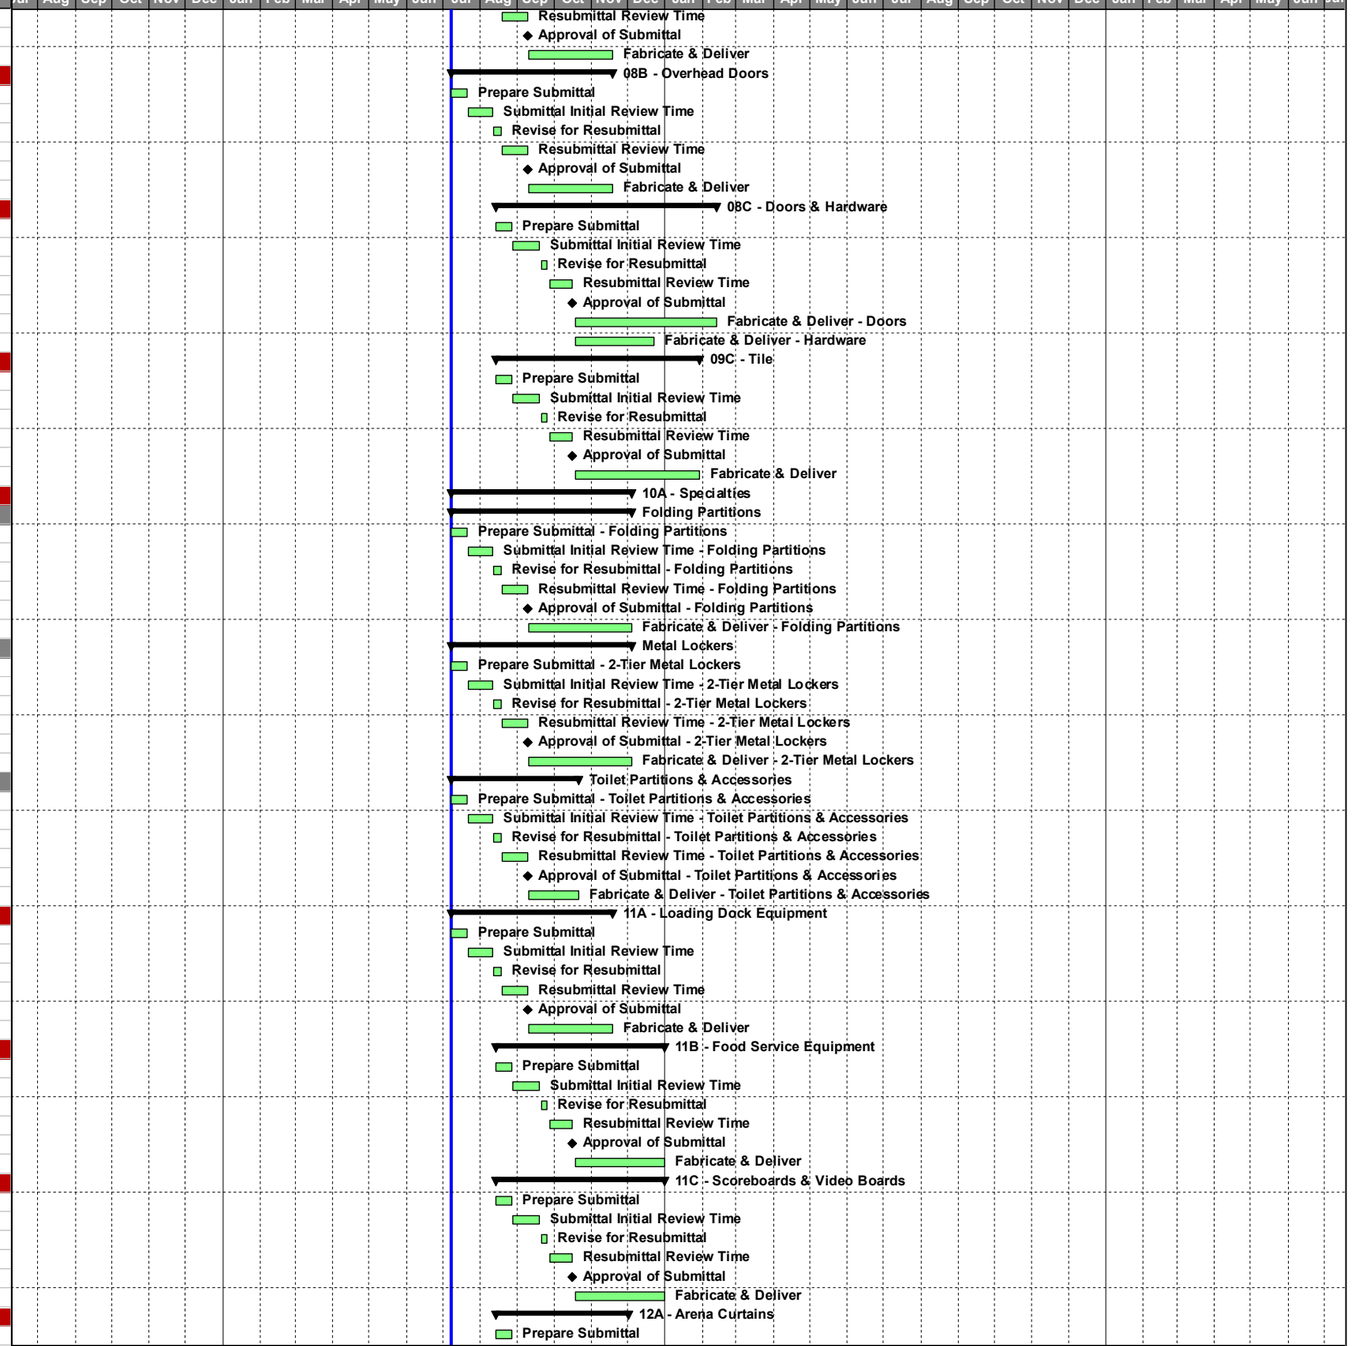

| Activity ID | Activity Name | Original Duration | Remaining Duration | Start | Finish |
|---|---|---|---|---|---|
| A32020 | Submittal Initial Review Time | 15 | 15 | 28-Aug-20 | 18-Sep-20 |
| A32030 | Revise for Resubmittal | 5 | 5 | 21-Sep-20 | 25-Sep-20 |
| A32040 | Resubmittal Review Time | 15 | 15 | 28-Sep-20 | 16-Oct-20 |
| A32050 | Approval of Submittal | 0 | 0 | | 16-Oct-20 |
| A32060 | Fabricate & Deliver - Arena Curtains/Half-House | 30 | 30 | 19-Oct-20 | 01-Dec-20 |
| A32070 | Fabricate & Deliver - Blackout Curtains | 30 | 30 | 19-Oct-20 | 01-Dec-20 |
| A32080 | Fabricate & Deliver - Shade System | 30 | 30 | 19-Oct-20 | 01-Dec-20 |
| 12C - Seating | | 135 | 135 | 14-Aug-20 | 26-Feb-21 |
| A6530 | Prepare Submittal | 20 | 20 | 14-Aug-20 | 11-Sep-20 |
| A6540 | Submittal Initial Review Time | 15 | 15 | 14-Sep-20 | 02-Oct-20 |
| A6550 | Revise for Resubmittal | 5 | 5 | 05-Oct-20 | 09-Oct-20 |
| A6560 | Resubmittal Review Time | 15 | 15 | 12-Oct-20 | 30-Oct-20 |
| A6570 | Approval of Submittal | 0 | 0 | | 30-Oct-20 |
| A6580 | Fabricate & Deliver - Retractables | 80 | 80 | 02-Nov-20 | 26-Feb-21 |
| A32000 | Fabricate & Deliver - Retractables | 60 | 60 | 02-Nov-20 | 29-Jan-21 |
| 13A - Ice Rink System | | 95 | 95 | 14-Aug-20 | 31-Dec-20 |
| A6470 | Prepare Submittal | 10 | 10 | 14-Aug-20 | 27-Aug-20 |
| A6480 | Submittal Initial Review Time | 15 | 15 | 28-Aug-20 | 18-Sep-20 |
| A6490 | Revise for Resubmittal | 5 | 5 | 21-Sep-20 | 25-Sep-20 |
| A6500 | Resubmittal Review Time | 15 | 15 | 28-Sep-20 | 16-Oct-20 |
| A6510 | Approval of Submittal | 0 | 0 | | 16-Oct-20 |
| A6520 | Fabricate & Deliver | 50 | 50 | 19-Oct-20 | 31-Dec-20 |
| 14A - Elevators & Escalators | | 95 | 95 | 08-Jul-20 | 18-Nov-20 |
| A6410 | Prepare Submittal | 10 | 10 | 08-Jul-20 | 21-Jul-20 |
| A6420 | Submittal Initial Review Time | 15 | 15 | 22-Jul-20 | 11-Aug-20 |
| A6430 | Revise for Resubmittal | 5 | 5 | 12-Aug-20 | 18-Aug-20 |
| A6440 | Resubmittal Review Time | 15 | 15 | 19-Aug-20 | 09-Sep-20 |
| A6450 | Approval of Submittal | 0 | 0 | | 09-Sep-20 |
| A6460 | Fabricate & Deliver | 50 | 50 | 10-Sep-20 | 18-Nov-20 |
| 21A - Fire Protection | | 95 | 95 | 08-Jul-20 | 18-Nov-20 |
| A6350 | Prepare Submittal | 10 | 10 | 08-Jul-20 | 21-Jul-20 |
| A6360 | Submittal Initial Review Time | 15 | 15 | 22-Jul-20 | 11-Aug-20 |
| A6370 | Revise for Resubmittal | 5 | 5 | 12-Aug-20 | 18-Aug-20 |
| A6380 | Resubmittal Review Time | 15 | 15 | 19-Aug-20 | 09-Sep-20 |
| A6390 | Approval of Submittal | 0 | 0 | | 09-Sep-20 |
| A6400 | Fabricate & Deliver | 50 | 50 | 10-Sep-20 | 18-Nov-20 |
| 22A - Plumbing | | 95 | 95 | 08-Jul-20 | 18-Nov-20 |
| A6290 | Prepare Submittal | 10 | 10 | 08-Jul-20 | 21-Jul-20 |
| A6300 | Submittal Initial Review Time | 15 | 15 | 22-Jul-20 | 11-Aug-20 |
| A6310 | Revise for Resubmittal | 5 | 5 | 12-Aug-20 | 18-Aug-20 |
| A6320 | Resubmittal Review Time | 15 | 15 | 19-Aug-20 | 09-Sep-20 |
| A6330 | Approval of Submittal | 0 | 0 | | 09-Sep-20 |
| A6340 | Fabricate & Deliver | 50 | 50 | 10-Sep-20 | 18-Nov-20 |
| 23A - HVAC | | 95 | 95 | 08-Jul-20 | 18-Nov-20 |
| A6230 | Prepare Submittal | 10 | 10 | 08-Jul-20 | 21-Jul-20 |
| A6240 | Submittal Initial Review Time | 15 | 15 | 22-Jul-20 | 11-Aug-20 |
| A6250 | Revise for Resubmittal | 5 | 5 | 12-Aug-20 | 18-Aug-20 |
| A6260 | Resubmittal Review Time | 15 | 15 | 19-Aug-20 | 09-Sep-20 |
| A6270 | Approval of Submittal | 0 | 0 | | 09-Sep-20 |
| A6280 | Fabricate & Deliver | 50 | 50 | 10-Sep-20 | 18-Nov-20 |
| 26B - Electrical | | 95 | 95 | 08-Jul-20 | 18-Nov-20 |
| A6170 | Prepare Submittal | 10 | 10 | 08-Jul-20 | 21-Jul-20 |
| A6180 | Submittal Initial Review Time | 15 | 15 | 22-Jul-20 | 11-Aug-20 |
| A6190 | Revise for Resubmittal | 5 | 5 | 12-Aug-20 | 18-Aug-20 |
| A6200 | Resubmittal Review Time | 15 | 15 | 19-Aug-20 | 09-Sep-20 |
| A6210 | Approval of Submittal | 0 | 0 | | 09-Sep-20 |
| A6220 | Fabricate & Deliver | 50 | 50 | 10-Sep-20 | 18-Nov-20 |
| 26D - Sports Lighting | | 107 | 95 | 05-Jun-20 A | 18-Nov-20 |
| A6110 | Prepare Submittal | 10 | 10 | 05-Jun-20 A | 21-Jul-20 |
| A6120 | Submittal Initial Review Time | 15 | 15 | 22-Jul-20 | 11-Aug-20 |
| A6130 | Revise for Resubmittal | 5 | 5 | 12-Aug-20 | 18-Aug-20 |
| A6140 | Resubmittal Review Time | 15 | 15 | 19-Aug-20 | 09-Sep-20 |
| A6150 | Approval of Submittal | 0 | 0 | | 09-Sep-20 |
| A6160 | Fabricate & Deliver | 50 | 50 | 10-Sep-20 | 18-Nov-20 |
| 31A - Sitework/Site Utilities | | 52 | 0 | 10-Feb-20 A | 05-May-20 A |
| A6050 | Prepare Submittal | 10 | 0 | 10-Feb-20 A | 25-Feb-20 A |
| A6060 | Submittal Initial Review Time | 15 | 0 | 26-Feb-20 A | 03-Apr-20 A |
| A6090 | Approval of Submittal | 0 | 0 | | 03-Apr-20 A |
| A6100 | Fabricate & Deliver | 10 | 0 | 04-Apr-20 A | 05-May-20 A |
| 31B - Piles / Deep Foundations | | 30 | 0 | 18-Feb-20 A | 17-Mar-20 A |

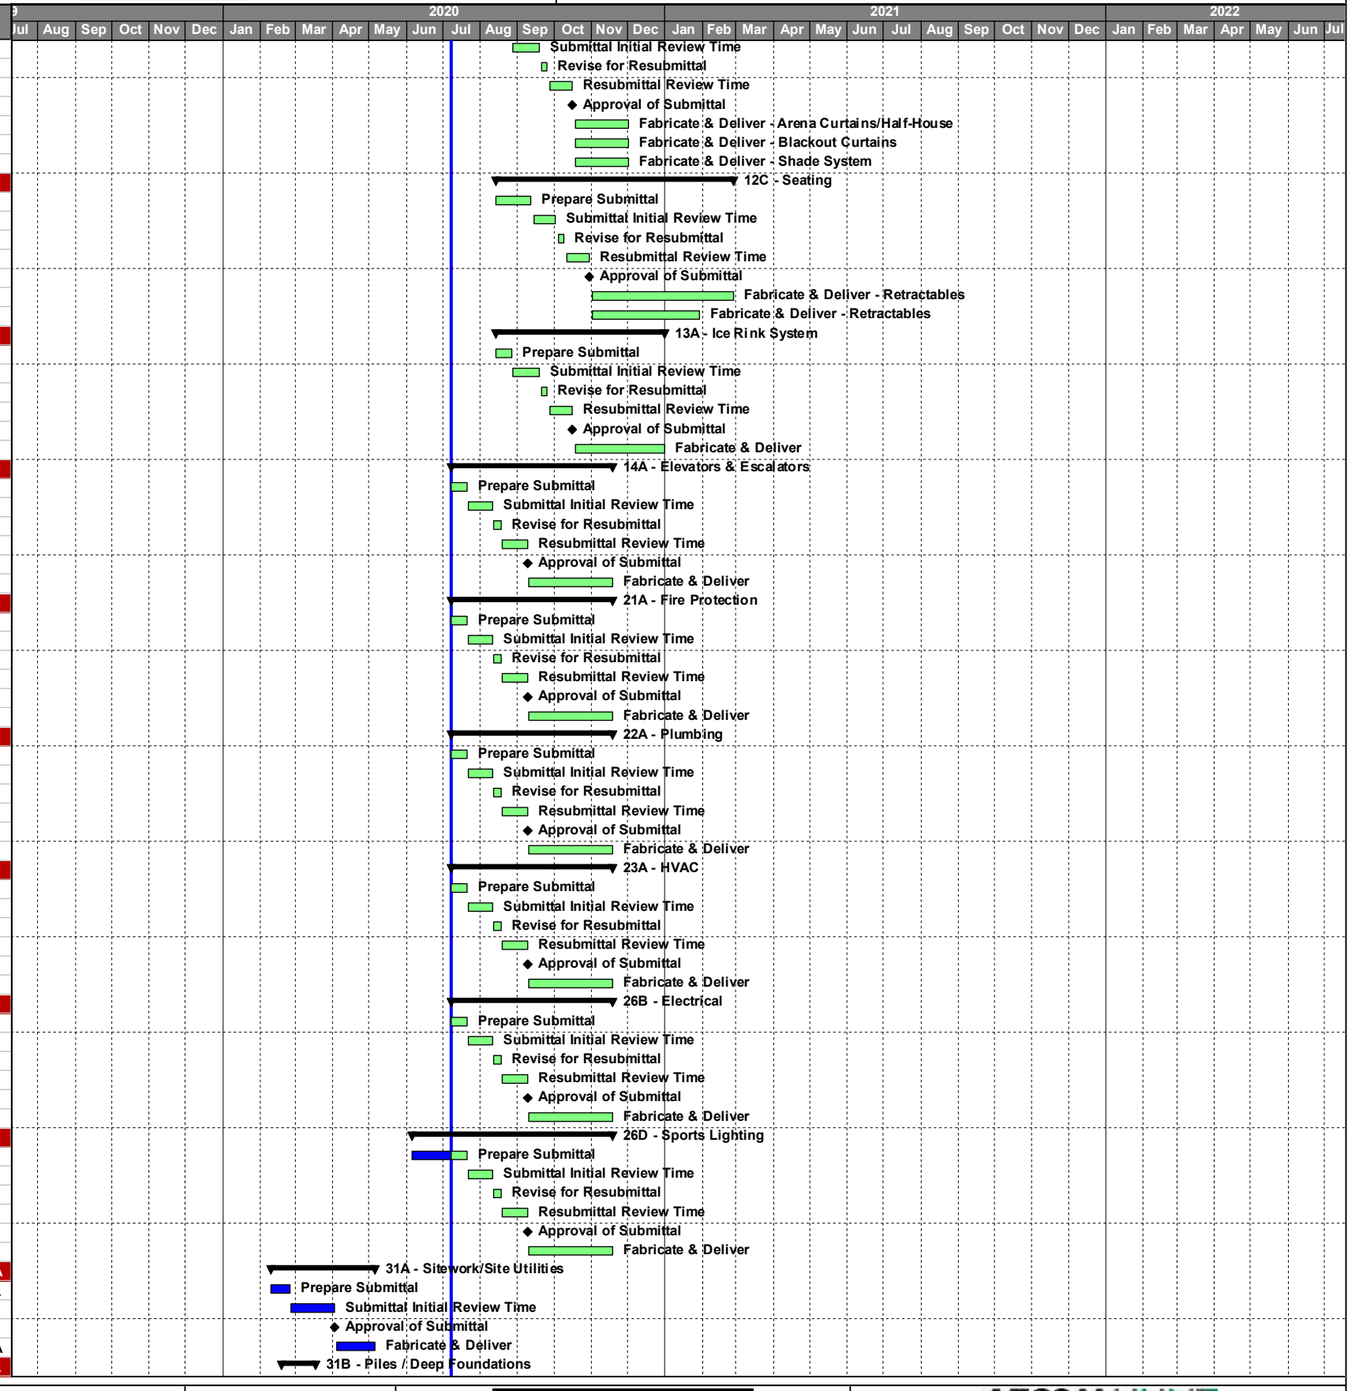


Remaining Level of Effort | Remainin...
Actual Level of Effort | Critical R...
Actual Work | Milestone



AECOM HUNT
in association with
Brownstone Construction Group
Pat Mathis Construction Company
A. Riley Consultants

Project: Savannah Arena | **Update - 08-Jul-20** | Date: 09-Jul-20 Time: 11:57

| Activity ID | Activity Name | Original Duration | Remaining Duration | Start | Finish |
|---|---|---|---|---|---|
| A5990 | Prepare Submittal | 10 | 0 | 18-Feb-20 A | 19-Feb-20 A |
| A6000 | Submittal Initial Review Time | 10 | 0 | 19-Feb-20 A | 12-Mar-20 A |
| A6030 | Approval of Submittal | 0 | 0 | | 12-Mar-20 A |
| A6040 | Fabricate & Deliver | 10 | 0 | 13-Mar-20 A | 17-Mar-20 A |
| 31C - Stiles Ave Widening | | 95 | 95 | 08-Jul-20 | 18-Nov-20 |
| A5930 | Prepare Submittal | 10 | 10 | 08-Jul-20 | 21-Jul-20 |
| A5940 | Submittal Initial Review Time | 15 | 15 | 22-Jul-20 | 11-Aug-20 |
| A5950 | Revise for Resubmittal | 5 | 5 | 12-Aug-20 | 18-Aug-20 |
| A5960 | Resubmittal Review Time | 15 | 15 | 19-Aug-20 | 09-Sep-20 |
| A5970 | Approval of Submittal | 0 | 0 | | 09-Sep-20 |
| A5980 | Fabricate & Deliver | 50 | 50 | 10-Sep-20 | 18-Nov-20 |
| 32A - Landscape | | 95 | 95 | 08-Jul-20 | 18-Nov-20 |
| A32630 | Prepare Submittal | 10 | 10 | 08-Jul-20 | 21-Jul-20 |
| A32640 | Submittal Initial Review Time | 15 | 15 | 22-Jul-20 | 11-Aug-20 |
| A32650 | Revise for Resubmittal | 5 | 5 | 12-Aug-20 | 18-Aug-20 |
| A32660 | Resubmittal Review Time | 15 | 15 | 19-Aug-20 | 09-Sep-20 |
| A32670 | Approval of Submittal | 0 | 0 | | 09-Sep-20 |
| A32680 | Fabricate & Deliver - Escofet Bollards/Benches | 50 | 50 | 10-Sep-20 | 18-Nov-20 |
| A32690 | Fabricate & Deliver - Waste Receptacles | 25 | 25 | 10-Sep-20 | 14-Oct-20 |
| A32700 | Fabricate & Deliver - Bike Racks | 40 | 40 | 10-Sep-20 | 04-Nov-20 |
| A32710 | Fabricate & Deliver - Blue Valley Benches | 30 | 30 | 10-Sep-20 | 21-Oct-20 |
| A32720 | Fabricate & Deliver - Tree Grates | 20 | 20 | 10-Sep-20 | 07-Oct-20 |
| 35A - Canal Widening | | 95 | 95 | 08-Jul-20 | 18-Nov-20 |
| A5870 | Prepare Submittal | 10 | 10 | 08-Jul-20 | 21-Jul-20 |
| A5880 | Submittal Initial Review Time | 15 | 15 | 22-Jul-20 | 11-Aug-20 |
| A5890 | Revise for Resubmittal | 5 | 5 | 12-Aug-20 | 18-Aug-20 |
| A5900 | Resubmittal Review Time | 15 | 15 | 19-Aug-20 | 09-Sep-20 |
| A5910 | Approval of Submittal | 0 | 0 | | 09-Sep-20 |
| A5920 | Fabricate & Deliver | 50 | 50 | 10-Sep-20 | 18-Nov-20 |
| Construction | | 508 | 368 | 23-Dec-19 A | 20-Dec-21 |
| MEP Coordination | | 114 | 114 | 14-Jul-20 | 23-Dec-20 |
| Below Grade | | 20 | 20 | 14-Jul-20 | 10-Aug-20 |
| MEPCO-BG-1000 | Below Grade - MEPFP Coordination - Quad 1 | 10 | 10 | 14-Jul-20 | 27-Jul-20 |
| MEPCO-BG-1010 | Below Grade - MEPFP Coordination - Quad 2 | 10 | 10 | 14-Jul-20 | 27-Jul-20 |
| MEPCO-BG-1020 | Below Grade - MEPFP Coordination - Quad 3 | 10 | 10 | 28-Jul-20 | 10-Aug-20 |
| MEPCO-BG-1030 | Below Grade - MEPFP Coordination - Quad 4 | 10 | 10 | 28-Jul-20 | 10-Aug-20 |
| Suite Level | | 10 | 10 | 11-Aug-20 | 24-Aug-20 |
| MEPCO-SL-1000 | Suite Level - MEPFP Coordination - Quad 1 | 10 | 10 | 11-Aug-20 | 24-Aug-20 |
| MEPCO-SL-1010 | Suite Level - MEPFP Coordination - Quad 2 | 10 | 10 | 11-Aug-20 | 24-Aug-20 |
| Concourse Level | | 24 | 24 | 25-Aug-20 | 28-Sep-20 |
| MEPCO-CL-1000 | Concourse Level - MEPFP Coordination - Quad 1 | 15 | 15 | 25-Aug-20 | 15-Sep-20 |
| MEPCO-CL-1010 | Concourse Level - MEPFP Coordination - Quad 2 | 15 | 15 | 25-Aug-20 | 15-Sep-20 |
| MEPCO-CL-1030 | Concourse Level - MEPFP Coordination - Quad 3 | 10 | 10 | 15-Sep-20 | 28-Sep-20 |
| MEPCO-CL-1050 | Concourse Level - MEPFP Coordination - Quad 4 | 10 | 10 | 15-Sep-20 | 28-Sep-20 |
| Event Level | | 30 | 30 | 29-Sep-20 | 09-Nov-20 |
| MEPCO-EL-1000 | Event Level - MEPFP Coordination - Quad 1 | 15 | 15 | 29-Sep-20 | 19-Oct-20 |
| MEPCO-EL-1010 | Event Level - MEPFP Coordination - Quad 2 | 15 | 15 | 29-Sep-20 | 19-Oct-20 |
| MEPCO-EL-1030 | Event Level - MEPFP Coordination - Quad 3 | 15 | 15 | 20-Oct-20 | 09-Nov-20 |
| MEPCO-EL-1050 | Event Level - MEPFP Coordination - Quad 4 | 15 | 15 | 20-Oct-20 | 09-Nov-20 |
| Overlook Level | | 10 | 10 | 10-Nov-20 | 23-Nov-20 |
| MEPCO-OL-1000 | Overlook Level - MEPFP Coordination - Quad 1 | 10 | 10 | 10-Nov-20 | 23-Nov-20 |
| MEPCO-OL-1010 | Overlook Level - MEPFP Coordination - Quad 2 | 10 | 10 | 10-Nov-20 | 23-Nov-20 |
| MEPCO-OL-1030 | Overlook Level - MEPFP Coordination - Quad 3 | 10 | 10 | 10-Nov-20 | 23-Nov-20 |
| MEPCO-OL-1050 | Overlook Level - MEPFP Coordination - Quad 4 | 10 | 10 | 10-Nov-20 | 23-Nov-20 |
| Bowl | | 20 | 20 | 24-Nov-20 | 23-Dec-20 |
| MEPCO-BL-1000 | Bowl - Catwalk Area - MEPFP Coordination - Quad 1 | 10 | 10 | 24-Nov-20 | 09-Dec-20 |
| MEPCO-BL-1020 | Bowl - Catwalk Area - MEPFP Coordination - Quad 2 | 10 | 10 | 24-Nov-20 | 09-Dec-20 |
| MEPCO-BL-1010 | Bowl - Catwalk Area - MEPFP Coordination - Quad 3 | 10 | 10 | 10-Dec-20 | 23-Dec-20 |
| MEPCO-BL-1030 | Bowl - Catwalk Area - MEPFP Coordination - Quad 4 | 10 | 10 | 10-Dec-20 | 23-Dec-20 |
| Initial Site Work | | 207 | 54 | 23-Dec-19 A | 22-Sep-20 |
| Site | | 97 | 0 | 23-Dec-19 A | 08-May-20 A |
| A1710 | Demolition | 30 | 0 | 23-Dec-19 A | 06-Feb-20 A |
| A7200 | Site Clearing | 30 | 0 | 23-Dec-19 A | 07-Feb-20 A |
| A1990 | Initial Erosion Control | 15 | 0 | 14-Jan-20 A | 21-Feb-20 A |
| A1980 | Site Fence | 15 | 0 | 28-Jan-20 A | 18-Feb-20 A |
| A1720 | Building Pad for Piles | 30 | 0 | 21-Feb-20 A | 26-Mar-20 A |
| PCI-00036-01 | Unforeseen Condition - Concrete & Washout Obstruction along Canal | 5 | 0 | 20-Mar-20 A | 25-Mar-20 A |
| A1780 | Undercut/Backfill/Grade Hardscape | 31 | 0 | 30-Mar-20 A | 08-May-20 A |
| Sanitary | | 121 | 38 | 12-Mar-20 A | 28-Aug-20 |
| PCI-00033-01 | Unforeseen Condition - Potential Contaminated Soils | 5 | 0 | 12-Mar-20 A | 12-Jun-20 A |

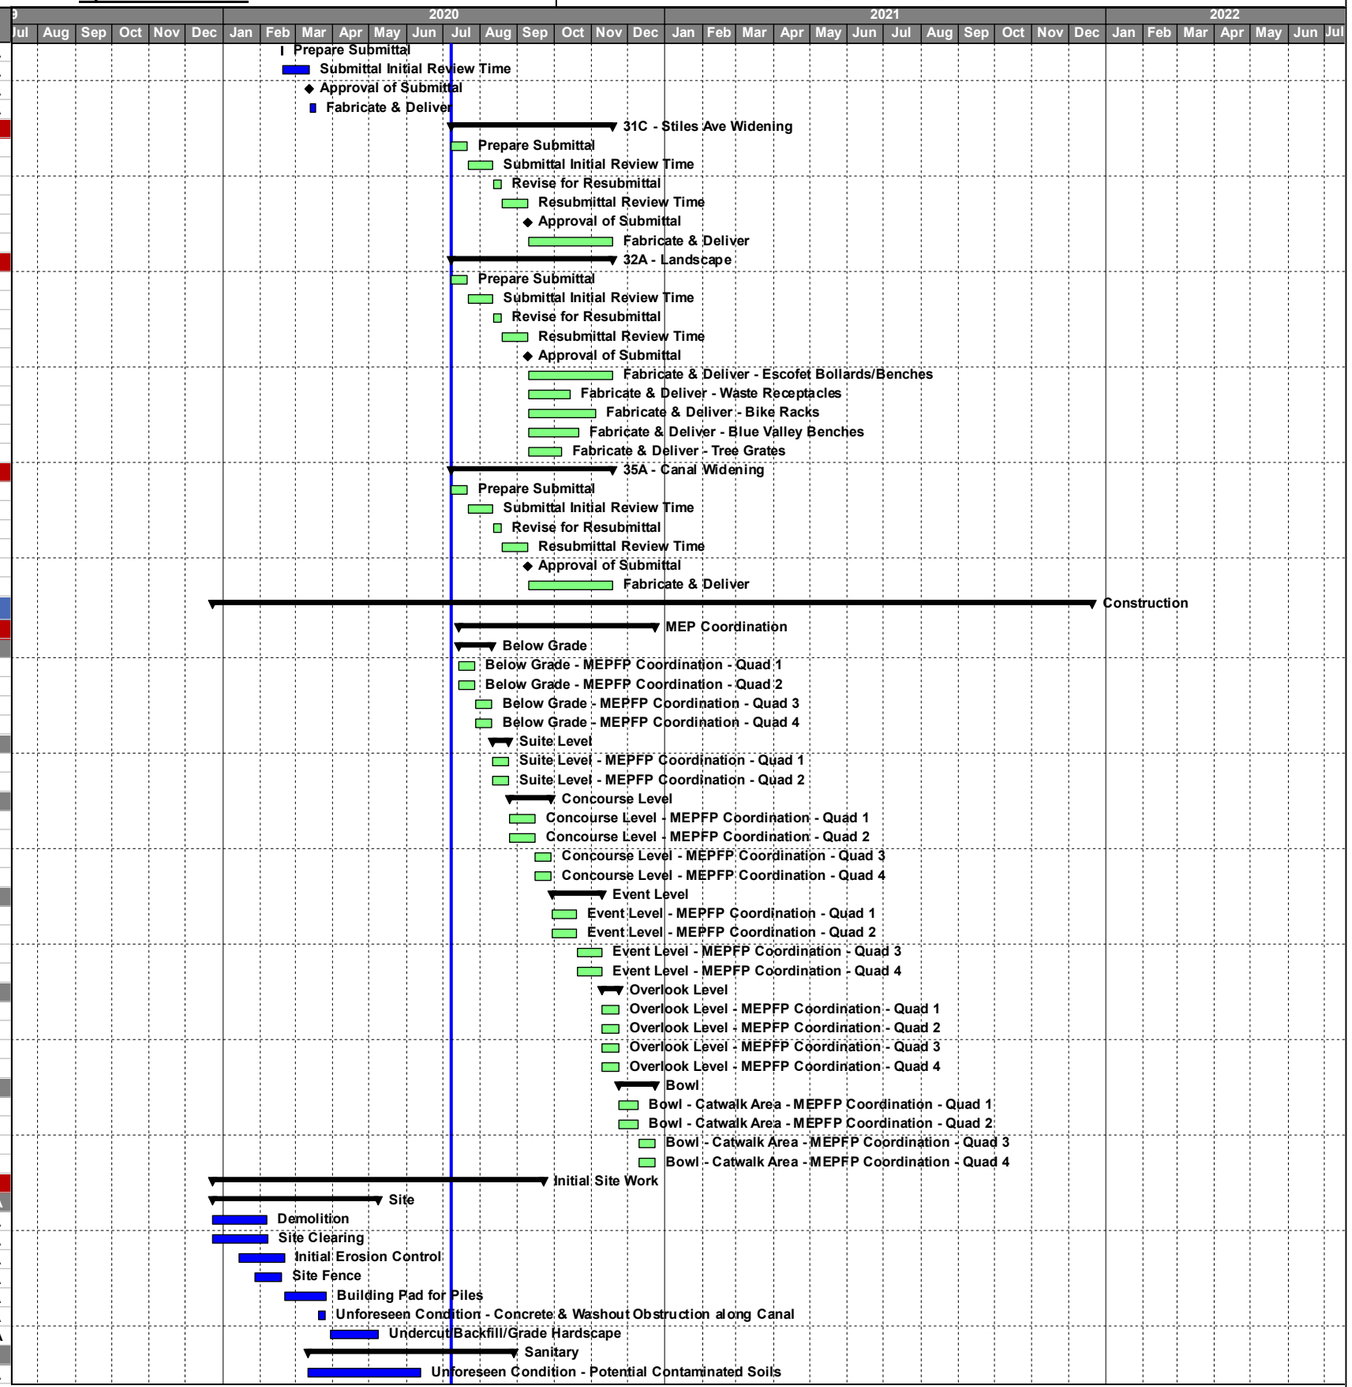


Remaining Level of Effort | Remainin...
Actual Level of Effort | Critical R...
Actual Work | Milestone

**Savannah Arena**
**Current Data Date: 08-Jul-20**



AECOM HUNT
in association with
Brownstone Construction Group
Pat Mathis Construction Company
A. Riley Consultants

| Activity ID | Activity Name | Original Duration | Remaining Duration | Start | Finish |
|---|---|---|---|---|---|
| A2000 | City of Savannah Kick-off Meeting - Site Utilities | 1 | 0 | 03-Apr-20 A | 03-Apr-20 A |
| A1850 | Install Sanitary Manhole 2 to Manhole 4 | 17 | 0 | 06-Apr-20 A | 15-May-20 A |
| A1840 | Install Sanitary Manhole 5 to Manhole 2 | 11 | 3 | 19-May-20 A | 10-Jul-20 |
| A2040 | CA Murren COVID Impact | 5 | 0 | 24-Jun-20 A | 06-Jul-20 A |
| A1830 | Install Sanitary Manhole 6 to Manhole 2 | 22 | 22 | 13-Jul-20 | 11-Aug-20 |
| A1860 | Install Grease Interceptor | 13 | 13 | 12-Aug-20 | 28-Aug-20 |
| Stormwater | | 51 | 51 | 13-Jul-20 | 22-Sep-20 |
| A1950 | Install Stormwater Piping, DI4, MH 7 & 8 | 8 | 8 | 13-Jul-20 | 22-Jul-20 |
| A1960 | Install Stormwater Piping, DI1-3, MH6-1 | 9 | 9 | 23-Jul-20 | 04-Aug-20 |
| A1970 | Install Stormwater Piping, DI6-11, MH9 | 7 | 7 | 05-Aug-20 | 13-Aug-20 |
| A1870 | Excavate for Stormwater Detention | 5 | 5 | 20-Aug-20* | 26-Aug-20 |
| A1880 | Support of Excavation | 5 | 5 | 21-Aug-20 | 27-Aug-20 |
| A1890 | Bottom of Stone | 2 | 2 | 28-Aug-20 | 31-Aug-20 |
| A1900 | Install Chamber Systems | 7 | 7 | 01-Sep-20 | 10-Sep-20 |
| A1910 | Backfill Stone | 5 | 5 | 08-Sep-20 | 14-Sep-20 |
| A1920 | Install Geotextile Fabric | 5 | 5 | 09-Sep-20 | 15-Sep-20 |
| A1930 | Initial Backfill | 3 | 3 | 15-Sep-20 | 17-Sep-20 |
| A1940 | Final Backfill | 3 | 3 | 18-Sep-20 | 22-Sep-20 |
| Domestic Water | | 63 | 10 | 30-Mar-20 A | 21-Jul-20 |
| A1820 | Install 12" Water Line & Hydrant - North | 16 | 0 | 30-Mar-20 A | 09-Jun-20 A |
| A1800 | Install 12" Water Line & Hydrant - South | 4 | 4 | 28-May-20 A | 13-Jul-20 |
| A1810 | Install 12" Water Line & Hydrant - East/Canal | 6 | 6 | 14-Jul-20 | 21-Jul-20 |
| Arena | | 463 | 368 | 25-Feb-20 A | 20-Dec-21 |
| Foundations | | 133 | 38 | 25-Feb-20 A | 28-Aug-20 |
| Deep Foundations | | 100 | 5 | 25-Feb-20 A | 14-Jul-20 |
| A1730 | Mobilize/Test Pile Program | 20 | 0 | 25-Feb-20 A | 18-Mar-20 A |
| A1430 | Deep Foundations - Group 1 (157) | 10 | 0 | 19-Mar-20 A | 30-Mar-20 A |
| A2930 | Deep Foundations - Group 2 (157) | 10 | 0 | 30-Mar-20 A | 06-Apr-20 A |
| A2940 | Deep Foundations - Group 3 (157) | 10 | 0 | 07-Apr-20 A | 17-Apr-20 A |
| A2950 | Deep Foundations - Group 4 (157) | 10 | 0 | 20-Apr-20 A | 27-Apr-20 A |
| A2980 | Ice Rink Piles (101) | 10 | 0 | 28-Apr-20 A | 01-May-20 A |
| A2990 | Cut/Chip Piles - Quad 1 | 10 | 0 | 29-Apr-20 A | 28-May-20 A |
| A3000 | Cut/Chip Piles - Quad 2 | 10 | 0 | 14-May-20 A | 10-Jun-20 A |
| A3010 | Cut/Chip Piles - Quad 3 | 10 | 0 | 11-Jun-20 A | 24-Jun-20 A |
| A3020 | Cut/Chip Piles - Quad 4 | 10 | 0 | 18-Jun-20 A | 01-Jul-20 A |
| A3030 | Cut/Chip Piles - Ice Rink | 5 | 5 | 08-Jul-20 | 14-Jul-20 |
| Pile Caps & Grade Beams | | 93 | 38 | 20-Apr-20 A | 28-Aug-20 |
| A2960 | Prep Piles for Cut/Chip - Quad 1 | 2 | 0 | 20-Apr-20 A | 21-Apr-20 A |
| FND-100 | Pile Caps & Grade Beams - Quad 1 (14) | 10 | 0 | 04-May-20 A | 18-May-20 A |
| A2970 | Prep Piles for Cut/Chip - Quad 2 | 5 | 0 | 13-May-20 A | 20-May-20 A |
| FND-110 | Pile Caps & Grade Beams - Quad 1 (13) | 10 | 0 | 18-May-20 A | 11-Jun-20 A |
| A3180 | Prep Piles for Cut/Chip- Quad 3 | 5 | 0 | 02-Jun-20 A | 12-Jun-20 A |
| FND-120 | Pile Caps & Grade Beams - Quad 2 - (20) | 13 | 0 | 10-Jun-20 A | 25-Jun-20 A |
| A3190 | Prep Piles for Cut/Chip - Quad 4 | 5 | 0 | 17-Jun-20 A | 02-Jul-20 A |
| FND-130 | Pile Caps & Grade Beams - Quad 2 - (20) | 12 | 0 | 22-Jun-20 A | 15-Jul-20 |
| FND-140 | Pile Caps & Grade Beams - Quad 3 - (25) | 13 | 6 | 29-Jun-20 A | 15-Jul-20 |
| FND-150 | Pile Caps & Grade Beams - Quad 3 - (25) | 12 | 12 | 16-Jul-20 | 31-Jul-20 |
| FND-160 | Pile Caps & Grade Beams - Quad 4 - (19) | 10 | 10 | 03-Aug-20 | 14-Aug-20 |
| FND-170 | Pile Caps & Grade Beams - Quad 4 - (19) | 10 | 10 | 17-Aug-20 | 28-Aug-20 |
| Steel | | 153 | 153 | 03-Aug-20 | 10-Mar-21 |
| Savannah Arena Baseline - Steel | | 153 | 153 | 03-Aug-20 | 10-Mar-21 |
| Mobilization | | 92 | 92 | 03-Aug-20 | 14-Dec-20 |
| PRECON-1000 | Survey Anchor Bolts | 10 | 10 | 03-Aug-20 | 14-Aug-20 |
| MOB-1000 | DIC Mobilize to Site | 1 | 1 | 03-Aug-20* | 03-Aug-20 |
| DICMOB1000 | Mobilize Crane 1 | 0 | 0 | 12-Aug-20 | |
| DICMOB1010 | Mobilize Crane 2 | 0 | 0 | 14-Dec-20* | |
| Construction | | 142 | 142 | 18-Aug-20 | 10-Mar-21 |
| 05100 Steel Erection | | 137 | 137 | 18-Aug-20 | 03-Mar-21 |
| Bowl | | 66 | 66 | 18-Aug-20 | 18-Nov-20 |
| Crane 1 | | 66 | 66 | 18-Aug-20 | 18-Nov-20 |
| CR1ERSTL1 | Erect Steel with Crane 1 - First Tier - Seq 101 | 5 | 5 | 18-Aug-20 | 24-Aug-20 |
| CR1ERSTL1 | Erect Steel with Crane 1 - First Tier - Seq 102 | 6 | 6 | 25-Aug-20 | 01-Sep-20 |
| CR1ERSTL1 | Erect Steel with Crane 1 - First Tier - Seq 103 | 6 | 6 | 02-Sep-20 | 10-Sep-20 |
| CR1ERSTL1 | Erect Steel with Crane 1 - First Tier - Seq 104 | 5 | 5 | 11-Sep-20 | 17-Sep-20 |
| CR1ERSTL1 | Erect Steel with Crane 1 - First Tier - Seq 105 | 4 | 4 | 18-Sep-20 | 23-Sep-20 |
| CR1ERSTL1 | Erect Steel with Crane 1 - First Tier - Seq 106 | 6 | 6 | 24-Sep-20 | 01-Oct-20 |
| CR1ERSTL1 | Erect Steel with Crane 1 - First Tier - Seq 107 | 6 | 6 | 02-Oct-20 | 09-Oct-20 |
| CR1ERSTL1 | Erect Steel with Crane 1 - First Tier - Seq 108 | 5 | 5 | 12-Oct-20 | 16-Oct-20 |
| CR1ERSTL1 | Erect Steel with Crane 1 - First Tier - Seq 109 | 6 | 6 | 19-Oct-20 | 26-Oct-20 |
| CR1ERSTL2 | Erect Steel with Crane 1 - 2nd Tier - Seq 201 | 4 | 4 | 27-Oct-20 | 30-Oct-20 |



| Activity ID | Activity Name | Original Duration | Remaining Duration | Start | Finish |
|---|---|---|---|---|---|
| CR1ERSTL2 | Erect Steel with Crane 1 - 2nd Tier - Seq 202 | 5 | 5 | 02-Nov-20 | 06-Nov-20 |
| CR1ERSTL2 | Erect Steel with Crane 1 - 2nd Tier - Seq 204 | 4 | 4 | 09-Nov-20 | 12-Nov-20 |
| CR1ERSTL2 | Erect Steel with Crane 1 - 2nd Tier - Seq 205 | 4 | 4 | 13-Nov-20 | 18-Nov-20 |
| Roof | | 71 | 71 | 19-Nov-20 | 03-Mar-21 |
| Erect and Move Shoring Towers | | 20 | 20 | 19-Nov-20 | 18-Dec-20 |
| Crane 1 | | 20 | 20 | 19-Nov-20 | 18-Dec-20 |
| CR1ERSHT | Erect Shoring Tower on Grid E4 with Crane 1 | 1 | 1 | 19-Nov-20 | 19-Nov-20 |
| CR1ERSHT | Erect Shoring Tower on Grid E3 with Crane 1 | 1 | 1 | 19-Nov-20 | 19-Nov-20 |
| CR1ERSHT | Erect Shoring Tower on Grid E2 with Crane 1 | 1 | 1 | 19-Nov-20 | 19-Nov-20 |
| CR1ERSHT | Move and Erect Shoring Tower on Grid E4 to Grid E1 with Crane 1 | 1 | 1 | 08-Dec-20 | 08-Dec-20 |
| CR1ERSHT | Move and Erect Shoring Tower on Grid E3 to Grid W1 with Crane 1 | 1 | 1 | 08-Dec-20 | 08-Dec-20 |
| CR1ERSHT | Move and Erect Shoring Tower on Grid E2 to Grid W2 with Crane 1 | 1 | 1 | 10-Dec-20 | 10-Dec-20 |
| CR1ERSHT | Move and Erect Shoring Tower on Grid E1 to Grid W3 with Crane 1 | 1 | 1 | 18-Dec-20 | 18-Dec-20 |
| Deshore Shoring Towers | | 40 | 40 | 07-Dec-20 | 02-Feb-21 |
| Crane 1 | | 40 | 40 | 07-Dec-20 | 02-Feb-21 |
| CR1DISSH1 | Deshore Shoring Tower on Grid E4 with Crane 1 | 1 | 1 | 07-Dec-20 | 07-Dec-20 |
| CR1DISSH1 | Deshore Shoring Tower on Grid E3 with Crane 1 | 1 | 1 | 07-Dec-20 | 07-Dec-20 |
| CR1DISSH1 | Deshore Shoring Tower on Grid E2 with Crane 1 | 1 | 1 | 09-Dec-20 | 09-Dec-20 |
| CR1DISSH1 | Deshore Shoring Tower on Grid E1 with Crane 1 | 1 | 1 | 17-Dec-20 | 17-Dec-20 |
| CR1DISSH1 | Deshore Shoring Tower on Grid W1 with Crane 1 | 1 | 1 | 18-Jan-21 | 18-Jan-21 |
| CR1DISSH1 | Deshore Shoring Tower on Grid W2 with Crane 1 | 1 | 1 | 18-Jan-21 | 18-Jan-21 |
| CR1DESHS | Deshore Shoring Tower on Grid W3 with Crane 1 | 1 | 1 | 02-Feb-21 | 02-Feb-21 |
| Bolt Up with Crane 1 | | 29 | 29 | 30-Nov-20 | 11-Jan-21 |
| CR1BLTSTL | Bolt Up of Sequences 301 thru 306 in order to deshore with Crane 1 | 5 | 5 | 30-Nov-20 | 04-Dec-20 |
| CR1BLTSTL | Bolt Up of Sequences 309 thru 310 in order to deshore with Crane 1 | 4 | 4 | 03-Dec-20 | 08-Dec-20 |
| CR1BLTSTL | Bolt Up of Sequences 313 thru 314 in order to deshore with Crane 1 | 4 | 4 | 11-Dec-20 | 16-Dec-20 |
| CR1BLTSTL | Bolt Up of Sequences 317 thru 318 in order to deshore with Crane 1 | 4 | 4 | 21-Dec-20 | 24-Dec-20 |
| CR1BLTSTL | Bolt Up of Sequences 321 thru 322 in order to deshore with Crane 1 | 4 | 4 | 29-Dec-20 | 04-Jan-21 |
| CR1BLTSTL | Bolt Up of Sequences 325 thru 326 in order to deshore with Crane 1 | 4 | 4 | 06-Jan-21 | 11-Jan-21 |
| Installation of Roof Trusses | | 70 | 70 | 20-Nov-20 | 03-Mar-21 |
| Crane 1 | | 70 | 70 | 20-Nov-20 | 03-Mar-21 |
| CR2ERSTL | Erect Steel with Crane 1 - Roof Infill - Seq 301, 303, 305 | 2 | 2 | 20-Nov-20 | 23-Nov-20 |
| CR2ERSTL | Erect Steel with Crane 1 - Roof Infill- Seq 302, 304, 306 | 2 | 2 | 24-Nov-20 | 25-Nov-20 |
| CR2ERSTL | Erect Steel with Crane 1 - Roof Truss - Seq 307 | 1 | 1 | 30-Nov-20 | 30-Nov-20 |
| CR2ERSTL | Erect Steel with Crane 1 - Roof Truss - Seq 309 | 1 | 1 | 01-Dec-20 | 01-Dec-20 |
| CR2ERSTL | Erect Steel with Crane 1 - Roof Truss - Seq 310 | 1 | 1 | 02-Dec-20 | 02-Dec-20 |
| CR2ERSTL | Erect Steel with Crane 1 - Roof Infill - Seq 311 | 2 | 2 | 03-Dec-20 | 04-Dec-20 |
| CR2ERSTL | Erect Steel with Crane 1 - Roof Infill - Seq 312 | 1 | 1 | 07-Dec-20 | 07-Dec-20 |
| CR2ERSTL | Erect Steel with Crane 1 - Roof Truss - Seq 313 | 1 | 1 | 09-Dec-20 | 09-Dec-20 |
| CR2ERSTL | Erect Steel with Crane 1 - Roof Truss - Seq 314 | 1 | 1 | 10-Dec-20 | 10-Dec-20 |
| CR2ERSTL | Erect Steel with Crane 1 - Roof Infill - Seq 315 | 3 | 3 | 11-Dec-20 | 15-Dec-20 |
| CR2ERSTL | Erect Steel with Crane 1 - Roof Infill - Seq 316 | 1 | 1 | 16-Dec-20 | 16-Dec-20 |
| CR2ERSTL | Erect Steel with Crane 1 - Roof Truss - Seq 317 | 1 | 1 | 17-Dec-20 | 17-Dec-20 |
| CR2ERSTL | Erect Steel with Crane 1 - Roof Truss - Seq 318 | 1 | 1 | 18-Dec-20 | 18-Dec-20 |
| CR2ERSTL | Erect Steel with Crane 1 - Roof Infill - Seq 319 | 2 | 2 | 21-Dec-20 | 22-Dec-20 |
| CR2ERSTL | Erect Steel with Crane 1 - Roof Infill - Seq 320 | 1 | 1 | 23-Dec-20 | 23-Dec-20 |
| CR2ERSTL | Erect Steel with Crane 1 - Roof Truss - Seq 321 | 1 | 1 | 24-Dec-20 | 24-Dec-20 |
| CR2ERSTL | Erect Steel with Crane 1 - Roof Truss - Seq 322 | 1 | 1 | 28-Dec-20 | 28-Dec-20 |
| CR2ERSTL | Erect Steel with Crane 1 - Roof Infill - Seq 323 | 2 | 2 | 29-Dec-20 | 30-Dec-20 |
| CR2ERSTL | Erect Steel with Crane 1 - Roof Infill - Seq 324 | 1 | 1 | 31-Dec-20 | 31-Dec-20 |
| CR2ERSTL | Erect Steel with Crane 1 - Roof Truss - Seq 325 | 1 | 1 | 04-Jan-21 | 04-Jan-21 |
| CR2ERSTL | Erect Steel with Crane 1 - Roof Truss - Seq 326 | 1 | 1 | 05-Jan-21 | 05-Jan-21 |
| CR2ERSTL | Erect Steel with Crane 1 - Roof Infill - Seq 327 | 2 | 2 | 06-Jan-21 | 07-Jan-21 |
| CR2ERSTL | Erect Steel with Crane 1 - Roof Infill - Seq 328 | 2 | 2 | 08-Jan-21 | 11-Jan-21 |
| CR1ERSTL | Erect Steel with Crane 1 - First Tier - Seq 110 | 1 | 1 | 12-Jan-21 | 12-Jan-21 |
| CR2ERSTL | Erect Steel with Crane 1 - Roof Truss - Seq 329 | 1 | 1 | 13-Jan-21 | 13-Jan-21 |
| CR2ERSTL | Erect Steel with Crane 1 - Roof Infill - Seq 330 | 4 | 4 | 14-Jan-21 | 19-Jan-21 |
| CR1ERSTL | Erect Steel with Crane 1 - 2nd Tier - Seq 206 | 7 | 7 | 20-Jan-21 | 28-Jan-21 |
| CR1ERSTL | Erect Steel with Crane 1 - 2nd Tier - Seq 207 | 4 | 4 | 29-Jan-21 | 03-Feb-21 |
| CR1ERSTL | Erect Steel Quadrant with Crane 1 - Seq 401 | 1 | 1 | 04-Feb-21 | 04-Feb-21 |
| CR1ERSTL | Erect Steel Quadrant with Crane 1 - Seq 404 | 3 | 3 | 05-Feb-21 | 09-Feb-21 |
| CR2ERSTL | Erect Steel with Crane 1 - Cooling Tower - Seq 501 | 1 | 1 | 03-Mar-21 | 03-Mar-21 |
| Crane 2 | | 12 | 12 | 15-Dec-20 | 31-Dec-20 |
| CR2ERSTL | Erect Steel with Crane 2 - Roof Infill - Seq 308 | 3 | 3 | 15-Dec-20 | 17-Dec-20 |
| CR2ERSTL | Erect Steel with Crane 2 - 2nd Tier - Seq 203 | 4 | 4 | 18-Dec-20 | 23-Dec-20 |
| CR2ERSTL | Erect Steel Quadrant with Crane 2 - Seq 402 | 1 | 1 | 28-Dec-20 | 28-Dec-20 |
| CR2ERSTL | Erect Steel Quadrant with Crane 2 - Seq 403 | 3 | 3 | 29-Dec-20 | 31-Dec-20 |
| Detail and Deck Steel | | 137 | 137 | 25-Aug-20 | 10-Mar-21 |
| Crane 1 | | 137 | 137 | 25-Aug-20 | 10-Mar-21 |
| CR1DETSTL' | Detail and Deck Steel with Crane 1 - 1st Tier Seq 101 | 15 | 15 | 25-Aug-20 | 15-Sep-20 |

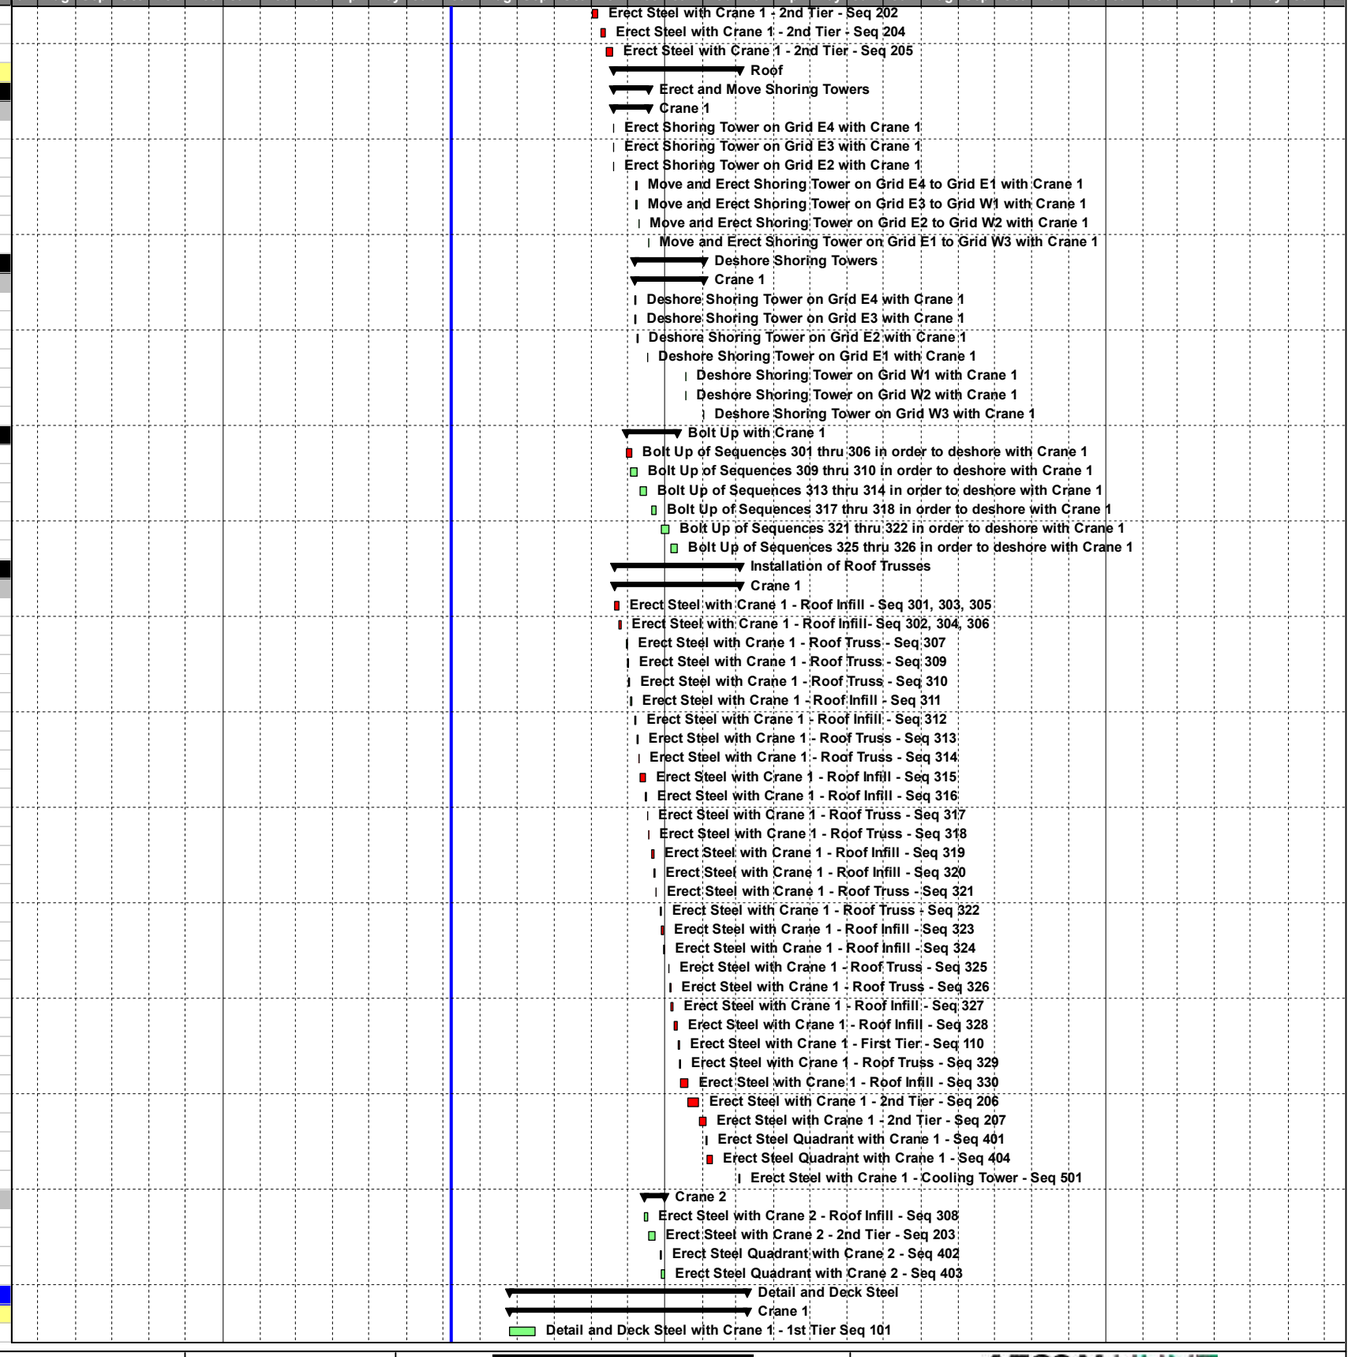

| Activity ID | Activity Name | Original Duration | Remaining Duration | Start | Finish |
|---|---|---|---|---|---|
| CR1DETSTL' | Detail and Deck Steel with Crane 1 - 1st Tier Seq 102 | 18 | 18 | 28-Aug-20 | 23-Sep-20 |
| CR1DETSTL' | Detail and Deck Steel with Crane 1 - 1st Tier Seq 103 | 18 | 18 | 08-Sep-20 | 01-Oct-20 |
| CR1DETSTL' | Detail and Deck Steel with Crane 1 - 1st Tier Seq 104 | 15 | 15 | 18-Sep-20 | 08-Oct-20 |
| CR1DETSTL' | Detail and Deck Steel with Crane 1 - 1st Tier Seq 105 | 12 | 12 | 29-Sep-20 | 14-Oct-20 |
| CR1DETSTL' | Detail and Deck Steel with Crane 1 - 1st Tier Seq 106 | 18 | 18 | 29-Sep-20 | 22-Oct-20 |
| CR1DETSTL' | Detail and Deck Steel with Crane 1 - 1st Tier Seq 107 | 18 | 18 | 07-Oct-20 | 30-Oct-20 |
| CR1DETSTL' | Detail and Deck Steel with Crane 1 - 1st Tier Seq 108 | 15 | 15 | 19-Oct-20 | 06-Nov-20 |
| CR1DETSTL' | Detail and Deck Steel with Crane 1 - 1st Tier Seq 109 | 18 | 18 | 22-Oct-20 | 16-Nov-20 |
| CR1DETSTL: | Detail and Deck Steel with Crane 1 - 2nd Tier Seq 201 | 12 | 12 | 05-Nov-20 | 20-Nov-20 |
| CR1DETSTL: | Detail and Deck Steel with Crane 1 - 2nd Tier Seq 202 | 15 | 15 | 09-Nov-20 | 01-Dec-20 |
| CR1DETSTL: | Detail and Deck Steel with Crane 1 - 2nd Tier Seq 204 | 12 | 12 | 18-Nov-20 | 07-Dec-20 |
| CR1DETSTL: | Detail and Deck Steel with Crane 1 - 2nd Tier Seq 205 | 12 | 12 | 24-Nov-20 | 11-Dec-20 |
| CR1DETSTL: | Detail and Deck Steel with Crane 1 - Roof Seq 301, 303, 305 | 12 | 12 | 02-Dec-20 | 17-Dec-20 |
| CR1DETSTL: | Detail and Deck Steel with Crane 1 - Roof Seq 302, 304, 306 | 12 | 12 | 03-Dec-20 | 18-Dec-20 |
| CR1DETSTL: | Detail and Deck Steel with Crane 1 - Roof Seq 307 | 3 | 3 | 17-Dec-20 | 21-Dec-20 |
| CR1DETSTL: | Detail and Deck Steel with Crane 1 - Roof Seq 309 | 4 | 4 | 17-Dec-20 | 22-Dec-20 |
| CR1DETSTL: | Detail and Deck Steel with Crane 1 - Roof Seq 311 | 6 | 6 | 18-Dec-20 | 28-Dec-20 |
| CR1DETSTL: | Detail and Deck Steel with Crane 1 - Roof Seq 310 | 3 | 3 | 21-Dec-20 | 23-Dec-20 |
| CR1DETSTL: | Detail and Deck Steel with Crane 1 - Roof Seq 312 | 3 | 3 | 24-Dec-20 | 29-Dec-20 |
| CR1DETSTL: | Detail and Deck Steel with Crane 1 - Roof Seq 315 | 9 | 9 | 24-Dec-20 | 07-Jan-21 |
| CR1DETSTL: | Detail and Deck Steel with Crane 1 - Roof Seq 313 | 3 | 3 | 29-Dec-20 | 31-Dec-20 |
| CR1DETSTL: | Detail and Deck Steel with Crane 1 - Roof Seq 314 | 3 | 3 | 30-Dec-20 | 04-Jan-21 |
| CR1DETSTL: | Detail and Deck Steel with Crane 1 - Roof Seq 316 | 3 | 3 | 06-Jan-21 | 08-Jan-21 |
| CR1DETSTL: | Detail and Deck Steel with Crane 1 - Roof Seq 317 | 3 | 3 | 07-Jan-21 | 11-Jan-21 |
| CR1DETSTL: | Detail and Deck Steel with Crane 1 - Roof Seq 319 | 6 | 6 | 07-Jan-21 | 14-Jan-21 |
| CR1DETSTL: | Detail and Deck Steel with Crane 1 - Roof Seq 318 | 3 | 3 | 08-Jan-21 | 12-Jan-21 |
| CR1DETSTL: | Detail and Deck Steel with Crane 1 - Roof Seq 320 | 3 | 3 | 13-Jan-21 | 15-Jan-21 |
| CR1DETSTL: | Detail and Deck Steel with Crane 1 - Roof Seq 321 | 3 | 3 | 14-Jan-21 | 18-Jan-21 |
| CR1DETSTL: | Detail and Deck Steel with Crane 1 - Roof Seq 323 | 6 | 6 | 14-Jan-21 | 21-Jan-21 |
| CR1DETSTL: | Detail and Deck Steel with Crane 1 - Roof Seq 322 | 3 | 3 | 15-Jan-21 | 19-Jan-21 |
| CR1DETSTL: | Detail and Deck Steel with Crane 1 - Roof Seq 324 | 3 | 3 | 20-Jan-21 | 22-Jan-21 |
| CR1DETSTL: | Detail and Deck Steel with Crane 1 - 2nd Tier Seq 206 | 21 | 21 | 21-Jan-21 | 18-Feb-21 |
| CR1DETSTL: | Detail and Deck Steel with Crane 1 - Roof Seq 325 | 3 | 3 | 21-Jan-21 | 25-Jan-21 |
| CR1DETSTL: | Detail and Deck Steel with Crane 1 - Roof Seq 327 | 6 | 6 | 21-Jan-21 | 28-Jan-21 |
| CR1DETSTL: | Detail and Deck Steel with Crane 1 - Roof Seq 326 | 3 | 3 | 22-Jan-21 | 26-Jan-21 |
| CR1DETSTL: | Detail and Deck Steel with Crane 1 - Roof Seq 328 | 6 | 6 | 25-Jan-21 | 01-Feb-21 |
| CR1DETSTL: | Detail and Deck Steel with Crane 1 - Roof Seq 330 | 12 | 12 | 25-Jan-21 | 09-Feb-21 |
| CR1DETSTL' | Detail and Deck Steel with Crane 1 - 1st Tier Seq 110 | 3 | 3 | 29-Jan-21 | 02-Feb-21 |
| CR1DETSTL: | Detail and Deck Steel with Crane 1 - Roof Seq 329 | 3 | 3 | 01-Feb-21 | 03-Feb-21 |
| CR1DETSTL: | Detail and Deck Steel with Crane 1 - 2nd Tier Seq 207 | 12 | 12 | 09-Feb-21 | 24-Feb-21 |
| CR1DETSTL4 | Detail and Deck Quadrant with Crane 1 - Seq 404 | 9 | 9 | 18-Feb-21 | 02-Mar-21 |
| CR1DETSTL4 | Detail and Deck Quadrant with Crane 1 - Seq 401 | 3 | 3 | 23-Feb-21 | 25-Feb-21 |
| CR1DETSTL! | Detail and Deck Steel with Crane 1 - Cooling Tower Seq 501 | 5 | 5 | 04-Mar-21 | 10-Mar-21 |
| Crane 2 | | 18 | 18 | 29-Dec-20 | 22-Jan-21 |
| CR2DETSTL: | Detail and Deck Steel with Crane 2 - Roof Seq 308 | 9 | 9 | 29-Dec-20 | 11-Jan-21 |
| CR2DETSTL: | Detail and Deck Steel with Crane 2 - 2nd Tier Seq 203 | 12 | 12 | 30-Dec-20 | 15-Jan-21 |
| CR2DETSTL4 | Detail and Deck Quadrant with Crane 2 - Seq 403 | 9 | 9 | 12-Jan-21 | 22-Jan-21 |
| CR2DETSTL4 | Detail and Deck Quadrant with Crane 2 - Seq 402 | 3 | 3 | 15-Jan-21 | 19-Jan-21 |
| Slabs | | 152 | 152 | 01-Oct-20 | 10-May-21 |
| A4020 | Sequence #101-103 Deck Turnover | 0 | 0 | | 01-Oct-20 |
| A29430 | Sequence #104-106 Deck Turnover | 0 | 0 | | 22-Oct-20 |
| A29590 | Sequence #107-108 Deck Turnover | 0 | 0 | | 06-Nov-20 |
| A29630 | Sequence #109 Deck Turnover | 0 | 0 | | 16-Nov-20 |
| A29640 | Sequence #110 Deck Turnover (Leave-out) | 0 | 0 | | 02-Feb-21 |
| Overlook Level | | 29 | 29 | 02-Oct-20 | 11-Nov-20 |
| A3840 | Install In-Slab Electrical | 3 | 3 | 02-Oct-20 | 06-Oct-20 |
| A4010 | Install In-Slab Plumbing | 3 | 3 | 02-Oct-20 | 06-Oct-20 |
| A29440 | Install In-Slab Electrical | 3 | 3 | 23-Oct-20 | 27-Oct-20 |
| A29450 | Install In-Slab Plumbing | 3 | 3 | 23-Oct-20 | 27-Oct-20 |
| A3830 | Prep & Place SOD - Quad 1-2 (Pour #1) | 5 | 5 | 29-Oct-20 | 04-Nov-20 |
| A3850 | Prep & Place SOD - Quad 2-3 (Pour #5) | 5 | 5 | 05-Nov-20 | 11-Nov-20 |
| Suite Level | | 6 | 6 | 07-Oct-20 | 14-Oct-20 |
| A29470 | Install In-Slab Electrical | 3 | 3 | 07-Oct-20 | 09-Oct-20 |
| A29480 | Install In-Slab Plumbing | 3 | 3 | 07-Oct-20 | 09-Oct-20 |
| A3730 | Prep & Place SOD - Quad 1-2 (Pour #2) | 5 | 5 | 08-Oct-20 | 14-Oct-20 |
| Concourse Level | | 85 | 85 | 12-Oct-20 | 12-Feb-21 |
| A29490 | Install In-Slab Electrical | 3 | 3 | 12-Oct-20 | 14-Oct-20 |
| A29500 | Install In-Slab Plumbing | 3 | 3 | 12-Oct-20 | 14-Oct-20 |
| A3750 | Prep & Place SOD - Quad 1-2 (Pour #3) | 5 | 5 | 13-Oct-20 | 19-Oct-20 |
| A29510 | Install In-Slab Electrical | 3 | 3 | 15-Oct-20 | 19-Oct-20 |

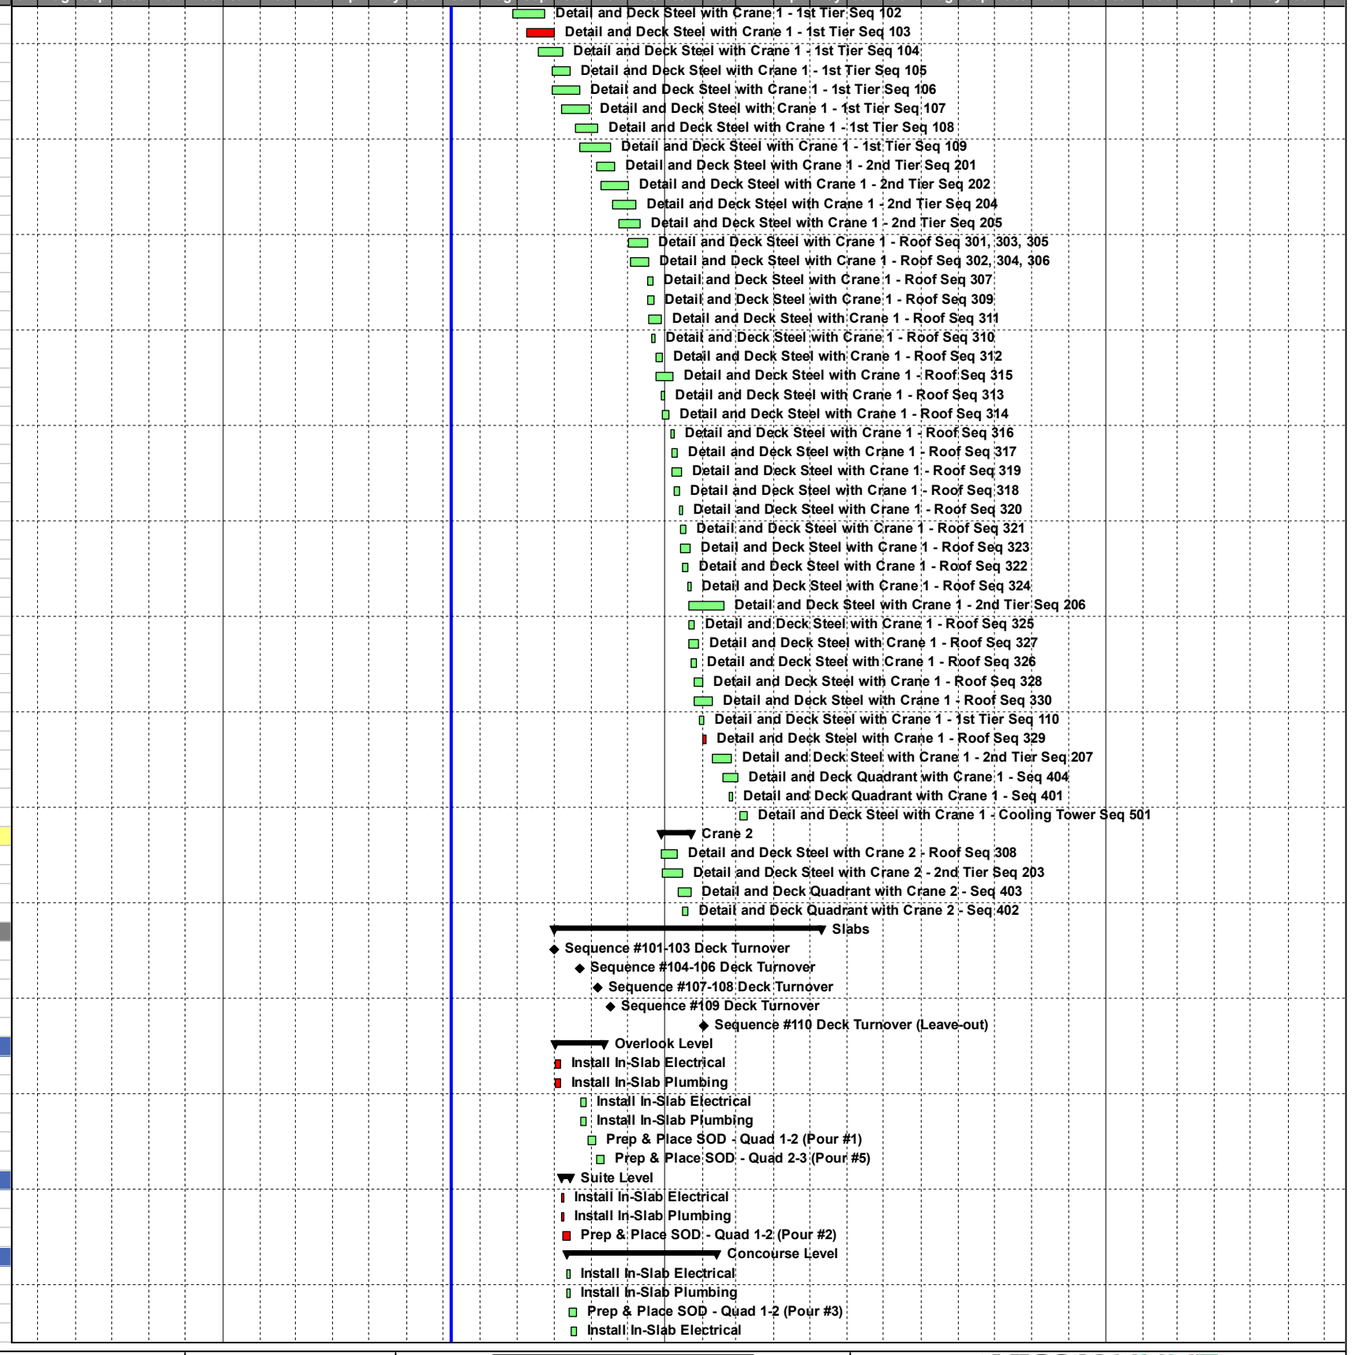

| Activity ID | Activity Name | Original Duration | Remaining Duration | Start | Finish |
|---|---|---|---|---|---|
| A29520 | Install In-Slab Plumbing | 3 | 3 | 15-Oct-20 | 19-Oct-20 |
| A3790 | Prep & Place SOD - Quad 2 (Pour #4) | 5 | 5 | 19-Oct-20 | 23-Oct-20 |
| A29530 | Install In-Slab Electrical | 3 | 3 | 28-Oct-20 | 30-Oct-20 |
| A29540 | Install In-Slab Plumbing | 3 | 3 | 28-Oct-20 | 30-Oct-20 |
| A3800 | Prep & Place SOD - Quad 3 (Pour #6) | 5 | 5 | 29-Oct-20 | 04-Nov-20 |
| A29550 | Install In-Slab Electrical | 3 | 3 | 09-Nov-20 | 11-Nov-20 |
| A29560 | Install In-Slab Plumbing | 3 | 3 | 09-Nov-20 | 11-Nov-20 |
| A3810 | Prep & Place SOD - Quad 4 (Pour #7) | 5 | 5 | 10-Nov-20 | 16-Nov-20 |
| A29600 | Install In-Slab Electrical | 3 | 3 | 17-Nov-20 | 19-Nov-20 |
| A29610 | Install In-Slab Plumbing | 3 | 3 | 17-Nov-20 | 19-Nov-20 |
| A29620 | Prep & Place SOD - Quad 4 (Pour #8) | 5 | 5 | 18-Nov-20 | 24-Nov-20 |
| A29570 | Install In-Slab Electrical | 3 | 3 | 03-Feb-21 | 05-Feb-21 |
| A29580 | Install In-Slab Plumbing | 3 | 3 | 03-Feb-21 | 05-Feb-21 |
| A3820 | Prep & Place SOD - Quad 4 (Pour #9) Leave-out | 5 | 5 | 08-Feb-21 | 12-Feb-21 |
| Event Level | | 60 | 60 | 15-Oct-20 | 13-Jan-21 |
| A1170 | Install Underground MEP | 40 | 40 | 15-Oct-20 | 11-Dec-20 |
| A3740 | Slab on Grade - Quad 1 | 10 | 10 | 12-Nov-20 | 25-Nov-20 |
| A3760 | Slab on Grade - Quad 2 | 10 | 10 | 30-Nov-20 | 11-Dec-20 |
| A3770 | Slab on Grade - Quad 3 | 10 | 10 | 14-Dec-20 | 29-Dec-20 |
| A3780 | Slab on Grade - Quad 4 | 10 | 10 | 30-Dec-20 | 13-Jan-21 |
| Ice Floor | | 30 | 30 | 30-Mar-21 | 10-May-21 |
| A3360 | Ice Floor Slab | 30 | 30 | 30-Mar-21 | 10-May-21 |
| A1280 | Structural Slab @ Ice Floor | 20 | 20 | 13-Apr-21 | 10-May-21 |
| Precast | | 68 | 68 | 07-Dec-20 | 15-Mar-21 |
| Upper Level | | 50 | 50 | 07-Dec-20 | 17-Feb-21 |
| A3870 | Erect Precast Risers - Quad 2 | 7 | 7 | 07-Dec-20 | 15-Dec-20 |
| A3880 | Erect Precast Risers - Quad 3 | 5 | 5 | 16-Dec-20 | 22-Dec-20 |
| A3890 | Erect Precast Risers - Quad 1 | 3 | 3 | 23-Dec-20 | 29-Dec-20 |
| A3900 | Erect Precast Risers - Quad 4 | 3 | 3 | 30-Dec-20 | 04-Jan-21 |
| A4030 | Erect Precast Risers - Quad 4 (Leave-Out) | 3 | 3 | 15-Feb-21 | 17-Feb-21 |
| Lower Level | | 24 | 24 | 10-Feb-21 | 15-Mar-21 |
| A3910 | Erect Precast Rakers - Quad 1 | 3 | 3 | 10-Feb-21 | 12-Feb-21 |
| A4380 | Erect Precast Risers - Quad 1 | 5 | 5 | 11-Feb-21 | 17-Feb-21 |
| A3920 | Erect Precast Rakers - Quad 2 | 3 | 3 | 18-Feb-21 | 22-Feb-21 |
| A4540 | Erect Precast Risers - Quad 2 | 5 | 5 | 19-Feb-21 | 25-Feb-21 |
| A3930 | Erect Precast Rakers - Quad 3 | 3 | 3 | 26-Feb-21 | 02-Mar-21 |
| A4630 | Erect Precast Risers - Quad 3 | 5 | 5 | 01-Mar-21 | 05-Mar-21 |
| A4280 | Erect Precast Rakers - Quad 4 | 3 | 3 | 08-Mar-21 | 10-Mar-21 |
| A4640 | Erect Precast Risers - Quad 4 | 5 | 5 | 09-Mar-21 | 15-Mar-21 |
| Enclosure | | 170 | 170 | 05-Nov-20 | 09-Jul-21 |
| Facade Dry-in | | 109 | 109 | 11-Dec-20 | 18-May-21 |
| A29720 | North Facade Dry-in | 0 | 0 | | 11-Dec-20 |
| A29730 | East Facade Dry-in | 0 | 0 | | 13-Apr-21 |
| A29740 | South Facade Dry-in | 0 | 0 | | 04-May-21 |
| A29750 | West Facade Dry-in | 0 | 0 | | 18-May-21 |
| Facade | | 170 | 170 | 05-Nov-20 | 09-Jul-21 |
| North | | 107 | 107 | 05-Nov-20 | 09-Apr-21 |
| A1230 | Exterior Framing | 15 | 15 | 05-Nov-20 | 25-Nov-20 |
| A1270 | Exterior Sheathing | 15 | 15 | 12-Nov-20 | 04-Dec-20 |
| A1330 | Install Air Barrier | 10 | 10 | 30-Nov-20 | 11-Dec-20 |
| A5230 | Install Brick | 30 | 30 | 14-Dec-20 | 27-Jan-21 |
| A5240 | Install Insulation | 15 | 15 | 24-Feb-21 | 16-Mar-21 |
| A29690 | Install Roof Screen | 18 | 18 | 17-Mar-21 | 09-Apr-21 |
| East | | 115 | 115 | 12-Nov-20 | 28-Apr-21 |
| A5350 | Install Curtain Wall Support Steel | 10 | 10 | 12-Nov-20 | 25-Nov-20 |
| A5440 | Exterior Framing | 10 | 10 | 12-Nov-20 | 25-Nov-20 |
| A5310 | Install Curtain Wall - Level 2-3 - S8-C | 3 | 3 | 30-Nov-20 | 02-Dec-20 |
| A5450 | Exterior Sheathing | 10 | 10 | 30-Nov-20 | 11-Dec-20 |
| A32290 | Install Curtain Wall - Level 2-3 - C-S2 | 3 | 3 | 03-Dec-20 | 07-Dec-20 |
| A32300 | Install Curtain Wall - Level 2-3 - S2-EW | 3 | 3 | 08-Dec-20 | 10-Dec-20 |
| A32310 | Install Curtain Wall - Level 2-3 - EW-N2 | 3 | 3 | 11-Dec-20 | 15-Dec-20 |
| A5460 | Install Air Barrier | 10 | 10 | 14-Dec-20 | 29-Dec-20 |
| A32320 | Install Curtain Wall - Level 2-3 - N2-N3 | 3 | 3 | 16-Dec-20 | 18-Dec-20 |
| A29650 | Install Curtain Wall - Level 4 - S6-S3 | 1 | 1 | 21-Dec-20 | 21-Dec-20 |
| A32240 | Install Curtain Wall - Level 4 - S3-S1 | 2 | 2 | 22-Dec-20 | 23-Dec-20 |
| A32250 | Install Curtain Wall - Level 4 - S1-S0 | 2 | 2 | 28-Dec-20 | 29-Dec-20 |
| A5340 | Install Metal Wall Panels | 30 | 30 | 30-Dec-20 | 10-Feb-21 |
| A32260 | Install Curtain Wall - Level 4 - S0-N0 | 1 | 1 | 30-Dec-20 | 30-Dec-20 |
| A32270 | Install Curtain Wall - Level 4 - N0-N1 | 1 | 1 | 31-Dec-20 | 31-Dec-20 |
| A32280 | Install Curtain Wall - Level 4 - N1-N2 | 3 | 3 | 04-Jan-21 | 06-Jan-21 |

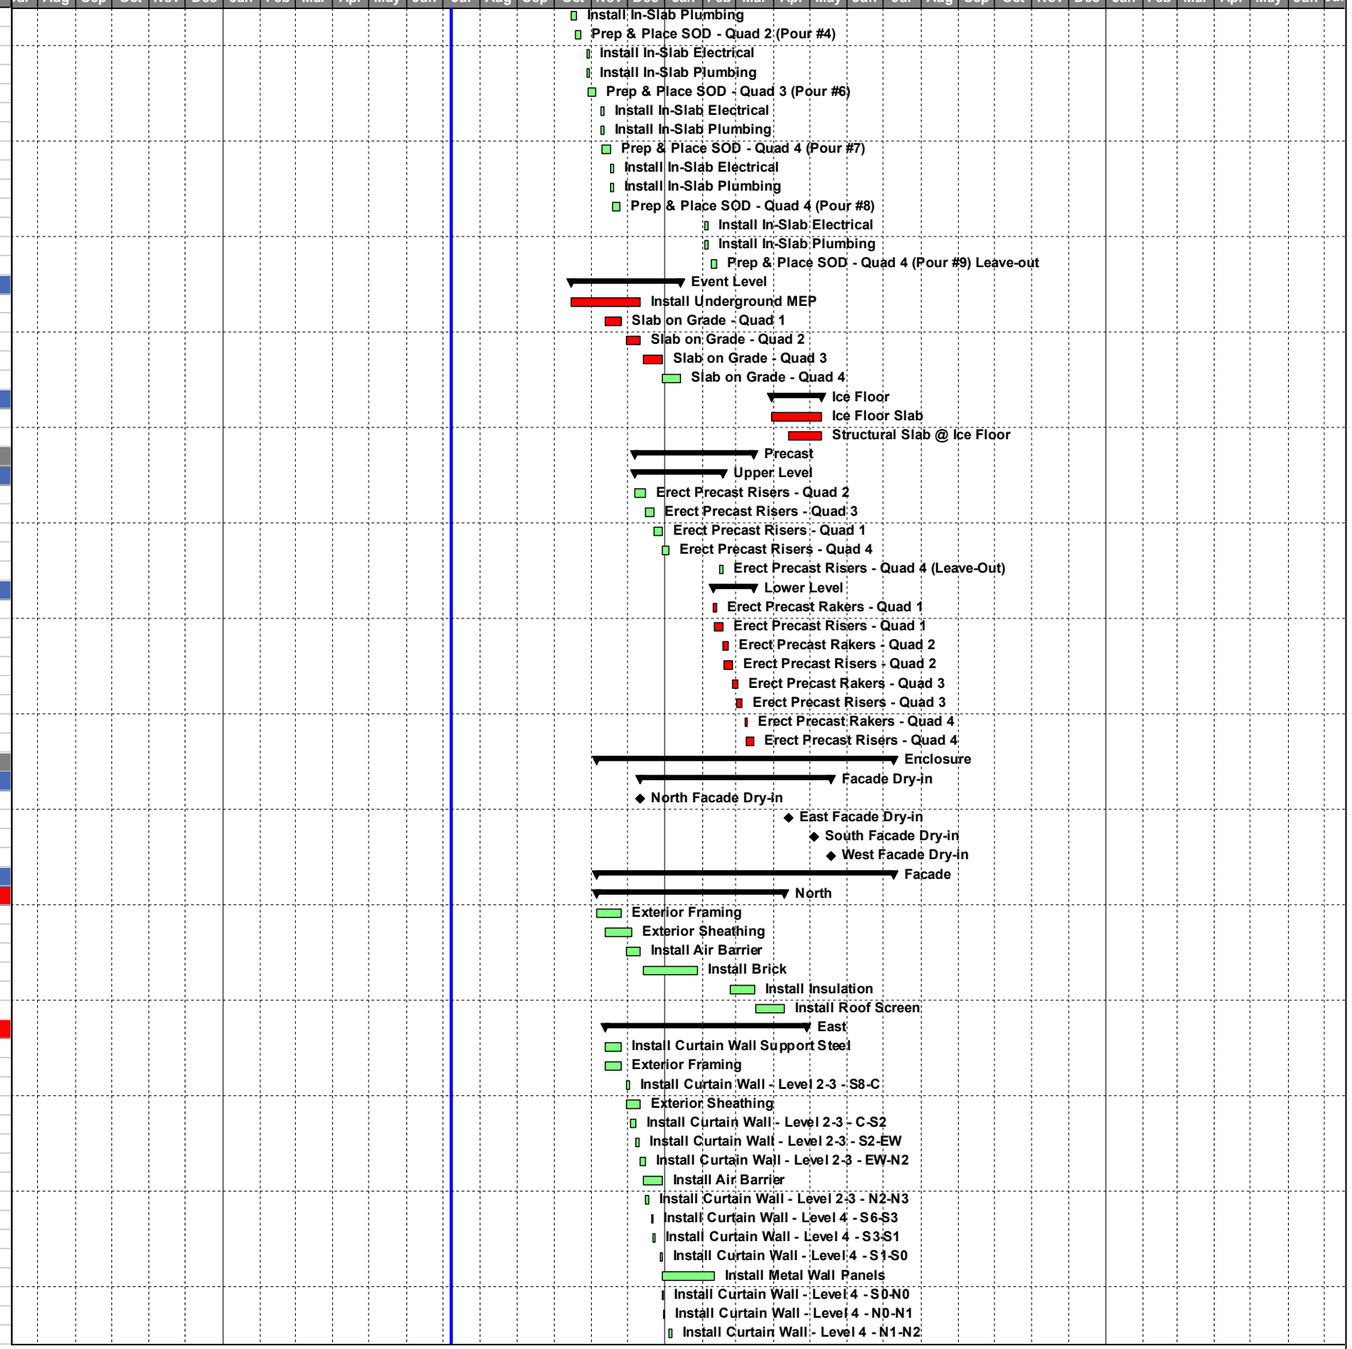

| Activity ID | Activity Name | Original Duration | Remaining Duration | Start | Finish |
|---|---|---|---|---|---|
| A5320 | Install Brick East (North) | 25 | 25 | 28-Jan-21 | 03-Mar-21 |
| A5330 | Install Brick East (South) | 25 | 25 | 11-Feb-21 | 17-Mar-21 |
| A5530 | Install Curtain Wall - Level 1 - S8-C | 3 | 3 | 24-Mar-21 | 26-Mar-21 |
| A32200 | Install Curtain Wall - Level 1 - C-S2 | 2 | 2 | 29-Mar-21 | 30-Mar-21 |
| A32210 | Install Curtain Wall - Level 1 - S2-EW | 3 | 3 | 31-Mar-21 | 02-Apr-21 |
| A32220 | Install Curtain Wall - Level 1 - EW-N2 | 4 | 4 | 05-Apr-21 | 08-Apr-21 |
| A32230 | Install Curtain Wall - Level 1 - N2-N3 | 3 | 3 | 09-Apr-21 | 13-Apr-21 |
| A5360 | Install Roof Screen | 13 | 13 | 12-Apr-21 | 28-Apr-21 |
| South | | 130 | 130 | 30-Nov-20 | 03-Jun-21 |
| A5300 | Install Curtain Wall Support Steel | 10 | 10 | 30-Nov-20 | 11-Dec-20 |
| A5470 | Exterior Framing | 15 | 15 | 30-Nov-20 | 18-Dec-20 |
| A5480 | Exterior Sheathing | 10 | 10 | 21-Dec-20 | 06-Jan-21 |
| A5260 | Install Curtain Wall - Level 2-4 - W4-W1 | 9 | 9 | 07-Jan-21 | 19-Jan-21 |
| A5490 | Install Air Barrier | 10 | 10 | 07-Jan-21 | 20-Jan-21 |
| A32140 | Install Curtain Wall - Level 2-4 - W1-E2 | 9 | 9 | 20-Jan-21 | 01-Feb-21 |
| A32150 | Install Curtain Wall - Level 2-4 - E2-E3.2 | 9 | 9 | 02-Feb-21 | 12-Feb-21 |
| A5290 | Install Metal Wall Panels | 80 | 80 | 11-Feb-21 | 03-Jun-21 |
| A5270 | Install Brick South (East) | 25 | 25 | 18-Mar-21 | 21-Apr-21 |
| A5280 | Install Brick South (West) | 20 | 20 | 01-Apr-21 | 28-Apr-21 |
| A5540 | Install Curtain Wall - Level 1 - W3-W1 | 2 | 2 | 14-Apr-21 | 15-Apr-21 |
| A32160 | Install Curtain Wall - Level 1 - W1-E2 | 2 | 2 | 16-Apr-21 | 19-Apr-21 |
| A32170 | Install Curtain Wall - Level 1 - E2-E3.1 | 3 | 3 | 20-Apr-21 | 22-Apr-21 |
| A32180 | Install Curtain Wall - Level 1 - E3.1-E6 | 4 | 4 | 23-Apr-21 | 28-Apr-21 |
| A5370 | Install Roof Screen | 18 | 18 | 29-Apr-21 | 24-May-21 |
| A32190 | Install Curtain Wall - Level 1 -W10-W5 | 4 | 4 | 29-Apr-21 | 04-May-21 |
| West | | 145 | 145 | 14-Dec-20 | 09-Jul-21 |
| A5420 | Install Curtain Wall Support Steel | 10 | 10 | 14-Dec-20 | 29-Dec-20 |
| A5500 | Exterior Framing | 10 | 10 | 21-Dec-20 | 06-Jan-21 |
| A5510 | Exterior Sheathing | 10 | 10 | 07-Jan-21 | 20-Jan-21 |
| A5520 | Install Air Barrier | 10 | 10 | 21-Jan-21 | 03-Feb-21 |
| A5390 | Install Brick West (South) | 30 | 30 | 04-Feb-21 | 17-Mar-21 |
| A5380 | Install Curtain Wall - Level 2-3 - N3-N2 | 3 | 3 | 15-Feb-21 | 17-Feb-21 |
| A29680 | Install Curtain Wall Support Steel - Leave-out | 4 | 4 | 15-Feb-21 | 18-Feb-21 |
| A5400 | Install Brick West (North) | 25 | 25 | 18-Feb-21 | 24-Mar-21 |
| A32350 | Install Curtain Wall - Level 2-3 - N2-N0 | 3 | 3 | 18-Feb-21 | 22-Feb-21 |
| A29670 | Install Curtain Wall - Leave-out | 8 | 8 | 19-Feb-21 | 02-Mar-21 |
| A32360 | Install Curtain Wall - Level 2-3 - N0-S0 | 3 | 3 | 23-Feb-21 | 25-Feb-21 |
| A32370 | Install Curtain Wall - Level 2-3 - S0-S1 | 3 | 3 | 26-Feb-21 | 02-Mar-21 |
| A32380 | Install Curtain Wall - Level 2-3 - S1-S3 | 3 | 3 | 03-Mar-21 | 05-Mar-21 |
| A32390 | Install Curtain Wall - Level 2-3 - S3-S8 | 2 | 2 | 08-Mar-21 | 09-Mar-21 |
| A29660 | Install Curtain Wall - Level 4 - N3-N2 | 2 | 2 | 10-Mar-21 | 11-Mar-21 |
| A32400 | Install Curtain Wall - Level 4 - N2-N0 | 2 | 2 | 12-Mar-21 | 15-Mar-21 |
| A32410 | Install Curtain Wall - Level 4 - N0-S0 | 1 | 1 | 16-Mar-21 | 16-Mar-21 |
| A32420 | Install Curtain Wall - Level 4 - S0-S1 | 2 | 2 | 17-Mar-21 | 18-Mar-21 |
| A32430 | Install Curtain Wall - Level 4 - S1-S3 | 2 | 2 | 19-Mar-21 | 22-Mar-21 |
| A32440 | Install Curtain Wall - Level 4 - S3-S6.6 | 1 | 1 | 23-Mar-21 | 23-Mar-21 |
| A5550 | Install Curtain Wall - Level 1 - N3-N2 | 3 | 3 | 05-May-21 | 07-May-21 |
| A32330 | Install Curtain Wall - Level 1 - S2-S3 | 3 | 3 | 10-May-21 | 12-May-21 |
| A32340 | Install Curtain Wall - Level 1 - C-S8 | 4 | 4 | 13-May-21 | 18-May-21 |
| A5430 | Install Roof Screen | 13 | 13 | 25-May-21 | 11-Jun-21 |
| A5410 | Install Metal Wall Panels | 25 | 25 | 04-Jun-21 | 09-Jul-21 |
| Roof | | 57 | 57 | 22-Jan-21 | 12-Apr-21 |
| ROOF-150 | Install Low Roof - Quad 2 | 10 | 10 | 22-Jan-21 | 04-Feb-21 |
| ROOF-100 | Install Main Roof - Section 1 | 12 | 12 | 04-Feb-21 | 19-Feb-21 |
| ROOF-160 | Install Low Roof - Quad 3 | 10 | 10 | 05-Feb-21 | 18-Feb-21 |
| ROOF-140 | Install Low Roof - Quad 1 | 10 | 10 | 10-Feb-21 | 23-Feb-21 |
| ROOF-110 | Install Main Roof - Section 2 | 12 | 12 | 22-Feb-21 | 09-Mar-21 |
| ROOF-170 | Install Low Roof - Quad 4 | 10 | 10 | 03-Mar-21 | 16-Mar-21 |
| ROOF-120 | Install Main Roof - Section 3 | 12 | 12 | 10-Mar-21 | 25-Mar-21 |
| ROOF-130 | Install Main Roof - Section 4 | 12 | 12 | 26-Mar-21 | 12-Apr-21 |
| Interior Fit-Out | | 211 | 211 | 20-Oct-20 | 19-Aug-21 |
| Vertical Transportation | | 105 | 105 | 05-Feb-21 | 02-Jul-21 |
| A3950 | Commissary Elevator #2 - Quad 2 | 20 | 20 | 05-Feb-21 | 04-Mar-21 |
| A3940 | Elevator #1 - Quad 1 -5W | 25 | 25 | 05-Mar-21 | 08-Apr-21 |
| A3960 | Elevator #3 - Quad 3 | 15 | 15 | 09-Apr-21 | 29-Apr-21 |
| A29700 | Elevator #4 - Quad 3 | 15 | 15 | 30-Apr-21 | 20-May-21 |
| A3970 | Escalator East - Quad 4 | 15 | 15 | 21-May-21 | 11-Jun-21 |
| A29710 | Escalator West - Quad 4 | 15 | 15 | 14-Jun-21 | 02-Jul-21 |
| Stair Towers | | 65 | 65 | 30-Nov-20 | 03-Mar-21 |
| A4840 | CMU @ Stair Tower - Quad 1 | 15 | 15 | 30-Nov-20 | 18-Dec-20 |

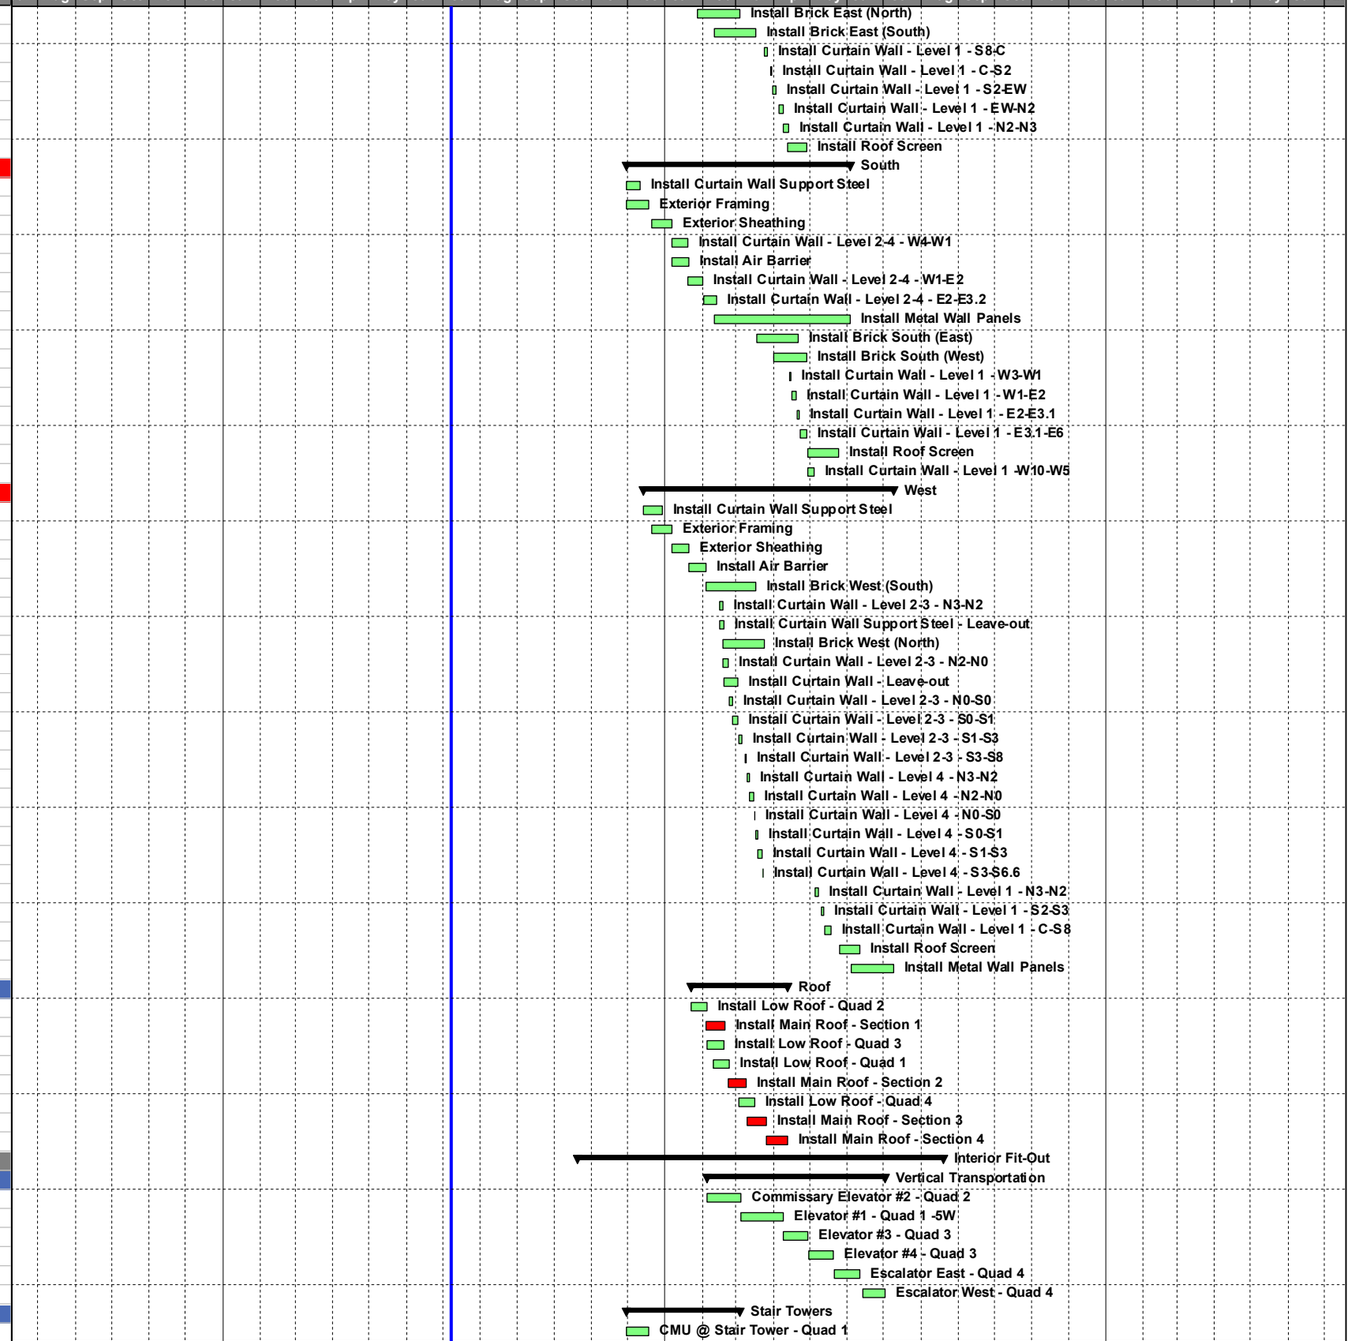

| Activity ID | Activity Name | Original Duration | Remaining Duration | Start | Finish |
|---|---|---|---|---|---|
| A4710 | Install Stair Towers - Quad 1 | 5 | 5 | 21-Dec-20 | 29-Dec-20 |
| A4850 | CMU @ Stair Tower - Quad 2 | 15 | 15 | 21-Dec-20 | 13-Jan-21 |
| A4810 | Install Stair Towers - Quad 2 | 5 | 5 | 14-Jan-21 | 20-Jan-21 |
| A4860 | CMU @ Stair Tower - Quad 3 | 15 | 15 | 14-Jan-21 | 03-Feb-21 |
| A4820 | Install Stair Towers - Quad 3 | 5 | 5 | 04-Feb-21 | 10-Feb-21 |
| A4870 | CMU @ Stair Tower - Quad 4 | 15 | 15 | 04-Feb-21 | 24-Feb-21 |
| A4830 | Install Stair Towers - Quad 4 | 5 | 5 | 25-Feb-21 | 03-Mar-21 |
| Event Level | | 184 | 184 | 30-Nov-20 | 19-Aug-21 |
| A29390 | Event Level Complete | 0 | 0 | | 19-Aug-21 |
| Quad 1 | | 163 | 163 | 30-Nov-20 | 21-Jul-21 |
| MEPFP Mains Rough-in | | 41 | 41 | 30-Nov-20 | 28-Jan-21 |
| OHRI-EL-Q1-0 | Spray Fireproofing - First Pass - CL-W10-N/S/N8-E/W | 10 | 10 | 30-Nov-20 | 11-Dec-20 |
| OHRI-EL-Q1-0 | Install Subroof - CL-W10-N/S/N8-E/W | 15 | 15 | 14-Dec-20 | 06-Jan-21 |
| OHRI-EL-Q1-1 | Mechanical Mains - CL-W10-N/S/N8-E/W | 10 | 10 | 28-Dec-20 | 11-Jan-21 |
| OHRI-EL-Q1-1 | Electrical Mains - CL-W10-N/S/N8-E/W | 10 | 10 | 30-Dec-20 | 13-Jan-21 |
| OHRI-EL-Q1-1 | Plumbing Mains - CL-W10-N/S/N8-E/W | 10 | 10 | 04-Jan-21 | 15-Jan-21 |
| OHRI-EL-Q1-1 | Fire Protection Mains - CL-W10-N/S/N8-E/W | 10 | 10 | 06-Jan-21 | 19-Jan-21 |
| OHRI-EL-Q1-1 | Cable Tray AV/IT Mains - CL-W10-N/S/N8-E/W | 10 | 10 | 08-Jan-21 | 21-Jan-21 |
| OHRI-EL-Q1-1 | Spray Fireproofing - Final Pass - CL-W10-N/S/N8-E/W | 10 | 10 | 15-Jan-21 | 28-Jan-21 |
| Masonry Walls & Partitions | | 20 | 20 | 20-Jan-21 | 16-Feb-21 |
| MAS-EL-Q1-1( | Masonry Wall - CL-W10-W5/N8-E/W | 10 | 10 | 20-Jan-21 | 02-Feb-21 |
| ELEC-EL-Q1-1 | Electrical Rough-in - CL-W10-W5/N8-E/W | 10 | 10 | 20-Jan-21 | 02-Feb-21 |
| PLM-EL-Q1-10 | Plumbing Rough-in - CL-W10-W5/N8-E/W | 10 | 10 | 20-Jan-21 | 02-Feb-21 |
| MAS-EL-Q1-1( | Masonry Wall - CL-W5-N/S/N8-E/W | 10 | 10 | 03-Feb-21 | 16-Feb-21 |
| ELEC-EL-Q1-1 | Electrical Rough-in - CL-W5-N/S/N8-E/W | 10 | 10 | 03-Feb-21 | 16-Feb-21 |
| PLM-EL-Q1-10 | Plumbing Rough-in - CL-W5-N/S/N8-E/W | 10 | 10 | 03-Feb-21 | 16-Feb-21 |
| Electrical , IT Rooms & Show Power - Rooms 11.19-11.21 | | 57 | 57 | 03-Feb-21 | 22-Apr-21 |
| A7210 | Layout & Top Track | 1 | 1 | 03-Feb-21 | 03-Feb-21 |
| A7310 | Frame C80 Walls | 2 | 2 | 04-Feb-21 | 05-Feb-21 |
| A7320 | Rough-in Electrical | 3 | 3 | 08-Feb-21 | 10-Feb-21 |
| A7330 | In-Wall Inspection | 1 | 1 | 11-Feb-21 | 11-Feb-21 |
| A7340 | In-Wall Insulation | 1 | 1 | 12-Feb-21 | 12-Feb-21 |
| A7350 | Hang, Tape & Finish Drywall | 4 | 4 | 15-Feb-21 | 18-Feb-21 |
| A7360 | OH Mechanical | 5 | 5 | 19-Feb-21 | 25-Feb-21 |
| A7390 | FRP Equipment Pads | 3 | 3 | 19-Feb-21 | 23-Feb-21 |
| A7370 | OH Electrical | 5 | 5 | 22-Feb-21 | 26-Feb-21 |
| A7380 | OH Fire Protection | 3 | 3 | 23-Feb-21 | 25-Feb-21 |
| A7490 | Prime Paint | 2 | 2 | 03-Mar-21 | 04-Mar-21 |
| A7400 | Set Transformers | 2 | 2 | 05-Mar-21 | 08-Mar-21 |
| A7410 | Set IT Racks | 2 | 2 | 05-Mar-21 | 08-Mar-21 |
| A7420 | Set Panel Boxes | 2 | 2 | 05-Mar-21 | 08-Mar-21 |
| A7540 | Set FCU | 1 | 1 | 05-Mar-21 | 05-Mar-21 |
| A7550 | Set AC Units | 2 | 2 | 08-Mar-21 | 09-Mar-21 |
| A7430 | Install Panel Interiors | 3 | 3 | 09-Mar-21 | 11-Mar-21 |
| A7450 | Pull Cable & Terminate | 15 | 15 | 09-Mar-21 | 29-Mar-21 |
| A7460 | Hook-up Transformers | 5 | 5 | 09-Mar-21 | 15-Mar-21 |
| A7510 | Install Doors & Hardware | 2 | 2 | 09-Mar-21 | 10-Mar-21 |
| A7560 | OH Mechanical Finishes | 2 | 2 | 10-Mar-21 | 11-Mar-21 |
| A7440 | Pull Wire & Terminate | 15 | 15 | 12-Mar-21 | 01-Apr-21 |
| A7470 | Install Lighting | 3 | 3 | 02-Apr-21 | 06-Apr-21 |
| A7480 | Install Electrical Finishes | 2 | 2 | 07-Apr-21 | 08-Apr-21 |
| A7790 | Install Fire Alarm Devices | 2 | 2 | 07-Apr-21 | 08-Apr-21 |
| A7500 | Seal Concrete Floors | 3 | 3 | 09-Apr-21 | 13-Apr-21 |
| A7810 | MEPFP Final Inspections | 2 | 2 | 09-Apr-21 | 12-Apr-21 |
| A7520 | Final Paint | 2 | 2 | 14-Apr-21 | 15-Apr-21 |
| A7530 | Punchlist | 5 | 5 | 16-Apr-21 | 22-Apr-21 |
| Loading & Recieving, Zamboni, Janitor/Storage - Rooms 11.01, 11.12 & 11.27 | | 64 | 64 | 17-Feb-21 | 17-May-21 |
| A7830 | OH Mechanical | 4 | 4 | 17-Feb-21 | 22-Feb-21 |
| A7840 | OH Plumbing | 4 | 4 | 18-Feb-21 | 23-Feb-21 |
| A7850 | OH Electrical | 4 | 4 | 19-Feb-21 | 24-Feb-21 |
| A7860 | OH Fire Protection | 4 | 4 | 22-Feb-21 | 25-Feb-21 |
| A7870 | OH Inspections | 1 | 1 | 26-Feb-21 | 26-Feb-21 |
| A7880 | Set & Install Ice Melt Equipment | 8 | 8 | 01-Mar-21 | 10-Mar-21 |
| A10920 | Install Loading Dock Equipment | 12 | 12 | 01-Mar-21 | 16-Mar-21 |
| A7890 | Install Ice Melt Steel Lid | 3 | 3 | 11-Mar-21 | 15-Mar-21 |
| A7900 | Install Ice Melt Pit Guard | 10 | 10 | 16-Mar-21 | 29-Mar-21 |
| A7905 | Install Floor Drains | 2 | 2 | 30-Mar-21 | 31-Mar-21 |
| A7960 | Prime Paint | 2 | 2 | 01-Apr-21 | 02-Apr-21 |
| A7940 | Sprinkler Heads | 2 | 2 | 05-Apr-21 | 06-Apr-21 |
| A9290 | Install 5 Roll-up Doors (4 L&R) (1 ZAM) | 15 | 15 | 05-Apr-21 | 23-Apr-21 |

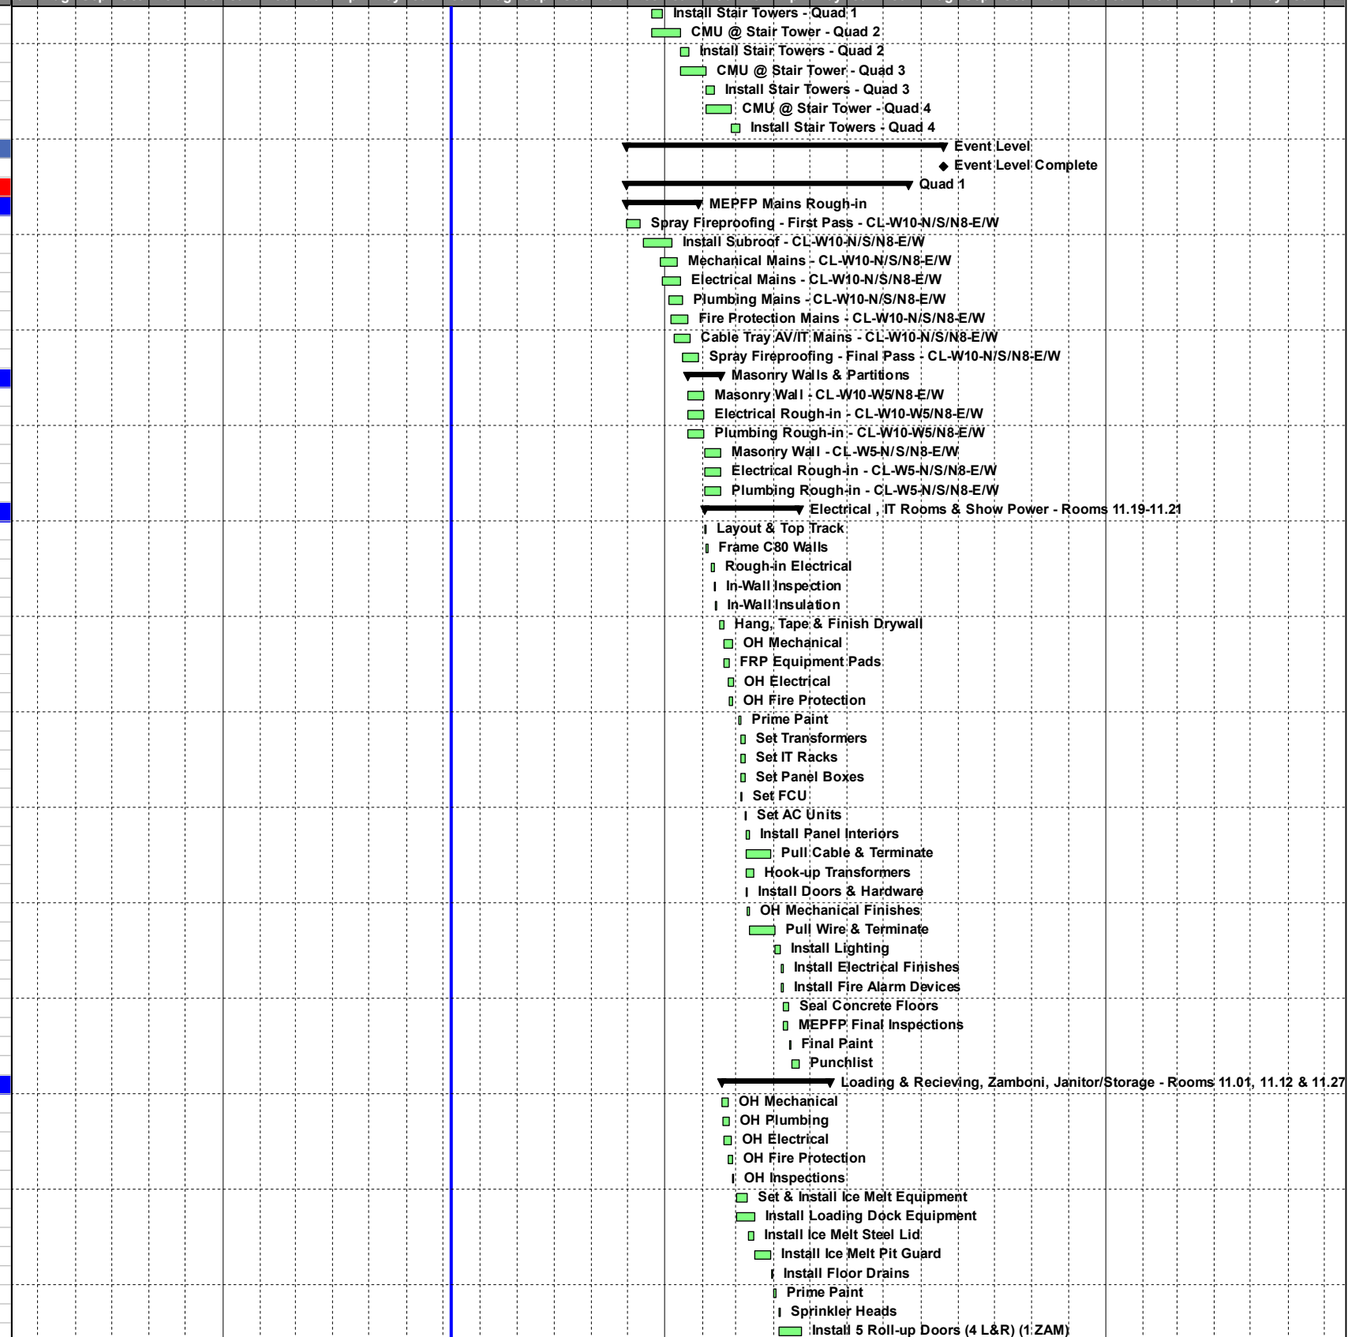


Remaining Level of Effort | Remainin...
Actual Level of Effort | Critical R...
Actual Work | Milestone



AECOM HUNT
in association with
Brownstone Construction Group
Pat Mathis Construction Company
A. Riley Consultants

| Activity ID | Activity Name | Original Duration | Remaining Duration | Start | Finish |
|---|---|---|---|---|---|
| A7950 | Grilles, Registers & Diffusers | 2 | 2 | 07-Apr-21 | 08-Apr-21 |
| A7910 | Install Lighting | 2 | 2 | 09-Apr-21 | 12-Apr-21 |
| A7930 | Fire Alarm Devices | 2 | 2 | 13-Apr-21 | 14-Apr-21 |
| A7920 | Electrical Trim-out | 2 | 2 | 26-Apr-21 | 27-Apr-21 |
| A7980 | Seal Concrete Floors | 5 | 5 | 28-Apr-21 | 04-May-21 |
| A8000 | MEPFP Final Inspections | 2 | 2 | 28-Apr-21 | 29-Apr-21 |
| A7990 | Install Doors & Hardware | 2 | 2 | 05-May-21 | 06-May-21 |
| A7970 | Final Paint | 2 | 2 | 07-May-21 | 10-May-21 |
| A8010 | Punchlist | 5 | 5 | 11-May-21 | 17-May-21 |
| Ice Chiller - Room 11.03 | | 50 | 50 | 17-Feb-21 | 27-Apr-21 |
| A7260 | OH Mechanical | 5 | 5 | 17-Feb-21 | 23-Feb-21 |
| A8300 | OH Electrical | 5 | 5 | 18-Feb-21 | 24-Feb-21 |
| A8320 | OH Plumbing | 5 | 5 | 19-Feb-21 | 25-Feb-21 |
| A8330 | OH Fire Protection | 5 | 5 | 22-Feb-21 | 26-Feb-21 |
| A8340 | Set & Install FCU | 5 | 5 | 24-Feb-21 | 02-Mar-21 |
| A8350 | FRP Equipment Pads | 5 | 5 | 01-Mar-21 | 05-Mar-21 |
| A8360 | Set Ice Cooling Tank | 2 | 2 | 08-Mar-21 | 09-Mar-21 |
| A8380 | Set Ammonia Relief Tank | 1 | 1 | 08-Mar-21 | 08-Mar-21 |
| A8370 | Set Ammonia Ice Chiler | 2 | 2 | 09-Mar-21 | 10-Mar-21 |
| A8460 | Piping for Cooling Tank | 10 | 10 | 10-Mar-21 | 23-Mar-21 |
| A8470 | Piping for Ammonia Ice Chiller | 15 | 15 | 11-Mar-21 | 31-Mar-21 |
| A8480 | Prime Paint | 5 | 5 | 24-Mar-21 | 30-Mar-21 |
| A8390 | Set Ice MCC's | 2 | 2 | 31-Mar-21 | 01-Apr-21 |
| A8400 | Set & Connect Ammonia Leak Detector | 2 | 2 | 31-Mar-21 | 01-Apr-21 |
| A8410 | Install Lighting | 3 | 3 | 31-Mar-21 | 02-Apr-21 |
| A8830 | Install Roll-up Door | 5 | 5 | 31-Mar-21 | 06-Apr-21 |
| A8420 | Fire Alarm Devices | 3 | 3 | 01-Apr-21 | 05-Apr-21 |
| A8430 | Sprinkler Heads | 3 | 3 | 02-Apr-21 | 06-Apr-21 |
| A8440 | Grilles, Registers & Diffusers | 3 | 3 | 05-Apr-21 | 07-Apr-21 |
| A8490 | Electrical Trim-out | 5 | 5 | 07-Apr-21 | 13-Apr-21 |
| A8450 | Ceiling Inspections | 2 | 2 | 08-Apr-21 | 09-Apr-21 |
| A8500 | Install Doors & Hardware | 2 | 2 | 14-Apr-21 | 15-Apr-21 |
| A8520 | MEPFP Final Inspections | 5 | 5 | 14-Apr-21 | 20-Apr-21 |
| A8570 | Start-up & Test Ice Chiller Equipment | 5 | 5 | 14-Apr-21 | 20-Apr-21 |
| A8510 | Final Paint | 2 | 2 | 16-Apr-21 | 19-Apr-21 |
| A8530 | Punchlist | 5 | 5 | 21-Apr-21 | 27-Apr-21 |
| Staff Check-in, Vestibule, Staff LR, Catering & Pantry - Rooms 11.10, 11.11, 11.14, 11.15 & 11.26 | | 105 | 105 | 23-Feb-21 | 21-Jul-21 |
| A8020 | OH Mechanical | 5 | 5 | 23-Feb-21 | 01-Mar-21 |
| A8030 | OH Electrical | 5 | 5 | 24-Feb-21 | 02-Mar-21 |
| A8040 | OH Plumbing | 5 | 5 | 25-Feb-21 | 03-Mar-21 |
| A8050 | OH Fire Protection | 5 | 5 | 26-Feb-21 | 04-Mar-21 |
| A8060 | Above Ceiling Inspections | 1 | 1 | 05-Mar-21 | 05-Mar-21 |
| A8260 | Layout & Top Track | 1 | 1 | 08-Mar-21 | 08-Mar-21 |
| A8270 | Frame C80 Walls | 2 | 2 | 09-Mar-21 | 10-Mar-21 |
| A8280 | Rough-in Electrical | 3 | 3 | 11-Mar-21 | 15-Mar-21 |
| A8290 | In-Wall Inspection | 1 | 1 | 16-Mar-21 | 16-Mar-21 |
| A8310 | Hang, Tape & Finish Drywall | 4 | 4 | 19-May-21 | 24-May-21 |
| A8070 | Prime Paint | 2 | 2 | 25-May-21 | 26-May-21 |
| A8080 | Install ACT Grid | 4 | 4 | 27-May-21 | 02-Jun-21 |
| A8090 | Sprinkler Heads | 2 | 2 | 03-Jun-21 | 04-Jun-21 |
| A8100 | Install Lighting | 3 | 3 | 04-Jun-21 | 08-Jun-21 |
| A8110 | Grilles, Registers & Diffusers | 3 | 3 | 07-Jun-21 | 09-Jun-21 |
| A8120 | Fire Alarm Devices - In-Ceiling | 3 | 3 | 08-Jun-21 | 10-Jun-21 |
| A8130 | Ceiling Inspections | 1 | 1 | 11-Jun-21 | 11-Jun-21 |
| A8140 | Install ACT Tiles | 2 | 2 | 14-Jun-21 | 15-Jun-21 |
| A8150 | Install Millwork | 5 | 5 | 16-Jun-21 | 22-Jun-21 |
| A8180 | Seal Concrete Floors - Check-in, Vestibule, Locker Room | 5 | 5 | 16-Jun-21 | 22-Jun-21 |
| A8190 | Resinous Flooring - Pantry | 5 | 5 | 16-Jun-21 | 22-Jun-21 |
| A8160 | Install Countertops | 2 | 2 | 23-Jun-21 | 24-Jun-21 |
| A8170 | Install Vinyl Floor Tile - Catering | 5 | 5 | 25-Jun-21 | 01-Jul-21 |
| A7240 | Install Doors & Hardware | 2 | 2 | 02-Jul-21 | 06-Jul-21 |
| A8200 | Electrical Finishes - On-Wall | 2 | 2 | 02-Jul-21 | 06-Jul-21 |
| A8210 | Fire Alarm Devices - On-Wall | 2 | 2 | 07-Jul-21 | 08-Jul-21 |
| A8220 | Install TVs | 2 | 2 | 09-Jul-21 | 12-Jul-21 |
| A8240 | MEPFP Final Inspections | 2 | 2 | 09-Jul-21 | 12-Jul-21 |
| A8230 | Final Paint | 2 | 2 | 13-Jul-21 | 14-Jul-21 |
| A8250 | Punchlist | 5 | 5 | 15-Jul-21 | 21-Jul-21 |
| SEC/FCC - Room 11.24 | | 57 | 57 | 17-Feb-21 | 06-May-21 |
| A29770 | OH Mechanical | 5 | 5 | 17-Feb-21 | 23-Feb-21 |
| A29780 | OH Electrical | 5 | 5 | 18-Feb-21 | 24-Feb-21 |

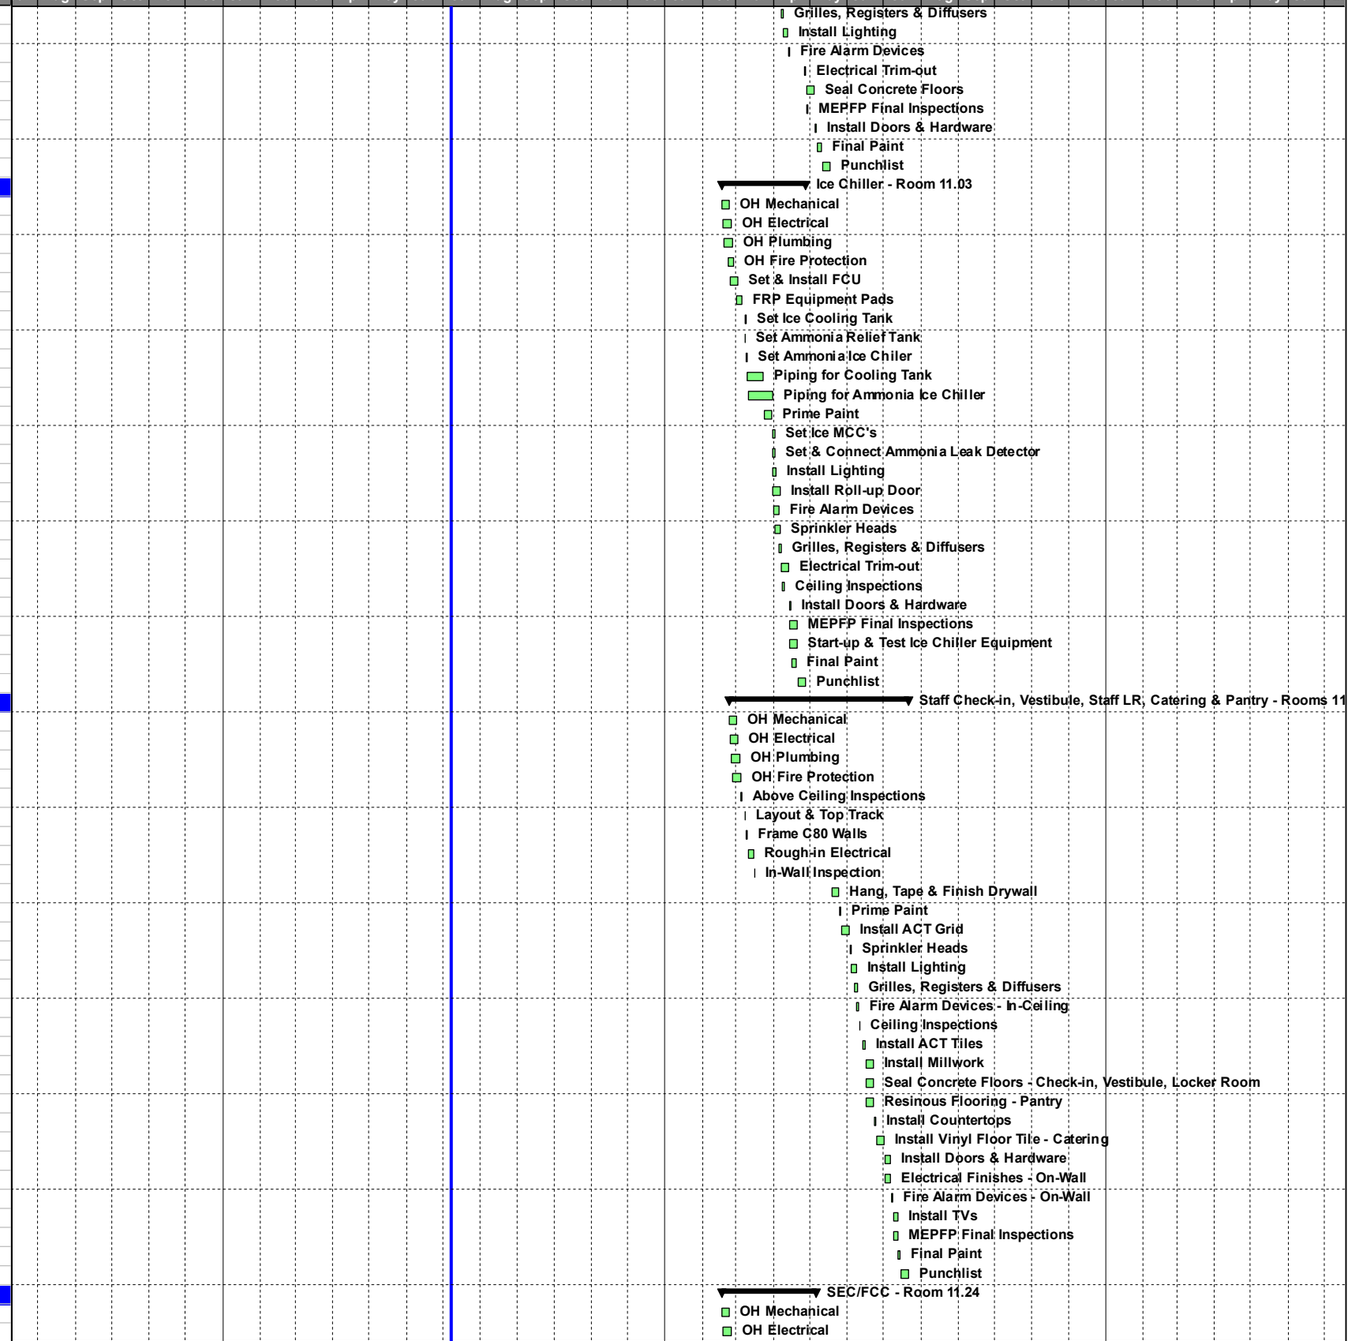

| Activity ID | Activity Name | Original Duration | Remaining Duration | Start | Finish |
|---|---|---|---|---|---|
| A29790 | OH Plumbing | 5 | 5 | 19-Feb-21 | 25-Feb-21 |
| A29800 | OH Fire Protection | 5 | 5 | 22-Feb-21 | 26-Feb-21 |
| A29810 | Above Ceiling Inspections | 1 | 1 | 01-Mar-21 | 01-Mar-21 |
| A29820 | Prime Paint | 2 | 2 | 02-Mar-21 | 03-Mar-21 |
| A29840 | Sprinkler Heads | 2 | 2 | 04-Mar-21 | 05-Mar-21 |
| A29850 | Install Lighting | 3 | 3 | 05-Mar-21 | 09-Mar-21 |
| A29860 | Grilles, Registers & Diffusers | 3 | 3 | 08-Mar-21 | 10-Mar-21 |
| A29870 | Fire Alarm Devices | 3 | 3 | 09-Mar-21 | 11-Mar-21 |
| A29900 | Install Millwork | 5 | 5 | 12-Mar-21 | 18-Mar-21 |
| A29910 | Install Countertops | 2 | 2 | 19-Mar-21 | 22-Mar-21 |
| A29760 | Install Doors & Hardware | 2 | 2 | 23-Mar-21 | 24-Mar-21 |
| A29930 | Seal Concrete Floors | 5 | 5 | 25-Mar-21 | 31-Mar-21 |
| A29950 | Electrical Trim-out | 2 | 2 | 01-Apr-21 | 02-Apr-21 |
| A30010 | Install FCC Equipment | 15 | 15 | 01-Apr-21 | 21-Apr-21 |
| A29960 | Fire Alarm Tri-out | 2 | 2 | 22-Apr-21 | 23-Apr-21 |
| A29970 | Install TVs | 2 | 2 | 26-Apr-21 | 27-Apr-21 |
| A29990 | MEPFP Final Inspections | 2 | 2 | 26-Apr-21 | 27-Apr-21 |
| A29980 | Final Paint | 2 | 2 | 28-Apr-21 | 29-Apr-21 |
| A30000 | Punchlist | 5 | 5 | 30-Apr-21 | 06-May-21 |
| BOH RR & Janitor/Laundry - Rooms 11.13, 11.17 & 11.18 | | 33 | 33 | 26-Feb-21 | 13-Apr-21 |
| A7630 | OH Mechanical | 5 | 5 | 26-Feb-21 | 04-Mar-21 |
| A7640 | OH Electrical | 5 | 5 | 01-Mar-21 | 05-Mar-21 |
| A7670 | OH Fire Protection | 5 | 5 | 02-Mar-21 | 08-Mar-21 |
| A7680 | Above Ceiling Inspection | 1 | 1 | 09-Mar-21 | 09-Mar-21 |
| A7570 | Install Concrete Curb for Mop Sink | 3 | 3 | 10-Mar-21 | 12-Mar-21 |
| A7600 | Epoxy Paint | 2 | 2 | 10-Mar-21 | 11-Mar-21 |
| A7610 | Install Floor Tile | 5 | 5 | 12-Mar-21 | 18-Mar-21 |
| A7580 | Install Mop Sink | 2 | 2 | 15-Mar-21 | 16-Mar-21 |
| A7590 | Prime Paint | 2 | 2 | 17-Mar-21 | 18-Mar-21 |
| A7620 | Set Plumbing Fixtures | 2 | 2 | 19-Mar-21 | 22-Mar-21 |
| A7800 | Seal Concrete Floors | 3 | 3 | 19-Mar-21 | 23-Mar-21 |
| A7660 | Install ACT Grid | 1 | 1 | 23-Mar-21 | 23-Mar-21 |
| A7690 | Sprinklers Head | 2 | 2 | 24-Mar-21 | 25-Mar-21 |
| A7710 | Set & Install OFCI Washer | 4 | 4 | 24-Mar-21 | 29-Mar-21 |
| A7720 | Set & Install OFCI Dryer | 4 | 4 | 24-Mar-21 | 29-Mar-21 |
| A7650 | Install Lighting | 3 | 3 | 26-Mar-21 | 30-Mar-21 |
| A7700 | Grilles, Registers & Diffusers | 2 | 2 | 26-Mar-21 | 29-Mar-21 |
| A7760 | Electrical Trim-out | 2 | 2 | 30-Mar-21 | 31-Mar-21 |
| A7730 | Ceiling Inspections | 1 | 1 | 31-Mar-21 | 31-Mar-21 |
| A7740 | Install ACT Tiles | 1 | 1 | 01-Apr-21 | 01-Apr-21 |
| A7750 | Install Toilet Accessories | 2 | 2 | 01-Apr-21 | 02-Apr-21 |
| A7770 | Fire Alarm Devices | 1 | 1 | 02-Apr-21 | 02-Apr-21 |
| A7780 | Final Paint | 2 | 2 | 05-Apr-21 | 06-Apr-21 |
| A7820 | MEPFP Final Inspections | 2 | 2 | 05-Apr-21 | 06-Apr-21 |
| A89A7220 | Punchlist | 5 | 5 | 07-Apr-21 | 13-Apr-21 |
| Water & Fire - Rooms 11.06 & 11.07 | | 65 | 65 | 24-Feb-21 | 25-May-21 |
| A7280 | OH Mechanical | 5 | 5 | 24-Feb-21 | 02-Mar-21 |
| A8760 | OH Plumbing | 5 | 5 | 25-Feb-21 | 03-Mar-21 |
| A8770 | OH Electrical | 5 | 5 | 26-Feb-21 | 04-Mar-21 |
| A8780 | OH Fire Protection | 5 | 5 | 01-Mar-21 | 05-Mar-21 |
| A8790 | Install FCU | 5 | 5 | 03-Mar-21 | 09-Mar-21 |
| A8920 | Ceiling Inspections | 2 | 2 | 10-Mar-21 | 11-Mar-21 |
| A8800 | FRP Equipment Pads | 5 | 5 | 12-Mar-21 | 18-Mar-21 |
| A8860 | Prime Paint | 2 | 2 | 19-Mar-21 | 22-Mar-21 |
| A8810 | Set Domestic Water Booster Pump | 2 | 2 | 23-Mar-21 | 24-Mar-21 |
| A8820 | Set Pressure Reducing Valve Station | 2 | 2 | 25-Mar-21 | 26-Mar-21 |
| A8840 | Piping for Plumbing Equipment | 15 | 15 | 29-Mar-21 | 16-Apr-21 |
| A8940 | Install Doors & Hardware | 2 | 2 | 29-Mar-21 | 30-Mar-21 |
| A8850 | Electrical for Plumbing Equipment | 5 | 5 | 19-Apr-21 | 23-Apr-21 |
| A8930 | Seal Concrete Floors | 5 | 5 | 26-Apr-21 | 30-Apr-21 |
| A8870 | Install Lighting | 2 | 2 | 03-May-21 | 04-May-21 |
| A8880 | Grilles, Registers & Diffusers | 2 | 2 | 05-May-21 | 06-May-21 |
| A8890 | Sprinkler Heads | 2 | 2 | 07-May-21 | 10-May-21 |
| A8900 | Fire Alarm Devices | 2 | 2 | 11-May-21 | 12-May-21 |
| A8910 | Electrical Trim-out | 2 | 2 | 13-May-21 | 14-May-21 |
| A8950 | Final MEPFP Inspections | 2 | 2 | 17-May-21 | 18-May-21 |
| A8970 | Final Paint | 2 | 2 | 17-May-21 | 18-May-21 |
| A8960 | Punchlist | 5 | 5 | 19-May-21 | 25-May-21 |
| Head In, AV, Main IT - Rooms 11.04, 11.08 & 11.25 | | 53 | 53 | 02-Mar-21 | 13-May-21 |
| A7270 | OH Mechanical | 5 | 5 | 02-Mar-21 | 08-Mar-21 |

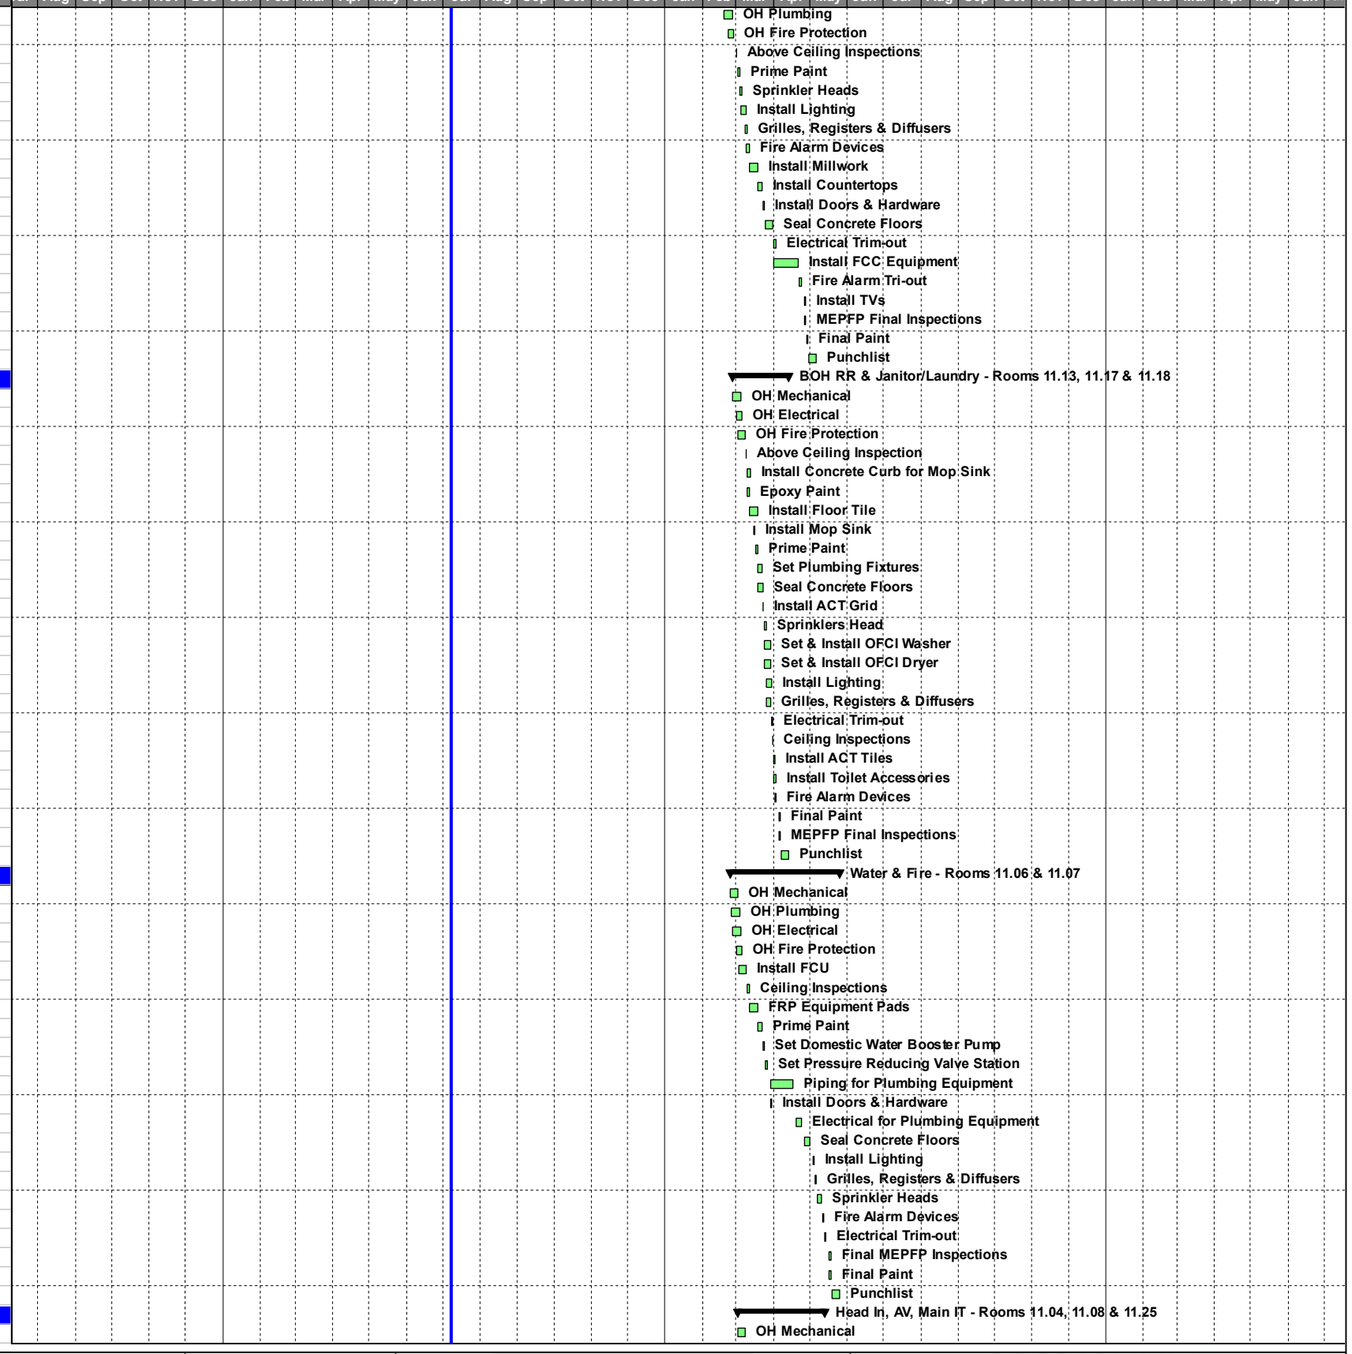

| Activity ID | Activity Name | Original Duration | Remaining Duration | Start | Finish |
|---|---|---|---|---|---|
| A8540 | OH Electrical | 5 | 5 | 03-Mar-21 | 09-Mar-21 |
| A8560 | OH Fire Protection | 5 | 5 | 04-Mar-21 | 10-Mar-21 |
| A8580 | Above Ceiling Inspection - AV Room | 1 | 1 | 11-Mar-21 | 11-Mar-21 |
| A8590 | Prime Paint | 3 | 3 | 12-Mar-21 | 16-Mar-21 |
| A8600 | Install ACT Grid - AV Room | 2 | 2 | 17-Mar-21 | 18-Mar-21 |
| A8750 | Seal Concrete Floors - Head In, Main IT | 5 | 5 | 19-Mar-21 | 25-Mar-21 |
| A8610 | Install Lighting | 3 | 3 | 26-Mar-21 | 30-Mar-21 |
| A8650 | Set AV Racks | 2 | 2 | 26-Mar-21 | 29-Mar-21 |
| A8670 | Install AV Equipment | 5 | 5 | 30-Mar-21 | 05-Apr-21 |
| A8620 | Sprinkler Heads | 2 | 2 | 31-Mar-21 | 01-Apr-21 |
| A8630 | Grilles, Registers & Diffusers | 2 | 2 | 02-Apr-21 | 05-Apr-21 |
| A8640 | Fire Alarm Devices | 3 | 3 | 06-Apr-21 | 08-Apr-21 |
| A8660 | Pull Cables & Terminate | 15 | 15 | 06-Apr-21 | 26-Apr-21 |
| A8680 | Install Doors & Hardware | 3 | 3 | 06-Apr-21 | 08-Apr-21 |
| A8690 | Ceiling Inspections | 1 | 1 | 09-Apr-21 | 09-Apr-21 |
| A8700 | Install ACT Tiles | 2 | 2 | 12-Apr-21 | 13-Apr-21 |
| A8710 | Electrical Trim-out | 5 | 5 | 27-Apr-21 | 03-May-21 |
| A8720 | Final Paint | 3 | 3 | 04-May-21 | 06-May-21 |
| A8730 | MEPFP Final Inspections | 2 | 2 | 04-May-21 | 05-May-21 |
| A8740 | Punchlist | 5 | 5 | 07-May-21 | 13-May-21 |
| Corridors - Rooms 11.09, 11.22 | | 40 | 40 | 17-Mar-21 | 11-May-21 |
| A8990 | Prime Paint | 5 | 5 | 17-Mar-21 | 23-Mar-21 |
| A7300 | Sprinkler Heads | 5 | 5 | 24-Mar-21 | 30-Mar-21 |
| A8550 | Lighting | 5 | 5 | 29-Mar-21 | 02-Apr-21 |
| A8980 | Fire Alarm Devices | 5 | 5 | 01-Apr-21 | 07-Apr-21 |
| A9030 | Install Doors & Hardware | 5 | 5 | 08-Apr-21 | 14-Apr-21 |
| A9000 | Seal Concrete Floors | 5 | 5 | 15-Apr-21 | 21-Apr-21 |
| A9010 | Electrical Trim-out | 5 | 5 | 22-Apr-21 | 28-Apr-21 |
| A9020 | Final MEPFP Inspections | 3 | 3 | 29-Apr-21 | 03-May-21 |
| A9040 | Final Paint | 4 | 4 | 29-Apr-21 | 04-May-21 |
| A9050 | Punchlist | 5 | 5 | 05-May-21 | 11-May-21 |
| Quad 2 | | 155 | 155 | 14-Dec-20 | 23-Jul-21 |
| MEPFP Mains Rough-in | | 41 | 41 | 14-Dec-20 | 11-Feb-21 |
| OHRI-EL-Q2-1 | Spray Fireproofing - First Pass - CL-N/S-E8/N8-E/W | 10 | 10 | 14-Dec-20 | 29-Dec-20 |
| OHRI-EL-Q2-1 | Install Subroof - CL-N/S-E8/N8-E/W | 15 | 15 | 30-Dec-20 | 20-Jan-21 |
| OHRI-EL-Q2-1 | Mechanical Mains - CL-N/S-E8/N8-E/W | 10 | 10 | 12-Jan-21 | 25-Jan-21 |
| OHRI-EL-Q2-1 | Electrical Mains - CL-N/S-E8/N8-E/W | 10 | 10 | 14-Jan-21 | 27-Jan-21 |
| OHRI-EL-Q2-1 | Plumbing Mains - CL-N/S-E8/N8-E/W | 10 | 10 | 18-Jan-21 | 29-Jan-21 |
| OHRI-EL-Q2-1 | Fire Protection Mains - CL-N/S-E8/N8-E/W | 10 | 10 | 20-Jan-21 | 02-Feb-21 |
| OHRI-EL-Q2-1 | Cable Tray AV/IT Mains - CL-N/S-E8/N8-E/W | 10 | 10 | 22-Jan-21 | 04-Feb-21 |
| OHRI-EL-Q2-1 | Spray Fireproofing - Final Pass - CL-N/S-E8/N8-E/W | 10 | 10 | 29-Jan-21 | 11-Feb-21 |
| Masonry Walls & Partitions | | 20 | 20 | 03-Feb-21 | 02-Mar-21 |
| MAS-EL-Q2-1( | Masonry Wall - CL-N/S-E4/N8-E/W | 10 | 10 | 03-Feb-21 | 16-Feb-21 |
| ELEC-EL-Q2-1 | Electrical Rough-in - CL-N/S-E4/N8-E/W | 10 | 10 | 03-Feb-21 | 16-Feb-21 |
| PLM-EL-Q2-10 | Plumbing Rough-in - CL-N/S-E4/N8-E/W | 10 | 10 | 03-Feb-21 | 16-Feb-21 |
| MAS-EL-Q2-1( | Masonry Wall - CL-E4-E8/N8-E/W | 10 | 10 | 17-Feb-21 | 02-Mar-21 |
| ELEC-EL-Q2-1 | Electrical Rough-in - CL-E4-E8/N8-E/W | 10 | 10 | 17-Feb-21 | 02-Mar-21 |
| PLM-EL-Q2-10 | Plumbing Rough-in - CL-E4-E8/N8-E/W | 10 | 10 | 17-Feb-21 | 02-Mar-21 |
| Shop, Storage - Rooms 11.28 & 12.05 | | 39 | 39 | 17-Feb-21 | 12-Apr-21 |
| A9130 | OH Mechanical | 5 | 5 | 17-Feb-21 | 23-Feb-21 |
| A9140 | OH Electrical | 5 | 5 | 18-Feb-21 | 24-Feb-21 |
| A9150 | OH Fire Protection | 5 | 5 | 19-Feb-21 | 25-Feb-21 |
| A9220 | Install FCU | 5 | 5 | 24-Feb-21 | 02-Mar-21 |
| A9160 | Prime Paint | 2 | 2 | 26-Feb-21 | 01-Mar-21 |
| A9170 | Install Doors & Hardware | 2 | 2 | 02-Mar-21 | 03-Mar-21 |
| A9230 | Grilles, Registers & Diffusers | 2 | 2 | 03-Mar-21 | 04-Mar-21 |
| A9180 | Install Roll-up Door | 5 | 5 | 04-Mar-21 | 10-Mar-21 |
| A9200 | Sprinkler Heads | 2 | 2 | 11-Mar-21 | 12-Mar-21 |
| A9190 | Install Lighting | 3 | 3 | 15-Mar-21 | 17-Mar-21 |
| A9210 | Fire Alarm Devices | 3 | 3 | 18-Mar-21 | 22-Mar-21 |
| A9240 | Seal Concrete Floors | 5 | 5 | 23-Mar-21 | 29-Mar-21 |
| A9250 | Electrical Trim-out | 2 | 2 | 30-Mar-21 | 31-Mar-21 |
| A9260 | Final MEPFP Inspections | 2 | 2 | 01-Apr-21 | 02-Apr-21 |
| A9270 | Final Paint | 3 | 3 | 01-Apr-21 | 05-Apr-21 |
| A9280 | Punchlist | 5 | 5 | 06-Apr-21 | 12-Apr-21 |
| Main Electrical, EE - Rooms 11.05 & 12.01 | | 97 | 97 | 17-Feb-21 | 02-Jul-21 |
| A9300 | OH Mechanical | 5 | 5 | 17-Feb-21 | 23-Feb-21 |
| A9310 | OH Electrical | 10 | 10 | 18-Feb-21 | 03-Mar-21 |
| A9320 | OH Fire Protection | 5 | 5 | 19-Feb-21 | 25-Feb-21 |
| A9330 | Install FCUs (2) | 5 | 5 | 24-Feb-21 | 02-Mar-21 |

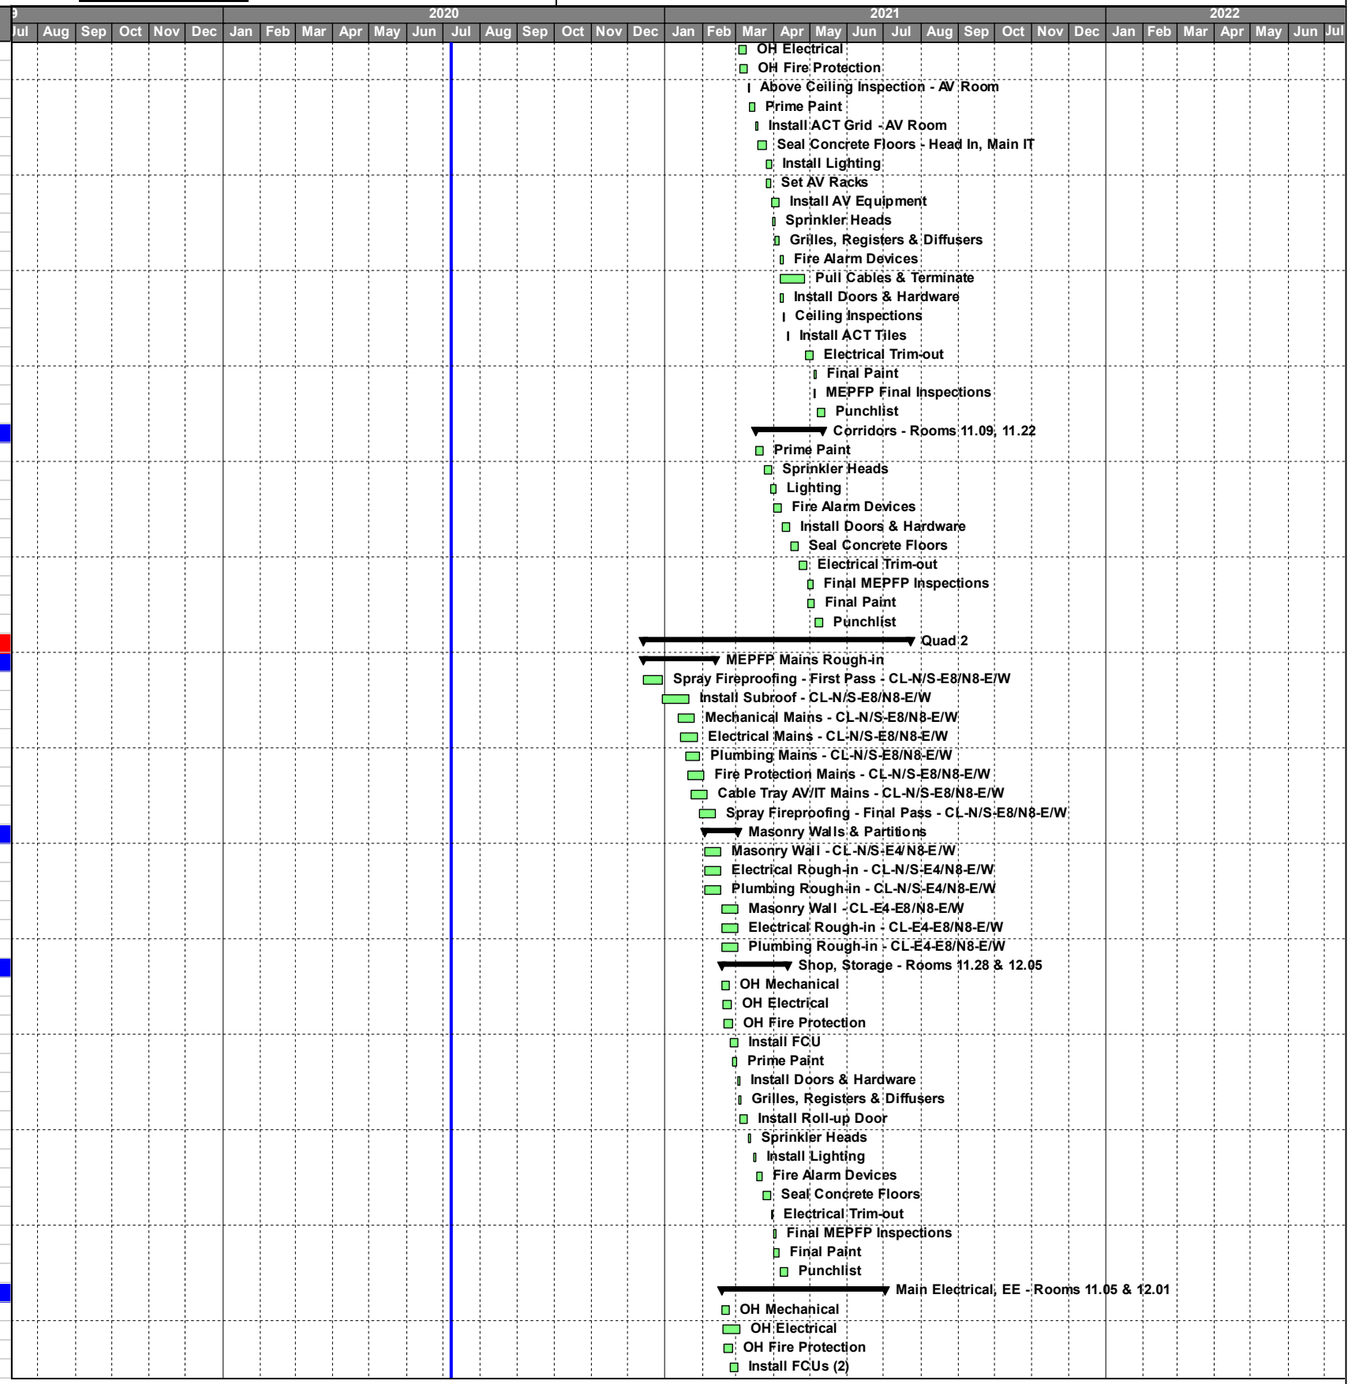

| Activity ID | Activity Name | Original Duration | Remaining Duration | Start | Finish |
|---|---|---|---|---|---|
| A9340 | Install AC Unit | 5 | 5 | 26-Feb-21 | 04-Mar-21 |
| A9350 | FRP Equipment Pads | 5 | 5 | 05-Mar-21 | 11-Mar-21 |
| A9360 | Set Transformers (5) | 5 | 5 | 12-Mar-21 | 18-Mar-21 |
| A9380 | Set ATS's (3) | 5 | 5 | 12-Mar-21 | 18-Mar-21 |
| A9390 | Set UPS's (2) | 5 | 5 | 12-Mar-21 | 18-Mar-21 |
| A9400 | Set MSS1 | 5 | 5 | 12-Mar-21 | 18-Mar-21 |
| A9410 | Set MSS2 | 5 | 5 | 12-Mar-21 | 18-Mar-21 |
| A9450 | Prime Paint | 5 | 5 | 12-Mar-21 | 18-Mar-21 |
| A9370 | Set Panels | 5 | 5 | 19-Mar-21 | 25-Mar-21 |
| A9420 | Electrical for Equipment | 30 | 30 | 19-Mar-21 | 29-Apr-21 |
| A9430 | Pull Wire & Terminate | 5 | 5 | 30-Apr-21 | 06-May-21 |
| A9460 | Sprinkler Heads | 5 | 5 | 07-May-21 | 13-May-21 |
| A9510 | Test & Start-up Electrical Equipment | 5 | 5 | 07-May-21 | 13-May-21 |
| A9520 | Permanent Power Available | 0 | 0 | | 13-May-21 |
| A9470 | Install Lighting | 5 | 5 | 14-May-21 | 20-May-21 |
| A9480 | Grilles, Registers & Diffusers | 5 | 5 | 21-May-21 | 27-May-21 |
| A9490 | Install Doors & Hardware | 5 | 5 | 28-May-21 | 04-Jun-21 |
| A9440 | Seal Concrete Floors | 5 | 5 | 07-Jun-21 | 11-Jun-21 |
| A9500 | Electrical Trim-out | 5 | 5 | 14-Jun-21 | 18-Jun-21 |
| A9530 | MEPFP Final Inspections | 5 | 5 | 21-Jun-21 | 25-Jun-21 |
| A9540 | Final Paint | 5 | 5 | 21-Jun-21 | 25-Jun-21 |
| A9550 | Punchlist | 5 | 5 | 28-Jun-21 | 02-Jul-21 |
| **Main Chiller & Boiler - Rooms 12.03 & 12.02** | | **71** | **71** | **17-Feb-21** | **26-May-21** |
| A9070 | OH Mechanical | 5 | 5 | 17-Feb-21 | 23-Feb-21 |
| A9560 | OH Electrical | 5 | 5 | 18-Feb-21 | 24-Feb-21 |
| A9570 | OH Plumbing | 5 | 5 | 19-Feb-21 | 25-Feb-21 |
| A9580 | OH Fire Protection | 5 | 5 | 22-Feb-21 | 26-Feb-21 |
| A9620 | Install FCU - Main Chiller | 5 | 5 | 24-Feb-21 | 02-Mar-21 |
| A9590 | FRP Equipment Pads | 5 | 5 | 01-Mar-21 | 05-Mar-21 |
| A9630 | Install FCU - Boiler | 5 | 5 | 03-Mar-21 | 09-Mar-21 |
| A9600 | Set Chiller 1 | 5 | 5 | 08-Mar-21 | 12-Mar-21 |
| A9610 | Set Chiller 2 | 5 | 5 | 08-Mar-21 | 12-Mar-21 |
| A9640 | Set Pumps | 5 | 5 | 08-Mar-21 | 12-Mar-21 |
| A9650 | Set Heat Exchanger | 5 | 5 | 08-Mar-21 | 12-Mar-21 |
| A9660 | Set Expansion Tank | 5 | 5 | 08-Mar-21 | 12-Mar-21 |
| A9670 | Set Gas Water Heater 1 | 5 | 5 | 08-Mar-21 | 12-Mar-21 |
| A9680 | Set Gas Water Heater 2 | 5 | 5 | 08-Mar-21 | 12-Mar-21 |
| A9690 | Set Boiler 1 | 5 | 5 | 08-Mar-21 | 12-Mar-21 |
| A9700 | Set Boiler 2 | 5 | 5 | 08-Mar-21 | 12-Mar-21 |
| A9710 | Set Boiler 3 | 5 | 5 | 08-Mar-21 | 12-Mar-21 |
| A9880 | Grilles, Registers & Diffusers | 5 | 5 | 10-Mar-21 | 16-Mar-21 |
| A9720 | Piping for Mechanical Equipment | 30 | 30 | 15-Mar-21 | 23-Apr-21 |
| A9730 | Piping for Plumbing Equipment | 15 | 15 | 15-Mar-21 | 02-Apr-21 |
| A9750 | Electrical for Plumbing Equipment | 10 | 10 | 29-Mar-21 | 09-Apr-21 |
| A9740 | Electrical for Mechanical Equipment | 15 | 15 | 12-Apr-21 | 30-Apr-21 |
| A9760 | Prime Paint | 3 | 3 | 12-Apr-21 | 14-Apr-21 |
| A9840 | Start-up & Test Plumbing Equipment | 5 | 5 | 12-Apr-21 | 16-Apr-21 |
| A9770 | Sprinkler Heads | 2 | 2 | 15-Apr-21 | 16-Apr-21 |
| A9780 | Install Lighting | 4 | 4 | 19-Apr-21 | 22-Apr-21 |
| A9790 | Fire Alarm Devices | 3 | 3 | 23-Apr-21 | 27-Apr-21 |
| A9800 | Electrical Trim-out | 5 | 5 | 28-Apr-21 | 04-May-21 |
| A9830 | Start-up & Test Mechanical Equipment | 5 | 5 | 03-May-21 | 07-May-21 |
| A9810 | Seal Concrete Floors | 5 | 5 | 05-May-21 | 11-May-21 |
| A9820 | Install Doors & Hardware | 3 | 3 | 12-May-21 | 14-May-21 |
| A9850 | MEPFP Final Inspections | 2 | 2 | 12-May-21 | 13-May-21 |
| A9860 | Final Paint | 3 | 3 | 17-May-21 | 19-May-21 |
| A9870 | Punchlist | 5 | 5 | 20-May-21 | 26-May-21 |
| **Vestibule, DAS Cell, Cash Room - Rooms 12.04, 12.07 & 12.11** | | **39** | **39** | **24-Feb-21** | **19-Apr-21** |
| A9890 | OH Mechanical | 5 | 5 | 24-Feb-21 | 02-Mar-21 |
| A9900 | OH Electrical | 5 | 5 | 25-Feb-21 | 03-Mar-21 |
| A9910 | OH Plumbing | 5 | 5 | 26-Feb-21 | 04-Mar-21 |
| A9920 | OH Fire Protection | 5 | 5 | 01-Mar-21 | 05-Mar-21 |
| A9990 | Prime Paint | 2 | 2 | 08-Mar-21 | 09-Mar-21 |
| A10000 | Install ACT Grid | 4 | 4 | 10-Mar-21 | 15-Mar-21 |
| A10010 | Sprinkler Heads | 2 | 2 | 16-Mar-21 | 17-Mar-21 |
| A10020 | Install Lighting | 3 | 3 | 17-Mar-21 | 19-Mar-21 |
| A10030 | Grilles, Registers & Diffusers | 3 | 3 | 18-Mar-21 | 22-Mar-21 |
| A10040 | Fire Alarm Devices - In-Ceiling | 3 | 3 | 19-Mar-21 | 23-Mar-21 |
| A10050 | Ceiling Inspections | 1 | 1 | 24-Mar-21 | 24-Mar-21 |
| A10060 | Install ACT Tiles | 2 | 2 | 25-Mar-21 | 26-Mar-21 |

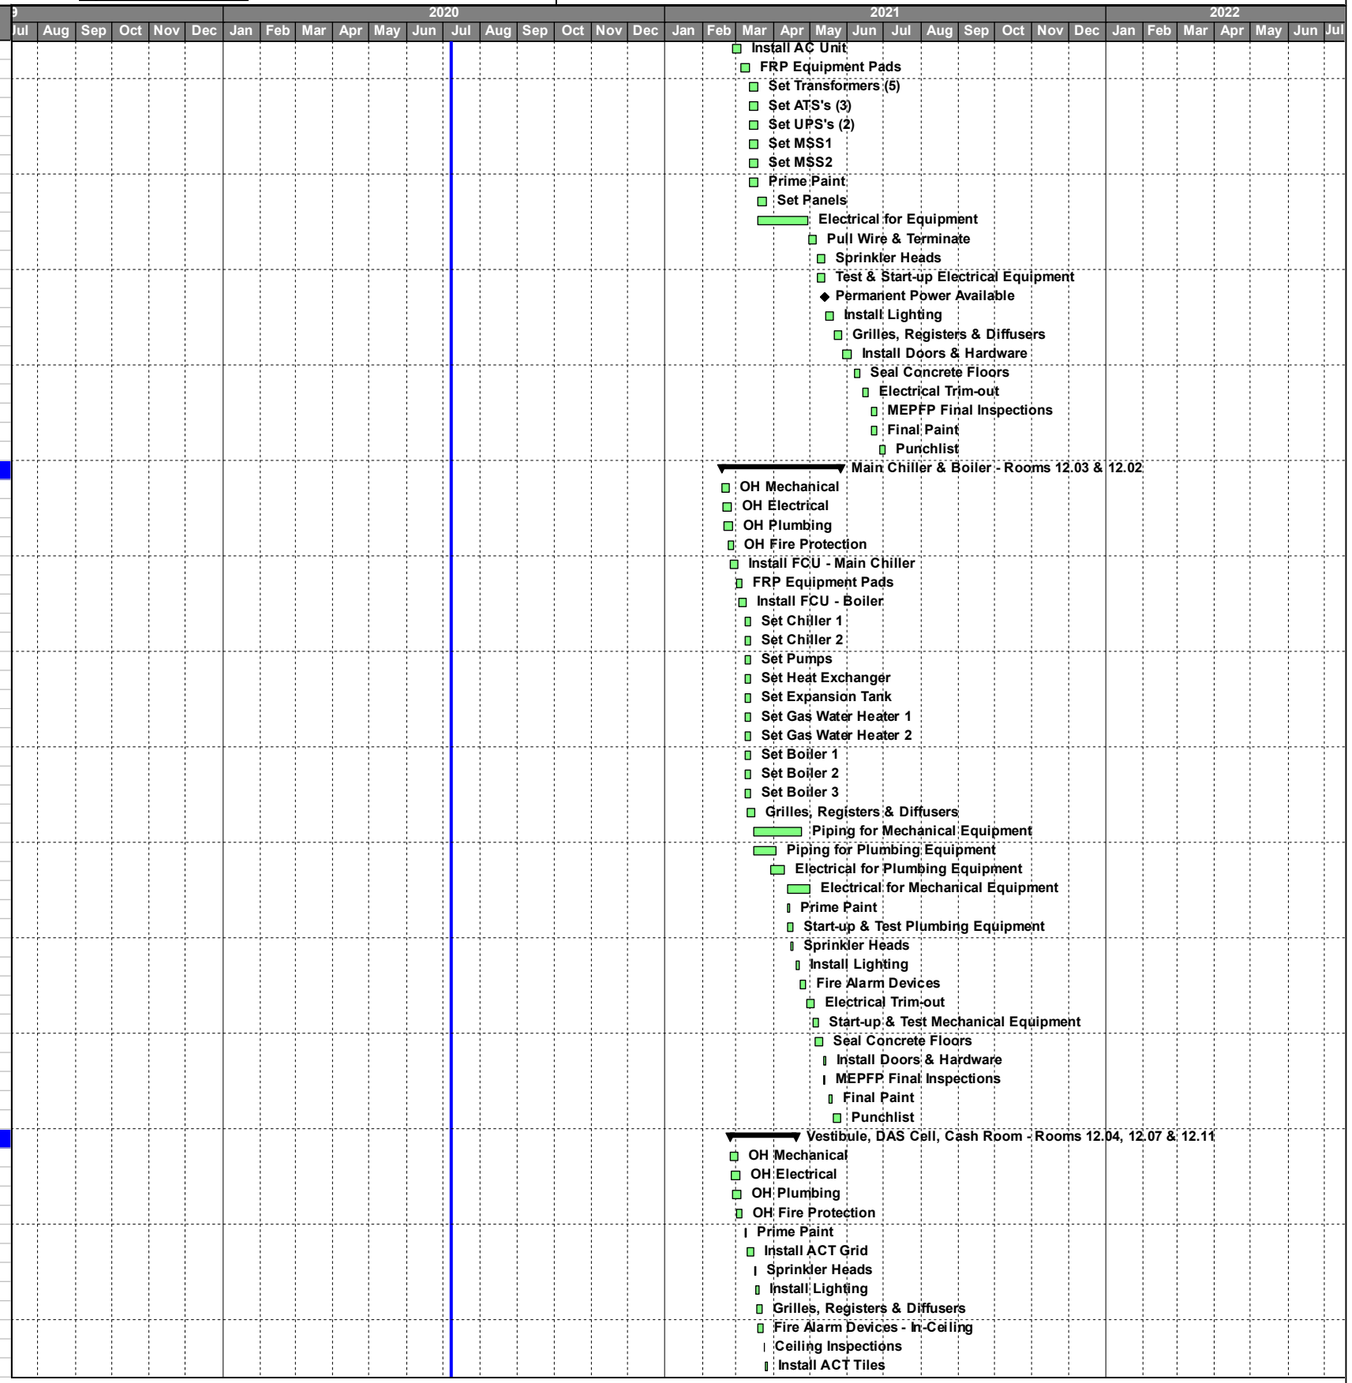

| Activity ID | Activity Name | Original Duration | Remaining Duration | Start | Finish |
|---|---|---|---|---|---|
| A10080 | Seal Concrete Floors | 5 | 5 | 29-Mar-21 | 02-Apr-21 |
| A10120 | Install Doors & Hardware | 2 | 2 | 05-Apr-21 | 06-Apr-21 |
| A10130 | Electrical Finishes - On-Wall | 2 | 2 | 05-Apr-21 | 06-Apr-21 |
| A10140 | Fire Alarm Devices - On-Wall | 2 | 2 | 07-Apr-21 | 08-Apr-21 |
| A10170 | Final Paint | 2 | 2 | 07-Apr-21 | 08-Apr-21 |
| A10160 | MEPFP Final Inspections | 2 | 2 | 09-Apr-21 | 12-Apr-21 |
| A10180 | Punchlist | 5 | 5 | 13-Apr-21 | 19-Apr-21 |
| Commissary/Club Kitchen & FS Office - 12.08 & 12.12 | | 80 | 80 | 03-Mar-21 | 23-Jun-21 |
| A9980 | Layout & Top Track | 3 | 3 | 03-Mar-21 | 05-Mar-21 |
| A9970 | OH Mechanical | 15 | 15 | 08-Mar-21 | 26-Mar-21 |
| A9960 | OH Plumbing | 15 | 15 | 11-Mar-21 | 31-Mar-21 |
| A9950 | OH Electrical | 10 | 10 | 16-Mar-21 | 29-Mar-21 |
| A9940 | OH Fire Protection | 10 | 10 | 19-Mar-21 | 01-Apr-21 |
| A9930 | Frame Walls | 3 | 3 | 02-Apr-21 | 06-Apr-21 |
| A10520 | In-Wall Electrical Rough-in | 3 | 3 | 06-Apr-21 | 08-Apr-21 |
| A10100 | Rough-in Exhaust Hoods | 5 | 5 | 07-Apr-21 | 13-Apr-21 |
| A10510 | In-Wall Plumbing Rough-in | 3 | 3 | 07-Apr-21 | 09-Apr-21 |
| A9100 | Hang, Tape & Finish Drywall | 8 | 8 | 14-Apr-21 | 23-Apr-21 |
| A10490 | Above Ceiling Inspections | 2 | 2 | 14-Apr-21 | 15-Apr-21 |
| A9090 | FRP Wall Panels | 4 | 4 | 26-Apr-21 | 29-Apr-21 |
| A10070 | Prime Paint - FS Office | 1 | 1 | 26-Apr-21 | 26-Apr-21 |
| A10500 | Install ACT Grid | 3 | 3 | 27-Apr-21 | 29-Apr-21 |
| A10150 | Sprinkler Heads | 2 | 2 | 30-Apr-21 | 03-May-21 |
| A10330 | Grilles, Registers & Diffusers | 2 | 2 | 03-May-21 | 04-May-21 |
| A10480 | Install Lighting | 4 | 4 | 04-May-21 | 07-May-21 |
| A10110 | Fire Alarm Devices | 2 | 2 | 10-May-21 | 11-May-21 |
| A10560 | Ceiling Inspections | 2 | 2 | 12-May-21 | 13-May-21 |
| A10090 | Resinous Flooring | 5 | 5 | 14-May-21 | 20-May-21 |
| A10530 | Install Kitchen Equipment | 10 | 10 | 21-May-21 | 04-Jun-21 |
| A10550 | Install ACT Tiles | 2 | 2 | 21-May-21 | 24-May-21 |
| A10540 | Electrical Trim-out | 3 | 3 | 07-Jun-21 | 09-Jun-21 |
| A10570 | Install Doors & Hardware | 3 | 3 | 10-Jun-21 | 14-Jun-21 |
| A10590 | MEPFP Final Inspections | 2 | 2 | 10-Jun-21 | 11-Jun-21 |
| A10580 | Final Paint | 2 | 2 | 15-Jun-21 | 16-Jun-21 |
| A10600 | Punchlist | 5 | 5 | 17-Jun-21 | 23-Jun-21 |
| Electrical & IT - Rooms 12.09 & 12.10 | | 74 | 74 | 03-Mar-21 | 15-Jun-21 |
| A10190 | Layout & Top Track | 1 | 1 | 03-Mar-21 | 03-Mar-21 |
| A10200 | Frame Walls | 2 | 2 | 04-Mar-21 | 05-Mar-21 |
| A10210 | Rough-in Electrical | 3 | 3 | 08-Mar-21 | 10-Mar-21 |
| A10220 | In-Wall Inspection | 1 | 1 | 11-Mar-21 | 11-Mar-21 |
| A10230 | In-Wall Insulation | 1 | 1 | 12-Mar-21 | 12-Mar-21 |
| A10240 | Hang, Tape & Finish Drywall | 4 | 4 | 14-Apr-21 | 19-Apr-21 |
| A10250 | OH Mechanical | 5 | 5 | 20-Apr-21 | 26-Apr-21 |
| A10260 | FRP Equipment Pads | 3 | 3 | 20-Apr-21 | 22-Apr-21 |
| A10270 | OH Electrical | 5 | 5 | 21-Apr-21 | 27-Apr-21 |
| A10280 | OH Fire Protection | 3 | 3 | 22-Apr-21 | 26-Apr-21 |
| A10290 | Prime Paint | 2 | 2 | 23-Apr-21 | 26-Apr-21 |
| A10300 | Set Transformers | 2 | 2 | 27-Apr-21 | 28-Apr-21 |
| A10310 | Set IT Racks | 2 | 2 | 27-Apr-21 | 28-Apr-21 |
| A10320 | Set Panel Boxes | 2 | 2 | 27-Apr-21 | 28-Apr-21 |
| A10340 | Set AC Units (4) | 2 | 2 | 27-Apr-21 | 28-Apr-21 |
| A10350 | Install Panel Interiors | 3 | 3 | 29-Apr-21 | 03-May-21 |
| A10360 | Pull Cable & Terminate | 15 | 15 | 29-Apr-21 | 19-May-21 |
| A10370 | Hook-up Transformers | 5 | 5 | 29-Apr-21 | 05-May-21 |
| A10380 | Install Doors & Hardware | 2 | 2 | 29-Apr-21 | 30-Apr-21 |
| A10390 | OH Mechanical Finishes | 2 | 2 | 29-Apr-21 | 30-Apr-21 |
| A10400 | Pull Wire & Terminate | 15 | 15 | 04-May-21 | 24-May-21 |
| A10410 | Install Lighting | 3 | 3 | 25-May-21 | 27-May-21 |
| A10420 | Install Electrical Finishes | 2 | 2 | 28-May-21 | 01-Jun-21 |
| A10430 | Install Fire Alarm Devices | 2 | 2 | 28-May-21 | 01-Jun-21 |
| A10440 | Seal Concrete Floors | 3 | 3 | 02-Jun-21 | 04-Jun-21 |
| A10450 | MEPFP Final Inspections | 2 | 2 | 02-Jun-21 | 03-Jun-21 |
| A10460 | Final Paint | 2 | 2 | 07-Jun-21 | 08-Jun-21 |
| A10470 | Punchlist | 5 | 5 | 09-Jun-21 | 15-Jun-21 |
| Equipment, Coach, Sports Med, Fitness, Team Lounge - Rooms 12.14-12.18 & 12.19 | | 93 | 93 | 03-Mar-21 | 13-Jul-21 |
| A9110 | Layout & Top Track | 2 | 2 | 03-Mar-21 | 04-Mar-21 |
| A10910 | OH Mechanical | 10 | 10 | 05-Mar-21 | 18-Mar-21 |
| A10900 | OH Electrical | 10 | 10 | 09-Mar-21 | 22-Mar-21 |
| A10890 | OH Plumbing | 10 | 10 | 11-Mar-21 | 24-Mar-21 |
| A10880 | OH Fire Protection | 10 | 10 | 15-Mar-21 | 26-Mar-21 |

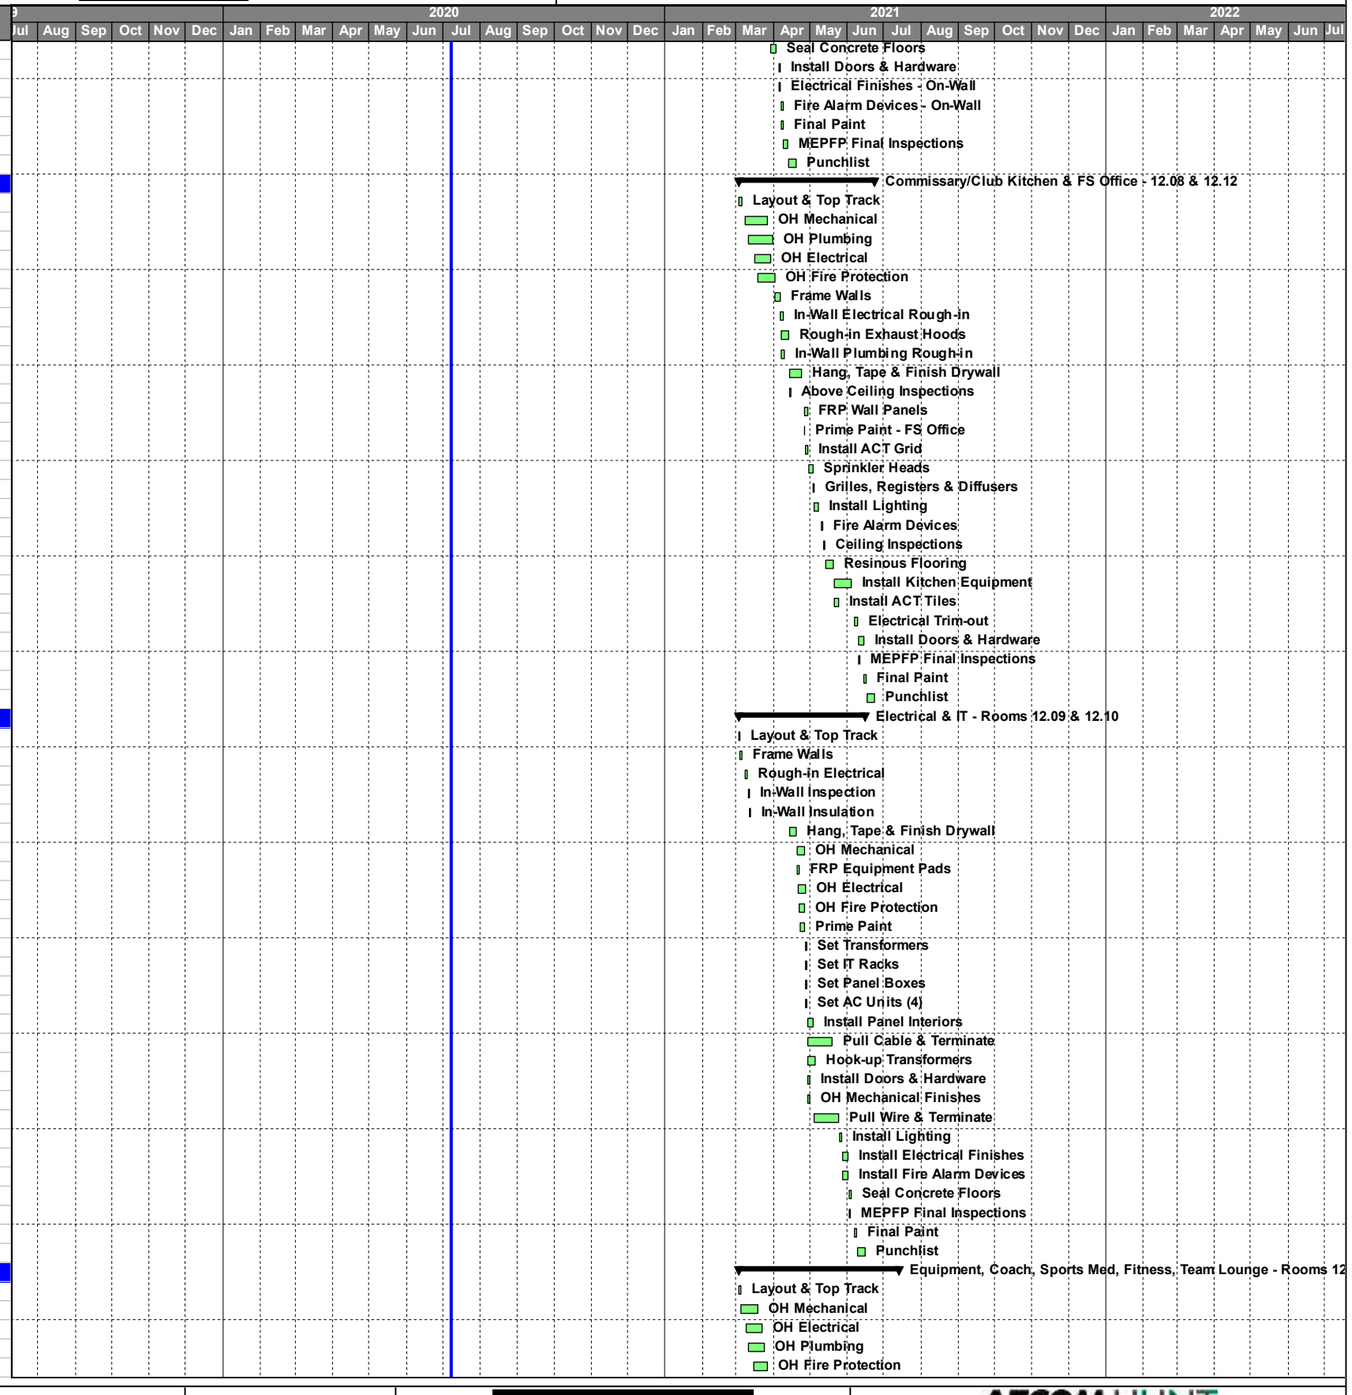

| Activity ID | Activity Name | Original Duration | Remaining Duration | Start | Finish |
|---|---|---|---|---|---|
| A10860 | Frame Walls | 5 | 5 | 29-Mar-21 | 02-Apr-21 |
| A10870 | Above Ceiling Inspections | 2 | 2 | 29-Mar-21 | 30-Mar-21 |
| A10850 | In-Wall Electrical Rough-in | 5 | 5 | 31-Mar-21 | 06-Apr-21 |
| A10840 | In-Wall Plumbing Rough-in | 5 | 5 | 02-Apr-21 | 08-Apr-21 |
| A10800 | Frame Drywall Ceilings | 5 | 5 | 05-Apr-21 | 09-Apr-21 |
| A10830 | In-Wall Inspections | 2 | 2 | 09-Apr-21 | 12-Apr-21 |
| A10820 | Hang, Tape & Finish Drywall | 8 | 8 | 14-Apr-21 | 23-Apr-21 |
| A10630 | Install Shower | 2 | 2 | 26-Apr-21 | 27-Apr-21 |
| A10810 | Prime Paint | 3 | 3 | 26-Apr-21 | 28-Apr-21 |
| A10640 | Install Wall Tile | 5 | 5 | 28-Apr-21 | 04-May-21 |
| A10790 | Install ACT Grid | 5 | 5 | 29-Apr-21 | 05-May-21 |
| A10980 | Install Washer & Dryer | 5 | 5 | 29-Apr-21 | 05-May-21 |
| A10750 | Install Lighting | 5 | 5 | 06-May-21 | 12-May-21 |
| A10740 | Sprinkler Heads | 5 | 5 | 10-May-21 | 14-May-21 |
| A10730 | Grilles, Registers & Diffusers | 5 | 5 | 12-May-21 | 18-May-21 |
| A10720 | Fire Alarm Devices | 5 | 5 | 14-May-21 | 20-May-21 |
| A10710 | ACT Ceiling Inspections | 2 | 2 | 21-May-21 | 24-May-21 |
| A10780 | Ceiling Inspections | 2 | 2 | 21-May-21 | 24-May-21 |
| A10700 | Install ACT Tiles | 2 | 2 | 25-May-21 | 26-May-21 |
| A10770 | Hang, Tape & Finish Drywall Ceilings | 5 | 5 | 25-May-21 | 01-Jun-21 |
| A10660 | Install Carpet | 3 | 3 | 27-May-21 | 01-Jun-21 |
| A10670 | Seal Concrete Floors | 5 | 5 | 27-May-21 | 03-Jun-21 |
| A10680 | Install Sports Flooring | 5 | 5 | 27-May-21 | 03-Jun-21 |
| A10690 | Install Floor Tile | 5 | 5 | 27-May-21 | 03-Jun-21 |
| A10760 | Prime Paint Ceilings | 5 | 5 | 02-Jun-21 | 08-Jun-21 |
| A10650 | Install Millwork | 10 | 10 | 04-Jun-21 | 17-Jun-21 |
| A10970 | Electrical Trim-out | 5 | 5 | 18-Jun-21 | 24-Jun-21 |
| A10990 | Install Countertops | 5 | 5 | 18-Jun-21 | 24-Jun-21 |
| A10620 | Install Sinks | 2 | 2 | 25-Jun-21 | 28-Jun-21 |
| A10950 | MEPFP Final Inspections | 2 | 2 | 25-Jun-21 | 28-Jun-21 |
| A10610 | Install Toilet Accessories | 2 | 2 | 29-Jun-21 | 30-Jun-21 |
| A10960 | Final Paint | 3 | 3 | 01-Jul-21 | 06-Jul-21 |
| A10940 | Punchlist | 5 | 5 | 07-Jul-21 | 13-Jul-21 |
| East Club - Room 12.20, 13.17-18 | | 99 | 99 | 05-Mar-21 | 23-Jul-21 |
| B1000 | Layout & Top Track | 5 | 5 | 05-Mar-21 | 11-Mar-21 |
| B1010 | OH Mechanical | 10 | 10 | 12-Mar-21 | 25-Mar-21 |
| B1020 | OH Electrical | 10 | 10 | 16-Mar-21 | 29-Mar-21 |
| B1030 | OH Plumbing | 10 | 10 | 18-Mar-21 | 31-Mar-21 |
| B1040 | OH Fire Protection | 10 | 10 | 22-Mar-21 | 02-Apr-21 |
| B1050 | Above Ceiling Inspections | 2 | 2 | 05-Apr-21 | 06-Apr-21 |
| B1060 | Frame Walls | 5 | 5 | 05-Apr-21 | 09-Apr-21 |
| B1110 | In-Wall Electrical | 5 | 5 | 07-Apr-21 | 13-Apr-21 |
| B1120 | In-Wall Plumbing | 5 | 5 | 09-Apr-21 | 15-Apr-21 |
| B1070 | Frame Ceilings & Soffitts | 3 | 3 | 12-Apr-21 | 14-Apr-21 |
| B1080 | Install In-Ceiling Lighting | 5 | 5 | 15-Apr-21 | 21-Apr-21 |
| B1130 | In-Wall Inspections | 2 | 2 | 16-Apr-21 | 19-Apr-21 |
| B1140 | Hang, Tape & Finish Drywall | 10 | 10 | 20-Apr-21 | 03-May-21 |
| B1090 | Sprinklers Heads | 4 | 4 | 22-Apr-21 | 27-Apr-21 |
| B1150 | Wood Panels on Wall | 8 | 8 | 04-May-21 | 13-May-21 |
| B1160 | Hang, Tape & Finish Ceilings & Soffitts | 5 | 5 | 04-May-21 | 10-May-21 |
| B1340 | FRP Wall Panels | 3 | 3 | 04-May-21 | 06-May-21 |
| B1170 | Wood Ceilings | 5 | 5 | 11-May-21 | 17-May-21 |
| B1380 | Prime Paint | 3 | 3 | 11-May-21 | 13-May-21 |
| B1100 | Install Custom Metal Ceilings | 10 | 10 | 14-May-21 | 27-May-21 |
| B1180 | Install ACT Grid | 3 | 3 | 14-May-21 | 18-May-21 |
| B1230 | Electrical Trim-out | 8 | 8 | 14-May-21 | 25-May-21 |
| B1240 | Install Millwork | 12 | 12 | 14-May-21 | 01-Jun-21 |
| B1270 | Install Die-Wall | 8 | 8 | 14-May-21 | 25-May-21 |
| B1210 | Grilles, Registers & Diffusers | 3 | 3 | 19-May-21 | 21-May-21 |
| B1220 | Fire Alarm Devices | 2 | 2 | 24-May-21 | 25-May-21 |
| B1190 | Install ACT Tiles | 2 | 2 | 26-May-21 | 27-May-21 |
| B1280 | Electrical Rough-in Bar | 5 | 5 | 26-May-21 | 02-Jun-21 |
| B1200 | Install Chandeliers | 5 | 5 | 28-May-21 | 04-Jun-21 |
| B1290 | Plumbing Rough-in Bar | 5 | 5 | 28-May-21 | 04-Jun-21 |
| B1250 | Install Countertops | 5 | 5 | 07-Jun-21 | 11-Jun-21 |
| B1330 | Install Luxury Vinyl Tile | 8 | 8 | 07-Jun-21 | 16-Jun-21 |
| B1260 | Install Plumbing Fixtures | 3 | 3 | 14-Jun-21 | 16-Jun-21 |
| B1310 | Install Resilient Floors | 8 | 8 | 17-Jun-21 | 28-Jun-21 |
| B1320 | Install Floor Tile | 5 | 5 | 17-Jun-21 | 23-Jun-21 |
| B1360 | MEPFP Final Inspections | 2 | 2 | 17-Jun-21 | 18-Jun-21 |

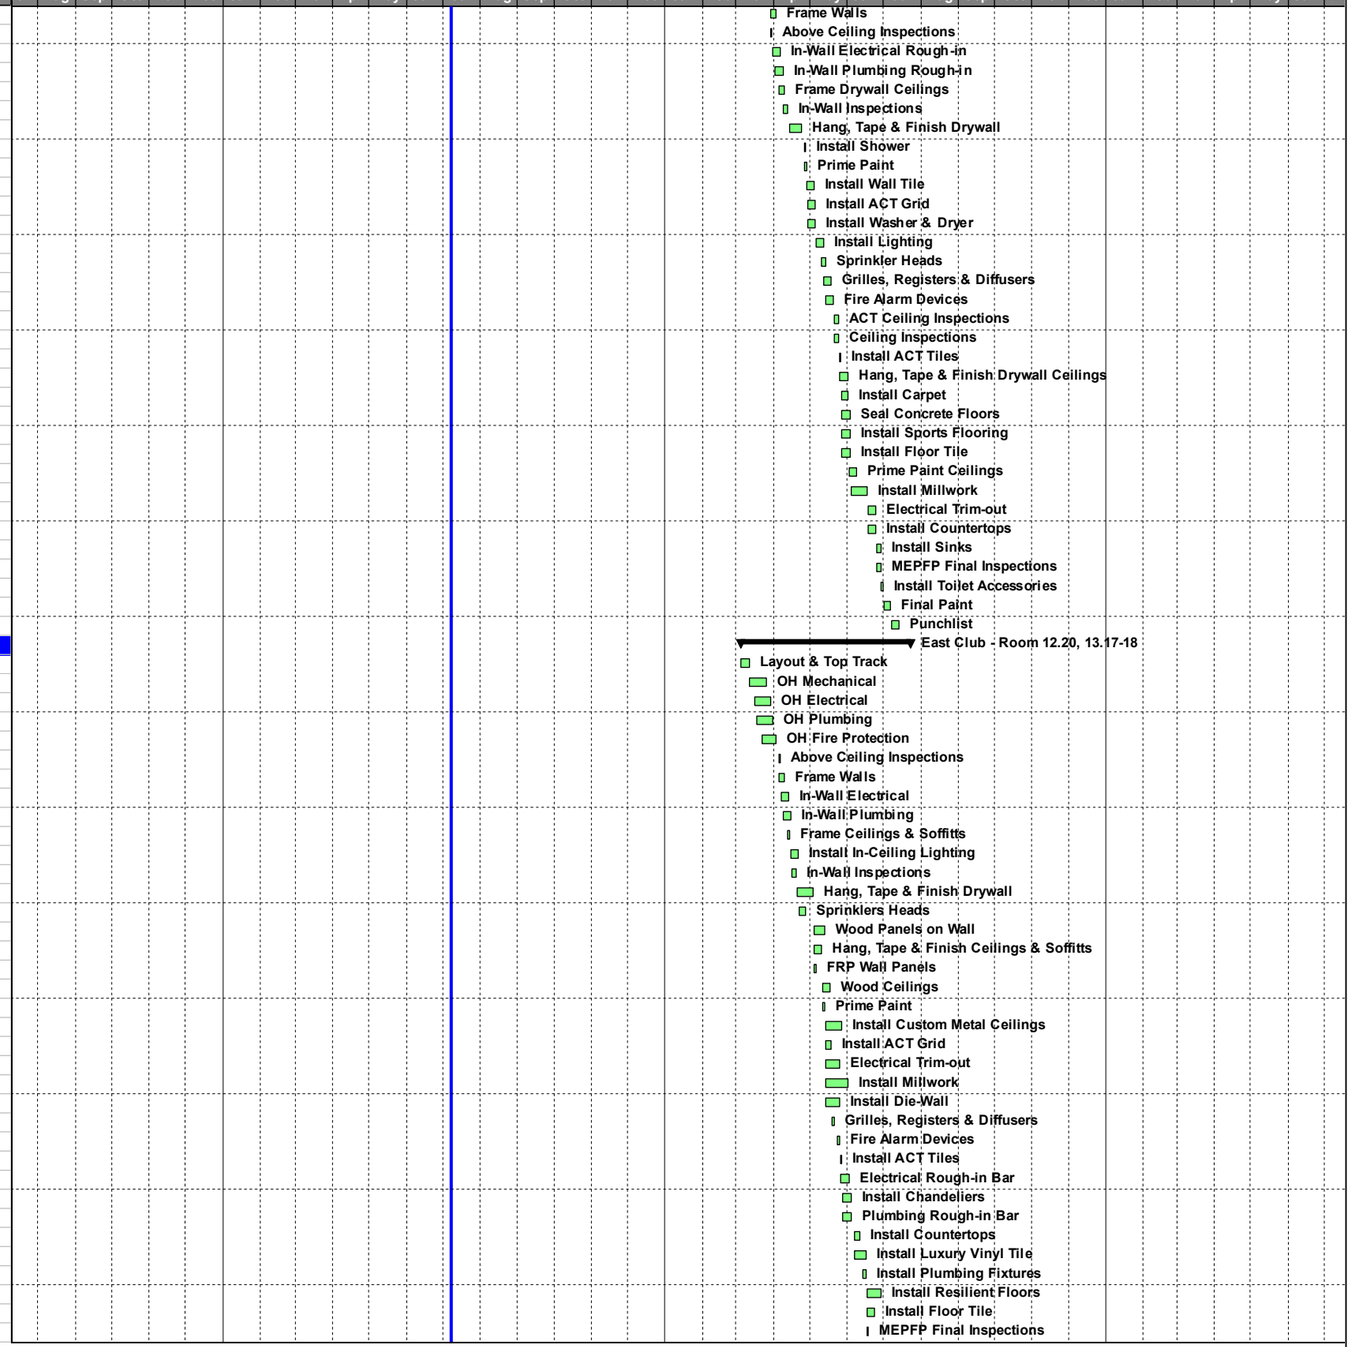

| Activity ID | Activity Name | Original Duration | Remaining Duration | Start | Finish |
|---|---|---|---|---|---|
| B1300 | Install Kitchen Equipment | 10 | 10 | 29-Jun-21 | 13-Jul-21 |
| B1350 | Final Paint | 3 | 3 | 14-Jul-21 | 16-Jul-21 |
| B1370 | Punchlist | 5 | 5 | 19-Jul-21 | 23-Jul-21 |
| Corridors - Room 12.06 | | 40 | 40 | 14-May-21 | 12-Jul-21 |
| A14890 | Prime Paint | 5 | 5 | 14-May-21 | 20-May-21 |
| A14860 | Sprinkler Heads | 5 | 5 | 21-May-21 | 27-May-21 |
| A14870 | Lighting | 5 | 5 | 26-May-21 | 02-Jun-21 |
| A14880 | Fire Alarm Devices | 5 | 5 | 01-Jun-21 | 07-Jun-21 |
| A14930 | Install Doors & Hardware | 5 | 5 | 08-Jun-21 | 14-Jun-21 |
| A14900 | Seal Concrete Floors | 5 | 5 | 15-Jun-21 | 21-Jun-21 |
| A14910 | Electrical Trim-out | 5 | 5 | 22-Jun-21 | 28-Jun-21 |
| A14920 | Final MEPFP Inspections | 3 | 3 | 29-Jun-21 | 01-Jul-21 |
| A14940 | Final Paint | 4 | 4 | 29-Jun-21 | 02-Jul-21 |
| A14950 | Punchlist | 5 | 5 | 06-Jul-21 | 12-Jul-21 |
| Quad 3 | | 164 | 164 | 30-Dec-20 | 19-Aug-21 |
| MEPFP Mains Rough-in | | 41 | 41 | 30-Dec-20 | 25-Feb-21 |
| OHRI-EL-Q3-1 | Spray Fireproofing - First Pass - CL-N/S-S8/E8-E/W | 10 | 10 | 30-Dec-20 | 13-Jan-21 |
| OHRI-EL-Q3-1 | Install Subroof - CL-N/S-S8/E8-E/W | 15 | 15 | 14-Jan-21 | 03-Feb-21 |
| OHRI-EL-Q3-1 | Mechanical Mains - CL-N/S-S8/E8-E/W | 10 | 10 | 26-Jan-21 | 08-Feb-21 |
| OHRI-EL-Q3-1 | Electrical Mains - CL-N/S-S8/E8-E/W | 10 | 10 | 28-Jan-21 | 10-Feb-21 |
| OHRI-EL-Q3-1 | Plumbing Mains - CL-N/S-S8/E8-E/W | 10 | 10 | 01-Feb-21 | 12-Feb-21 |
| OHRI-EL-Q3-1 | Fire Protection Mains - CL-N/S-S8/E8-E/W | 10 | 10 | 03-Feb-21 | 16-Feb-21 |
| OHRI-EL-Q3-1 | Cable Tray AV/IT Mains - CL-N/S-S8/E8-E/W | 10 | 10 | 05-Feb-21 | 18-Feb-21 |
| OHRI-EL-Q3-1 | Spray Fireproofing - Final Pass - CL-N/S-S8/E8-E/W | 10 | 10 | 12-Feb-21 | 25-Feb-21 |
| Masonry Walls & Partitions | | 20 | 20 | 17-Feb-21 | 16-Mar-21 |
| MAS-EL-Q3-1( | Masonry Wall - CL-E4-E8/E/W-S8 | 10 | 10 | 17-Feb-21 | 02-Mar-21 |
| ELEC-EL-Q3-1 | Electrical Rough-in - CL-E4-E8/E/W-S8 | 10 | 10 | 17-Feb-21 | 02-Mar-21 |
| PLM-EL-Q3-10 | Plumbing Rough-in - CL-E4-E8/E/W-S8 | 10 | 10 | 17-Feb-21 | 02-Mar-21 |
| MAS-EL-Q3-1( | Masonry Wall - CL-E4-N/S/E/W-S8 | 10 | 10 | 03-Mar-21 | 16-Mar-21 |
| ELEC-EL-Q3-1 | Electrical Rough-in - CL-E4-N/S/E/W-S8 | 10 | 10 | 03-Mar-21 | 16-Mar-21 |
| PLM-EL-Q3-10 | Plumbing Rough-in - CL-E4-N/S/E/W-S8 | 10 | 10 | 03-Mar-21 | 16-Mar-21 |
| Main Electrical - Room 13.38 | | 97 | 97 | 17-Mar-21 | 02-Aug-21 |
| A11280 | OH Mechanical | 5 | 5 | 17-Mar-21 | 23-Mar-21 |
| A11290 | OH Electrical | 10 | 10 | 18-Mar-21 | 31-Mar-21 |
| A11300 | OH Fire Protection | 5 | 5 | 19-Mar-21 | 25-Mar-21 |
| A11310 | Install FCUs (2) | 5 | 5 | 24-Mar-21 | 30-Mar-21 |
| A11320 | Install AC Unit | 5 | 5 | 26-Mar-21 | 01-Apr-21 |
| A11330 | FRP Equipment Pads | 5 | 5 | 02-Apr-21 | 08-Apr-21 |
| A11340 | Set Transformers (5) | 5 | 5 | 09-Apr-21 | 15-Apr-21 |
| A11360 | Set ATS's (3) | 5 | 5 | 09-Apr-21 | 15-Apr-21 |
| A11370 | Set UPS's (2) | 5 | 5 | 09-Apr-21 | 15-Apr-21 |
| A11380 | Set MSS1 | 5 | 5 | 09-Apr-21 | 15-Apr-21 |
| A11390 | Set MSS2 | 5 | 5 | 09-Apr-21 | 15-Apr-21 |
| A11430 | Prime Paint | 5 | 5 | 09-Apr-21 | 15-Apr-21 |
| A11350 | Set Panels | 5 | 5 | 16-Apr-21 | 22-Apr-21 |
| A11400 | Electrical for Equipment | 30 | 30 | 16-Apr-21 | 27-May-21 |
| A11410 | Pull Wire & Terminate | 5 | 5 | 28-May-21 | 04-Jun-21 |
| A11440 | Sprinkler Heads | 5 | 5 | 07-Jun-21 | 11-Jun-21 |
| A11490 | Test & Start-up Electrical Equipment | 5 | 5 | 07-Jun-21 | 11-Jun-21 |
| A11500 | Permanent Power Available | 0 | 0 | | 11-Jun-21 |
| A11450 | Install Lighting | 5 | 5 | 14-Jun-21 | 18-Jun-21 |
| A11460 | Grilles, Registers & Diffusers | 5 | 5 | 21-Jun-21 | 25-Jun-21 |
| A11470 | Install Doors & Hardware | 5 | 5 | 28-Jun-21 | 02-Jul-21 |
| A11420 | Seal Concrete Floors | 5 | 5 | 06-Jul-21 | 12-Jul-21 |
| A11480 | Electrical Trim-out | 5 | 5 | 13-Jul-21 | 19-Jul-21 |
| A11510 | MEPFP Final Inspections | 5 | 5 | 20-Jul-21 | 26-Jul-21 |
| A11520 | Final Paint | 5 | 5 | 20-Jul-21 | 26-Jul-21 |
| A11530 | Punchlist | 5 | 5 | 27-Jul-21 | 02-Aug-21 |
| Electrical & IT - Rooms 13.14 & 13.15 | | 74 | 74 | 03-Mar-21 | 15-Jun-21 |
| A11000 | Layout & Top Track | 1 | 1 | 03-Mar-21 | 03-Mar-21 |
| A11010 | Frame Walls | 2 | 2 | 04-Mar-21 | 05-Mar-21 |
| A11020 | Rough-in Electrical | 3 | 3 | 08-Mar-21 | 10-Mar-21 |
| A11030 | In-Wall Inspection | 1 | 1 | 11-Mar-21 | 11-Mar-21 |
| A11040 | In-Wall Insulation | 1 | 1 | 12-Mar-21 | 12-Mar-21 |
| A11050 | Hang, Tape & Finish Drywall | 4 | 4 | 14-Apr-21 | 19-Apr-21 |
| A11060 | OH Mechanical | 5 | 5 | 20-Apr-21 | 26-Apr-21 |
| A11090 | FRP Equipment Pads | 3 | 3 | 20-Apr-21 | 22-Apr-21 |
| A11070 | OH Electrical | 5 | 5 | 21-Apr-21 | 27-Apr-21 |
| A11080 | OH Fire Protection | 3 | 3 | 22-Apr-21 | 26-Apr-21 |
| A11190 | Prime Paint | 2 | 2 | 23-Apr-21 | 26-Apr-21 |

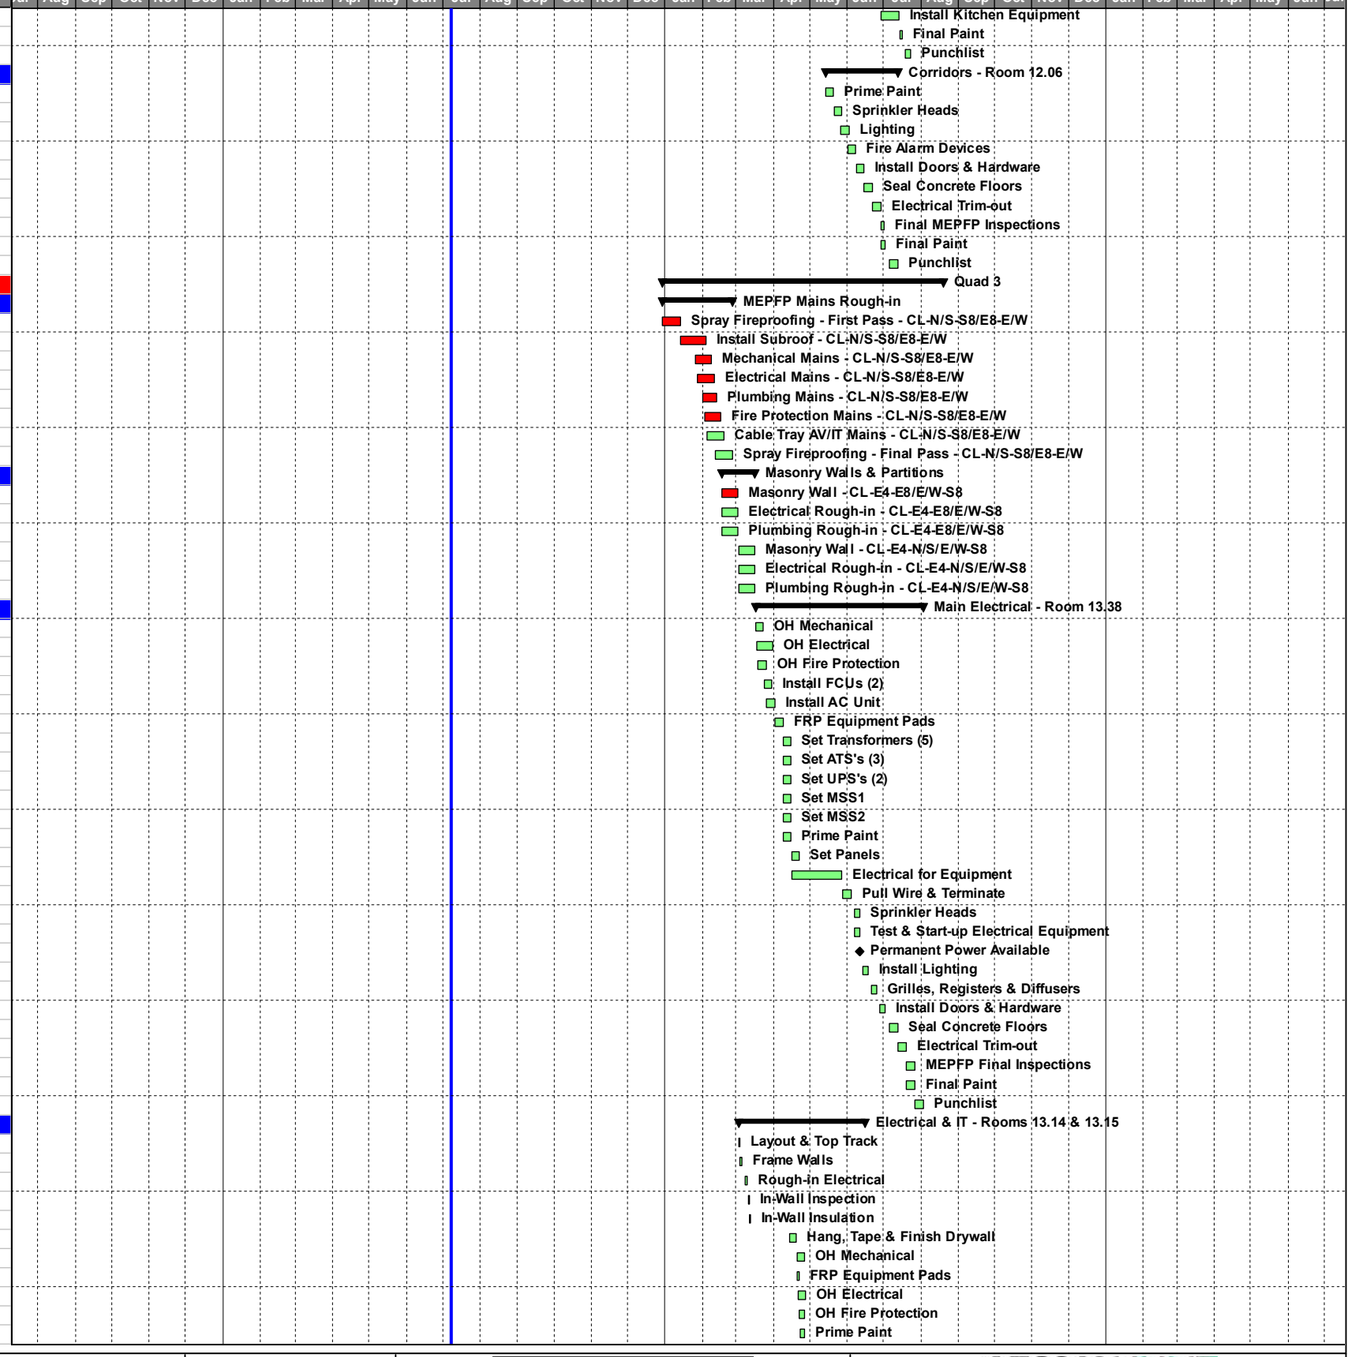

| Activity ID | Activity Name | Original Duration | Remaining Duration | Start | Finish |
|---|---|---|---|---|---|
| A11100 | Set Transformers | 2 | 2 | 27-Apr-21 | 28-Apr-21 |
| A11110 | Set IT Racks | 2 | 2 | 27-Apr-21 | 28-Apr-21 |
| A11120 | Set Panel Boxes | 2 | 2 | 27-Apr-21 | 28-Apr-21 |
| A11240 | Set AC Units | 2 | 2 | 27-Apr-21 | 28-Apr-21 |
| A11130 | Install Panel Interiors | 3 | 3 | 29-Apr-21 | 03-May-21 |
| A11150 | Pull Cable & Terminate | 15 | 15 | 29-Apr-21 | 19-May-21 |
| A11160 | Hook-up Transformers | 5 | 5 | 29-Apr-21 | 05-May-21 |
| A11210 | Install Doors & Hardware | 2 | 2 | 29-Apr-21 | 30-Apr-21 |
| A11250 | OH Mechanical Finishes | 2 | 2 | 29-Apr-21 | 30-Apr-21 |
| A11140 | Pull Wire & Terminate | 15 | 15 | 04-May-21 | 24-May-21 |
| A11170 | Install Lighting | 3 | 3 | 25-May-21 | 27-May-21 |
| A11180 | Install Electrical Finishes | 2 | 2 | 28-May-21 | 01-Jun-21 |
| A11260 | Install Fire Alarm Devices | 2 | 2 | 28-May-21 | 01-Jun-21 |
| A11200 | Seal Concrete Floors | 3 | 3 | 02-Jun-21 | 04-Jun-21 |
| A11270 | MEPFP Final Inspections | 2 | 2 | 02-Jun-21 | 03-Jun-21 |
| A11220 | Final Paint | 2 | 2 | 07-Jun-21 | 08-Jun-21 |
| A11230 | Punchlist | 5 | 5 | 09-Jun-21 | 15-Jun-21 |
| Home Team Locker Room - Rooms 13.02-13.07 | | 120 | 120 | 03-Mar-21 | 19-Aug-21 |
| A30310 | Layout & Top Track | 2 | 2 | 03-Mar-21 | 04-Mar-21 |
| A30320 | OH Mechanical | 5 | 5 | 05-Mar-21 | 11-Mar-21 |
| A30330 | OH Electrical | 5 | 5 | 09-Mar-21 | 15-Mar-21 |
| A30340 | OH Plumbing | 5 | 5 | 11-Mar-21 | 17-Mar-21 |
| A30350 | OH Fire Protection | 5 | 5 | 15-Mar-21 | 19-Mar-21 |
| A30360 | Above Ceiling Inspections | 1 | 1 | 22-Mar-21 | 22-Mar-21 |
| A30370 | Frame Walls | 3 | 3 | 23-Mar-21 | 25-Mar-21 |
| A30380 | In-Wall Electrical | 4 | 4 | 26-Mar-21 | 31-Mar-21 |
| A30390 | In-Wall Plumbing | 8 | 8 | 30-Mar-21 | 08-Apr-21 |
| A30400 | In-Wall Inspections | 1 | 1 | 09-Apr-21 | 09-Apr-21 |
| A30410 | Frame Ceilings | 3 | 3 | 12-Apr-21 | 14-Apr-21 |
| A30660 | Hang, Tape & Finish Drywall Walls | 12 | 12 | 12-Apr-21 | 27-Apr-21 |
| A30420 | In-Ceiling Lighting | 2 | 2 | 15-Apr-21 | 16-Apr-21 |
| A30430 | In-Ceiling Fire Protection | 2 | 2 | 19-Apr-21 | 20-Apr-21 |
| A30440 | In-Ceiling Inspections | 1 | 1 | 21-Apr-21 | 21-Apr-21 |
| A30450 | Hang, Tape & Finish Drywall Ceilings | 12 | 12 | 22-Apr-21 | 07-May-21 |
| A30460 | Prime Paint Walls | 2 | 2 | 10-May-21 | 11-May-21 |
| A30670 | Prime Paint Ceilings | 2 | 2 | 10-May-21 | 11-May-21 |
| A30470 | Install ACT Grid | 2 | 2 | 12-May-21 | 13-May-21 |
| A30520 | Epoxy Walls | 5 | 5 | 12-May-21 | 18-May-21 |
| A30480 | Install Lighting | 2 | 2 | 14-May-21 | 17-May-21 |
| A30490 | Grilles, Registers & Diffusers | 2 | 2 | 18-May-21 | 19-May-21 |
| A30530 | Install Floor Tile (Shower Area) | 5 | 5 | 19-May-21 | 25-May-21 |
| A30500 | Sprinkler Heads | 2 | 2 | 20-May-21 | 21-May-21 |
| A30510 | Fire Alarm Devices | 2 | 2 | 24-May-21 | 25-May-21 |
| A30690 | Install Wall Tile (Shower Area) | 6 | 6 | 26-May-21 | 03-Jun-21 |
| A30710 | Above Ceiling Inspections | 1 | 1 | 26-May-21 | 26-May-21 |
| A30720 | Install ACT Tiles | 2 | 2 | 27-May-21 | 28-May-21 |
| A30540 | Install Millwork | 15 | 15 | 04-Jun-21 | 24-Jun-21 |
| A30680 | Install Casework | 15 | 15 | 11-Jun-21 | 01-Jul-21 |
| A30550 | Install Countertops | 2 | 2 | 25-Jun-21 | 28-Jun-21 |
| A30560 | Install Sinks | 2 | 2 | 29-Jun-21 | 30-Jun-21 |
| A30570 | Install Toilet Fixtures | 4 | 4 | 01-Jul-21 | 07-Jul-21 |
| A30580 | Install Toilet/Shower Partitions | 2 | 2 | 08-Jul-21 | 09-Jul-21 |
| A30700 | Trim-out Showers | 4 | 4 | 08-Jul-21 | 13-Jul-21 |
| A30590 | Install Toilet Accessories | 2 | 2 | 12-Jul-21 | 13-Jul-21 |
| A30600 | Install Sports Flooring | 8 | 8 | 14-Jul-21 | 23-Jul-21 |
| A30610 | Install Lockers | 8 | 8 | 26-Jul-21 | 04-Aug-21 |
| A30620 | Electrical Trim-out | 3 | 3 | 05-Aug-21 | 09-Aug-21 |
| A30630 | Final Paint | 3 | 3 | 10-Aug-21 | 12-Aug-21 |
| A30640 | MEPFP Final Inspections | 2 | 2 | 10-Aug-21 | 11-Aug-21 |
| A30650 | Punchlist | 5 | 5 | 13-Aug-21 | 19-Aug-21 |
| Concession & Prep - Rooms 13.20 & 13.21 | | 66 | 66 | 17-Mar-21 | 17-Jun-21 |
| A11560 | OH Mechanical | 4 | 4 | 17-Mar-21 | 22-Mar-21 |
| A11610 | OH Electrical | 4 | 4 | 19-Mar-21 | 24-Mar-21 |
| A11620 | OH Plumbing | 4 | 4 | 23-Mar-21 | 26-Mar-21 |
| A11630 | OH Fire Protection | 4 | 4 | 25-Mar-21 | 30-Mar-21 |
| A11680 | Frame Ceilings | 2 | 2 | 25-Mar-21 | 26-Mar-21 |
| A11690 | Install Lighting (Drywall Ceilings) | 2 | 2 | 29-Mar-21 | 30-Mar-21 |
| A11640 | Install Exhaust Hood | 5 | 5 | 31-Mar-21 | 06-Apr-21 |
| A11650 | Above Ceiling Inspections | 1 | 1 | 07-Apr-21 | 07-Apr-21 |
| A11700 | Hang, Tape & Finish Drywall | 5 | 5 | 14-Apr-21 | 20-Apr-21 |

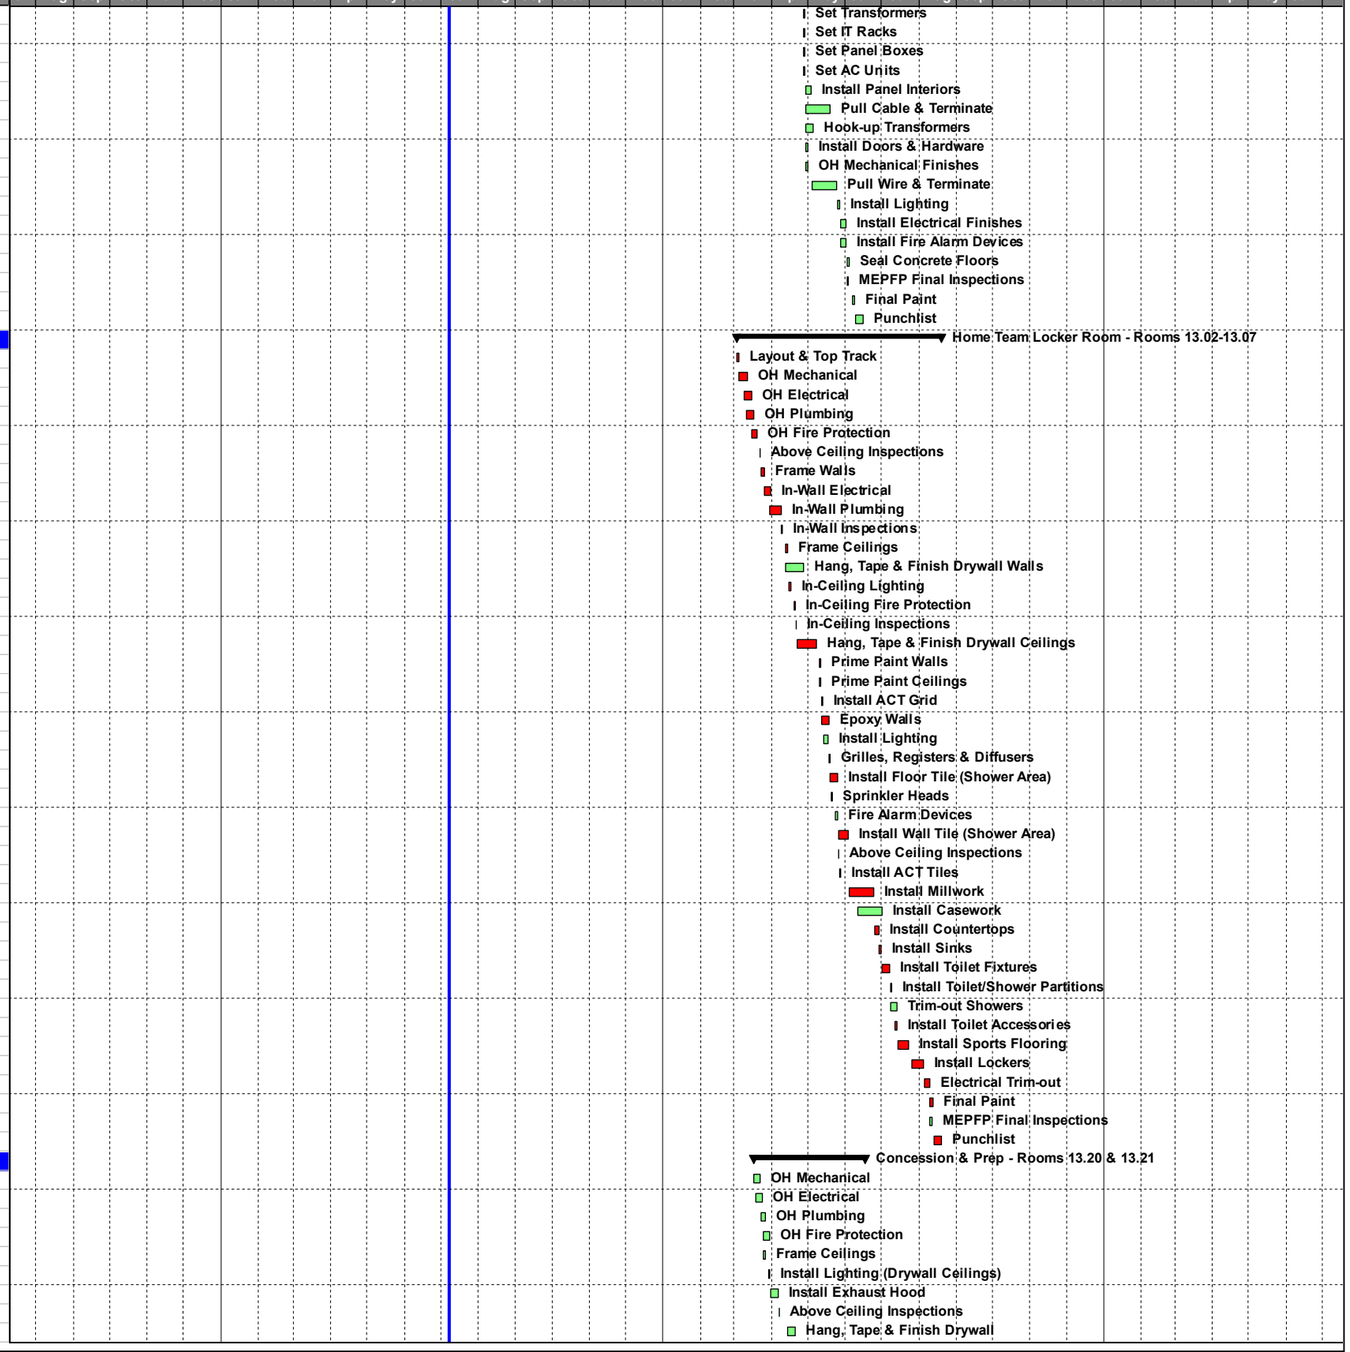

| Activity ID | Activity Name | Original Duration | Remaining Duration | Start | Finish |
|---|---|---|---|---|---|
| A11660 | Prime Paint | 1 | 1 | 21-Apr-21 | 21-Apr-21 |
| A11760 | FRP Wall Panels | 3 | 3 | 22-Apr-21 | 26-Apr-21 |
| A11670 | Install ACT Grid | 1 | 1 | 27-Apr-21 | 27-Apr-21 |
| A11710 | Install Lighting (Grid Ceilings) | 2 | 2 | 28-Apr-21 | 29-Apr-21 |
| A11720 | Sprinkler Heads | 1 | 1 | 30-Apr-21 | 30-Apr-21 |
| A11730 | Grilles, Registers & Diffusers | 1 | 1 | 03-May-21 | 03-May-21 |
| A11740 | Fire Alarm Devices | 1 | 1 | 04-May-21 | 04-May-21 |
| A11870 | In-Ceiling Inspections | 1 | 1 | 05-May-21 | 05-May-21 |
| A11750 | Install ACT Tiles | 1 | 1 | 06-May-21 | 06-May-21 |
| A11770 | Resilient Flooring | 5 | 5 | 07-May-21 | 13-May-21 |
| A11810 | Millwork | 5 | 5 | 14-May-21 | 20-May-21 |
| A11880 | Install Doors & Hardware | 1 | 1 | 14-May-21 | 14-May-21 |
| A11780 | Install Plumbing Fixtures | 2 | 2 | 21-May-21 | 24-May-21 |
| A11850 | Tile Concession Wall | 3 | 3 | 21-May-21 | 25-May-21 |
| A11860 | Install Countertops | 2 | 2 | 26-May-21 | 27-May-21 |
| A11800 | Food Service Equipment | 5 | 5 | 28-May-21 | 04-Jun-21 |
| A11790 | Electrical Trim-out | 2 | 2 | 07-Jun-21 | 08-Jun-21 |
| A11820 | Final Paint | 2 | 2 | 09-Jun-21 | 10-Jun-21 |
| A11830 | MEPFP Final Inspections | 2 | 2 | 09-Jun-21 | 10-Jun-21 |
| A11840 | Punchlist | 5 | 5 | 11-Jun-21 | 17-Jun-21 |
| **Storage - Rooms 13.22 & 13.25** | | **39** | **39** | **23-Mar-21** | **14-May-21** |
| A11890 | OH Mechanical | 5 | 5 | 23-Mar-21 | 29-Mar-21 |
| A11900 | OH Electrical | 5 | 5 | 24-Mar-21 | 30-Mar-21 |
| A11910 | OH Fire Protection | 5 | 5 | 25-Mar-21 | 31-Mar-21 |
| A11920 | Install FCUs | 5 | 5 | 30-Mar-21 | 05-Apr-21 |
| A11930 | Prime Paint | 2 | 2 | 01-Apr-21 | 02-Apr-21 |
| A11940 | Install Doors & Hardware | 2 | 2 | 05-Apr-21 | 06-Apr-21 |
| A11950 | Grilles, Registers & Diffusers | 2 | 2 | 06-Apr-21 | 07-Apr-21 |
| A11960 | Install Roll-up Door | 5 | 5 | 07-Apr-21 | 13-Apr-21 |
| A11970 | Sprinkler Heads | 2 | 2 | 14-Apr-21 | 15-Apr-21 |
| A11980 | Install Lighting | 3 | 3 | 16-Apr-21 | 20-Apr-21 |
| A11990 | Fire Alarm Devices | 3 | 3 | 21-Apr-21 | 23-Apr-21 |
| A12000 | Seal Concrete Floors | 5 | 5 | 26-Apr-21 | 30-Apr-21 |
| A12010 | Electrical Trim-out | 2 | 2 | 03-May-21 | 04-May-21 |
| A12020 | Final MEPFP Inspections | 2 | 2 | 05-May-21 | 06-May-21 |
| A12030 | Final Paint | 3 | 3 | 05-May-21 | 07-May-21 |
| A12040 | Punchlist | 5 | 5 | 10-May-21 | 14-May-21 |
| **Mens & Womens Restrooms - Rooms 13.11 & 13.12** | | **83** | **83** | **03-Mar-21** | **28-Jun-21** |
| A11580 | Layout & Top Track | 2 | 2 | 03-Mar-21 | 04-Mar-21 |
| A12050 | OH Mechanical | 5 | 5 | 05-Mar-21 | 11-Mar-21 |
| A12060 | OH Electrical | 5 | 5 | 09-Mar-21 | 15-Mar-21 |
| A12070 | OH Plumbing | 5 | 5 | 11-Mar-21 | 17-Mar-21 |
| A12080 | OH Fire Protection | 5 | 5 | 15-Mar-21 | 19-Mar-21 |
| A12090 | Above Ceiling Inspections | 1 | 1 | 22-Mar-21 | 22-Mar-21 |
| A12100 | Frame Walls | 3 | 3 | 23-Mar-21 | 25-Mar-21 |
| A12110 | In-Wall Electrical | 5 | 5 | 26-Mar-21 | 01-Apr-21 |
| A12120 | In-Wall Plumbing | 8 | 8 | 26-Mar-21 | 06-Apr-21 |
| A12130 | In-Wall Inspections | 1 | 1 | 07-Apr-21 | 07-Apr-21 |
| A12140 | Hang Cement Board | 3 | 3 | 14-Apr-21 | 16-Apr-21 |
| A12150 | Install Wall Tile | 7 | 7 | 19-Apr-21 | 27-Apr-21 |
| A12155 | Install Floor Tile | 5 | 5 | 28-Apr-21 | 04-May-21 |
| A12160 | Install ACT Grid | 2 | 2 | 05-May-21 | 06-May-21 |
| A12170 | Install Lighting | 2 | 2 | 07-May-21 | 10-May-21 |
| A12180 | Grilles, Registers & Diffusers | 2 | 2 | 10-May-21 | 11-May-21 |
| A12190 | Sprinkler Heads | 2 | 2 | 11-May-21 | 12-May-21 |
| A12200 | Fire Alarm Devices | 2 | 2 | 13-May-21 | 14-May-21 |
| A12210 | In-Ceiling Inspections | 1 | 1 | 17-May-21 | 17-May-21 |
| A12230 | Install ACT Tiles | 2 | 2 | 18-May-21 | 19-May-21 |
| A12240 | Install Toilets & Urinals | 5 | 5 | 20-May-21 | 26-May-21 |
| A12250 | Install Millwork | 4 | 4 | 27-May-21 | 02-Jun-21 |
| A12260 | Install Countertops | 2 | 2 | 03-Jun-21 | 04-Jun-21 |
| A12270 | Install Plumbing Fixtures | 2 | 2 | 07-Jun-21 | 08-Jun-21 |
| A12280 | Toilet Partitions | 3 | 3 | 09-Jun-21 | 11-Jun-21 |
| A12290 | Install Toilet Accessories | 2 | 2 | 14-Jun-21 | 15-Jun-21 |
| A12300 | Electrical Trim-out | 2 | 2 | 16-Jun-21 | 17-Jun-21 |
| A12310 | MEPFP Final Inspections | 2 | 2 | 18-Jun-21 | 21-Jun-21 |
| A12320 | Punchlist | 5 | 5 | 22-Jun-21 | 28-Jun-21 |
| **Media & Team Store - Rooms 13.24 & 13.28** | | **72** | **72** | **17-Mar-21** | **25-Jun-21** |
| A11590 | Layout & Top Track | 2 | 2 | 17-Mar-21 | 18-Mar-21 |
| A12220 | OH Mechanical | 5 | 5 | 19-Mar-21 | 25-Mar-21 |

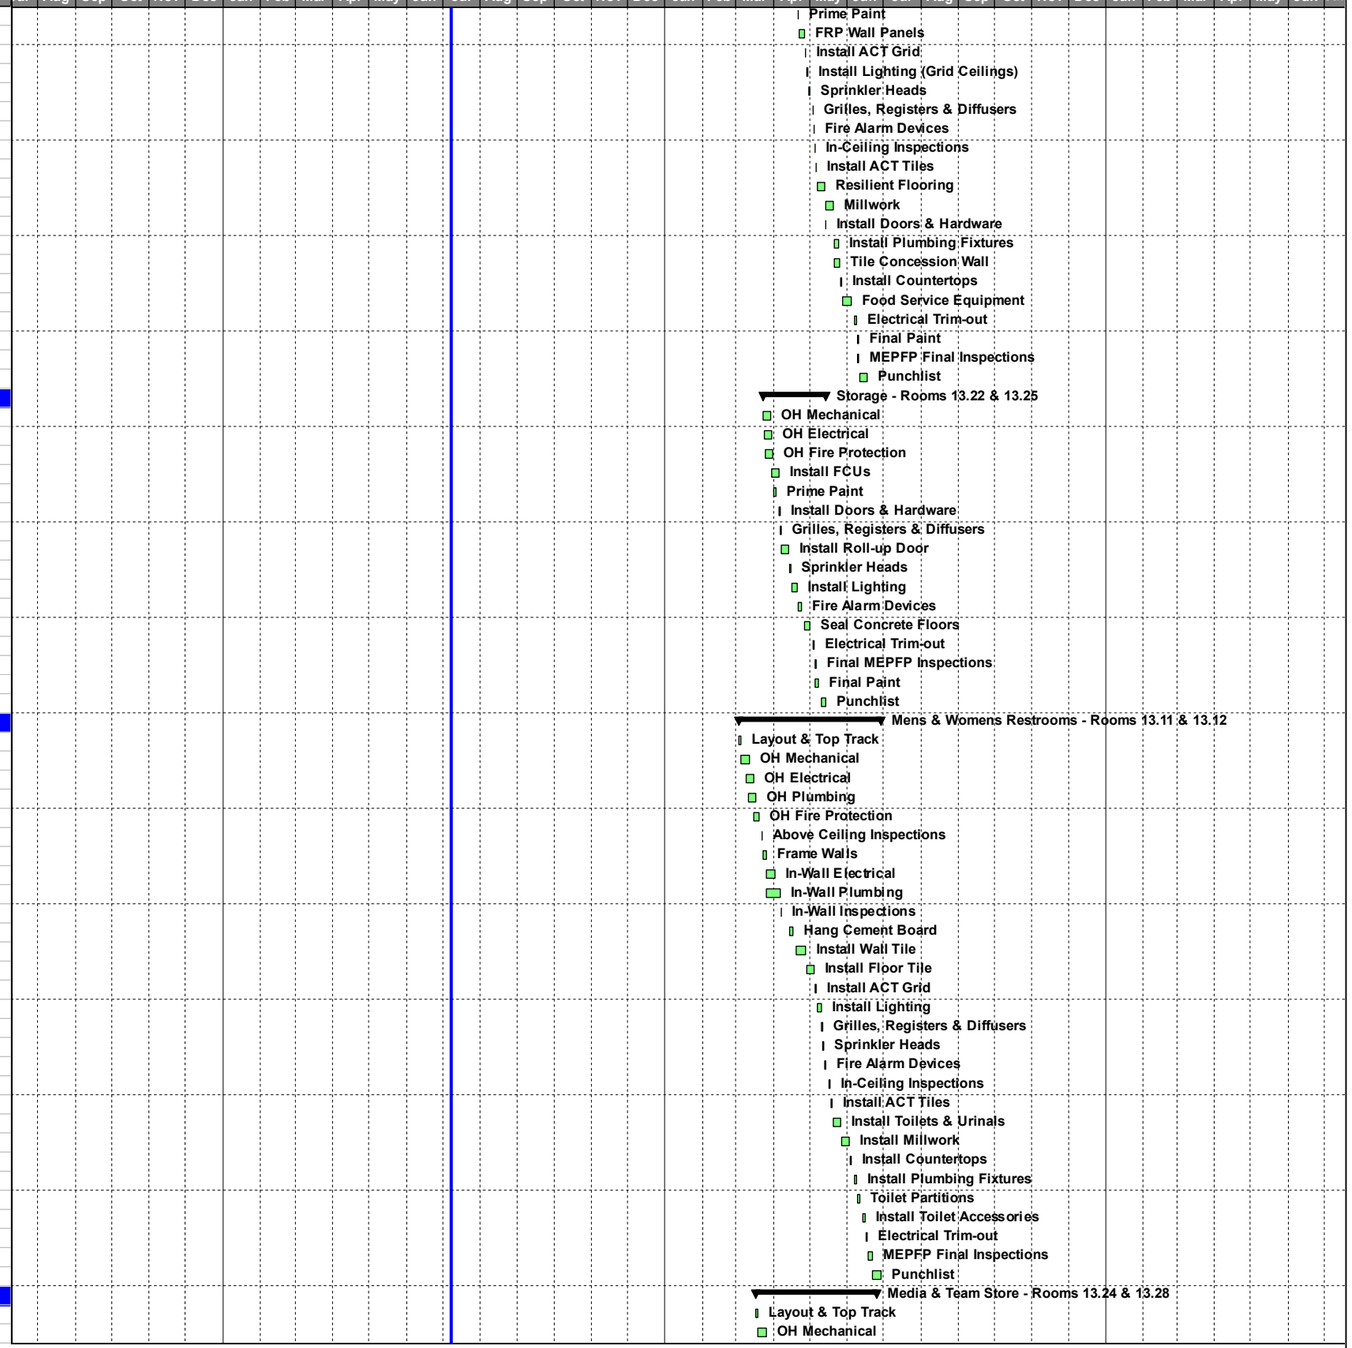

| Activity ID | Activity Name | Original Duration | Remaining Duration | Start | Finish |
|---|---|---|---|---|---|
| A12330 | OH Electrical | 5 | 5 | 23-Mar-21 | 29-Mar-21 |
| A12340 | OH Plumbing | 5 | 5 | 25-Mar-21 | 31-Mar-21 |
| A12350 | OH Fire Protection | 5 | 5 | 29-Mar-21 | 02-Apr-21 |
| A12360 | Above Ceiling Inspections | 1 | 1 | 05-Apr-21 | 05-Apr-21 |
| A12370 | Frame Walls | 3 | 3 | 06-Apr-21 | 08-Apr-21 |
| A12380 | In-Wall Electrical Rough-in | 5 | 5 | 09-Apr-21 | 15-Apr-21 |
| A12430 | Frame Ceilings | 3 | 3 | 09-Apr-21 | 13-Apr-21 |
| A12440 | In-Ceiling Lighting | 2 | 2 | 14-Apr-21 | 15-Apr-21 |
| A12390 | In-Wall Inspections | 1 | 1 | 16-Apr-21 | 16-Apr-21 |
| A12450 | In-Ceiling Mechanical | 2 | 2 | 16-Apr-21 | 19-Apr-21 |
| A12460 | In-Ceiling Fire Protection | 2 | 2 | 20-Apr-21 | 21-Apr-21 |
| A12400 | Hang, Tape & Finish Drywall | 8 | 8 | 22-Apr-21 | 03-May-21 |
| A12410 | Prime Paint | 2 | 2 | 04-May-21 | 05-May-21 |
| A12420 | Install Operable Partition | 5 | 5 | 06-May-21 | 12-May-21 |
| A12470 | Install ACT Grid | 3 | 3 | 06-May-21 | 10-May-21 |
| A12480 | Install Lighting (Grid) | 2 | 2 | 11-May-21 | 12-May-21 |
| A12490 | Grilles, Registers & Diffusers (Grid) | 2 | 2 | 13-May-21 | 14-May-21 |
| A12500 | Sprinkler Heads (Grid) | 2 | 2 | 17-May-21 | 18-May-21 |
| A12510 | Fire Alarm Devices | 2 | 2 | 19-May-21 | 20-May-21 |
| A12520 | Electrical Trim-out | 5 | 5 | 21-May-21 | 27-May-21 |
| A12530 | Seal Concrete Floors | 5 | 5 | 28-May-21 | 04-Jun-21 |
| A12560 | MEPFP Final Inspections | 5 | 5 | 28-May-21 | 04-Jun-21 |
| A12540 | Install Carpet | 5 | 5 | 07-Jun-21 | 11-Jun-21 |
| A12550 | Final Paint | 5 | 5 | 14-Jun-21 | 18-Jun-21 |
| A12570 | Punchlist | 5 | 5 | 21-Jun-21 | 25-Jun-21 |
| Visitor Locker Room 1&2 - Rooms 13.30-31 & 14.39-40 | | 90 | 90 | 17-Mar-21 | 22-Jul-21 |
| A11600 | Layout & Top Track | 2 | 2 | 17-Mar-21 | 18-Mar-21 |
| A12580 | OH Mechanical | 5 | 5 | 19-Mar-21 | 25-Mar-21 |
| A12590 | OH Electrical | 5 | 5 | 23-Mar-21 | 29-Mar-21 |
| A12600 | OH Plumbing | 5 | 5 | 25-Mar-21 | 31-Mar-21 |
| A12610 | OH Fire Protection | 5 | 5 | 29-Mar-21 | 02-Apr-21 |
| A12620 | Above Ceiling Inspections | 1 | 1 | 05-Apr-21 | 05-Apr-21 |
| A12630 | Frame Walls | 3 | 3 | 06-Apr-21 | 08-Apr-21 |
| A12640 | In-Wall Electrical | 4 | 4 | 09-Apr-21 | 14-Apr-21 |
| A12650 | In-Wall Plumbing | 8 | 8 | 13-Apr-21 | 22-Apr-21 |
| A12660 | In-Wall Inspections | 1 | 1 | 23-Apr-21 | 23-Apr-21 |
| A12670 | Frame Ceilings | 3 | 3 | 26-Apr-21 | 28-Apr-21 |
| A12680 | In-Ceiling Lighting | 2 | 2 | 29-Apr-21 | 30-Apr-21 |
| A12690 | In-Ceiling Fire Protection | 2 | 2 | 03-May-21 | 04-May-21 |
| A12700 | In-Ceiling Inspections | 1 | 1 | 05-May-21 | 05-May-21 |
| A12710 | Hang, Tape & Finish Drywall | 8 | 8 | 06-May-21 | 17-May-21 |
| A12720 | Prime Paint | 2 | 2 | 18-May-21 | 19-May-21 |
| A12780 | Epoxy Walls | 3 | 3 | 18-May-21 | 20-May-21 |
| A12730 | Install ACT Grid | 2 | 2 | 20-May-21 | 21-May-21 |
| A12790 | Install Floor Tile (Shower Area) | 5 | 5 | 21-May-21 | 27-May-21 |
| A12740 | Install Lighting | 2 | 2 | 24-May-21 | 25-May-21 |
| A12750 | Grilles, Registers & Diffusers | 2 | 2 | 26-May-21 | 27-May-21 |
| A12760 | Sprinkler Heads | 2 | 2 | 28-May-21 | 01-Jun-21 |
| A12800 | Install Millwork | 3 | 3 | 28-May-21 | 02-Jun-21 |
| A12770 | Fire Alarm Devices | 2 | 2 | 02-Jun-21 | 03-Jun-21 |
| A12810 | Install Countertops | 2 | 2 | 03-Jun-21 | 04-Jun-21 |
| A12820 | Install Sinks | 2 | 2 | 07-Jun-21 | 08-Jun-21 |
| A12830 | Install Plumbing Fixtures | 4 | 4 | 09-Jun-21 | 14-Jun-21 |
| A12840 | Install Toilet/Shower Partitions | 2 | 2 | 15-Jun-21 | 16-Jun-21 |
| A12850 | Install Toilet Accessories | 2 | 2 | 17-Jun-21 | 18-Jun-21 |
| A12860 | Install Sports Flooring | 5 | 5 | 21-Jun-21 | 25-Jun-21 |
| A12870 | Install Lockers | 8 | 8 | 28-Jun-21 | 08-Jul-21 |
| A12880 | Electrical Trim-out | 3 | 3 | 09-Jul-21 | 13-Jul-21 |
| A12890 | Final Paint | 2 | 2 | 14-Jul-21 | 15-Jul-21 |
| A12900 | MEPFP Final Inspections | 2 | 2 | 14-Jul-21 | 15-Jul-21 |
| A12910 | Punchlist | 5 | 5 | 16-Jul-21 | 22-Jul-21 |
| Mens & Womens Restrooms - Rooms 13.35 & 13.26 | | 81 | 81 | 05-Mar-21 | 28-Jun-21 |
| A30020 | Layout & Top Track | 2 | 2 | 05-Mar-21 | 08-Mar-21 |
| A30030 | OH Mechanical | 5 | 5 | 09-Mar-21 | 15-Mar-21 |
| A30040 | OH Electrical | 5 | 5 | 11-Mar-21 | 17-Mar-21 |
| A30050 | OH Plumbing | 5 | 5 | 15-Mar-21 | 19-Mar-21 |
| A30060 | OH Fire Protection | 5 | 5 | 17-Mar-21 | 23-Mar-21 |
| A30070 | Above Ceiling Inspections | 1 | 1 | 24-Mar-21 | 24-Mar-21 |
| A30080 | Frame Walls | 3 | 3 | 25-Mar-21 | 29-Mar-21 |
| A30090 | In-Wall Electrical | 5 | 5 | 30-Mar-21 | 05-Apr-21 |

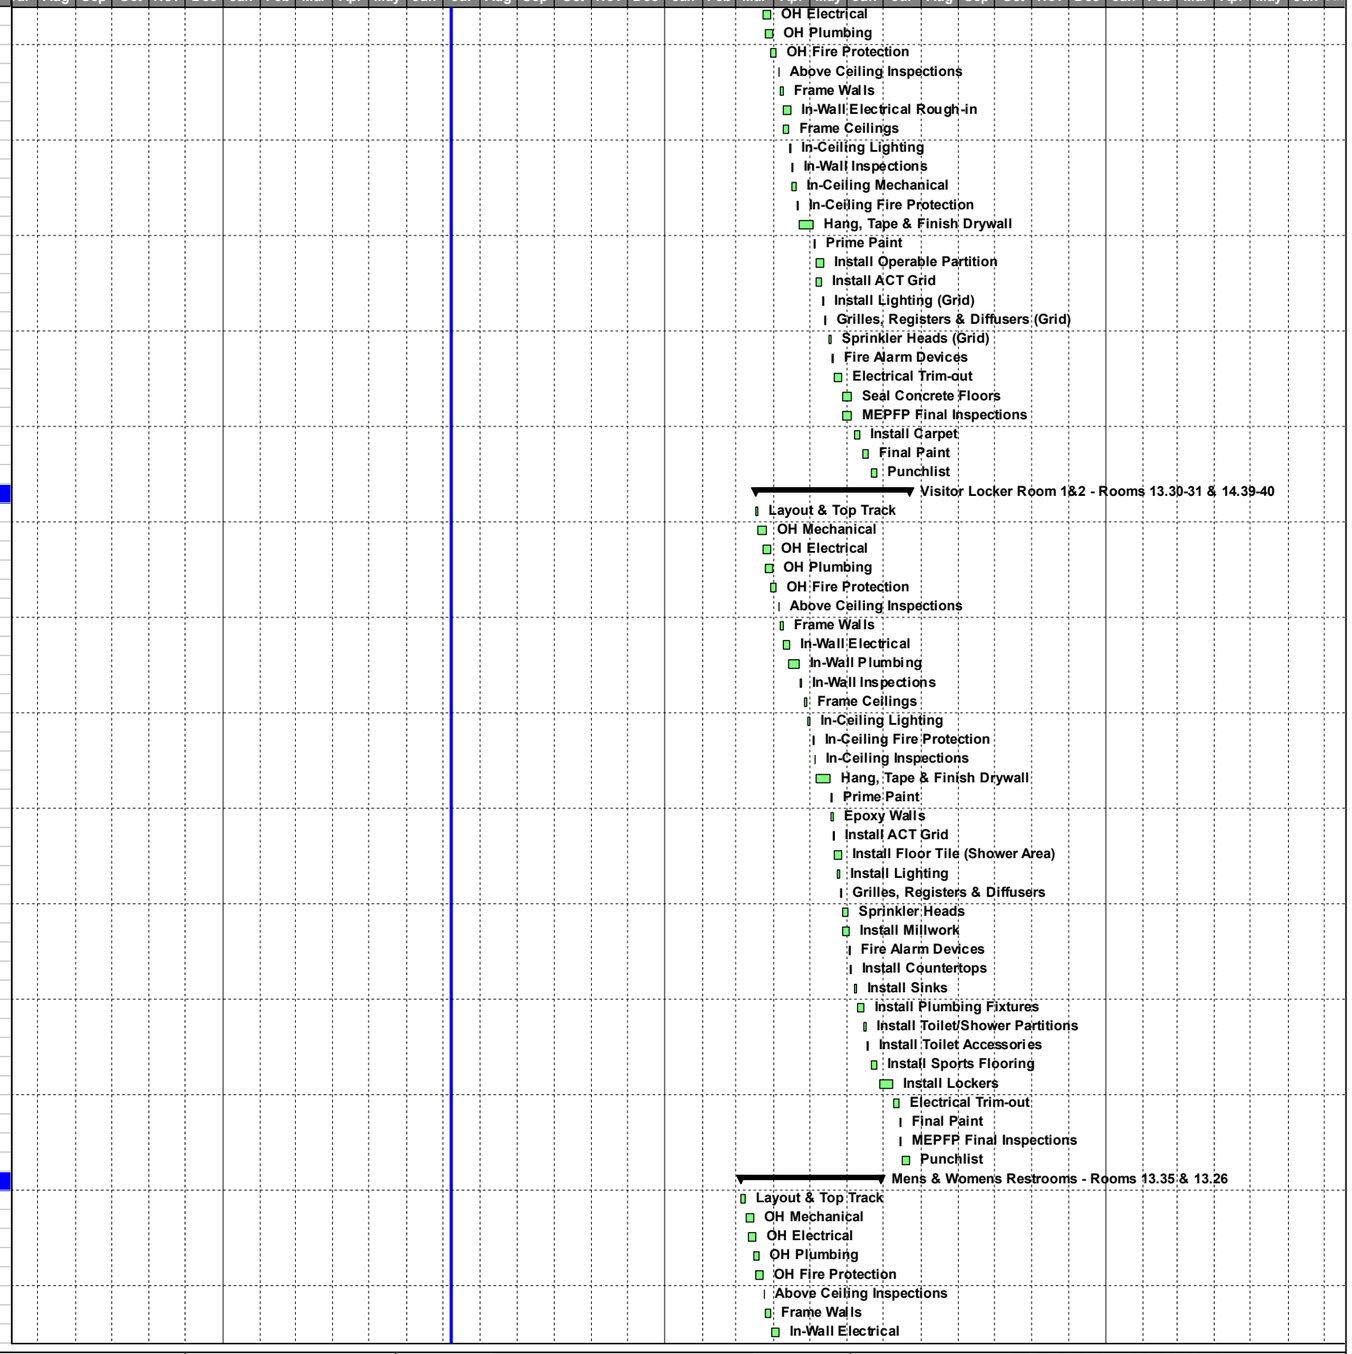

| Activity ID | Activity Name | Original Duration | Remaining Duration | Start | Finish |
|---|---|---|---|---|---|
| A30100 | In-Wall Plumbing | 8 | 8 | 30-Mar-21 | 08-Apr-21 |
| A30110 | In-Wall Inspections | 1 | 1 | 09-Apr-21 | 09-Apr-21 |
| A30120 | Hang Cement Board | 3 | 3 | 14-Apr-21 | 16-Apr-21 |
| A30130 | Install Wall Tile | 7 | 7 | 19-Apr-21 | 27-Apr-21 |
| A30200 | Install Floor Tile | 5 | 5 | 28-Apr-21 | 04-May-21 |
| A30140 | Install ACT Grid | 2 | 2 | 05-May-21 | 06-May-21 |
| A30150 | Install Lighting | 2 | 2 | 07-May-21 | 10-May-21 |
| A30160 | Grilles, Registers & Diffusers | 2 | 2 | 10-May-21 | 11-May-21 |
| A30170 | Sprinkler Heads | 2 | 2 | 11-May-21 | 12-May-21 |
| A30180 | Fire Alarm Devices | 2 | 2 | 13-May-21 | 14-May-21 |
| A30190 | In-Ceiling Inspections | 1 | 1 | 17-May-21 | 17-May-21 |
| A30210 | Install ACT Tiles | 2 | 2 | 18-May-21 | 19-May-21 |
| A30220 | Install Toilets & Urinals | 5 | 5 | 20-May-21 | 26-May-21 |
| A30230 | Install Millwork | 4 | 4 | 27-May-21 | 02-Jun-21 |
| A30240 | Install Countertops | 2 | 2 | 03-Jun-21 | 04-Jun-21 |
| A30250 | Install Plumbing Fixtures | 2 | 2 | 07-Jun-21 | 08-Jun-21 |
| A30260 | Toilet Partitions | 3 | 3 | 09-Jun-21 | 11-Jun-21 |
| A30270 | Install Toilet Accessories | 2 | 2 | 14-Jun-21 | 15-Jun-21 |
| A30280 | Electrical Trim-out | 2 | 2 | 16-Jun-21 | 17-Jun-21 |
| A30290 | MEPFP Final Inspections | 2 | 2 | 18-Jun-21 | 21-Jun-21 |
| A30300 | Punchlist | 5 | 5 | 22-Jun-21 | 28-Jun-21 |
| Corridors & Lobby - Room 13.01 & 13.16 | | 40 | 40 | 20-May-21 | 16-Jul-21 |
| A14990 | Prime Paint | 5 | 5 | 20-May-21 | 26-May-21 |
| A14960 | Sprinkler Heads | 5 | 5 | 27-May-21 | 03-Jun-21 |
| A14970 | Lighting | 5 | 5 | 02-Jun-21 | 08-Jun-21 |
| A14980 | Fire Alarm Devices | 5 | 5 | 07-Jun-21 | 11-Jun-21 |
| A15030 | Install Doors & Hardware | 5 | 5 | 14-Jun-21 | 18-Jun-21 |
| A15000 | Seal Concrete Floors | 5 | 5 | 21-Jun-21 | 25-Jun-21 |
| A15010 | Electrical Trim-out | 5 | 5 | 28-Jun-21 | 02-Jul-21 |
| A15020 | Final MEPFP Inspections | 3 | 3 | 06-Jul-21 | 08-Jul-21 |
| A15040 | Final Paint | 4 | 4 | 06-Jul-21 | 09-Jul-21 |
| A15050 | Punchlist | 5 | 5 | 12-Jul-21 | 16-Jul-21 |
| Quad 4 | | 144 | 144 | 14-Jan-21 | 05-Aug-21 |
| MEPFP Mains Rough-in | | 41 | 41 | 14-Jan-21 | 11-Mar-21 |
| OHRI-EL-Q4-1 | Spray Fireproofing - First Pass - CL-E/W-W10/S8-N/S | 10 | 10 | 14-Jan-21 | 27-Jan-21 |
| OHRI-EL-Q4-1 | Install Subroof - CL-E/W-W10/S8-N/S | 15 | 15 | 28-Jan-21 | 17-Feb-21 |
| OHRI-EL-Q4-1 | Mechanical Mains - CL-E/W-W10/S8-N/S | 10 | 10 | 09-Feb-21 | 22-Feb-21 |
| OHRI-EL-Q4-1 | Electrical Mains - CL-E/W-W10/S8-N/S | 10 | 10 | 11-Feb-21 | 24-Feb-21 |
| OHRI-EL-Q4-1 | Plumbing Mains - CL-E/W-W10/S8-N/S | 10 | 10 | 15-Feb-21 | 26-Feb-21 |
| OHRI-EL-Q4-1 | Fire Protection Mains - CL-E/W-W10/S8-N/S | 10 | 10 | 17-Feb-21 | 02-Mar-21 |
| OHRI-EL-Q4-1 | Cable Tray AV/IT Mains - CL-E/W-W10/S8-N/S | 10 | 10 | 19-Feb-21 | 04-Mar-21 |
| OHRI-EL-Q4-1 | Spray Fireproofing - Final Pass - CL-E/W-W10/S8-N/S | 10 | 10 | 26-Feb-21 | 11-Mar-21 |
| Masonry Walls & Partitions | | 20 | 20 | 17-Mar-21 | 13-Apr-21 |
| MAS-EL-Q4-10 | Masonry Wall - CL-N/S-W3/S8-S2 | 10 | 10 | 17-Mar-21 | 30-Mar-21 |
| ELEC-EL-Q4-1 | Electrical Rough-in - CL-N/S-W3/S8-S2 | 10 | 10 | 17-Mar-21 | 30-Mar-21 |
| PLM-EL-Q4-10 | Plumbing Rough-in - CL-N/S-W3/S8-S2 | 10 | 10 | 17-Mar-21 | 30-Mar-21 |
| MAS-EL-Q4-10 | Masonry Wall - CL-W3-W10/S2-EW | 10 | 10 | 31-Mar-21 | 13-Apr-21 |
| ELEC-EL-Q4-1 | Electrical Rough-in - CL-W3-W10/S2-EW | 10 | 10 | 31-Mar-21 | 13-Apr-21 |
| PLM-EL-Q4-10 | Plumbing Rough-in - CL-W3-W10/S2-EW | 10 | 10 | 31-Mar-21 | 13-Apr-21 |
| Show Power - Room 14.29 | | 45 | 45 | 14-Apr-21 | 16-Jun-21 |
| A13610 | OH Mechanical | 5 | 5 | 14-Apr-21 | 20-Apr-21 |
| A13620 | OH Electrical | 5 | 5 | 15-Apr-21 | 21-Apr-21 |
| A13630 | OH Fire Protection | 3 | 3 | 16-Apr-21 | 20-Apr-21 |
| A13640 | FRP Equipment Pads | 3 | 3 | 21-Apr-21 | 23-Apr-21 |
| A13740 | Prime Paint | 2 | 2 | 26-Apr-21 | 27-Apr-21 |
| A13670 | Set Panel Boxes | 2 | 2 | 28-Apr-21 | 29-Apr-21 |
| A13790 | Set FCU | 1 | 1 | 28-Apr-21 | 28-Apr-21 |
| A13800 | Set AC Units | 2 | 2 | 29-Apr-21 | 30-Apr-21 |
| A13680 | Install Panel Interiors | 3 | 3 | 30-Apr-21 | 04-May-21 |
| A13760 | Install Doors & Hardware | 2 | 2 | 30-Apr-21 | 03-May-21 |
| A13810 | OH Mechanical Finishes | 2 | 2 | 03-May-21 | 04-May-21 |
| A13690 | Pull Wire & Terminate | 15 | 15 | 05-May-21 | 25-May-21 |
| A13700 | Pull Cable & Terminate | 15 | 15 | 05-May-21 | 25-May-21 |
| A13720 | Install Lighting | 3 | 3 | 26-May-21 | 28-May-21 |
| A13730 | Install Electrical Finishes | 2 | 2 | 01-Jun-21 | 02-Jun-21 |
| A13820 | Install Fire Alarm Devices | 2 | 2 | 01-Jun-21 | 02-Jun-21 |
| A13750 | Seal Concrete Floors | 3 | 3 | 03-Jun-21 | 07-Jun-21 |
| A13830 | MEPFP Final Inspections | 2 | 2 | 03-Jun-21 | 04-Jun-21 |
| A13770 | Final Paint | 2 | 2 | 08-Jun-21 | 09-Jun-21 |
| A13780 | Punchlist | 5 | 5 | 10-Jun-21 | 16-Jun-21 |

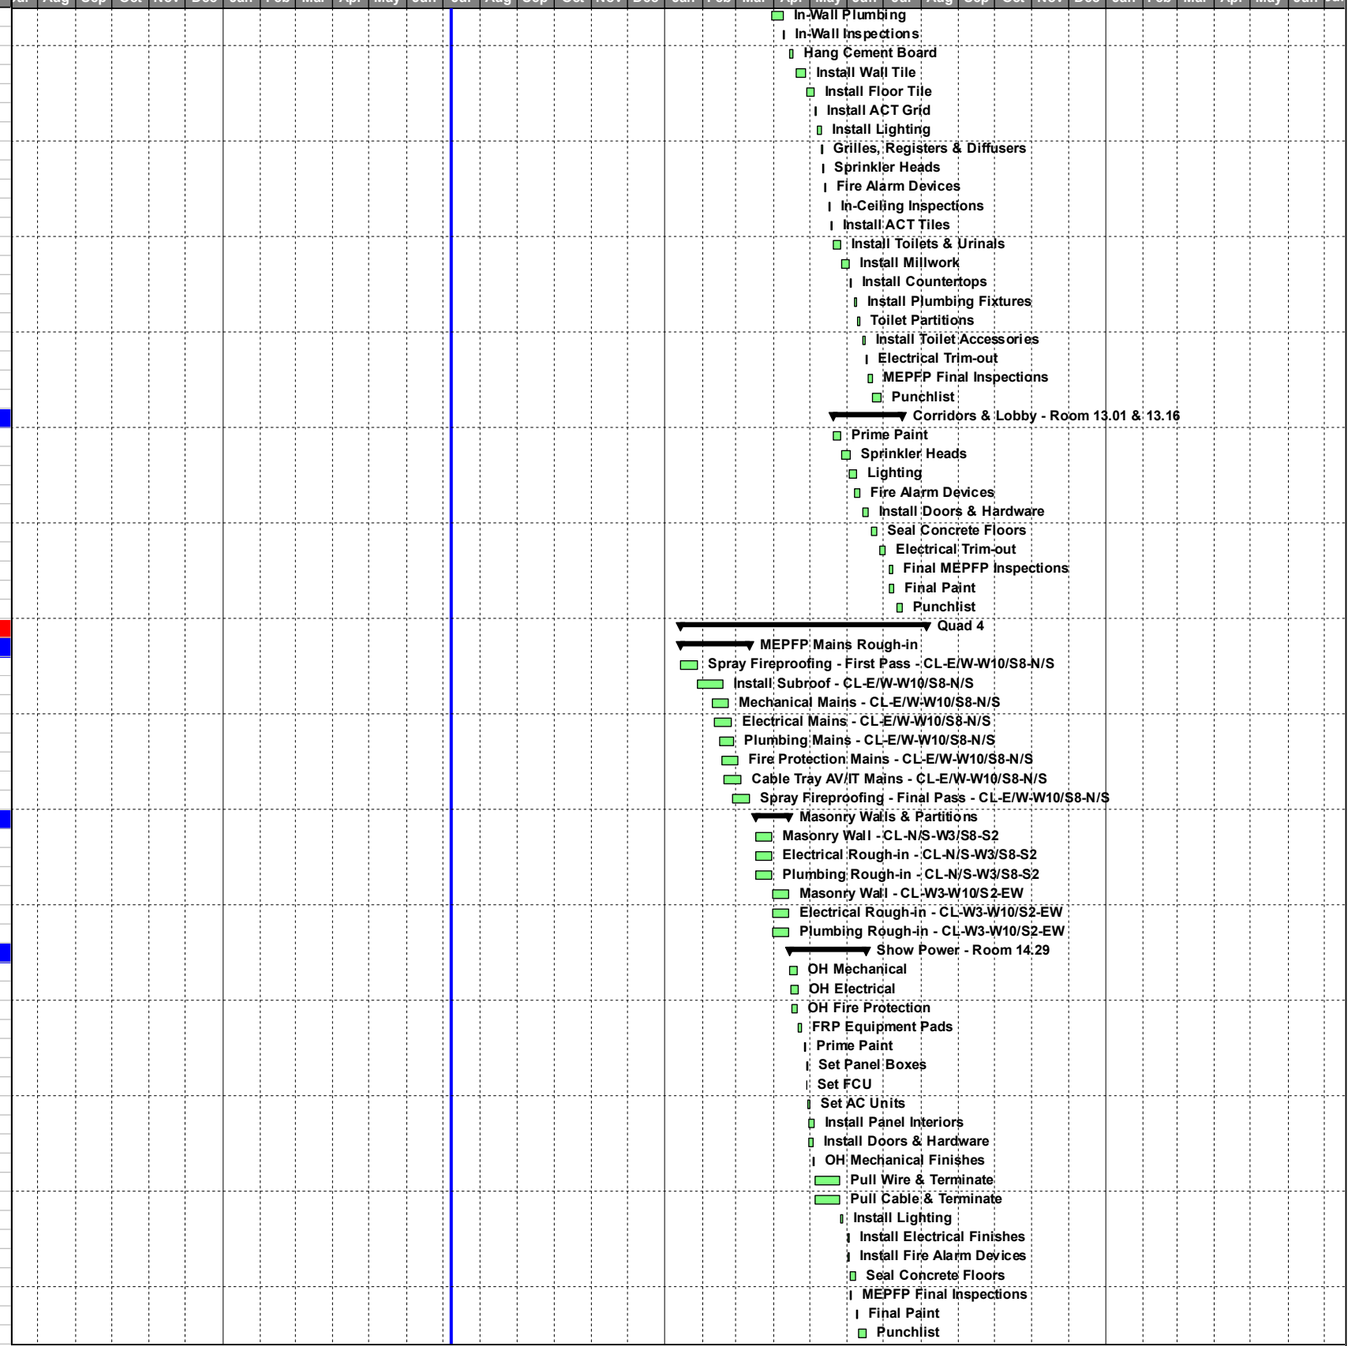

| Activity ID | Activity Name | Original Duration | Remaining Duration | Start | Finish |
|---|---|---|---|---|---|
| **Electrical & IT - Rooms 14.10-11** | | **69** | **69** | **14-Apr-21** | **21-Jul-21** |
| A13270 | Layout & Top Track | 1 | 1 | 14-Apr-21 | 14-Apr-21 |
| A13280 | Frame Walls | 2 | 2 | 15-Apr-21 | 16-Apr-21 |
| A13290 | Rough-in Electrical | 3 | 3 | 19-Apr-21 | 21-Apr-21 |
| A13300 | In-Wall Inspection | 1 | 1 | 22-Apr-21 | 22-Apr-21 |
| A13310 | In-Wall Insulation | 1 | 1 | 23-Apr-21 | 23-Apr-21 |
| A13320 | Hang, Tape & Finish Drywall | 4 | 4 | 19-May-21 | 24-May-21 |
| A13330 | OH Mechanical | 5 | 5 | 25-May-21 | 01-Jun-21 |
| A13360 | FRP Equipment Pads | 3 | 3 | 25-May-21 | 27-May-21 |
| A13340 | OH Electrical | 5 | 5 | 26-May-21 | 02-Jun-21 |
| A13350 | OH Fire Protection | 3 | 3 | 27-May-21 | 01-Jun-21 |
| A13460 | Prime Paint | 2 | 2 | 28-May-21 | 01-Jun-21 |
| A13370 | Set Transformers | 2 | 2 | 02-Jun-21 | 03-Jun-21 |
| A13380 | Set IT Racks | 2 | 2 | 02-Jun-21 | 03-Jun-21 |
| A13390 | Set Panel Boxes | 2 | 2 | 02-Jun-21 | 03-Jun-21 |
| A13510 | Set AC Units | 2 | 2 | 02-Jun-21 | 03-Jun-21 |
| A13400 | Install Panel Interiors | 3 | 3 | 04-Jun-21 | 08-Jun-21 |
| A13420 | Pull Cable & Terminate | 15 | 15 | 04-Jun-21 | 24-Jun-21 |
| A13430 | Hook-up Transformers | 5 | 5 | 04-Jun-21 | 10-Jun-21 |
| A13480 | Install Doors & Hardware | 2 | 2 | 04-Jun-21 | 07-Jun-21 |
| A13520 | OH Mechanical Finishes | 2 | 2 | 04-Jun-21 | 07-Jun-21 |
| A13410 | Pull Wire & Terminate | 15 | 15 | 09-Jun-21 | 29-Jun-21 |
| A13440 | Install Lighting | 3 | 3 | 30-Jun-21 | 02-Jul-21 |
| A13450 | Install Electrical Finishes | 2 | 2 | 06-Jul-21 | 07-Jul-21 |
| A13530 | Install Fire Alarm Devices | 2 | 2 | 06-Jul-21 | 07-Jul-21 |
| A13470 | Seal Concrete Floors | 3 | 3 | 08-Jul-21 | 12-Jul-21 |
| A13540 | MEPFP Final Inspections | 2 | 2 | 08-Jul-21 | 09-Jul-21 |
| A13490 | Final Paint | 2 | 2 | 13-Jul-21 | 14-Jul-21 |
| A13500 | Punchlist | 5 | 5 | 15-Jul-21 | 21-Jul-21 |
| **Visitor Locker Room 3&4 - Rooms 14.34-38** | | **90** | **90** | **31-Mar-21** | **05-Aug-21** |
| A12920 | Layout & Top Track | 2 | 2 | 31-Mar-21 | 01-Apr-21 |
| A12930 | OH Mechanical | 5 | 5 | 02-Apr-21 | 08-Apr-21 |
| A12940 | OH Electrical | 5 | 5 | 06-Apr-21 | 12-Apr-21 |
| A12950 | OH Plumbing | 5 | 5 | 08-Apr-21 | 14-Apr-21 |
| A12960 | OH Fire Protection | 5 | 5 | 12-Apr-21 | 16-Apr-21 |
| A12970 | Above Ceiling Inspections | 1 | 1 | 19-Apr-21 | 19-Apr-21 |
| A12980 | Frame Walls | 3 | 3 | 20-Apr-21 | 22-Apr-21 |
| A12990 | In-Wall Electrical | 4 | 4 | 23-Apr-21 | 28-Apr-21 |
| A13000 | In-Wall Plumbing | 8 | 8 | 27-Apr-21 | 06-May-21 |
| A13010 | In-Wall Inspections | 1 | 1 | 07-May-21 | 07-May-21 |
| A13020 | Frame Ceilings | 3 | 3 | 10-May-21 | 12-May-21 |
| A13030 | In-Ceiling Lighting | 2 | 2 | 13-May-21 | 14-May-21 |
| A13040 | In-Ceiling Fire Protection | 2 | 2 | 17-May-21 | 18-May-21 |
| A13050 | In-Ceiling Inspections | 1 | 1 | 19-May-21 | 19-May-21 |
| A13060 | Hang, Tape & Finish Drywall | 8 | 8 | 20-May-21 | 01-Jun-21 |
| A13070 | Prime Paint | 2 | 2 | 02-Jun-21 | 03-Jun-21 |
| A13130 | Epoxy Walls | 3 | 3 | 02-Jun-21 | 04-Jun-21 |
| A13080 | Install ACT Grid | 2 | 2 | 04-Jun-21 | 07-Jun-21 |
| A13140 | Install Floor Tile (Shower Area) | 5 | 5 | 07-Jun-21 | 11-Jun-21 |
| A13090 | Install Lighting | 2 | 2 | 08-Jun-21 | 09-Jun-21 |
| A13100 | Grilles, Registers & Diffusers | 2 | 2 | 10-Jun-21 | 11-Jun-21 |
| A13110 | Sprinkler Heads | 2 | 2 | 14-Jun-21 | 15-Jun-21 |
| A13150 | Install Millwork | 3 | 3 | 14-Jun-21 | 16-Jun-21 |
| A13120 | Fire Alarm Devices | 2 | 2 | 16-Jun-21 | 17-Jun-21 |
| A13160 | Install Countertops | 2 | 2 | 17-Jun-21 | 18-Jun-21 |
| A13170 | Install Sinks | 2 | 2 | 21-Jun-21 | 22-Jun-21 |
| A13180 | Install Plumbing Fixtures | 4 | 4 | 23-Jun-21 | 28-Jun-21 |
| A13190 | Install Toilet/Shower Partitions | 2 | 2 | 29-Jun-21 | 30-Jun-21 |
| A13200 | Install Toilet Accessories | 2 | 2 | 01-Jul-21 | 02-Jul-21 |
| A13210 | Install Sports Flooring | 5 | 5 | 06-Jul-21 | 12-Jul-21 |
| A13220 | Install Lockers | 8 | 8 | 13-Jul-21 | 22-Jul-21 |
| A13230 | Electrical Trim-out | 3 | 3 | 23-Jul-21 | 27-Jul-21 |
| A13240 | Final Paint | 2 | 2 | 28-Jul-21 | 29-Jul-21 |
| A13250 | MEPFP Final Inspections | 2 | 2 | 28-Jul-21 | 29-Jul-21 |
| A13260 | Punchlist | 5 | 5 | 30-Jul-21 | 05-Aug-21 |
| **Star 1 & 2 - Rooms 14.30-14.33** | | **83** | **83** | **07-Apr-21** | **03-Aug-21** |
| A13840 | Layout & Top Track | 2 | 2 | 07-Apr-21 | 08-Apr-21 |
| A13850 | OH Mechanical | 5 | 5 | 09-Apr-21 | 15-Apr-21 |
| A13860 | OH Electrical | 5 | 5 | 13-Apr-21 | 19-Apr-21 |
| A13870 | OH Plumbing | 5 | 5 | 15-Apr-21 | 21-Apr-21 |

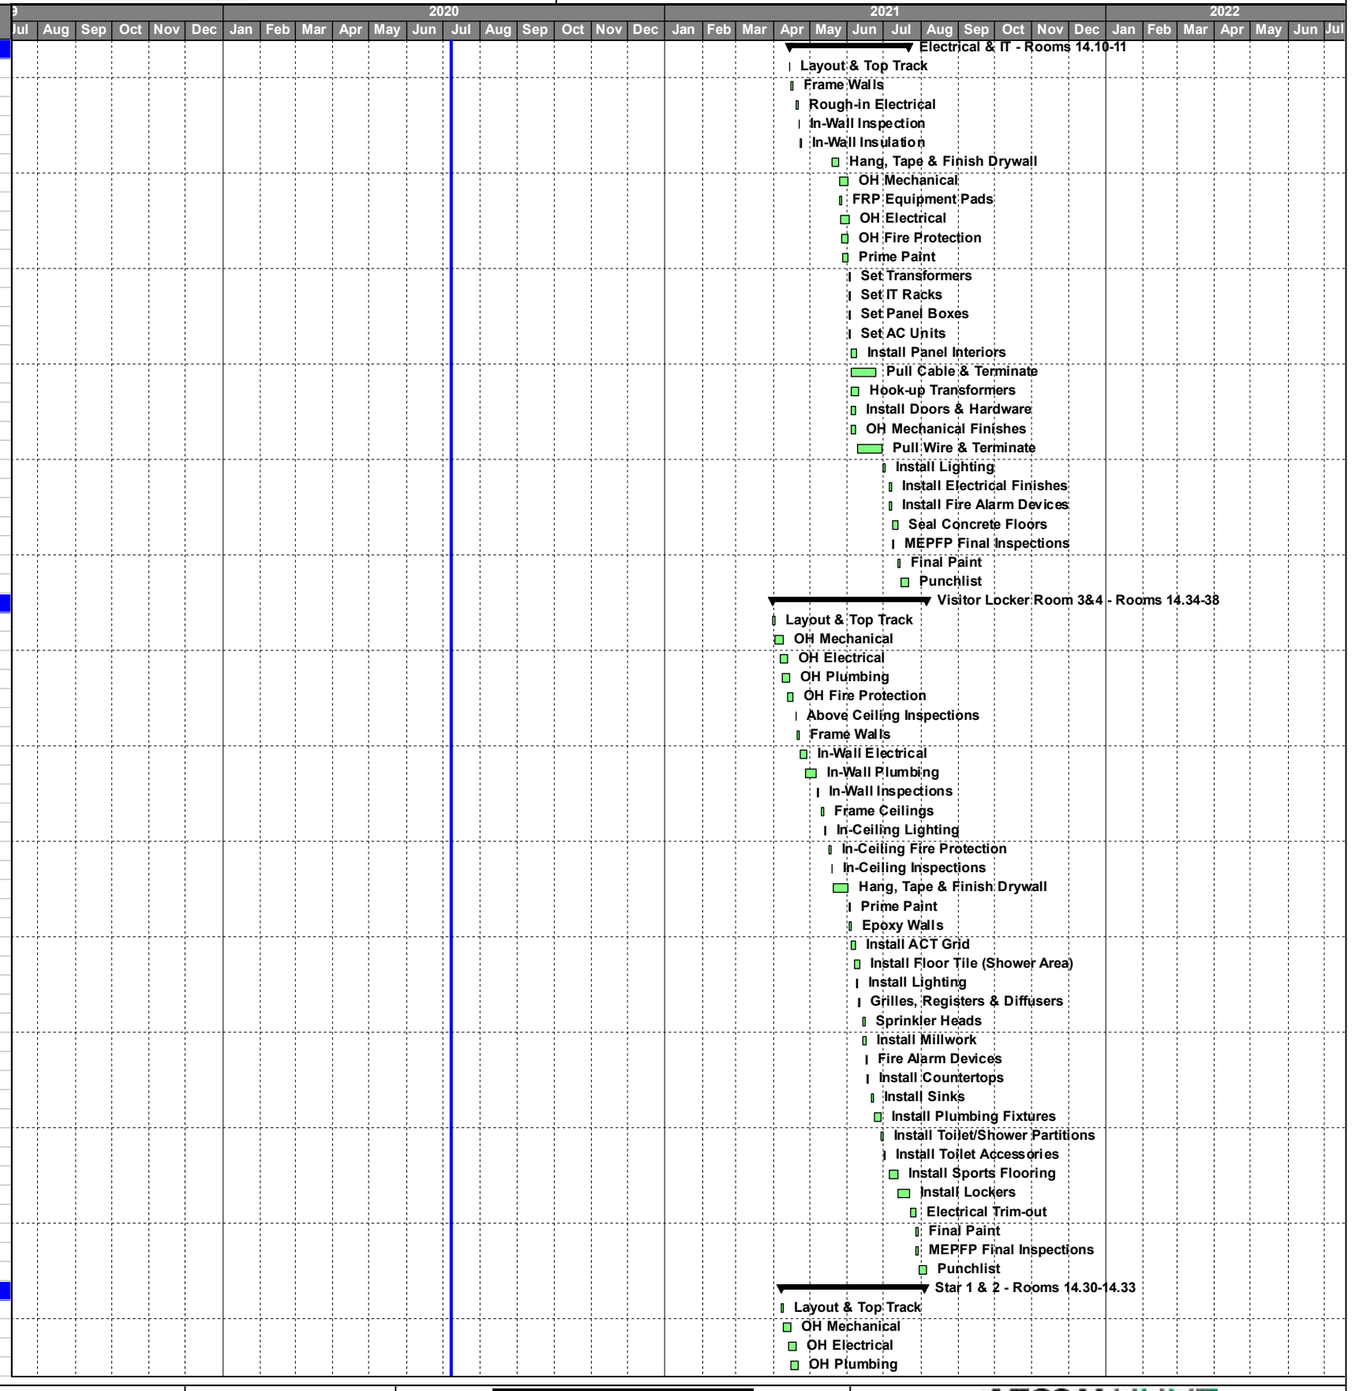

| Activity ID | Activity Name | Original Duration | Remaining Duration | Start | Finish |
|---|---|---|---|---|---|
| A13880 | OH Fire Protection | 5 | 5 | 19-Apr-21 | 23-Apr-21 |
| A13890 | Above Ceiling Inspections | 1 | 1 | 26-Apr-21 | 26-Apr-21 |
| A13900 | Frame Walls | 3 | 3 | 27-Apr-21 | 29-Apr-21 |
| A13910 | In-Wall Electrical | 4 | 4 | 30-Apr-21 | 05-May-21 |
| A13920 | In-Wall Plumbing | 4 | 4 | 04-May-21 | 07-May-21 |
| A13930 | In-Wall Inspections | 1 | 1 | 10-May-21 | 10-May-21 |
| A13940 | Frame Ceilings | 3 | 3 | 11-May-21 | 13-May-21 |
| A13950 | In-Ceiling Lighting | 2 | 2 | 14-May-21 | 17-May-21 |
| A13960 | In-Ceiling Fire Protection | 2 | 2 | 18-May-21 | 19-May-21 |
| A13970 | In-Ceiling Inspections | 1 | 1 | 20-May-21 | 20-May-21 |
| A13980 | Hang, Tape & Finish Drywall | 8 | 8 | 21-May-21 | 02-Jun-21 |
| A13990 | Prime Paint | 2 | 2 | 03-Jun-21 | 04-Jun-21 |
| A14020 | Install Floor Tile (Restrooms) | 5 | 5 | 03-Jun-21 | 09-Jun-21 |
| A14010 | Install ACT Grid | 2 | 2 | 07-Jun-21 | 08-Jun-21 |
| A14030 | Install Lighting | 2 | 2 | 09-Jun-21 | 10-Jun-21 |
| A14060 | Install Millwork | 3 | 3 | 10-Jun-21 | 14-Jun-21 |
| A14040 | Grilles, Registers & Diffusers | 2 | 2 | 11-Jun-21 | 14-Jun-21 |
| A14050 | Sprinkler Heads | 2 | 2 | 15-Jun-21 | 16-Jun-21 |
| A14080 | Install Countertops | 2 | 2 | 15-Jun-21 | 16-Jun-21 |
| A14070 | Fire Alarm Devices | 2 | 2 | 17-Jun-21 | 18-Jun-21 |
| A14090 | Install Sinks | 2 | 2 | 17-Jun-21 | 18-Jun-21 |
| A14100 | Install Plumbing Fixtures | 4 | 4 | 21-Jun-21 | 24-Jun-21 |
| A14110 | Install Showers | 2 | 2 | 25-Jun-21 | 28-Jun-21 |
| A14120 | Install Toilet Accessories | 2 | 2 | 29-Jun-21 | 30-Jun-21 |
| A14130 | Install Carpet | 5 | 5 | 01-Jul-21 | 08-Jul-21 |
| A14140 | Install Doors & Hardware | 8 | 8 | 09-Jul-21 | 20-Jul-21 |
| A14150 | Electrical Trim-out | 3 | 3 | 21-Jul-21 | 23-Jul-21 |
| A14160 | Final Paint | 2 | 2 | 26-Jul-21 | 27-Jul-21 |
| A14170 | MEPFP Final Inspections | 2 | 2 | 26-Jul-21 | 27-Jul-21 |
| A14180 | Punchlist | 5 | 5 | 28-Jul-21 | 03-Aug-21 |
| Ticket Sales, Support, Closet & Sensory Rooms - 14.04-08 | | 86 | 86 | 31-Mar-21 | 30-Jul-21 |
| A14190 | Layout & Top Track | 2 | 2 | 31-Mar-21 | 01-Apr-21 |
| A14200 | OH Mechanical | 5 | 5 | 02-Apr-21 | 08-Apr-21 |
| A14210 | OH Electrical | 5 | 5 | 06-Apr-21 | 12-Apr-21 |
| A14220 | OH Plumbing | 5 | 5 | 08-Apr-21 | 14-Apr-21 |
| A14230 | OH Fire Protection | 5 | 5 | 12-Apr-21 | 16-Apr-21 |
| A14240 | Above Ceiling Inspections | 1 | 1 | 19-Apr-21 | 19-Apr-21 |
| A14250 | Frame Walls | 3 | 3 | 20-Apr-21 | 22-Apr-21 |
| A14260 | Frame Ceilings | 3 | 3 | 23-Apr-21 | 27-Apr-21 |
| A14270 | In-Wall Electrical | 5 | 5 | 23-Apr-21 | 29-Apr-21 |
| A14300 | In-Ceiling Lighting | 2 | 2 | 28-Apr-21 | 29-Apr-21 |
| A14280 | In-Wall Inspections | 1 | 1 | 30-Apr-21 | 30-Apr-21 |
| A14310 | In-Ceiling Mechanical | 2 | 2 | 30-Apr-21 | 03-May-21 |
| A14320 | In-Ceiling Fire Protection | 2 | 2 | 04-May-21 | 05-May-21 |
| A14330 | In-Ceiling Inspections | 1 | 1 | 06-May-21 | 06-May-21 |
| A14290 | Hang, Tape & Finish Drywall | 6 | 6 | 19-May-21 | 26-May-21 |
| A14335 | Hang, Tape & Finish Ceilings | 7 | 7 | 19-May-21 | 27-May-21 |
| A14340 | Prime Paint | 2 | 2 | 28-May-21 | 01-Jun-21 |
| A14350 | Install ACT Grid | 2 | 2 | 02-Jun-21 | 03-Jun-21 |
| A14360 | Install Lighting | 4 | 4 | 04-Jun-21 | 09-Jun-21 |
| A14510 | Fire Alarm Devices | 3 | 3 | 04-Jun-21 | 08-Jun-21 |
| A14370 | Sprinkler Heads | 2 | 2 | 10-Jun-21 | 11-Jun-21 |
| A14380 | Grilles, Registers & Diffusers | 2 | 2 | 14-Jun-21 | 15-Jun-21 |
| A14390 | Grid Inspections | 1 | 1 | 16-Jun-21 | 16-Jun-21 |
| A14400 | Install ACT Tiles | 1 | 1 | 17-Jun-21 | 17-Jun-21 |
| A14410 | Install Millwork | 5 | 5 | 18-Jun-21 | 24-Jun-21 |
| A14420 | Install Countertops | 2 | 2 | 25-Jun-21 | 28-Jun-21 |
| A14430 | Ticket Sales Windows | 5 | 5 | 29-Jun-21 | 06-Jul-21 |
| A14500 | Electrical Trim-out | 3 | 3 | 29-Jun-21 | 01-Jul-21 |
| A14480 | MEPFP Final Inspections | 2 | 2 | 02-Jul-21 | 06-Jul-21 |
| A14440 | Install Doors & Hardware | 2 | 2 | 07-Jul-21 | 08-Jul-21 |
| A14450 | Seal Concrete Floors | 5 | 5 | 09-Jul-21 | 15-Jul-21 |
| A14460 | Install Carpet | 4 | 4 | 16-Jul-21 | 21-Jul-21 |
| A14470 | Final Paint | 2 | 2 | 22-Jul-21 | 23-Jul-21 |
| A14490 | Punchlist | 5 | 5 | 26-Jul-21 | 30-Jul-21 |
| Ticket Lobby, Storage, Janitor Closet - 14.02-03 & 14.12 | | 67 | 67 | 02-Apr-21 | 07-Jul-21 |
| A30730 | Layout & Top Track | 2 | 2 | 02-Apr-21 | 05-Apr-21 |
| A30740 | OH Mechanical | 5 | 5 | 06-Apr-21 | 12-Apr-21 |
| A30750 | OH Electrical | 5 | 5 | 08-Apr-21 | 14-Apr-21 |
| A30760 | OH Plumbing | 5 | 5 | 12-Apr-21 | 16-Apr-21 |

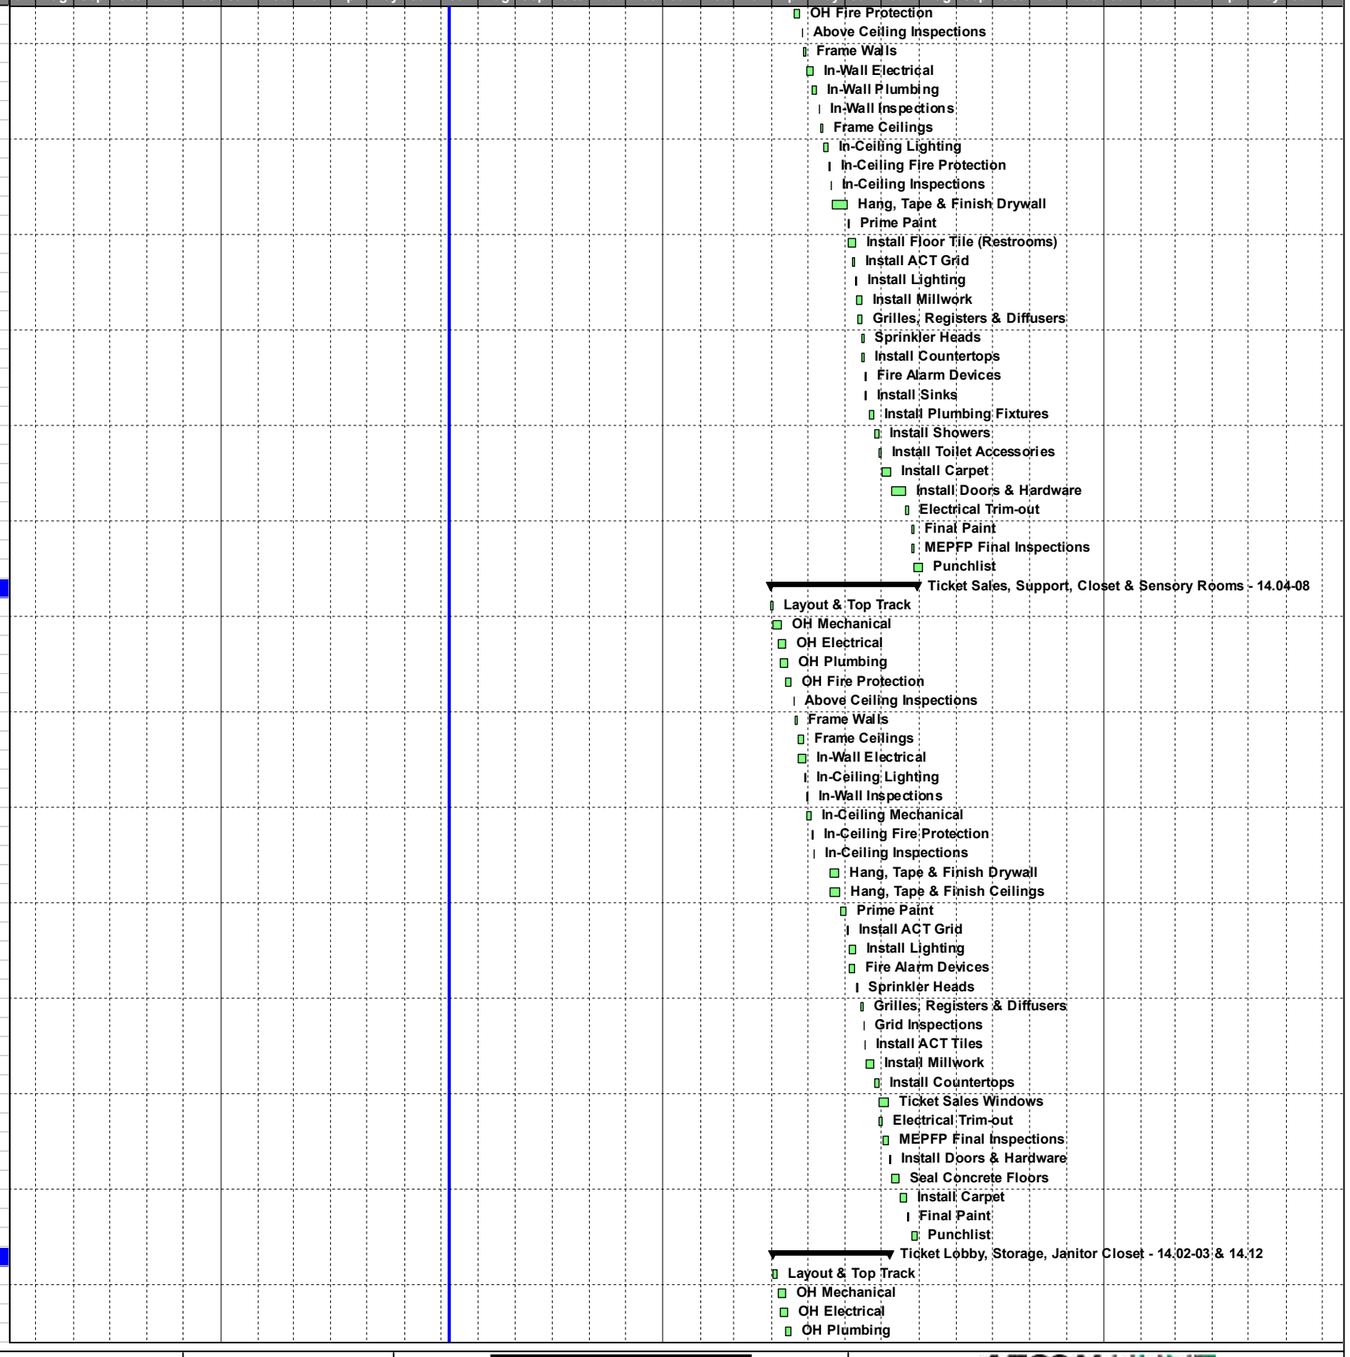

| Activity ID | Activity Name | Original Duration | Remaining Duration | Start | Finish |
|---|---|---|---|---|---|
| A30770 | OH Fire Protection | 5 | 5 | 14-Apr-21 | 20-Apr-21 |
| A30780 | Above Ceiling Inspections | 1 | 1 | 21-Apr-21 | 21-Apr-21 |
| A30790 | Frame Walls | 3 | 3 | 22-Apr-21 | 26-Apr-21 |
| A30800 | Frame Ceilings | 3 | 3 | 27-Apr-21 | 29-Apr-21 |
| A30810 | In-Wall Electrical | 5 | 5 | 27-Apr-21 | 03-May-21 |
| A30840 | In-Ceiling Lighting | 2 | 2 | 30-Apr-21 | 03-May-21 |
| A30820 | In-Wall Inspections | 1 | 1 | 04-May-21 | 04-May-21 |
| A30850 | In-Ceiling Mechanical | 2 | 2 | 04-May-21 | 05-May-21 |
| A30830 | Hang, Tape & Finish Drywall | 6 | 6 | 05-May-21 | 12-May-21 |
| A30860 | In-Ceiling Fire Protection | 2 | 2 | 06-May-21 | 07-May-21 |
| A30870 | In-Ceiling Inspections | 1 | 1 | 10-May-21 | 10-May-21 |
| A31040 | Hang, Tape & Finish Ceilings | 7 | 7 | 11-May-21 | 19-May-21 |
| A30880 | Prime Paint | 2 | 2 | 20-May-21 | 21-May-21 |
| A30890 | Install ACT Grid | 2 | 2 | 24-May-21 | 25-May-21 |
| A30900 | Install Lighting | 4 | 4 | 26-May-21 | 01-Jun-21 |
| A31060 | Fire Alarm Devices | 3 | 3 | 26-May-21 | 28-May-21 |
| A30910 | Sprinkler Heads | 2 | 2 | 02-Jun-21 | 03-Jun-21 |
| A30920 | Grilles, Registers & Diffusers | 2 | 2 | 04-Jun-21 | 07-Jun-21 |
| A30930 | Grid Inspections | 1 | 1 | 08-Jun-21 | 08-Jun-21 |
| A30940 | Install ACT Tiles | 1 | 1 | 09-Jun-21 | 09-Jun-21 |
| A30950 | Install Millwork | 5 | 5 | 10-Jun-21 | 16-Jun-21 |
| A30980 | Install Doors & Hardware | 2 | 2 | 17-Jun-21 | 18-Jun-21 |
| A31050 | Electrical Trim-out | 3 | 3 | 17-Jun-21 | 21-Jun-21 |
| A30990 | Seal Concrete Floors | 5 | 5 | 21-Jun-21 | 25-Jun-21 |
| A31020 | MEPFP Final Inspections | 2 | 2 | 22-Jun-21 | 23-Jun-21 |
| A31010 | Final Paint | 2 | 2 | 28-Jun-21 | 29-Jun-21 |
| A31030 | Punchlist | 5 | 5 | 30-Jun-21 | 07-Jul-21 |
| Reception & Offices - 14.09-25 | | 70 | 70 | 14-Apr-21 | 22-Jul-21 |
| A14520 | Layout & Top Track | 2 | 2 | 14-Apr-21 | 15-Apr-21 |
| A14530 | OH Mechanical | 5 | 5 | 16-Apr-21 | 22-Apr-21 |
| A14540 | OH Electrical | 5 | 5 | 20-Apr-21 | 26-Apr-21 |
| A14550 | OH Plumbing | 5 | 5 | 22-Apr-21 | 28-Apr-21 |
| A14560 | OH Fire Protection | 5 | 5 | 26-Apr-21 | 30-Apr-21 |
| A14570 | Above Ceiling Inspections | 1 | 1 | 03-May-21 | 03-May-21 |
| A14580 | Frame Walls | 3 | 3 | 04-May-21 | 06-May-21 |
| A14590 | In-Wall Plumbing | 3 | 3 | 07-May-21 | 11-May-21 |
| A14600 | In-Wall Electrical | 5 | 5 | 11-May-21 | 17-May-21 |
| A14620 | In-Wall Inspections | 1 | 1 | 18-May-21 | 18-May-21 |
| A14640 | Hang, Tape & Finish Drywall | 6 | 6 | 19-May-21 | 26-May-21 |
| A14610 | Epoxy Walls | 2 | 2 | 27-May-21 | 28-May-21 |
| A14680 | Prime Paint | 2 | 2 | 27-May-21 | 28-May-21 |
| A14630 | Install Floor Tile | 2 | 2 | 01-Jun-21 | 02-Jun-21 |
| A14690 | Install ACT Grid | 2 | 2 | 01-Jun-21 | 02-Jun-21 |
| A14650 | Install Plumbing Fixtures | 2 | 2 | 03-Jun-21 | 04-Jun-21 |
| A14700 | Install Lighting | 4 | 4 | 03-Jun-21 | 08-Jun-21 |
| A14710 | Fire Alarm Devices | 3 | 3 | 03-Jun-21 | 07-Jun-21 |
| A14660 | Install Toilet Accessories | 1 | 1 | 07-Jun-21 | 07-Jun-21 |
| A14720 | Sprinkler Heads | 2 | 2 | 09-Jun-21 | 10-Jun-21 |
| A14730 | Grilles, Registers & Diffusers | 2 | 2 | 11-Jun-21 | 14-Jun-21 |
| A14740 | Grid Inspections | 1 | 1 | 15-Jun-21 | 15-Jun-21 |
| A14750 | Install ACT Tiles | 1 | 1 | 16-Jun-21 | 16-Jun-21 |
| A14760 | Install Millwork | 5 | 5 | 17-Jun-21 | 23-Jun-21 |
| A14770 | Install Countertops | 2 | 2 | 24-Jun-21 | 25-Jun-21 |
| A14810 | Install Doors & Hardware | 2 | 2 | 28-Jun-21 | 29-Jun-21 |
| A14790 | Electrical Trim-out | 3 | 3 | 28-Jun-21 | 30-Jun-21 |
| A14820 | Seal Concrete Floors | 5 | 5 | 30-Jun-21 | 07-Jul-21 |
| A14800 | MEPFP Final Inspections | 2 | 2 | 01-Jul-21 | 02-Jul-21 |
| A14830 | Install Carpet | 4 | 4 | 08-Jul-21 | 13-Jul-21 |
| A14840 | Final Paint | 2 | 2 | 14-Jul-21 | 15-Jul-21 |
| A14850 | Punchlist | 5 | 5 | 16-Jul-21 | 22-Jul-21 |
| Corridors | | 40 | 40 | 01-Jun-21 | 27-Jul-21 |
| A15090 | Prime Paint | 5 | 5 | 01-Jun-21 | 07-Jun-21 |
| A15060 | Sprinkler Heads | 5 | 5 | 08-Jun-21 | 14-Jun-21 |
| A15070 | Lighting | 5 | 5 | 11-Jun-21 | 17-Jun-21 |
| A15080 | Fire Alarm Devices | 5 | 5 | 16-Jun-21 | 22-Jun-21 |
| A15130 | Install Doors & Hardware | 5 | 5 | 23-Jun-21 | 29-Jun-21 |
| A15100 | Seal Concrete Floors | 5 | 5 | 30-Jun-21 | 07-Jul-21 |
| A15110 | Electrical Trim-out | 5 | 5 | 08-Jul-21 | 14-Jul-21 |
| A15120 | Final MEPFP Inspections | 3 | 3 | 15-Jul-21 | 19-Jul-21 |
| A15140 | Final Paint | 4 | 4 | 15-Jul-21 | 20-Jul-21 |

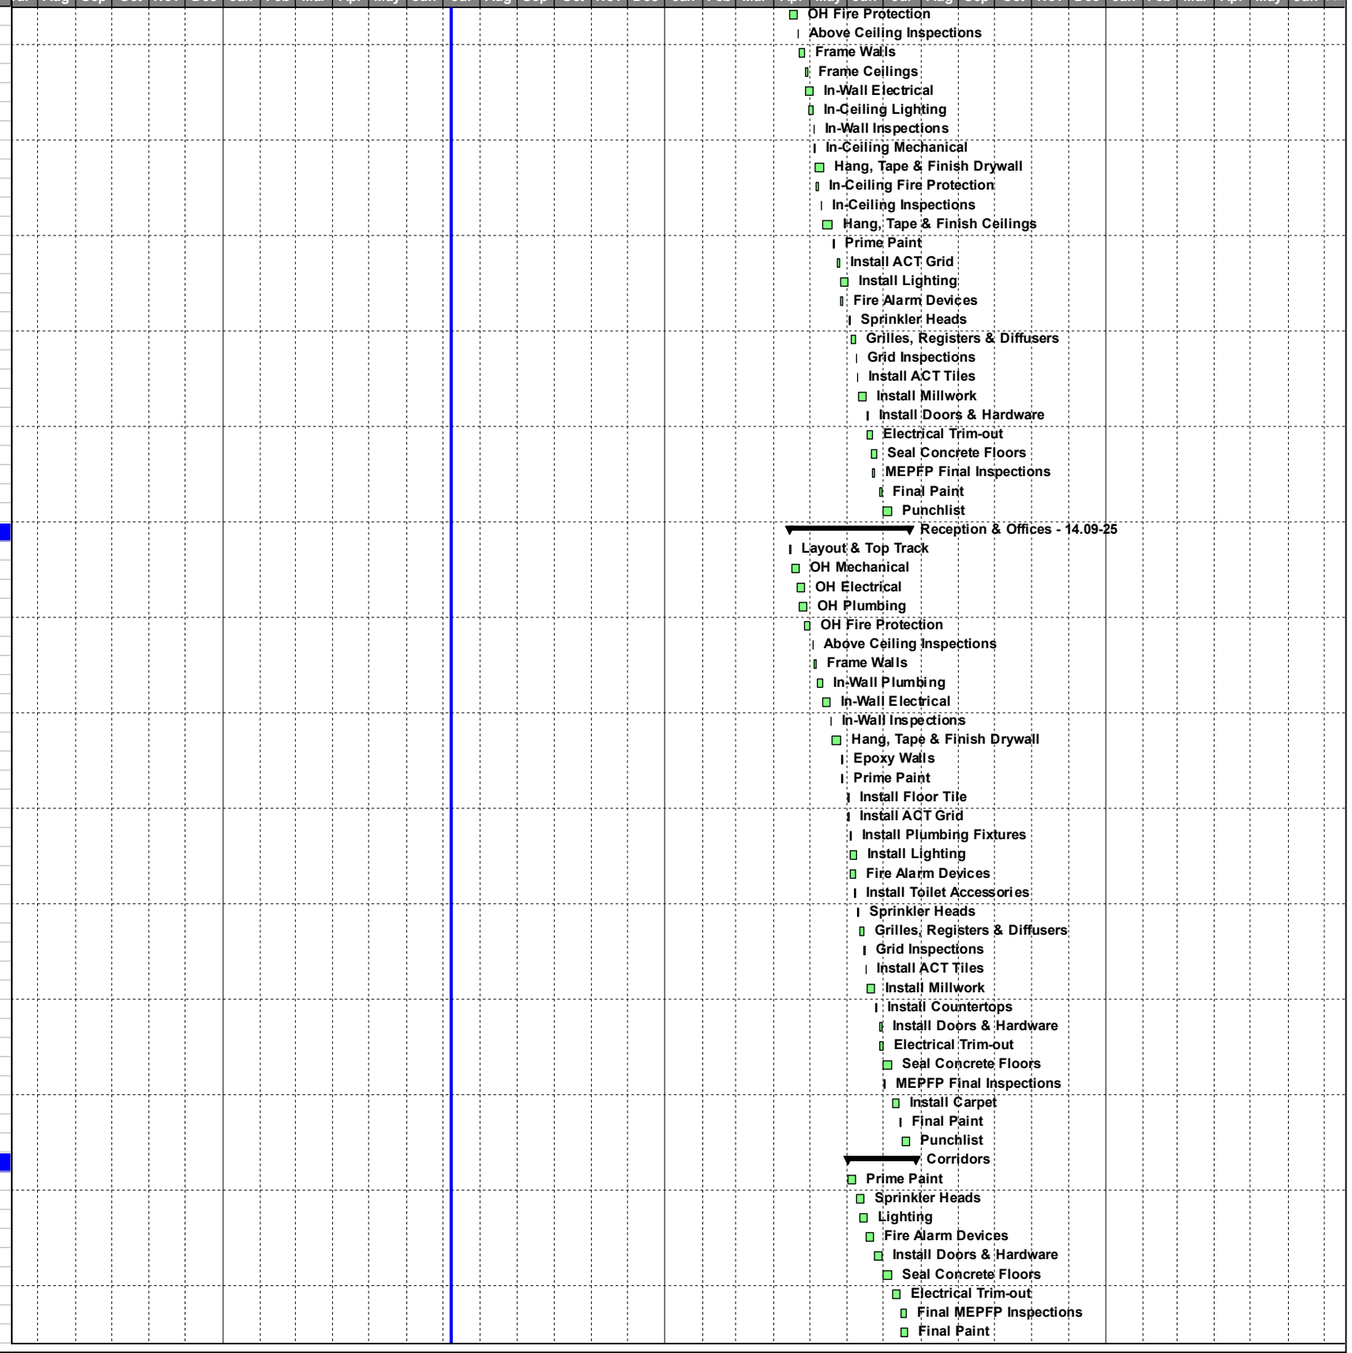

| Activity ID | Activity Name | Original Duration | Remaining Duration | Start | Finish |
|---|---|---|---|---|---|
| A15150 | Punchlist | 5 | 5 | 21-Jul-21 | 27-Jul-21 |
| Concourse Level | | 150 | 150 | 20-Oct-20 | 24-May-21 |
| A29400 | Concourse Level Complete | 0 | 0 | | 24-May-21 |
| Quad 1 | | 120 | 120 | 20-Oct-20 | 12-Apr-21 |
| MEPFP Mains Rough-in | | 45 | 45 | 20-Oct-20 | 23-Dec-20 |
| OHRI-EL-Q1-1 | Spray Fireproofing - First Pass - CL-W10-N/S/N8-E/W | 10 | 10 | 20-Oct-20 | 02-Nov-20 |
| OHRI-EL-Q1-1 | Install Subroof - CL-W10-N/S/N8-E/W | 15 | 15 | 03-Nov-20 | 23-Nov-20 |
| OHRI-EL-Q1-1 | Mechanical Mains - CL-W10-N/S/N8-E/W | 10 | 10 | 19-Nov-20 | 04-Dec-20 |
| OHRI-EL-Q1-1 | Electrical Mains - CL-W10-N/S/N8-E/W | 10 | 10 | 23-Nov-20 | 08-Dec-20 |
| OHRI-EL-Q1-1 | Plumbing Mains - CL-W10-N/S/N8-E/W | 10 | 10 | 25-Nov-20 | 10-Dec-20 |
| OHRI-EL-Q1-1 | Fire Protection Mains - CL-W10-N/S/N8-E/W | 10 | 10 | 01-Dec-20 | 14-Dec-20 |
| OHRI-EL-Q1-1 | Cable Tray AV/IT Mains - CL-W10-N/S/N8-E/W | 10 | 10 | 03-Dec-20 | 16-Dec-20 |
| OHRI-EL-Q1-1 | Spray Fireproofing - Final Pass - CL-W10-N/S/N8-E/W | 10 | 10 | 10-Dec-20 | 23-Dec-20 |
| Electrical & IT - Rooms 21.04 & 21.05 | | 52 | 52 | 15-Dec-20 | 01-Mar-21 |
| A16330 | Layout & Top Track | 1 | 1 | 15-Dec-20 | 15-Dec-20 |
| A16340 | Frame Walls | 2 | 2 | 16-Dec-20 | 17-Dec-20 |
| A16350 | Rough-in Electrical | 3 | 3 | 18-Dec-20 | 22-Dec-20 |
| A16360 | In-Wall Inspection | 1 | 1 | 23-Dec-20 | 23-Dec-20 |
| A16370 | In-Wall Insulation | 1 | 1 | 28-Dec-20 | 28-Dec-20 |
| A16380 | Hang, Tape & Finish Drywall | 4 | 4 | 29-Dec-20 | 04-Jan-21 |
| A16390 | OH Mechanical | 5 | 5 | 05-Jan-21 | 11-Jan-21 |
| A16420 | FRP Equipment Pads | 3 | 3 | 05-Jan-21 | 07-Jan-21 |
| A16400 | OH Electrical | 5 | 5 | 06-Jan-21 | 12-Jan-21 |
| A16410 | OH Fire Protection | 3 | 3 | 07-Jan-21 | 11-Jan-21 |
| A16520 | Prime Paint | 2 | 2 | 08-Jan-21 | 11-Jan-21 |
| A16430 | Set Transformers | 2 | 2 | 12-Jan-21 | 13-Jan-21 |
| A16440 | Set IT Racks | 2 | 2 | 12-Jan-21 | 13-Jan-21 |
| A16450 | Set Panel Boxes | 2 | 2 | 12-Jan-21 | 13-Jan-21 |
| A16570 | Set AC Units | 2 | 2 | 12-Jan-21 | 13-Jan-21 |
| A16460 | Install Panel Interiors | 3 | 3 | 14-Jan-21 | 18-Jan-21 |
| A16480 | Pull Cable & Terminate | 15 | 15 | 14-Jan-21 | 03-Feb-21 |
| A16490 | Hook-up Transformers | 5 | 5 | 14-Jan-21 | 20-Jan-21 |
| A16540 | Install Doors & Hardware | 2 | 2 | 14-Jan-21 | 15-Jan-21 |
| A16580 | OH Mechanical Finishes | 2 | 2 | 14-Jan-21 | 15-Jan-21 |
| A16470 | Pull Wire & Terminate | 15 | 15 | 19-Jan-21 | 08-Feb-21 |
| A16500 | Install Lighting | 3 | 3 | 09-Feb-21 | 11-Feb-21 |
| A16510 | Install Electrical Finishes | 2 | 2 | 12-Feb-21 | 15-Feb-21 |
| A16590 | Install Fire Alarm Devices | 2 | 2 | 12-Feb-21 | 15-Feb-21 |
| A16530 | Seal Concrete Floors | 3 | 3 | 16-Feb-21 | 18-Feb-21 |
| A16600 | MEPFP Final Inspections | 2 | 2 | 16-Feb-21 | 17-Feb-21 |
| A16550 | Final Paint | 2 | 2 | 19-Feb-21 | 22-Feb-21 |
| A16560 | Punchlist | 5 | 5 | 23-Feb-21 | 01-Mar-21 |
| Mens & Womens Restrooms - Rooms 21.08 & 21.09 | | 79 | 79 | 16-Dec-20 | 08-Apr-21 |
| A15160 | Layout & Top Track | 2 | 2 | 16-Dec-20 | 17-Dec-20 |
| A15170 | OH Mechanical | 5 | 5 | 18-Dec-20 | 28-Dec-20 |
| A15180 | OH Electrical | 5 | 5 | 22-Dec-20 | 30-Dec-20 |
| A15190 | OH Plumbing | 5 | 5 | 28-Dec-20 | 04-Jan-21 |
| A15200 | OH Fire Protection | 5 | 5 | 30-Dec-20 | 06-Jan-21 |
| A15210 | Above Ceiling Inspections | 1 | 1 | 07-Jan-21 | 07-Jan-21 |
| A15220 | Frame Walls | 3 | 3 | 08-Jan-21 | 12-Jan-21 |
| A15230 | In-Wall Electrical | 5 | 5 | 13-Jan-21 | 19-Jan-21 |
| A15240 | In-Wall Plumbing | 8 | 8 | 13-Jan-21 | 22-Jan-21 |
| A15250 | In-Wall Inspections | 1 | 1 | 25-Jan-21 | 25-Jan-21 |
| A15260 | Hang Cement Board | 3 | 3 | 26-Jan-21 | 28-Jan-21 |
| A15270 | Install Wall Tile | 7 | 7 | 29-Jan-21 | 08-Feb-21 |
| A15340 | Install Floor Tile | 5 | 5 | 09-Feb-21 | 15-Feb-21 |
| A15280 | Install ACT Grid | 2 | 2 | 16-Feb-21 | 17-Feb-21 |
| A15290 | Install Lighting | 2 | 2 | 18-Feb-21 | 19-Feb-21 |
| A15300 | Grilles, Registers & Diffusers | 2 | 2 | 19-Feb-21 | 22-Feb-21 |
| A15310 | Sprinkler Heads | 2 | 2 | 22-Feb-21 | 23-Feb-21 |
| A15320 | Fire Alarm Devices | 2 | 2 | 24-Feb-21 | 25-Feb-21 |
| A15330 | In-Ceiling Inspections | 1 | 1 | 26-Feb-21 | 26-Feb-21 |
| A15350 | Install ACT Tiles | 2 | 2 | 01-Mar-21 | 02-Mar-21 |
| A15360 | Install Toilets & Urinals | 5 | 5 | 03-Mar-21 | 09-Mar-21 |
| A15370 | Install Millwork | 4 | 4 | 10-Mar-21 | 15-Mar-21 |
| A15380 | Install Countertops | 2 | 2 | 16-Mar-21 | 17-Mar-21 |
| A15390 | Install Plumbing Fixtures | 2 | 2 | 18-Mar-21 | 19-Mar-21 |
| A15400 | Toilet Partitions | 3 | 3 | 22-Mar-21 | 24-Mar-21 |
| A15410 | Install Toilet Accessories | 2 | 2 | 25-Mar-21 | 26-Mar-21 |
| A15420 | Electrical Trim-out | 2 | 2 | 29-Mar-21 | 30-Mar-21 |

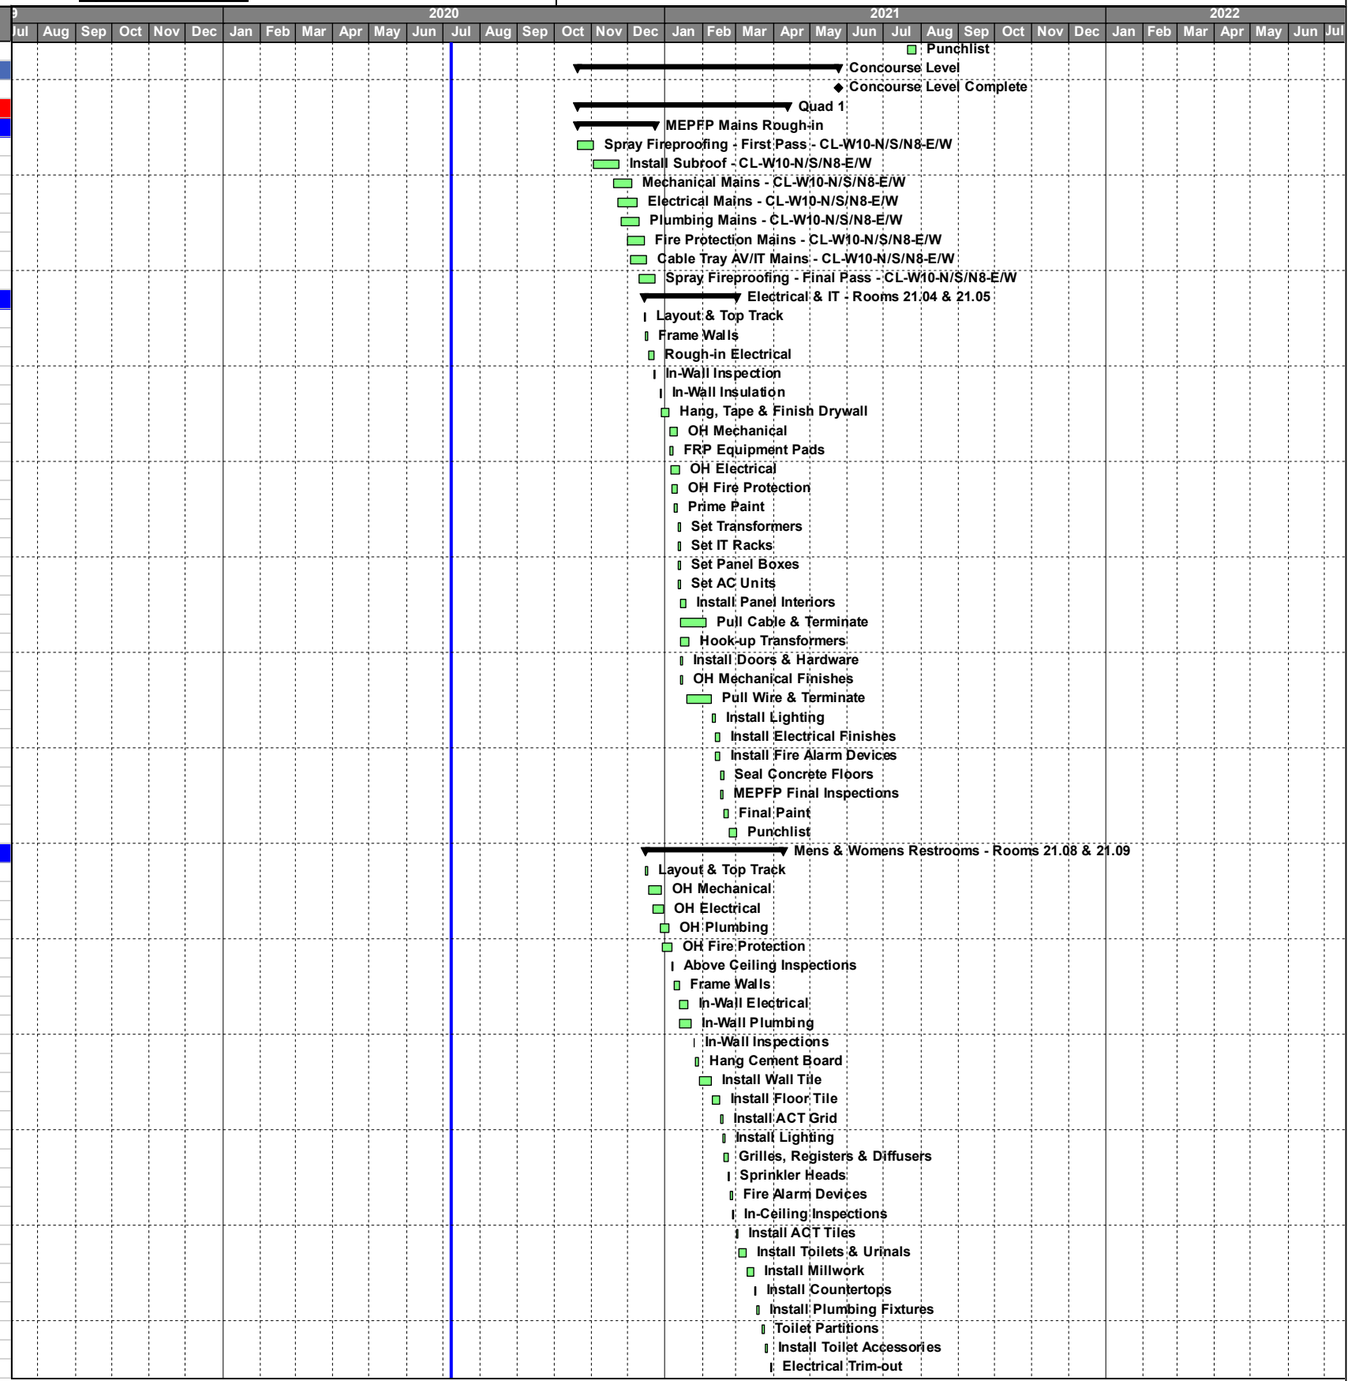

| Activity ID | Activity Name | Original Duration | Remaining Duration | Start | Finish |
|---|---|---|---|---|---|
| A15430 | MEPFP Final Inspections | 2 | 2 | 31-Mar-21 | 01-Apr-21 |
| A15440 | Punchlist | 5 | 5 | 02-Apr-21 | 08-Apr-21 |
| **Womens Club Restrooms - Rooms 21.10** | | **79** | **79** | **18-Dec-20** | **12-Apr-21** |
| A15740 | Layout & Top Track | 2 | 2 | 18-Dec-20 | 21-Dec-20 |
| A15750 | OH Mechanical | 5 | 5 | 22-Dec-20 | 30-Dec-20 |
| A15760 | OH Electrical | 5 | 5 | 28-Dec-20 | 04-Jan-21 |
| A15770 | OH Plumbing | 5 | 5 | 30-Dec-20 | 06-Jan-21 |
| A15780 | OH Fire Protection | 5 | 5 | 04-Jan-21 | 08-Jan-21 |
| A15790 | Above Ceiling Inspections | 1 | 1 | 11-Jan-21 | 11-Jan-21 |
| A15800 | Frame Walls | 3 | 3 | 12-Jan-21 | 14-Jan-21 |
| A15810 | In-Wall Electrical | 5 | 5 | 15-Jan-21 | 21-Jan-21 |
| A15820 | In-Wall Plumbing | 8 | 8 | 15-Jan-21 | 26-Jan-21 |
| A15830 | In-Wall Inspections | 1 | 1 | 27-Jan-21 | 27-Jan-21 |
| A15840 | Hang Cement Board | 3 | 3 | 28-Jan-21 | 01-Feb-21 |
| A15850 | Install Wall Tile | 7 | 7 | 02-Feb-21 | 10-Feb-21 |
| A15920 | Install Floor Tile | 5 | 5 | 11-Feb-21 | 17-Feb-21 |
| A15860 | Install ACT Grid | 2 | 2 | 18-Feb-21 | 19-Feb-21 |
| A15870 | Install Lighting | 2 | 2 | 22-Feb-21 | 23-Feb-21 |
| A15880 | Grilles, Registers & Diffusers | 2 | 2 | 23-Feb-21 | 24-Feb-21 |
| A15890 | Sprinkler Heads | 2 | 2 | 24-Feb-21 | 25-Feb-21 |
| A15900 | Fire Alarm Devices | 2 | 2 | 26-Feb-21 | 01-Mar-21 |
| A15910 | In-Ceiling Inspections | 1 | 1 | 02-Mar-21 | 02-Mar-21 |
| A15930 | Install ACT Tiles | 2 | 2 | 03-Mar-21 | 04-Mar-21 |
| A15940 | Install Toilets & Urinals | 5 | 5 | 05-Mar-21 | 11-Mar-21 |
| A15950 | Install Millwork | 4 | 4 | 12-Mar-21 | 17-Mar-21 |
| A15960 | Install Countertops | 2 | 2 | 18-Mar-21 | 19-Mar-21 |
| A15970 | Install Plumbing Fixtures | 2 | 2 | 22-Mar-21 | 23-Mar-21 |
| A15980 | Toilet Partitions | 3 | 3 | 24-Mar-21 | 26-Mar-21 |
| A15990 | Install Toilet Accessories | 2 | 2 | 29-Mar-21 | 30-Mar-21 |
| A16000 | Electrical Trim-out | 2 | 2 | 31-Mar-21 | 01-Apr-21 |
| A16010 | MEPFP Final Inspections | 2 | 2 | 02-Apr-21 | 05-Apr-21 |
| A16020 | Punchlist | 5 | 5 | 06-Apr-21 | 12-Apr-21 |
| **Concession & Prep - Rooms 21.06 & 21.07** | | **58** | **58** | **22-Dec-20** | **16-Mar-21** |
| A16320 | Layout & Top Track | 2 | 2 | 22-Dec-20 | 23-Dec-20 |
| A15450 | OH Mechanical | 4 | 4 | 28-Dec-20 | 31-Dec-20 |
| A15460 | OH Electrical | 4 | 4 | 30-Dec-20 | 05-Jan-21 |
| A15470 | OH Plumbing | 4 | 4 | 04-Jan-21 | 07-Jan-21 |
| A15480 | OH Fire Protection | 4 | 4 | 06-Jan-21 | 11-Jan-21 |
| A15530 | Frame Ceilings | 2 | 2 | 06-Jan-21 | 07-Jan-21 |
| A15540 | Install Lighting (Drywall Ceilings) | 2 | 2 | 08-Jan-21 | 11-Jan-21 |
| A15490 | Install Exhaust Hood | 5 | 5 | 12-Jan-21 | 18-Jan-21 |
| A15550 | Hang, Tape & Finish Drywall | 5 | 5 | 12-Jan-21 | 18-Jan-21 |
| A15500 | Above Ceiling Inspections | 1 | 1 | 19-Jan-21 | 19-Jan-21 |
| A15510 | Prime Paint | 1 | 1 | 19-Jan-21 | 19-Jan-21 |
| A15610 | FRP Wall Panels | 3 | 3 | 20-Jan-21 | 22-Jan-21 |
| A15520 | Install ACT Grid | 1 | 1 | 25-Jan-21 | 25-Jan-21 |
| A15560 | Install Lighting (Grid Ceilings) | 2 | 2 | 26-Jan-21 | 27-Jan-21 |
| A15570 | Sprinkler Heads | 1 | 1 | 28-Jan-21 | 28-Jan-21 |
| A15580 | Grilles, Registers & Diffusers | 1 | 1 | 29-Jan-21 | 29-Jan-21 |
| A15590 | Fire Alarm Devices | 1 | 1 | 01-Feb-21 | 01-Feb-21 |
| A15720 | In-Ceiling Inspections | 1 | 1 | 02-Feb-21 | 02-Feb-21 |
| A15600 | Install ACT Tiles | 1 | 1 | 03-Feb-21 | 03-Feb-21 |
| A15620 | Resilient Flooring | 5 | 5 | 04-Feb-21 | 10-Feb-21 |
| A15660 | Millwork | 5 | 5 | 11-Feb-21 | 17-Feb-21 |
| A15730 | Install Doors & Hardware | 1 | 1 | 11-Feb-21 | 11-Feb-21 |
| A15630 | Install Plumbing Fixtures | 2 | 2 | 18-Feb-21 | 19-Feb-21 |
| A15700 | Tile Concession Wall | 3 | 3 | 18-Feb-21 | 22-Feb-21 |
| A15710 | Install Countertops | 2 | 2 | 23-Feb-21 | 24-Feb-21 |
| A15650 | Food Service Equipment | 5 | 5 | 25-Feb-21 | 03-Mar-21 |
| A15640 | Electrical Trim-out | 2 | 2 | 04-Mar-21 | 05-Mar-21 |
| A15670 | Final Paint | 2 | 2 | 08-Mar-21 | 09-Mar-21 |
| A15680 | MEPFP Final Inspections | 2 | 2 | 08-Mar-21 | 09-Mar-21 |
| A15690 | Punchlist | 5 | 5 | 10-Mar-21 | 16-Mar-21 |
| **N Club West Bar - Rooms 21.15** | | **61** | **61** | **28-Dec-20** | **23-Mar-21** |
| A20300 | Layout & Top Track | 5 | 5 | 28-Dec-20 | 04-Jan-21 |
| A16030 | OH Mechanical | 4 | 4 | 05-Jan-21 | 08-Jan-21 |
| A16040 | OH Electrical | 4 | 4 | 07-Jan-21 | 12-Jan-21 |
| A16050 | OH Plumbing | 4 | 4 | 11-Jan-21 | 14-Jan-21 |
| A16060 | OH Fire Protection | 4 | 4 | 13-Jan-21 | 18-Jan-21 |
| A16110 | Frame Ceilings | 2 | 2 | 13-Jan-21 | 14-Jan-21 |

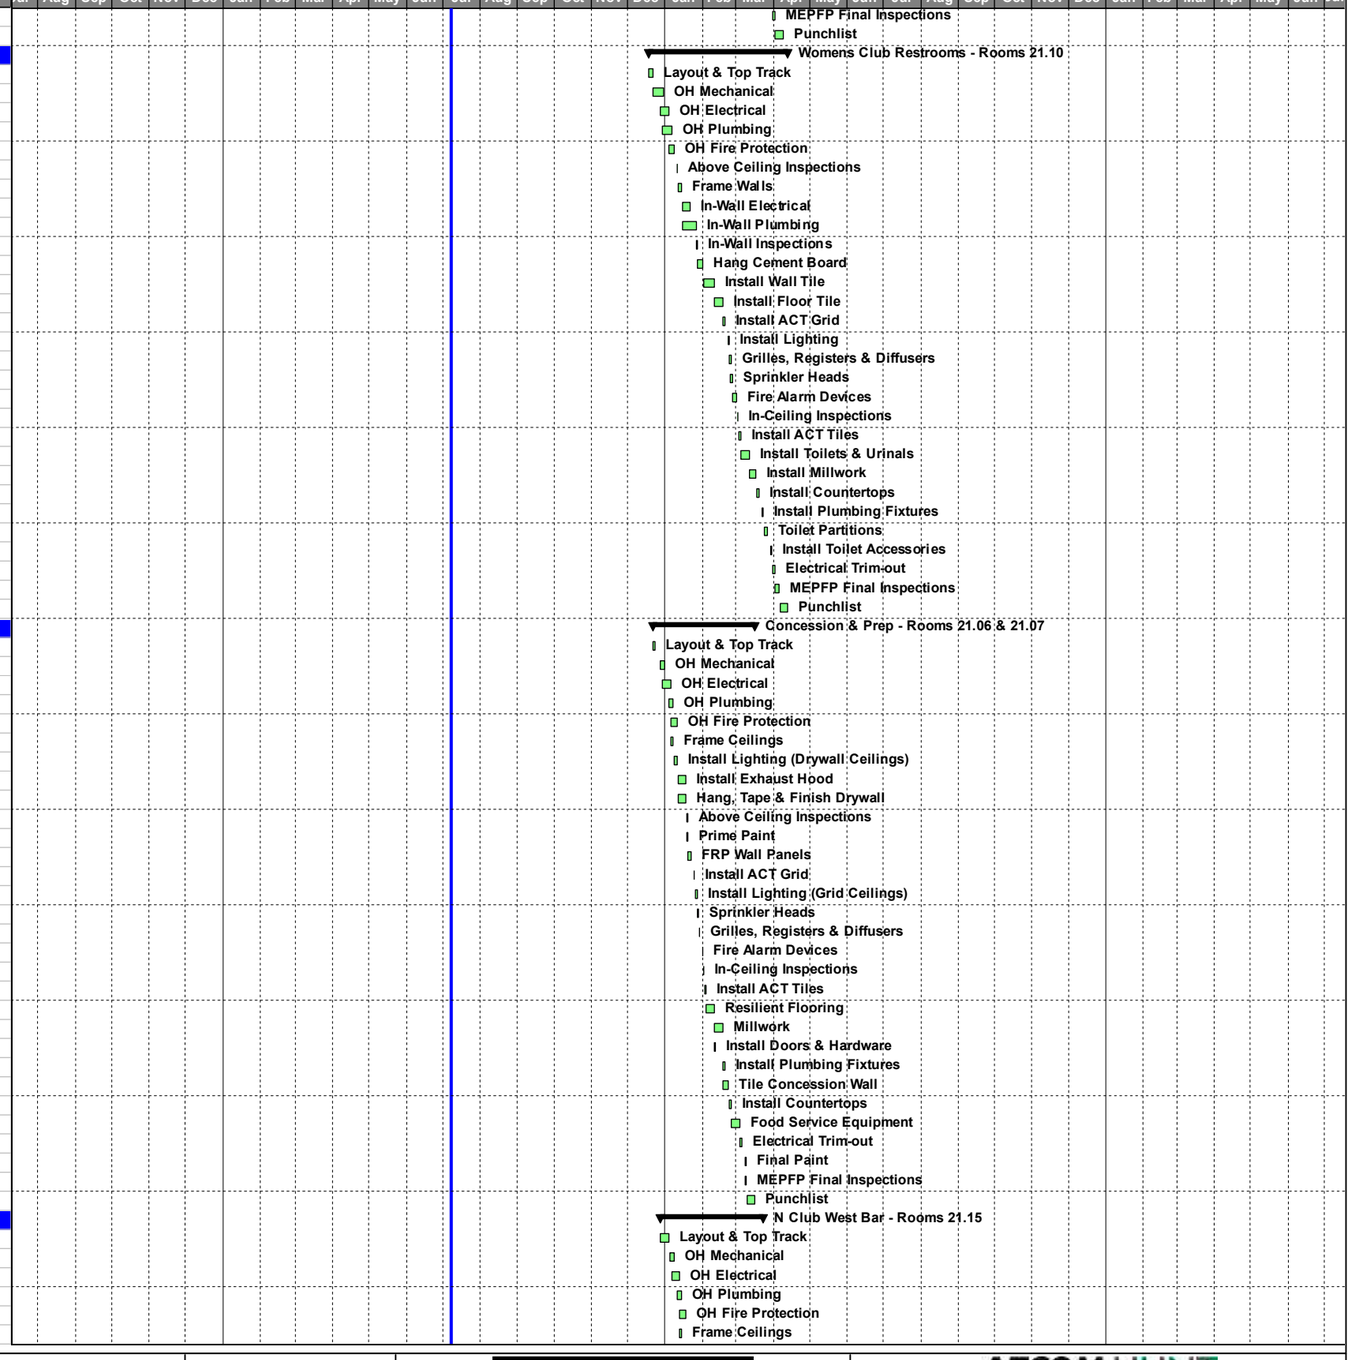

| Activity ID | Activity Name | Original Duration | Remaining Duration | Start | Finish |
|---|---|---|---|---|---|
| A16120 | Install Lighting (Drywall Ceilings) | 2 | 2 | 15-Jan-21 | 18-Jan-21 |
| A16070 | Install Exhaust Hood | 5 | 5 | 19-Jan-21 | 25-Jan-21 |
| A16130 | Hang, Tape & Finish Drywall | 5 | 5 | 19-Jan-21 | 25-Jan-21 |
| A16080 | Above Ceiling Inspections | 1 | 1 | 26-Jan-21 | 26-Jan-21 |
| A16090 | Prime Paint | 1 | 1 | 26-Jan-21 | 26-Jan-21 |
| A16190 | FRP Wall Panels | 3 | 3 | 27-Jan-21 | 29-Jan-21 |
| A16100 | Install ACT Grid | 1 | 1 | 01-Feb-21 | 01-Feb-21 |
| A16140 | Install Lighting (Grid Ceilings) | 2 | 2 | 02-Feb-21 | 03-Feb-21 |
| A16150 | Sprinkler Heads | 1 | 1 | 04-Feb-21 | 04-Feb-21 |
| A16160 | Grilles, Registers & Diffusers | 1 | 1 | 05-Feb-21 | 05-Feb-21 |
| A16170 | Fire Alarm Devices | 1 | 1 | 08-Feb-21 | 08-Feb-21 |
| A16300 | In-Ceiling Inspections | 1 | 1 | 09-Feb-21 | 09-Feb-21 |
| A16180 | Install ACT Tiles | 1 | 1 | 10-Feb-21 | 10-Feb-21 |
| A16200 | Resilient Flooring | 5 | 5 | 11-Feb-21 | 17-Feb-21 |
| A16240 | Millwork | 5 | 5 | 18-Feb-21 | 24-Feb-21 |
| A16310 | Install Doors & Hardware | 1 | 1 | 18-Feb-21 | 18-Feb-21 |
| A16210 | Install Plumbing Fixtures | 2 | 2 | 25-Feb-21 | 26-Feb-21 |
| A16280 | Tile Concession Wall | 3 | 3 | 25-Feb-21 | 01-Mar-21 |
| A16290 | Install Countertops | 2 | 2 | 02-Mar-21 | 03-Mar-21 |
| A16230 | Food Service Equipment | 5 | 5 | 04-Mar-21 | 10-Mar-21 |
| A16220 | Electrical Trim-out | 2 | 2 | 11-Mar-21 | 12-Mar-21 |
| A16250 | Final Paint | 2 | 2 | 15-Mar-21 | 16-Mar-21 |
| A16260 | MEPFP Final Inspections | 2 | 2 | 15-Mar-21 | 16-Mar-21 |
| A16270 | Punchlist | 5 | 5 | 17-Mar-21 | 23-Mar-21 |
| Corridors | | 40 | 40 | 27-Jan-21 | 23-Mar-21 |
| A16640 | Prime Paint | 5 | 5 | 27-Jan-21 | 02-Feb-21 |
| A16610 | Sprinkler Heads | 5 | 5 | 03-Feb-21 | 09-Feb-21 |
| A16620 | Lighting | 5 | 5 | 08-Feb-21 | 12-Feb-21 |
| A16630 | Fire Alarm Devices | 5 | 5 | 11-Feb-21 | 17-Feb-21 |
| A16680 | Install Doors & Hardware | 5 | 5 | 18-Feb-21 | 24-Feb-21 |
| A16650 | Seal Concrete Floors | 5 | 5 | 25-Feb-21 | 03-Mar-21 |
| A16660 | Electrical Trim-out | 5 | 5 | 04-Mar-21 | 10-Mar-21 |
| A16670 | Final MEPFP Inspections | 3 | 3 | 11-Mar-21 | 15-Mar-21 |
| A16690 | Final Paint | 4 | 4 | 11-Mar-21 | 16-Mar-21 |
| A16700 | Punchlist | 5 | 5 | 17-Mar-21 | 23-Mar-21 |
| Quad 2 | | 135 | 135 | 05-Nov-20 | 19-May-21 |
| MEPFP Mains Rough-in | | 43 | 43 | 05-Nov-20 | 11-Jan-21 |
| OHRI-EL-Q2-1 | Spray Fireproofing - First Pass - CL-N/S-E8/N8-E/W | 10 | 10 | 05-Nov-20 | 18-Nov-20 |
| OHRI-EL-Q2-1 | Install Subroof - CL-N/S-E8/N8-E/W | 15 | 15 | 19-Nov-20 | 11-Dec-20 |
| OHRI-EL-Q2-1 | Intumescent Coatings - CL-N/S-E8/N8-E/W | 10 | 10 | 19-Nov-20 | 04-Dec-20 |
| OHRI-EL-Q2-1 | Mechanical Mains - CL-N/S-E8/N8-E/W | 10 | 10 | 07-Dec-20 | 18-Dec-20 |
| OHRI-EL-Q2-1 | Electrical Mains - CL-N/S-E8/N8-E/W | 10 | 10 | 09-Dec-20 | 22-Dec-20 |
| OHRI-EL-Q2-1 | Plumbing Mains - CL-N/S-E8/N8-E/W | 10 | 10 | 11-Dec-20 | 28-Dec-20 |
| OHRI-EL-Q2-1 | Fire Protection Mains - CL-N/S-E8/N8-E/W | 10 | 10 | 15-Dec-20 | 30-Dec-20 |
| OHRI-EL-Q2-1 | Cable Tray AV/IT Mains - CL-N/S-E8/N8-E/W | 10 | 10 | 17-Dec-20 | 04-Jan-21 |
| OHRI-EL-Q2-1 | Spray Fireproofing - Final Pass - CL-N/S-E8/N8-E/W | 10 | 10 | 28-Dec-20 | 11-Jan-21 |
| North Club - 21.12 & 21.16 | | 99 | 99 | 31-Dec-20 | 19-May-21 |
| B1390 | Layout & Top Track | 5 | 5 | 31-Dec-20 | 07-Jan-21 |
| B1400 | OH Mechanical | 10 | 10 | 08-Jan-21 | 21-Jan-21 |
| B1410 | OH Electrical | 10 | 10 | 12-Jan-21 | 25-Jan-21 |
| B1420 | OH Plumbing | 10 | 10 | 14-Jan-21 | 27-Jan-21 |
| B1430 | OH Fire Protection | 10 | 10 | 18-Jan-21 | 29-Jan-21 |
| B1440 | Above Ceiling Inspections | 2 | 2 | 01-Feb-21 | 02-Feb-21 |
| B1450 | Frame Walls | 5 | 5 | 01-Feb-21 | 05-Feb-21 |
| B1500 | In-Wall Electrical | 5 | 5 | 03-Feb-21 | 09-Feb-21 |
| B1510 | In-Wall Plumbing | 5 | 5 | 05-Feb-21 | 11-Feb-21 |
| B1460 | Frame Ceilings & Soffitts | 3 | 3 | 08-Feb-21 | 10-Feb-21 |
| B1470 | Install In-Ceiling Lighting | 5 | 5 | 11-Feb-21 | 17-Feb-21 |
| B1520 | In-Wall Inspections | 2 | 2 | 12-Feb-21 | 15-Feb-21 |
| B1530 | Hang, Tape & Finish Drywall | 10 | 10 | 16-Feb-21 | 01-Mar-21 |
| B1480 | Sprinklers Heads | 4 | 4 | 18-Feb-21 | 23-Feb-21 |
| B1540 | Wood Panels on Wall | 8 | 8 | 02-Mar-21 | 11-Mar-21 |
| B1550 | Hang, Tape & Finish Ceilings & Soffitts | 5 | 5 | 02-Mar-21 | 08-Mar-21 |
| B1730 | FRP Wall Panels | 3 | 3 | 02-Mar-21 | 04-Mar-21 |
| B1560 | Wood Ceilings | 5 | 5 | 09-Mar-21 | 15-Mar-21 |
| B1770 | Prime Paint | 3 | 3 | 09-Mar-21 | 11-Mar-21 |
| B1490 | Install Custom Metal Ceilings | 10 | 10 | 12-Mar-21 | 25-Mar-21 |
| B1570 | Install ACT Grid | 3 | 3 | 12-Mar-21 | 16-Mar-21 |
| B1620 | Electrical Trim-out | 8 | 8 | 12-Mar-21 | 23-Mar-21 |
| B1630 | Install Millwork | 12 | 12 | 12-Mar-21 | 29-Mar-21 |

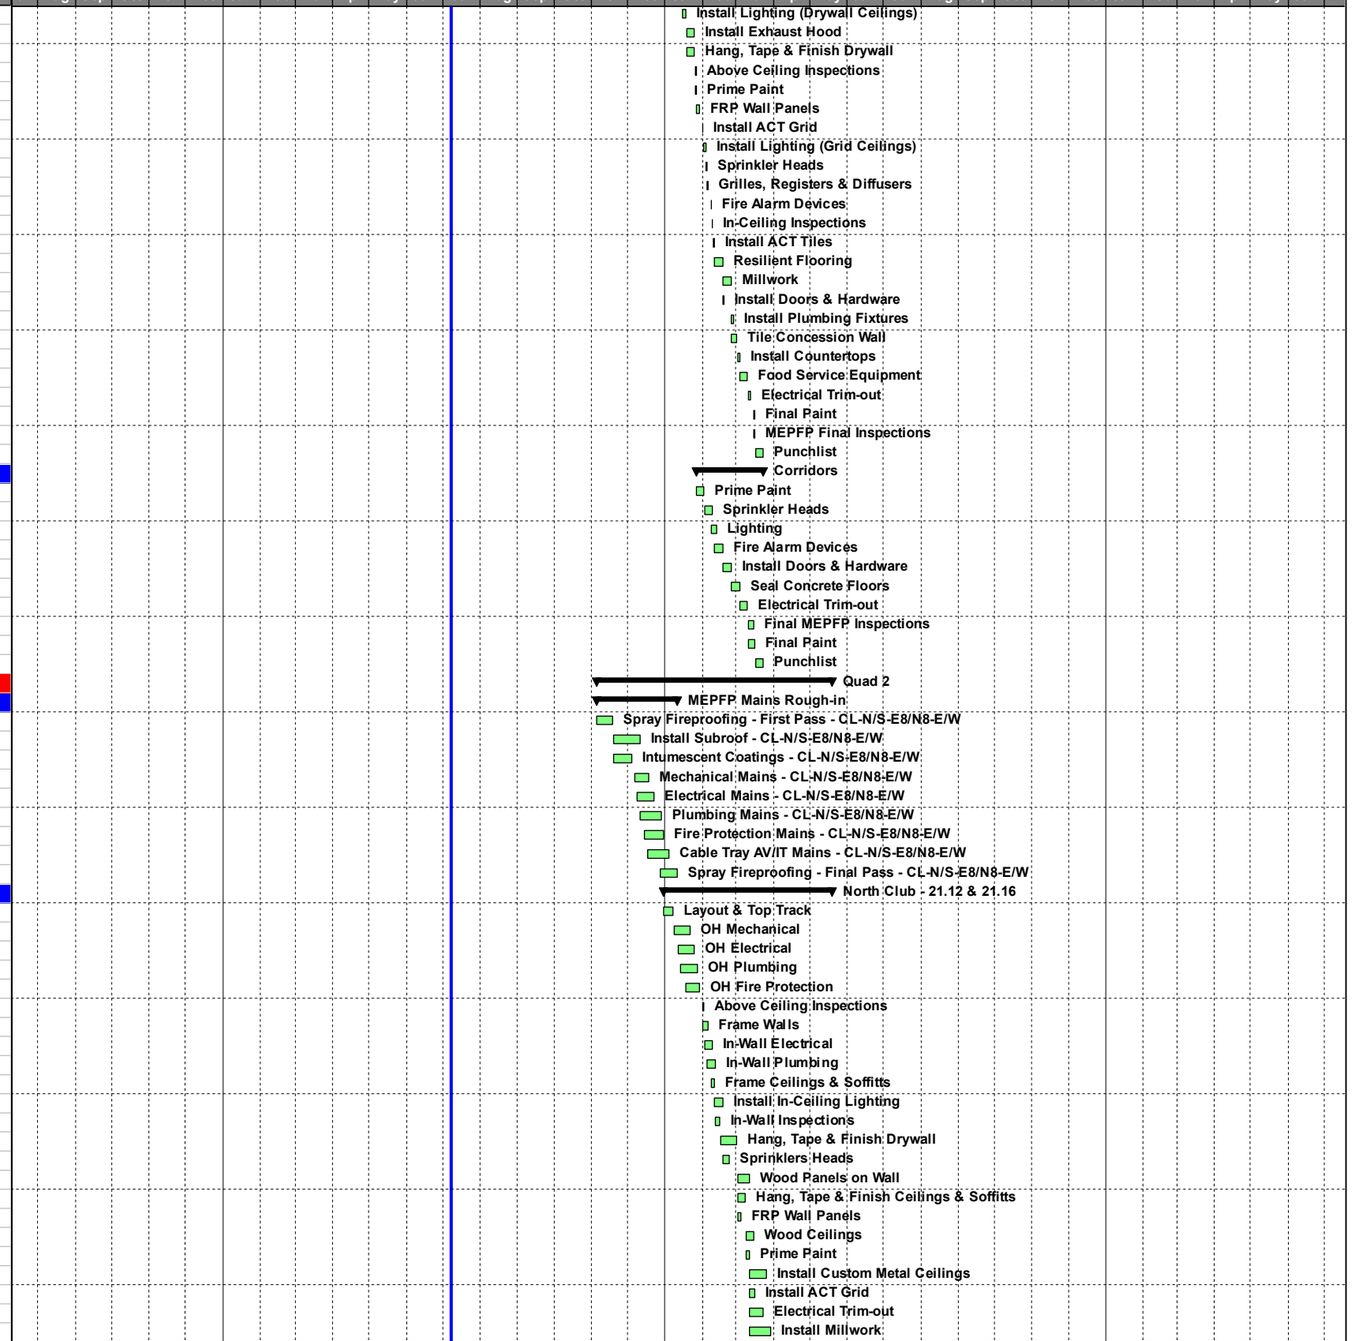

| Activity ID | Activity Name | Original Duration | Remaining Duration | Start | Finish |
|---|---|---|---|---|---|
| B1660 | Install Die-Wall | 8 | 8 | 12-Mar-21 | 23-Mar-21 |
| B1600 | Grilles, Registers & Diffusers | 3 | 3 | 17-Mar-21 | 19-Mar-21 |
| B1610 | Fire Alarm Devices | 2 | 2 | 22-Mar-21 | 23-Mar-21 |
| B1580 | Install ACT Tiles | 2 | 2 | 24-Mar-21 | 25-Mar-21 |
| B1670 | Electrical Rough-in Bar | 5 | 5 | 24-Mar-21 | 30-Mar-21 |
| B1590 | Install Chandeliers | 5 | 5 | 26-Mar-21 | 01-Apr-21 |
| B1680 | Plumbing Rough-in Bar | 5 | 5 | 26-Mar-21 | 01-Apr-21 |
| B1640 | Install Countertops | 5 | 5 | 02-Apr-21 | 08-Apr-21 |
| B1720 | Install Luxury Vinyl Tile | 8 | 8 | 02-Apr-21 | 13-Apr-21 |
| B1650 | Install Plumbing Fixtures | 3 | 3 | 09-Apr-21 | 13-Apr-21 |
| B1700 | Resilient Flooring | 8 | 8 | 14-Apr-21 | 23-Apr-21 |
| B1710 | Install Tile Floors | 5 | 5 | 14-Apr-21 | 20-Apr-21 |
| B1750 | MEPFP Final Inspections | 2 | 2 | 14-Apr-21 | 15-Apr-21 |
| B1690 | Install Kitchen Equipment | 10 | 10 | 26-Apr-21 | 07-May-21 |
| B1740 | Final Paint | 3 | 3 | 10-May-21 | 12-May-21 |
| B1760 | Punchlist | 5 | 5 | 13-May-21 | 19-May-21 |
| **Mens Club Restrooms - Rooms 22.04** | | **79** | **79** | **08-Jan-21** | **28-Apr-21** |
| A16810 | Layout & Top Track | 2 | 2 | 08-Jan-21 | 11-Jan-21 |
| A16820 | OH Mechanical | 5 | 5 | 12-Jan-21 | 18-Jan-21 |
| A16830 | OH Electrical | 5 | 5 | 14-Jan-21 | 20-Jan-21 |
| A16840 | OH Plumbing | 5 | 5 | 18-Jan-21 | 22-Jan-21 |
| A16850 | OH Fire Protection | 5 | 5 | 20-Jan-21 | 26-Jan-21 |
| A16860 | Above Ceiling Inspections | 1 | 1 | 27-Jan-21 | 27-Jan-21 |
| A16870 | Frame Walls | 3 | 3 | 28-Jan-21 | 01-Feb-21 |
| A16880 | In-Wall Electrical | 5 | 5 | 02-Feb-21 | 08-Feb-21 |
| A16890 | In-Wall Plumbing | 8 | 8 | 02-Feb-21 | 11-Feb-21 |
| A16900 | In-Wall Inspections | 1 | 1 | 12-Feb-21 | 12-Feb-21 |
| A16910 | Hang Cement Board | 3 | 3 | 15-Feb-21 | 17-Feb-21 |
| A16920 | Install Wall Tile | 7 | 7 | 18-Feb-21 | 26-Feb-21 |
| A16990 | Install Floor Tile | 5 | 5 | 01-Mar-21 | 05-Mar-21 |
| A16930 | Install ACT Grid | 2 | 2 | 08-Mar-21 | 09-Mar-21 |
| A16940 | Install Lighting | 2 | 2 | 10-Mar-21 | 11-Mar-21 |
| A16950 | Grilles, Registers & Diffusers | 2 | 2 | 11-Mar-21 | 12-Mar-21 |
| A16960 | Sprinkler Heads | 2 | 2 | 12-Mar-21 | 15-Mar-21 |
| A16970 | Fire Alarm Devices | 2 | 2 | 16-Mar-21 | 17-Mar-21 |
| A16980 | In-Ceiling Inspections | 1 | 1 | 18-Mar-21 | 18-Mar-21 |
| A17000 | Install ACT Tiles | 2 | 2 | 19-Mar-21 | 22-Mar-21 |
| A17010 | Install Toilets & Urinals | 5 | 5 | 23-Mar-21 | 29-Mar-21 |
| A17020 | Install Millwork | 4 | 4 | 30-Mar-21 | 02-Apr-21 |
| A17030 | Install Countertops | 2 | 2 | 05-Apr-21 | 06-Apr-21 |
| A17040 | Install Plumbing Fixtures | 2 | 2 | 07-Apr-21 | 08-Apr-21 |
| A17050 | Toilet Partitions | 3 | 3 | 09-Apr-21 | 13-Apr-21 |
| A17060 | Install Toilet Accessories | 2 | 2 | 14-Apr-21 | 15-Apr-21 |
| A17070 | Electrical Trim-out | 2 | 2 | 16-Apr-21 | 19-Apr-21 |
| A17080 | MEPFP Final Inspections | 2 | 2 | 20-Apr-21 | 21-Apr-21 |
| A17090 | Punchlist | 5 | 5 | 22-Apr-21 | 28-Apr-21 |
| **Electrical & IT - Rooms 22.11 & 21.12** | | **52** | **52** | **12-Jan-21** | **24-Mar-21** |
| A17660 | Layout & Top Track | 1 | 1 | 12-Jan-21 | 12-Jan-21 |
| A17670 | Frame Walls | 2 | 2 | 13-Jan-21 | 14-Jan-21 |
| A17680 | Rough-in Electrical | 3 | 3 | 15-Jan-21 | 19-Jan-21 |
| A17690 | In-Wall Inspection | 1 | 1 | 20-Jan-21 | 20-Jan-21 |
| A17700 | In-Wall Insulation | 1 | 1 | 21-Jan-21 | 21-Jan-21 |
| A17710 | Hang, Tape & Finish Drywall | 4 | 4 | 22-Jan-21 | 27-Jan-21 |
| A17720 | OH Mechanical | 5 | 5 | 28-Jan-21 | 03-Feb-21 |
| A17750 | FRP Equipment Pads | 3 | 3 | 28-Jan-21 | 01-Feb-21 |
| A17730 | OH Electrical | 5 | 5 | 29-Jan-21 | 04-Feb-21 |
| A17740 | OH Fire Protection | 3 | 3 | 01-Feb-21 | 03-Feb-21 |
| A17850 | Prime Paint | 2 | 2 | 02-Feb-21 | 03-Feb-21 |
| A17760 | Set Transformers | 2 | 2 | 04-Feb-21 | 05-Feb-21 |
| A17770 | Set IT Racks | 2 | 2 | 04-Feb-21 | 05-Feb-21 |
| A17780 | Set Panel Boxes | 2 | 2 | 04-Feb-21 | 05-Feb-21 |
| A17900 | Set AC Units | 2 | 2 | 04-Feb-21 | 05-Feb-21 |
| A17790 | Install Panel Interiors | 3 | 3 | 08-Feb-21 | 10-Feb-21 |
| A17810 | Pull Cable & Terminate | 15 | 15 | 08-Feb-21 | 26-Feb-21 |
| A17820 | Hook-up Transformers | 5 | 5 | 08-Feb-21 | 12-Feb-21 |
| A17870 | Install Doors & Hardware | 2 | 2 | 08-Feb-21 | 09-Feb-21 |
| A17910 | OH Mechanical Finishes | 2 | 2 | 08-Feb-21 | 09-Feb-21 |
| A17800 | Pull Wire & Terminate | 15 | 15 | 11-Feb-21 | 03-Mar-21 |
| A17830 | Install Lighting | 3 | 3 | 04-Mar-21 | 08-Mar-21 |
| A17840 | Install Electrical Finishes | 2 | 2 | 09-Mar-21 | 10-Mar-21 |



| Activity ID | Activity Name | Original Duration | Remaining Duration | Start | Finish |
|---|---|---|---|---|---|
| A17920 | Install Fire Alarm Devices | 2 | 2 | 09-Mar-21 | 10-Mar-21 |
| A17860 | Seal Concrete Floors | 3 | 3 | 11-Mar-21 | 15-Mar-21 |
| A17930 | MEPFP Final Inspections | 2 | 2 | 11-Mar-21 | 12-Mar-21 |
| A17880 | Final Paint | 2 | 2 | 16-Mar-21 | 17-Mar-21 |
| A17890 | Punchlist | 5 | 5 | 18-Mar-21 | 24-Mar-21 |
| **Mens & Womens Restrooms - Rooms 22.13 & 22.14** | | **82** | **82** | **13-Jan-21** | **06-May-21** |
| A17370 | Layout & Top Track | 2 | 2 | 13-Jan-21 | 14-Jan-21 |
| A17380 | OH Mechanical | 5 | 5 | 15-Jan-21 | 21-Jan-21 |
| A17390 | OH Electrical | 5 | 5 | 19-Jan-21 | 25-Jan-21 |
| A17400 | OH Plumbing | 5 | 5 | 21-Jan-21 | 27-Jan-21 |
| A17410 | OH Fire Protection | 5 | 5 | 25-Jan-21 | 29-Jan-21 |
| A17420 | Above Ceiling Inspections | 1 | 1 | 01-Feb-21 | 01-Feb-21 |
| A17430 | Frame Walls | 3 | 3 | 02-Feb-21 | 04-Feb-21 |
| A17440 | In-Wall Electrical | 5 | 5 | 05-Feb-21 | 11-Feb-21 |
| A17450 | In-Wall Plumbing | 8 | 8 | 05-Feb-21 | 16-Feb-21 |
| A17460 | In-Wall Inspections | 1 | 1 | 17-Feb-21 | 17-Feb-21 |
| A17470 | Hang Cement Board/Drywall | 3 | 3 | 18-Feb-21 | 22-Feb-21 |
| A17480 | Install Wall Tile | 7 | 7 | 23-Feb-21 | 03-Mar-21 |
| A18310 | Prime Paint | 2 | 2 | 23-Feb-21 | 24-Feb-21 |
| A17550 | Install Floor Tile | 5 | 5 | 04-Mar-21 | 10-Mar-21 |
| A17490 | Install ACT Grid | 2 | 2 | 11-Mar-21 | 12-Mar-21 |
| A17500 | Install Lighting | 2 | 2 | 15-Mar-21 | 16-Mar-21 |
| A17510 | Grilles, Registers & Diffusers | 2 | 2 | 16-Mar-21 | 17-Mar-21 |
| A17520 | Sprinkler Heads | 2 | 2 | 17-Mar-21 | 18-Mar-21 |
| A17530 | Fire Alarm Devices | 2 | 2 | 19-Mar-21 | 22-Mar-21 |
| A17540 | In-Ceiling Inspections | 1 | 1 | 23-Mar-21 | 23-Mar-21 |
| A17560 | Install ACT Tiles | 2 | 2 | 24-Mar-21 | 25-Mar-21 |
| A18290 | Install Luxury Vinyl Tile - First Aid | 5 | 5 | 24-Mar-21 | 30-Mar-21 |
| A17570 | Install Toilets & Urinals | 5 | 5 | 31-Mar-21 | 06-Apr-21 |
| A17580 | Install Millwork | 4 | 4 | 07-Apr-21 | 12-Apr-21 |
| A17590 | Install Countertops | 2 | 2 | 13-Apr-21 | 14-Apr-21 |
| A17600 | Install Plumbing Fixtures | 2 | 2 | 15-Apr-21 | 16-Apr-21 |
| A17610 | Toilet Partitions | 3 | 3 | 19-Apr-21 | 21-Apr-21 |
| A17620 | Install Toilet Accessories | 2 | 2 | 22-Apr-21 | 23-Apr-21 |
| A17630 | Electrical Trim-out | 2 | 2 | 26-Apr-21 | 27-Apr-21 |
| A17640 | MEPFP Final Inspections | 2 | 2 | 28-Apr-21 | 29-Apr-21 |
| A18300 | Final Paint | 2 | 2 | 28-Apr-21 | 29-Apr-21 |
| A17650 | Punchlist | 5 | 5 | 30-Apr-21 | 06-May-21 |
| **N Club Kitchen - 22.05** | | **81** | **81** | **15-Jan-21** | **07-May-21** |
| A17170 | Layout & Top Track | 3 | 3 | 15-Jan-21 | 19-Jan-21 |
| A17160 | OH Mechanical | 15 | 15 | 20-Jan-21 | 09-Feb-21 |
| A17150 | OH Plumbing | 15 | 15 | 25-Jan-21 | 12-Feb-21 |
| A17140 | OH Electrical | 10 | 10 | 28-Jan-21 | 10-Feb-21 |
| A17130 | OH Fire Protection | 10 | 10 | 02-Feb-21 | 15-Feb-21 |
| A17120 | Frame Walls | 3 | 3 | 16-Feb-21 | 18-Feb-21 |
| A17280 | In-Wall Electrical Rough-in | 3 | 3 | 18-Feb-21 | 22-Feb-21 |
| A17200 | Rough-in Exhaust Hoods | 5 | 5 | 19-Feb-21 | 25-Feb-21 |
| A17270 | In-Wall Plumbing Rough-in | 3 | 3 | 19-Feb-21 | 23-Feb-21 |
| A17110 | Hang, Tape & Finish Drywall | 8 | 8 | 24-Feb-21 | 05-Mar-21 |
| A17250 | Above Ceiling Inspections | 2 | 2 | 26-Feb-21 | 01-Mar-21 |
| A17100 | FRP Wall Panels | 4 | 4 | 08-Mar-21 | 11-Mar-21 |
| A17180 | Prime Paint | 1 | 1 | 08-Mar-21 | 08-Mar-21 |
| A17260 | Install ACT Grid | 3 | 3 | 12-Mar-21 | 16-Mar-21 |
| A17220 | Sprinkler Heads | 2 | 2 | 17-Mar-21 | 18-Mar-21 |
| A17230 | Grilles, Registers & Diffusers | 2 | 2 | 18-Mar-21 | 19-Mar-21 |
| A17240 | Install Lighting | 4 | 4 | 19-Mar-21 | 24-Mar-21 |
| A17210 | Fire Alarm Devices | 2 | 2 | 25-Mar-21 | 26-Mar-21 |
| A17320 | Ceiling Inspections | 2 | 2 | 29-Mar-21 | 30-Mar-21 |
| A17190 | Resinous Flooring | 5 | 5 | 31-Mar-21 | 06-Apr-21 |
| A17290 | Install Kitchen Equipment | 10 | 10 | 07-Apr-21 | 20-Apr-21 |
| A17310 | Install ACT Tiles | 2 | 2 | 07-Apr-21 | 08-Apr-21 |
| A17300 | Electrical Trim-out | 3 | 3 | 21-Apr-21 | 23-Apr-21 |
| A17330 | Install Doors & Hardware | 3 | 3 | 26-Apr-21 | 28-Apr-21 |
| A17350 | MEPFP Final Inspections | 2 | 2 | 26-Apr-21 | 27-Apr-21 |
| A17340 | Final Paint | 2 | 2 | 29-Apr-21 | 30-Apr-21 |
| A17360 | Punchlist | 5 | 5 | 03-May-21 | 07-May-21 |
| **First Aid & Restroom - Rooms 22.07 & 22.08** | | **46** | **46** | **22-Dec-20** | **26-Feb-21** |
| A31610 | Layout & Top Track | 1 | 1 | 22-Dec-20 | 22-Dec-20 |
| A31430 | OH Mechanical | 5 | 5 | 23-Dec-20 | 31-Dec-20 |
| A31440 | OH Electrical | 5 | 5 | 28-Dec-20 | 04-Jan-21 |

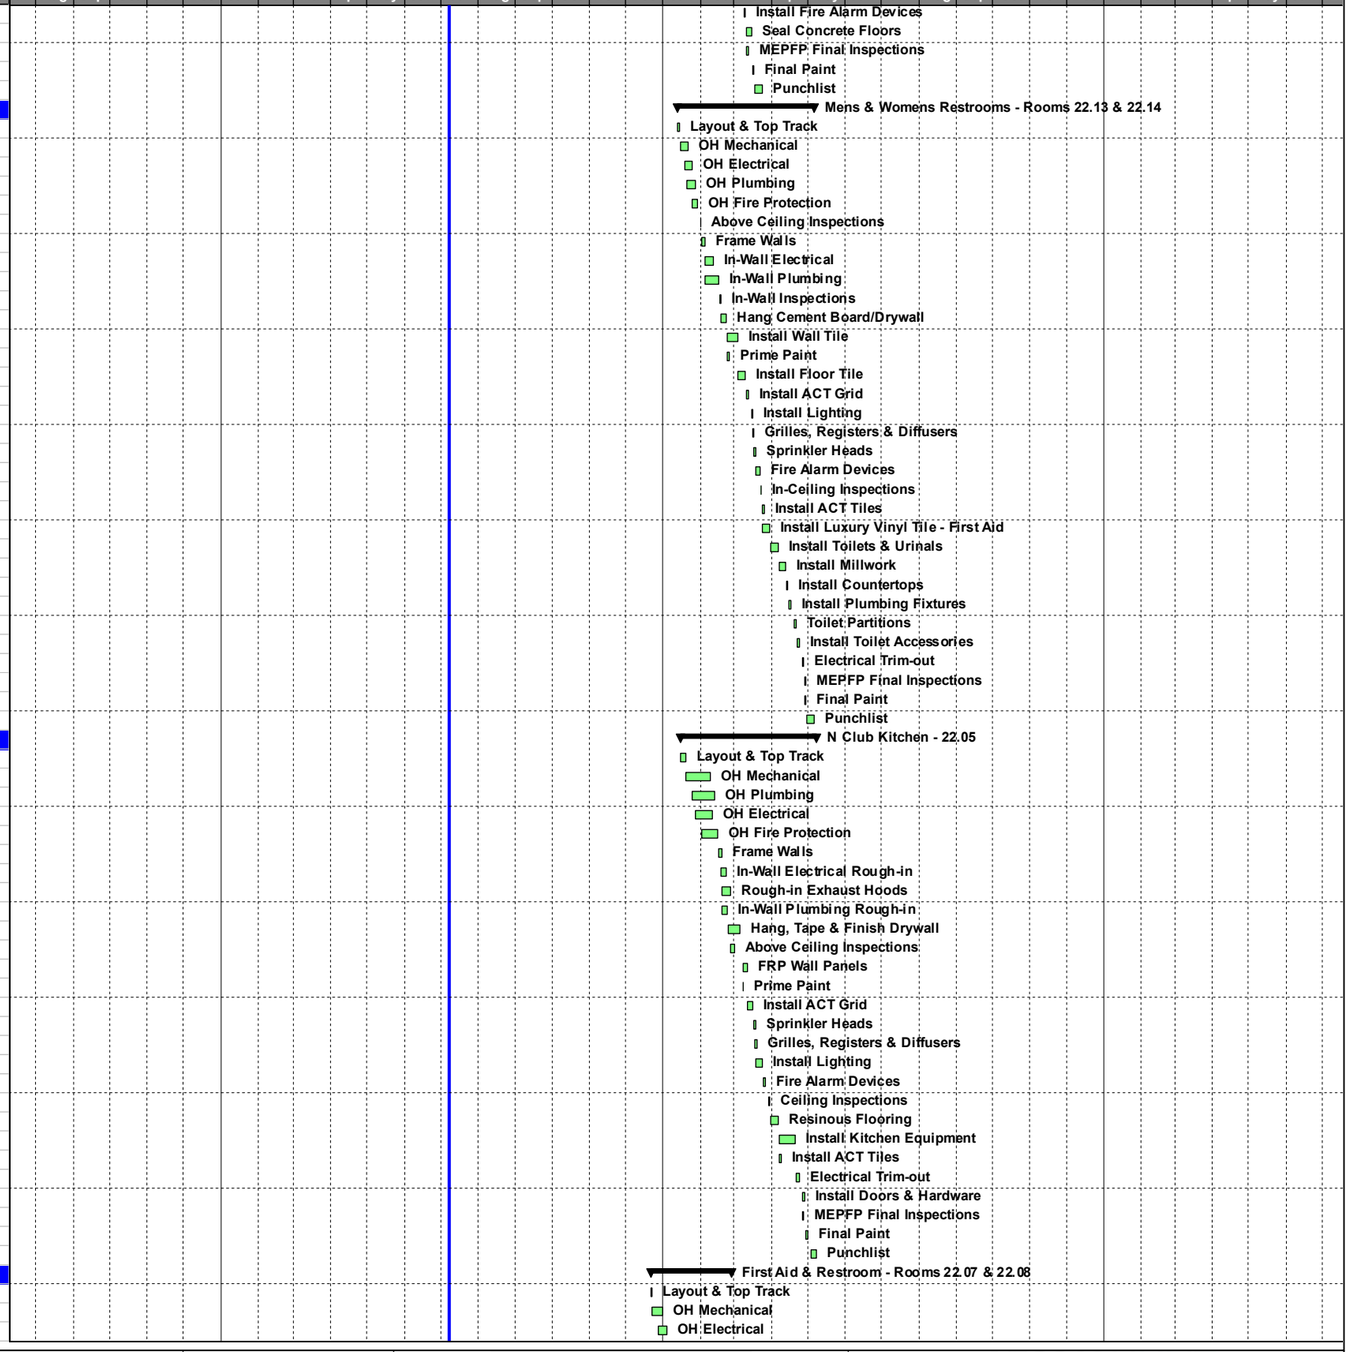

| Activity ID | Activity Name | Original Duration | Remaining Duration | Start | Finish |
|---|---|---|---|---|---|
| A31470 | OH Fire Protection | 5 | 5 | 29-Dec-20 | 05-Jan-21 |
| A31480 | Above Ceiling Inspection | 1 | 1 | 06-Jan-21 | 06-Jan-21 |
| A31620 | Frame Walls | 2 | 2 | 07-Jan-21 | 08-Jan-21 |
| A31630 | In-Wall Plumbing | 2 | 2 | 11-Jan-21 | 12-Jan-21 |
| A31640 | In-Wall Electrical | 2 | 2 | 11-Jan-21 | 12-Jan-21 |
| A31650 | In-Wall Inspections | 1 | 1 | 13-Jan-21 | 13-Jan-21 |
| A31660 | Hang, Tape & Finish Drywall | 5 | 5 | 14-Jan-21 | 20-Jan-21 |
| A31390 | Prime Paint | 2 | 2 | 21-Jan-21 | 22-Jan-21 |
| A31410 | Install Floor Tile | 5 | 5 | 21-Jan-21 | 27-Jan-21 |
| A31420 | Set Plumbing Fixtures | 2 | 2 | 28-Jan-21 | 29-Jan-21 |
| A31510 | Install Wall Tile | 4 | 4 | 28-Jan-21 | 02-Feb-21 |
| A31460 | Install ACT Grid | 1 | 1 | 03-Feb-21 | 03-Feb-21 |
| A31490 | Sprinklers Head | 2 | 2 | 04-Feb-21 | 05-Feb-21 |
| A31450 | Install Lighting | 3 | 3 | 08-Feb-21 | 10-Feb-21 |
| A31500 | Grilles, Registers & Diffusers | 2 | 2 | 08-Feb-21 | 09-Feb-21 |
| A31530 | Ceiling Inspections | 1 | 1 | 11-Feb-21 | 11-Feb-21 |
| A31540 | Install ACT Tiles | 1 | 1 | 12-Feb-21 | 12-Feb-21 |
| A31550 | Install Toilet Accessories | 2 | 2 | 12-Feb-21 | 15-Feb-21 |
| A31590 | Install Luxury Vinyl Tile | 2 | 2 | 12-Feb-21 | 15-Feb-21 |
| A31560 | Electrical Trim-out | 2 | 2 | 15-Feb-21 | 16-Feb-21 |
| A31570 | Fire Alarm Devices | 1 | 1 | 17-Feb-21 | 17-Feb-21 |
| A31580 | Final Paint | 2 | 2 | 18-Feb-21 | 19-Feb-21 |
| A31600 | MEPFP Final Inspections | 2 | 2 | 18-Feb-21 | 19-Feb-21 |
| A89A7230 | Punchlist | 5 | 5 | 22-Feb-21 | 26-Feb-21 |
| **Concession & Prep - Rooms 22.09 & 21.10** | | **58** | **58** | **23-Dec-20** | **17-Mar-21** |
| A31360 | Layout & Top Track | 2 | 2 | 23-Dec-20 | 28-Dec-20 |
| A31070 | OH Mechanical | 4 | 4 | 29-Dec-20 | 04-Jan-21 |
| A31080 | OH Electrical | 4 | 4 | 31-Dec-20 | 06-Jan-21 |
| A31090 | OH Plumbing | 4 | 4 | 05-Jan-21 | 08-Jan-21 |
| A31100 | OH Fire Protection | 4 | 4 | 07-Jan-21 | 12-Jan-21 |
| A31150 | Frame Ceilings | 2 | 2 | 07-Jan-21 | 08-Jan-21 |
| A31160 | Install Lighting (Drywall Ceilings) | 2 | 2 | 11-Jan-21 | 12-Jan-21 |
| A31110 | Install Exhaust Hood | 5 | 5 | 13-Jan-21 | 19-Jan-21 |
| A31170 | Hang, Tape & Finish Drywall | 5 | 5 | 13-Jan-21 | 19-Jan-21 |
| A31120 | Above Ceiling Inspections | 1 | 1 | 20-Jan-21 | 20-Jan-21 |
| A31130 | Prime Paint | 1 | 1 | 20-Jan-21 | 20-Jan-21 |
| A31230 | FRP Wall Panels | 3 | 3 | 21-Jan-21 | 25-Jan-21 |
| A31140 | Install ACT Grid | 1 | 1 | 26-Jan-21 | 26-Jan-21 |
| A31180 | Install Lighting (Grid Ceilings) | 2 | 2 | 27-Jan-21 | 28-Jan-21 |
| A31190 | Sprinkler Heads | 1 | 1 | 29-Jan-21 | 29-Jan-21 |
| A31200 | Grilles, Registers & Diffusers | 1 | 1 | 01-Feb-21 | 01-Feb-21 |
| A31210 | Fire Alarm Devices | 1 | 1 | 02-Feb-21 | 02-Feb-21 |
| A31340 | In-Ceiling Inspections | 1 | 1 | 03-Feb-21 | 03-Feb-21 |
| A31220 | Install ACT Tiles | 1 | 1 | 04-Feb-21 | 04-Feb-21 |
| A31240 | Resilient Flooring | 5 | 5 | 05-Feb-21 | 11-Feb-21 |
| A31280 | Millwork | 5 | 5 | 12-Feb-21 | 18-Feb-21 |
| A31350 | Install Doors & Hardware | 1 | 1 | 12-Feb-21 | 12-Feb-21 |
| A31250 | Install Plumbing Fixtures | 2 | 2 | 19-Feb-21 | 22-Feb-21 |
| A31320 | Tile Concession Wall | 3 | 3 | 19-Feb-21 | 23-Feb-21 |
| A31330 | Install Countertops | 2 | 2 | 24-Feb-21 | 25-Feb-21 |
| A31270 | Food Service Equipment | 5 | 5 | 26-Feb-21 | 04-Mar-21 |
| A31260 | Electrical Trim-out | 2 | 2 | 05-Mar-21 | 08-Mar-21 |
| A31290 | Final Paint | 2 | 2 | 09-Mar-21 | 10-Mar-21 |
| A31300 | MEPFP Final Inspections | 2 | 2 | 09-Mar-21 | 10-Mar-21 |
| A31310 | Punchlist | 5 | 5 | 11-Mar-21 | 17-Mar-21 |
| **East Bar - Room 22.16** | | **52** | **52** | **31-Dec-20** | **15-Mar-21** |
| A20600 | Layout & Top Track | 5 | 5 | 31-Dec-20 | 07-Jan-21 |
| A20310 | OH Mechanical | 4 | 4 | 08-Jan-21 | 13-Jan-21 |
| A20320 | OH Electrical | 4 | 4 | 12-Jan-21 | 15-Jan-21 |
| A20330 | OH Plumbing | 4 | 4 | 14-Jan-21 | 19-Jan-21 |
| A20340 | OH Fire Protection | 4 | 4 | 18-Jan-21 | 21-Jan-21 |
| A20390 | Frame Ceilings | 2 | 2 | 18-Jan-21 | 19-Jan-21 |
| A20360 | Above Ceiling Inspections | 1 | 1 | 22-Jan-21 | 22-Jan-21 |
| A20380 | Install Suspended Wood Ceiling | 1 | 1 | 25-Jan-21 | 25-Jan-21 |
| A20420 | Install Lighting | 2 | 2 | 26-Jan-21 | 27-Jan-21 |
| A20430 | Sprinkler Heads | 1 | 1 | 28-Jan-21 | 28-Jan-21 |
| A20440 | Grilles, Registers & Diffusers | 1 | 1 | 29-Jan-21 | 29-Jan-21 |
| A20450 | Fire Alarm Devices | 1 | 1 | 01-Feb-21 | 01-Feb-21 |
| A20580 | In-Ceiling Inspections | 1 | 1 | 02-Feb-21 | 02-Feb-21 |
| A20480 | Resilient Flooring | 5 | 5 | 03-Feb-21 | 09-Feb-21 |

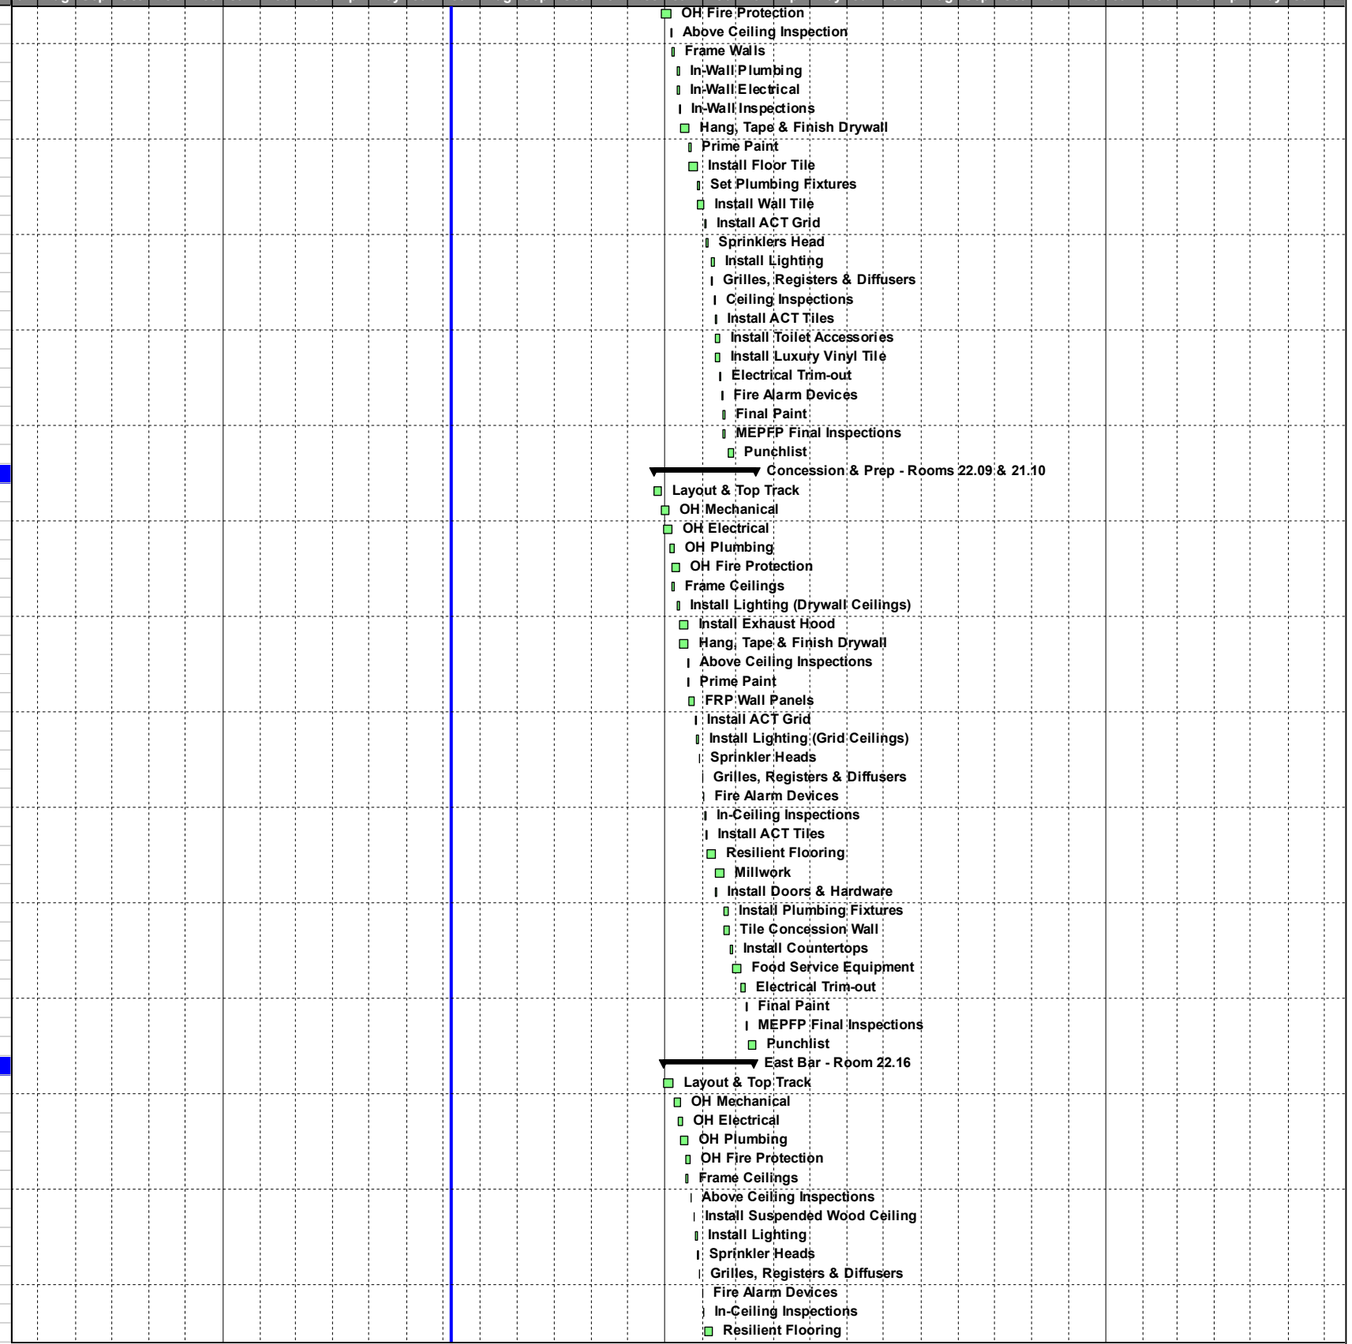

| Activity ID | Activity Name | Original Duration | Remaining Duration | Start | Finish |
|---|---|---|---|---|---|
| A20520 | Millwork | 5 | 5 | 10-Feb-21 | 16-Feb-21 |
| A20590 | Install Doors & Hardware | 1 | 1 | 10-Feb-21 | 10-Feb-21 |
| A20370 | Prime Paint | 1 | 1 | 17-Feb-21 | 17-Feb-21 |
| A20490 | Install Plumbing Fixtures | 2 | 2 | 17-Feb-21 | 18-Feb-21 |
| A20560 | Tile Concession Wall | 3 | 3 | 17-Feb-21 | 19-Feb-21 |
| A20570 | Install Countertops | 2 | 2 | 22-Feb-21 | 23-Feb-21 |
| A20510 | Food Service Equipment | 5 | 5 | 24-Feb-21 | 02-Mar-21 |
| A20500 | Electrical Trim-out | 2 | 2 | 03-Mar-21 | 04-Mar-21 |
| A20530 | Final Paint | 2 | 2 | 05-Mar-21 | 08-Mar-21 |
| A20540 | MEPFP Final Inspections | 2 | 2 | 05-Mar-21 | 08-Mar-21 |
| A20550 | Punchlist | 5 | 5 | 09-Mar-21 | 15-Mar-21 |
| Corridors | | 40 | 40 | 09-Mar-21 | 03-May-21 |
| A16740 | Prime Paint | 5 | 5 | 09-Mar-21 | 15-Mar-21 |
| A16710 | Sprinkler Heads | 5 | 5 | 16-Mar-21 | 22-Mar-21 |
| A16720 | Lighting | 5 | 5 | 19-Mar-21 | 25-Mar-21 |
| A16730 | Fire Alarm Devices | 5 | 5 | 24-Mar-21 | 30-Mar-21 |
| A16780 | Install Doors & Hardware | 5 | 5 | 31-Mar-21 | 06-Apr-21 |
| A16750 | Seal Concrete Floors | 5 | 5 | 07-Apr-21 | 13-Apr-21 |
| A16760 | Electrical Trim-out | 5 | 5 | 14-Apr-21 | 20-Apr-21 |
| A16770 | Final MEPFP Inspections | 3 | 3 | 21-Apr-21 | 23-Apr-21 |
| A16790 | Final Paint | 4 | 4 | 21-Apr-21 | 26-Apr-21 |
| A16800 | Punchlist | 5 | 5 | 27-Apr-21 | 03-May-21 |
| Quad 3 | | 118 | 118 | 19-Nov-20 | 10-May-21 |
| MEPFP Mains Rough-in | | 43 | 43 | 19-Nov-20 | 25-Jan-21 |
| OHRI-EL-Q3-1 | Spray Fireproofing - First Pass - CL-N/S-S8/E8-E/W | 10 | 10 | 19-Nov-20 | 04-Dec-20 |
| OHRI-EL-Q3-1 | Install Subroof - CL-N/S-S8/E8-E/W | 15 | 15 | 07-Dec-20 | 29-Dec-20 |
| OHRI-EL-Q3-1 | Intumescent Coatings - CL-N/S-S8/E8-E/W | 10 | 10 | 07-Dec-20 | 18-Dec-20 |
| OHRI-EL-Q3-1 | Mechanical Mains - CL-N/S-S8/E8-E/W | 10 | 10 | 21-Dec-20 | 06-Jan-21 |
| OHRI-EL-Q3-1 | Electrical Mains - CL-N/S-S8/E8-E/W | 10 | 10 | 23-Dec-20 | 08-Jan-21 |
| OHRI-EL-Q3-1 | Plumbing Mains - CL-N/S-S8/E8-E/W | 10 | 10 | 29-Dec-20 | 12-Jan-21 |
| OHRI-EL-Q3-1 | Fire Protection Mains - CL-N/S-S8/E8-E/W | 10 | 10 | 31-Dec-20 | 14-Jan-21 |
| OHRI-EL-Q3-1 | Cable Tray AV/IT Mains - CL-N/S-S8/E8-E/W | 10 | 10 | 05-Jan-21 | 18-Jan-21 |
| OHRI-EL-Q3-1 | Spray Fireproofing - Final Pass - CL-N/S-S8/E8-E/W | 10 | 10 | 12-Jan-21 | 25-Jan-21 |
| Electrical & IT - Rooms 23.11 & 23.12 | | 52 | 52 | 15-Jan-21 | 29-Mar-21 |
| A20610 | Layout & Top Track | 1 | 1 | 15-Jan-21 | 15-Jan-21 |
| A20620 | Frame Walls | 2 | 2 | 18-Jan-21 | 19-Jan-21 |
| A20630 | Rough-in Electrical | 3 | 3 | 20-Jan-21 | 22-Jan-21 |
| A20640 | In-Wall Inspection | 1 | 1 | 25-Jan-21 | 25-Jan-21 |
| A20650 | In-Wall Insulation | 1 | 1 | 26-Jan-21 | 26-Jan-21 |
| A20660 | Hang, Tape & Finish Drywall | 4 | 4 | 27-Jan-21 | 01-Feb-21 |
| A20670 | OH Mechanical | 5 | 5 | 02-Feb-21 | 08-Feb-21 |
| A20700 | FRP Equipment Pads | 3 | 3 | 02-Feb-21 | 04-Feb-21 |
| A20680 | OH Electrical | 5 | 5 | 03-Feb-21 | 09-Feb-21 |
| A20690 | OH Fire Protection | 3 | 3 | 04-Feb-21 | 08-Feb-21 |
| A20800 | Prime Paint | 2 | 2 | 05-Feb-21 | 08-Feb-21 |
| A20710 | Set Transformers | 2 | 2 | 09-Feb-21 | 10-Feb-21 |
| A20720 | Set IT Racks | 2 | 2 | 09-Feb-21 | 10-Feb-21 |
| A20730 | Set Panel Boxes | 2 | 2 | 09-Feb-21 | 10-Feb-21 |
| A20850 | Set AC Units | 2 | 2 | 09-Feb-21 | 10-Feb-21 |
| A20740 | Install Panel Interiors | 3 | 3 | 11-Feb-21 | 15-Feb-21 |
| A20760 | Pull Cable & Terminate | 15 | 15 | 11-Feb-21 | 03-Mar-21 |
| A20770 | Hook-up Transformers | 5 | 5 | 11-Feb-21 | 17-Feb-21 |
| A20820 | Install Doors & Hardware | 2 | 2 | 11-Feb-21 | 12-Feb-21 |
| A20860 | OH Mechanical Finishes | 2 | 2 | 11-Feb-21 | 12-Feb-21 |
| A20750 | Pull Wire & Terminate | 15 | 15 | 16-Feb-21 | 08-Mar-21 |
| A20780 | Install Lighting | 3 | 3 | 09-Mar-21 | 11-Mar-21 |
| A20790 | Install Electrical Finishes | 2 | 2 | 12-Mar-21 | 15-Mar-21 |
| A20870 | Install Fire Alarm Devices | 2 | 2 | 12-Mar-21 | 15-Mar-21 |
| A20810 | Seal Concrete Floors | 3 | 3 | 16-Mar-21 | 18-Mar-21 |
| A20880 | MEPFP Final Inspections | 2 | 2 | 16-Mar-21 | 17-Mar-21 |
| A20830 | Final Paint | 2 | 2 | 19-Mar-21 | 22-Mar-21 |
| A20840 | Punchlist | 5 | 5 | 23-Mar-21 | 29-Mar-21 |
| Mens & Womens Restrooms - Rooms 21.02 & 23.09 | | 82 | 82 | 15-Jan-21 | 10-May-21 |
| A18320 | Layout & Top Track | 2 | 2 | 15-Jan-21 | 18-Jan-21 |
| A18330 | OH Mechanical | 5 | 5 | 19-Jan-21 | 25-Jan-21 |
| A18340 | OH Electrical | 5 | 5 | 21-Jan-21 | 27-Jan-21 |
| A18350 | OH Plumbing | 5 | 5 | 25-Jan-21 | 29-Jan-21 |
| A18360 | OH Fire Protection | 5 | 5 | 27-Jan-21 | 02-Feb-21 |
| A18370 | Above Ceiling Inspections | 1 | 1 | 03-Feb-21 | 03-Feb-21 |
| A18380 | Frame Walls | 3 | 3 | 04-Feb-21 | 08-Feb-21 |

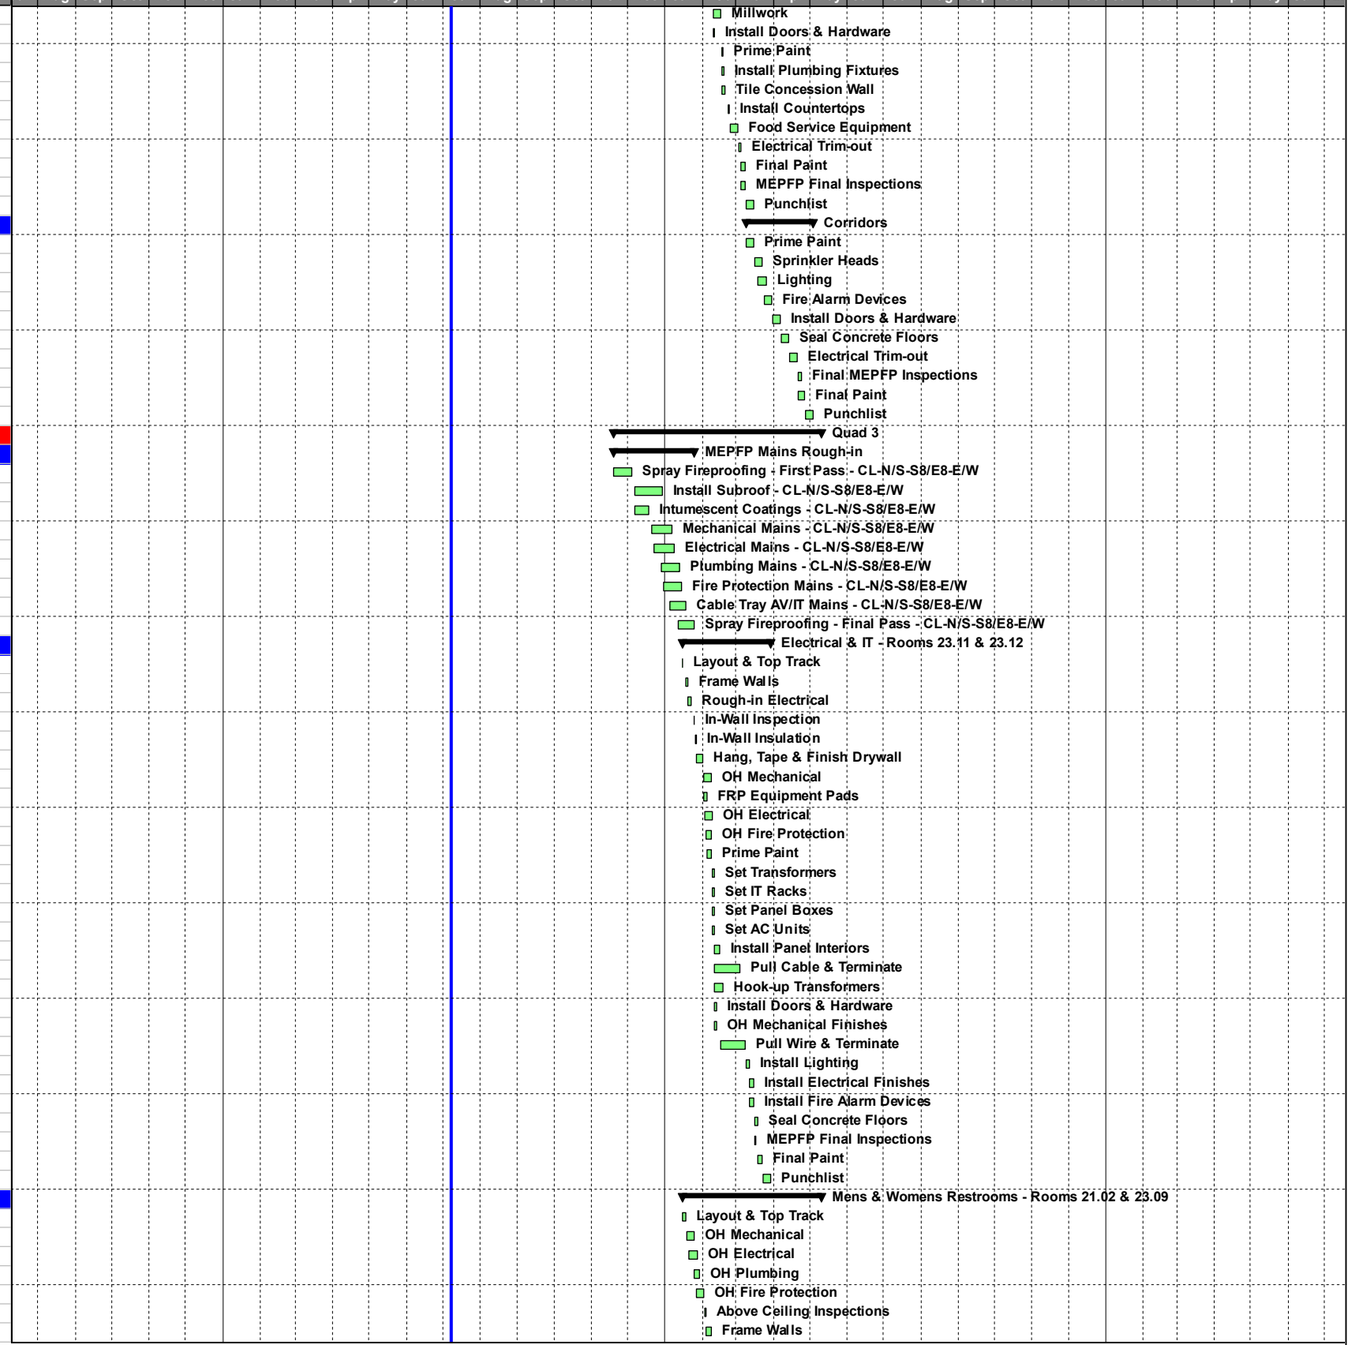

| Activity ID | Activity Name | Original Duration | Remaining Duration | Start | Finish |
|---|---|---|---|---|---|
| A18390 | In-Wall Electrical | 5 | 5 | 09-Feb-21 | 15-Feb-21 |
| A18400 | In-Wall Plumbing | 8 | 8 | 09-Feb-21 | 18-Feb-21 |
| A18410 | In-Wall Inspections | 1 | 1 | 19-Feb-21 | 19-Feb-21 |
| A18420 | Hang Cement Board/Drywall | 3 | 3 | 22-Feb-21 | 24-Feb-21 |
| A18430 | Install Wall Tile | 7 | 7 | 25-Feb-21 | 05-Mar-21 |
| A18630 | Prime Paint | 2 | 2 | 25-Feb-21 | 26-Feb-21 |
| A18500 | Install Floor Tile | 5 | 5 | 08-Mar-21 | 12-Mar-21 |
| A18440 | Install ACT Grid | 2 | 2 | 15-Mar-21 | 16-Mar-21 |
| A18450 | Install Lighting | 2 | 2 | 17-Mar-21 | 18-Mar-21 |
| A18460 | Grilles, Registers & Diffusers | 2 | 2 | 18-Mar-21 | 19-Mar-21 |
| A18470 | Sprinkler Heads | 2 | 2 | 19-Mar-21 | 22-Mar-21 |
| A18480 | Fire Alarm Devices | 2 | 2 | 23-Mar-21 | 24-Mar-21 |
| A18490 | In-Ceiling Inspections | 1 | 1 | 25-Mar-21 | 25-Mar-21 |
| A18510 | Install ACT Tiles | 2 | 2 | 26-Mar-21 | 29-Mar-21 |
| A18610 | Install Luxury Vinyl Tile - First Aid | 5 | 5 | 26-Mar-21 | 01-Apr-21 |
| A18520 | Install Toilets & Urinals | 5 | 5 | 02-Apr-21 | 08-Apr-21 |
| A18530 | Install Millwork | 4 | 4 | 09-Apr-21 | 14-Apr-21 |
| A18540 | Install Countertops | 2 | 2 | 15-Apr-21 | 16-Apr-21 |
| A18550 | Install Plumbing Fixtures | 2 | 2 | 19-Apr-21 | 20-Apr-21 |
| A18560 | Toilet Partitions | 3 | 3 | 21-Apr-21 | 23-Apr-21 |
| A18570 | Install Toilet Accessories | 2 | 2 | 26-Apr-21 | 27-Apr-21 |
| A18580 | Electrical Trim-out | 2 | 2 | 28-Apr-21 | 29-Apr-21 |
| A18590 | MEPFP Final Inspections | 2 | 2 | 30-Apr-21 | 03-May-21 |
| A18620 | Final Paint | 2 | 2 | 30-Apr-21 | 03-May-21 |
| A18600 | Punchlist | 5 | 5 | 04-May-21 | 10-May-21 |
| South Bar & Pantry x2 - Rooms 24.01, 23.15 & 24.02 | | 62 | 62 | 15-Jan-21 | 12-Apr-21 |
| A24340 | Layout & Top Track | 5 | 5 | 15-Jan-21 | 21-Jan-21 |
| A24350 | OH Mechanical | 4 | 4 | 22-Jan-21 | 27-Jan-21 |
| A24360 | OH Electrical | 4 | 4 | 26-Jan-21 | 29-Jan-21 |
| A24370 | OH Plumbing | 4 | 4 | 28-Jan-21 | 02-Feb-21 |
| A24380 | OH Fire Protection | 4 | 4 | 01-Feb-21 | 04-Feb-21 |
| A24390 | Frame Ceilings | 2 | 2 | 01-Feb-21 | 02-Feb-21 |
| A24400 | Above Ceiling Inspections | 1 | 1 | 05-Feb-21 | 05-Feb-21 |
| A24410 | Install Suspended Wood Ceiling | 1 | 1 | 08-Feb-21 | 08-Feb-21 |
| A29460 | Frame Walls | 3 | 3 | 08-Feb-21 | 10-Feb-21 |
| A24420 | Install Lighting | 2 | 2 | 09-Feb-21 | 10-Feb-21 |
| A24430 | Sprinkler Heads | 1 | 1 | 11-Feb-21 | 11-Feb-21 |
| A29830 | In-Wall Electrical | 2 | 2 | 11-Feb-21 | 12-Feb-21 |
| A24440 | Grilles, Registers & Diffusers | 1 | 1 | 12-Feb-21 | 12-Feb-21 |
| A24450 | Fire Alarm Devices | 1 | 1 | 15-Feb-21 | 15-Feb-21 |
| A29880 | In-Wall Plumbing | 2 | 2 | 15-Feb-21 | 16-Feb-21 |
| A24460 | In-Ceiling Inspections | 1 | 1 | 16-Feb-21 | 16-Feb-21 |
| A29890 | In-Wall Inspections | 2 | 2 | 17-Feb-21 | 18-Feb-21 |
| A29920 | Hang, Tape & Finish Drywall | 5 | 5 | 19-Feb-21 | 25-Feb-21 |
| A29940 | Install FRP Panels | 3 | 3 | 26-Feb-21 | 02-Mar-21 |
| A24470 | Resilient Flooring | 5 | 5 | 03-Mar-21 | 09-Mar-21 |
| A24480 | Millwork | 5 | 5 | 10-Mar-21 | 16-Mar-21 |
| A24490 | Install Doors & Hardware | 1 | 1 | 10-Mar-21 | 10-Mar-21 |
| A24500 | Prime Paint | 1 | 1 | 17-Mar-21 | 17-Mar-21 |
| A24510 | Install Plumbing Fixtures | 2 | 2 | 17-Mar-21 | 18-Mar-21 |
| A24520 | Tile Concession Wall | 3 | 3 | 17-Mar-21 | 19-Mar-21 |
| A24530 | Install Countertops | 2 | 2 | 22-Mar-21 | 23-Mar-21 |
| A24540 | Food Service Equipment | 5 | 5 | 24-Mar-21 | 30-Mar-21 |
| A24550 | Electrical Trim-out | 2 | 2 | 31-Mar-21 | 01-Apr-21 |
| A24560 | Final Paint | 2 | 2 | 02-Apr-21 | 05-Apr-21 |
| A24570 | MEPFP Final Inspections | 2 | 2 | 02-Apr-21 | 05-Apr-21 |
| A24580 | Punchlist | 5 | 5 | 06-Apr-21 | 12-Apr-21 |
| Concession & Prep - Rooms 23.03 & 23.04 | | 67 | 67 | 15-Jan-21 | 19-Apr-21 |
| A19220 | Layout & Top Track | 2 | 2 | 15-Jan-21 | 18-Jan-21 |
| A18930 | OH Mechanical | 4 | 4 | 19-Jan-21 | 22-Jan-21 |
| A18940 | OH Electrical | 4 | 4 | 21-Jan-21 | 26-Jan-21 |
| A18950 | OH Plumbing | 4 | 4 | 25-Jan-21 | 28-Jan-21 |
| A18960 | OH Fire Protection | 4 | 4 | 27-Jan-21 | 01-Feb-21 |
| A19010 | Frame Ceilings | 2 | 2 | 27-Jan-21 | 28-Jan-21 |
| A19020 | Install Lighting (Drywall Ceilings) | 2 | 2 | 29-Jan-21 | 01-Feb-21 |
| A18970 | Install Exhaust Hood | 5 | 5 | 02-Feb-21 | 08-Feb-21 |
| A18980 | Above Ceiling Inspections | 1 | 1 | 09-Feb-21 | 09-Feb-21 |
| A19030 | Hang, Tape & Finish Drywall | 5 | 5 | 15-Feb-21 | 19-Feb-21 |
| A18990 | Prime Paint | 1 | 1 | 22-Feb-21 | 22-Feb-21 |
| A19090 | FRP Wall Panels | 3 | 3 | 23-Feb-21 | 25-Feb-21 |

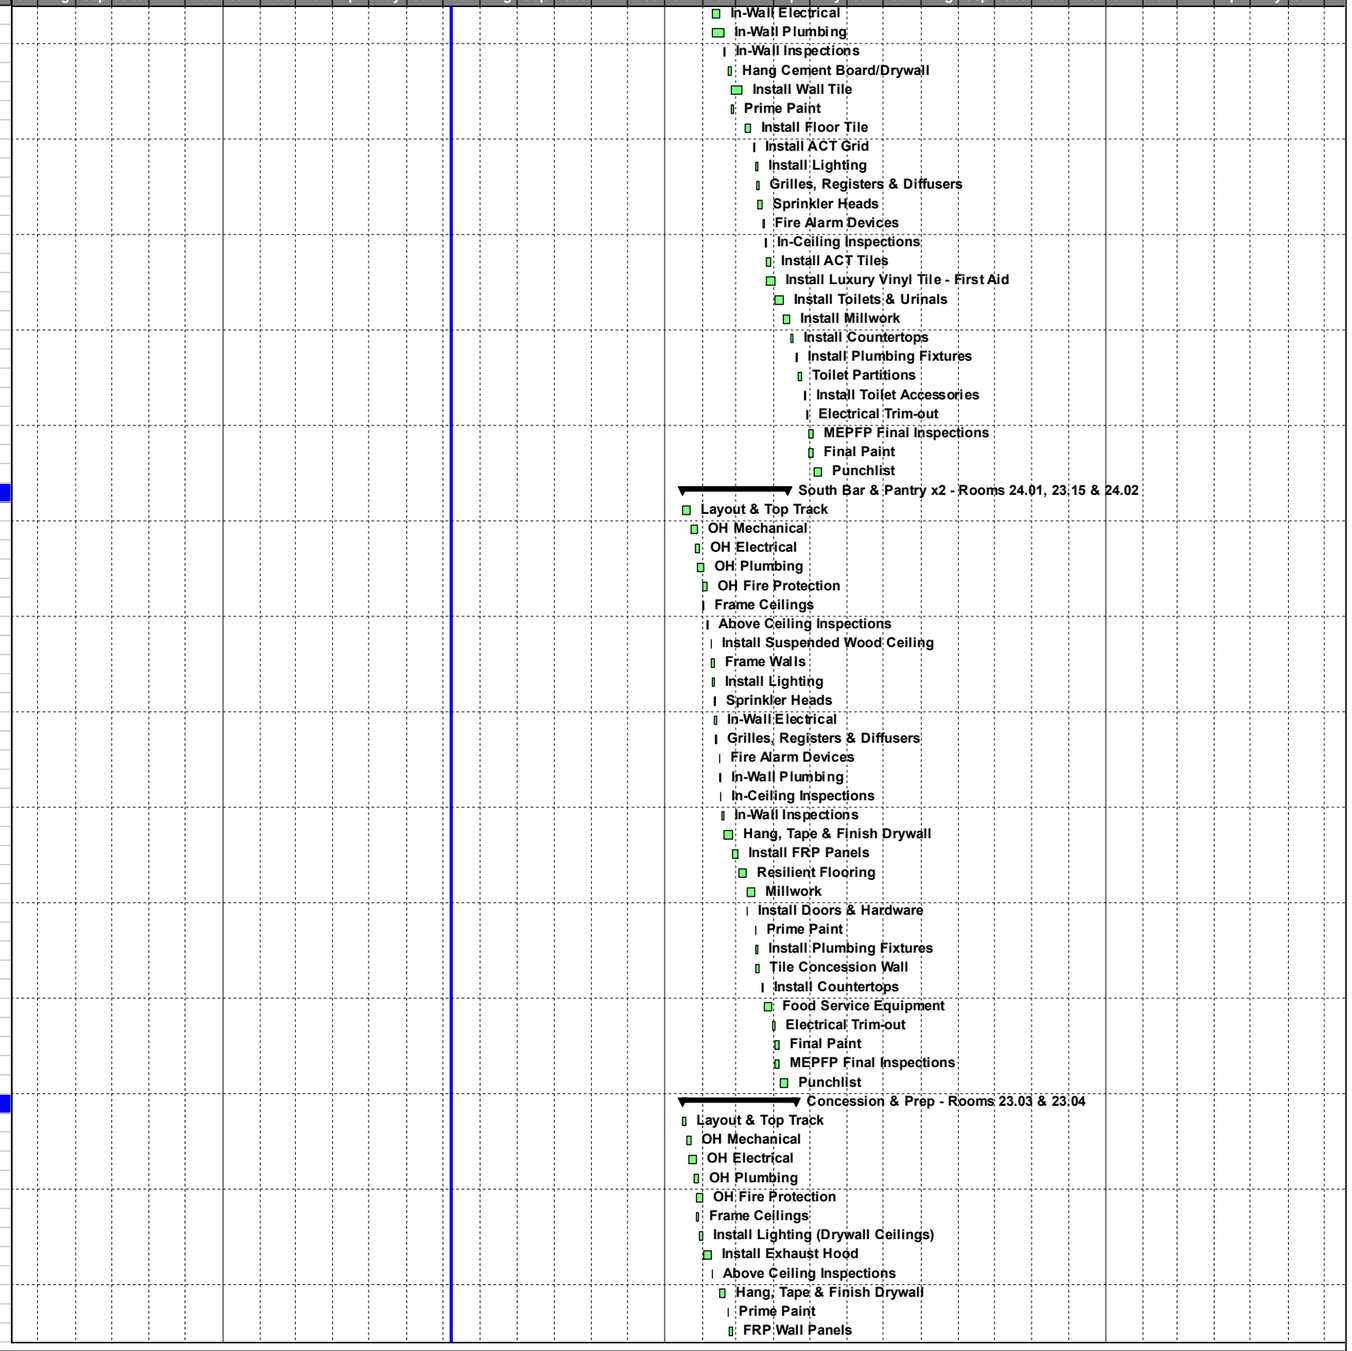

| Activity ID | Activity Name | Original Duration | Remaining Duration | Start | Finish |
|---|---|---|---|---|---|
| A19000 | Install ACT Grid | 1 | 1 | 26-Feb-21 | 26-Feb-21 |
| A19040 | Install Lighting (Grid Ceilings) | 2 | 2 | 01-Mar-21 | 02-Mar-21 |
| A19050 | Sprinkler Heads | 1 | 1 | 03-Mar-21 | 03-Mar-21 |
| A19060 | Grilles, Registers & Diffusers | 1 | 1 | 04-Mar-21 | 04-Mar-21 |
| A19070 | Fire Alarm Devices | 1 | 1 | 05-Mar-21 | 05-Mar-21 |
| A19200 | In-Ceiling Inspections | 1 | 1 | 08-Mar-21 | 08-Mar-21 |
| A19080 | Install ACT Tiles | 1 | 1 | 09-Mar-21 | 09-Mar-21 |
| A19100 | Resilient Flooring | 5 | 5 | 10-Mar-21 | 16-Mar-21 |
| A19140 | Millwork | 5 | 5 | 17-Mar-21 | 23-Mar-21 |
| A19210 | Install Doors & Hardware | 1 | 1 | 17-Mar-21 | 17-Mar-21 |
| A19110 | Install Plumbing Fixtures | 2 | 2 | 24-Mar-21 | 25-Mar-21 |
| A19180 | Tile Concession Wall | 3 | 3 | 24-Mar-21 | 26-Mar-21 |
| A19190 | Install Countertops | 2 | 2 | 29-Mar-21 | 30-Mar-21 |
| A19130 | Food Service Equipment | 5 | 5 | 31-Mar-21 | 06-Apr-21 |
| A19120 | Electrical Trim-out | 2 | 2 | 07-Apr-21 | 08-Apr-21 |
| A19150 | Final Paint | 2 | 2 | 09-Apr-21 | 12-Apr-21 |
| A19160 | MEPFP Final Inspections | 2 | 2 | 09-Apr-21 | 12-Apr-21 |
| A19170 | Punchlist | 5 | 5 | 13-Apr-21 | 19-Apr-21 |
| **Womens, Nursing, Janitor & Family - Rooms 23.06-08 & 23.14** | | **82** | **82** | **15-Jan-21** | **10-May-21** |
| A19230 | Layout & Top Track | 2 | 2 | 15-Jan-21 | 18-Jan-21 |
| A19240 | OH Mechanical | 5 | 5 | 19-Jan-21 | 25-Jan-21 |
| A19250 | OH Electrical | 5 | 5 | 21-Jan-21 | 27-Jan-21 |
| A19260 | OH Plumbing | 5 | 5 | 25-Jan-21 | 29-Jan-21 |
| A19270 | OH Fire Protection | 5 | 5 | 27-Jan-21 | 02-Feb-21 |
| A19280 | Above Ceiling Inspections | 1 | 1 | 03-Feb-21 | 03-Feb-21 |
| A19290 | Frame Walls | 3 | 3 | 04-Feb-21 | 08-Feb-21 |
| A19300 | In-Wall Electrical | 5 | 5 | 09-Feb-21 | 15-Feb-21 |
| A19310 | In-Wall Plumbing | 8 | 8 | 09-Feb-21 | 18-Feb-21 |
| A19320 | In-Wall Inspections | 1 | 1 | 19-Feb-21 | 19-Feb-21 |
| A19330 | Hang Cement Board/Drywall | 3 | 3 | 22-Feb-21 | 24-Feb-21 |
| A19340 | Install Wall Tile | 7 | 7 | 25-Feb-21 | 05-Mar-21 |
| A19540 | Prime Paint | 2 | 2 | 25-Feb-21 | 26-Feb-21 |
| A19410 | Install Floor Tile | 5 | 5 | 08-Mar-21 | 12-Mar-21 |
| A19350 | Install ACT Grid | 2 | 2 | 15-Mar-21 | 16-Mar-21 |
| A19360 | Install Lighting | 2 | 2 | 17-Mar-21 | 18-Mar-21 |
| A19370 | Grilles, Registers & Diffusers | 2 | 2 | 18-Mar-21 | 19-Mar-21 |
| A19380 | Sprinkler Heads | 2 | 2 | 19-Mar-21 | 22-Mar-21 |
| A19390 | Fire Alarm Devices | 2 | 2 | 23-Mar-21 | 24-Mar-21 |
| A19400 | In-Ceiling Inspections | 1 | 1 | 25-Mar-21 | 25-Mar-21 |
| A19420 | Install ACT Tiles | 2 | 2 | 26-Mar-21 | 29-Mar-21 |
| A19520 | Install Luxury Vinyl Tile - First Aid | 5 | 5 | 26-Mar-21 | 01-Apr-21 |
| A19430 | Install Toilets & Urinals | 5 | 5 | 02-Apr-21 | 08-Apr-21 |
| A19440 | Install Millwork | 4 | 4 | 09-Apr-21 | 14-Apr-21 |
| A19450 | Install Countertops | 2 | 2 | 15-Apr-21 | 16-Apr-21 |
| A19460 | Install Plumbing Fixtures | 2 | 2 | 19-Apr-21 | 20-Apr-21 |
| A19470 | Toilet Partitions | 3 | 3 | 21-Apr-21 | 23-Apr-21 |
| A19480 | Install Toilet Accessories | 2 | 2 | 26-Apr-21 | 27-Apr-21 |
| A19490 | Electrical Trim-out | 2 | 2 | 28-Apr-21 | 29-Apr-21 |
| A19500 | MEPFP Final Inspections | 2 | 2 | 30-Apr-21 | 03-May-21 |
| A19530 | Final Paint | 2 | 2 | 30-Apr-21 | 03-May-21 |
| A19510 | Punchlist | 5 | 5 | 04-May-21 | 10-May-21 |
| **Corridors** | | **48** | **48** | **01-Mar-21** | **05-May-21** |
| A22530 | Prime Paint | 5 | 5 | 01-Mar-21 | 05-Mar-21 |
| A22500 | Sprinkler Heads | 5 | 5 | 08-Mar-21 | 12-Mar-21 |
| A22510 | Lighting | 5 | 5 | 11-Mar-21 | 17-Mar-21 |
| A22520 | Fire Alarm Devices | 5 | 5 | 16-Mar-21 | 22-Mar-21 |
| A22570 | Install Doors & Hardware | 5 | 5 | 23-Mar-21 | 29-Mar-21 |
| A22540 | Seal Concrete Floors | 5 | 5 | 30-Mar-21 | 05-Apr-21 |
| A23470 | Install Millwork @ Customer Service | 8 | 8 | 06-Apr-21 | 15-Apr-21 |
| A22550 | Electrical Trim-out | 5 | 5 | 16-Apr-21 | 22-Apr-21 |
| A22560 | Final MEPFP Inspections | 3 | 3 | 23-Apr-21 | 27-Apr-21 |
| A22580 | Final Paint | 4 | 4 | 23-Apr-21 | 28-Apr-21 |
| A22590 | Punchlist | 5 | 5 | 29-Apr-21 | 05-May-21 |
| **Quad 4** | | **118** | **118** | **07-Dec-20** | **24-May-21** |
| **MEPFP Mains Rough-in** | | **43** | **43** | **07-Dec-20** | **08-Feb-21** |
| OHRI-EL-Q4-1 | Spray Fireproofing - First Pass - CL-E/W-W10/S8-N/S | 10 | 10 | 07-Dec-20 | 18-Dec-20 |
| OHRI-EL-Q4-1 | Install Subroof - CL-E/W-W10/S8-N/S | 15 | 15 | 21-Dec-20 | 13-Jan-21 |
| OHRI-EL-Q4-1 | Intumescent Coatings - CL-E/W-W10/S8-N/S | 10 | 10 | 21-Dec-20 | 06-Jan-21 |
| OHRI-EL-Q4-1 | Mechanical Mains - CL-E/W-W10/S8-N/S | 10 | 10 | 07-Jan-21 | 20-Jan-21 |
| OHRI-EL-Q4-1 | Electrical Mains - CL-E/W-W10/S8-N/S | 10 | 10 | 11-Jan-21 | 22-Jan-21 |

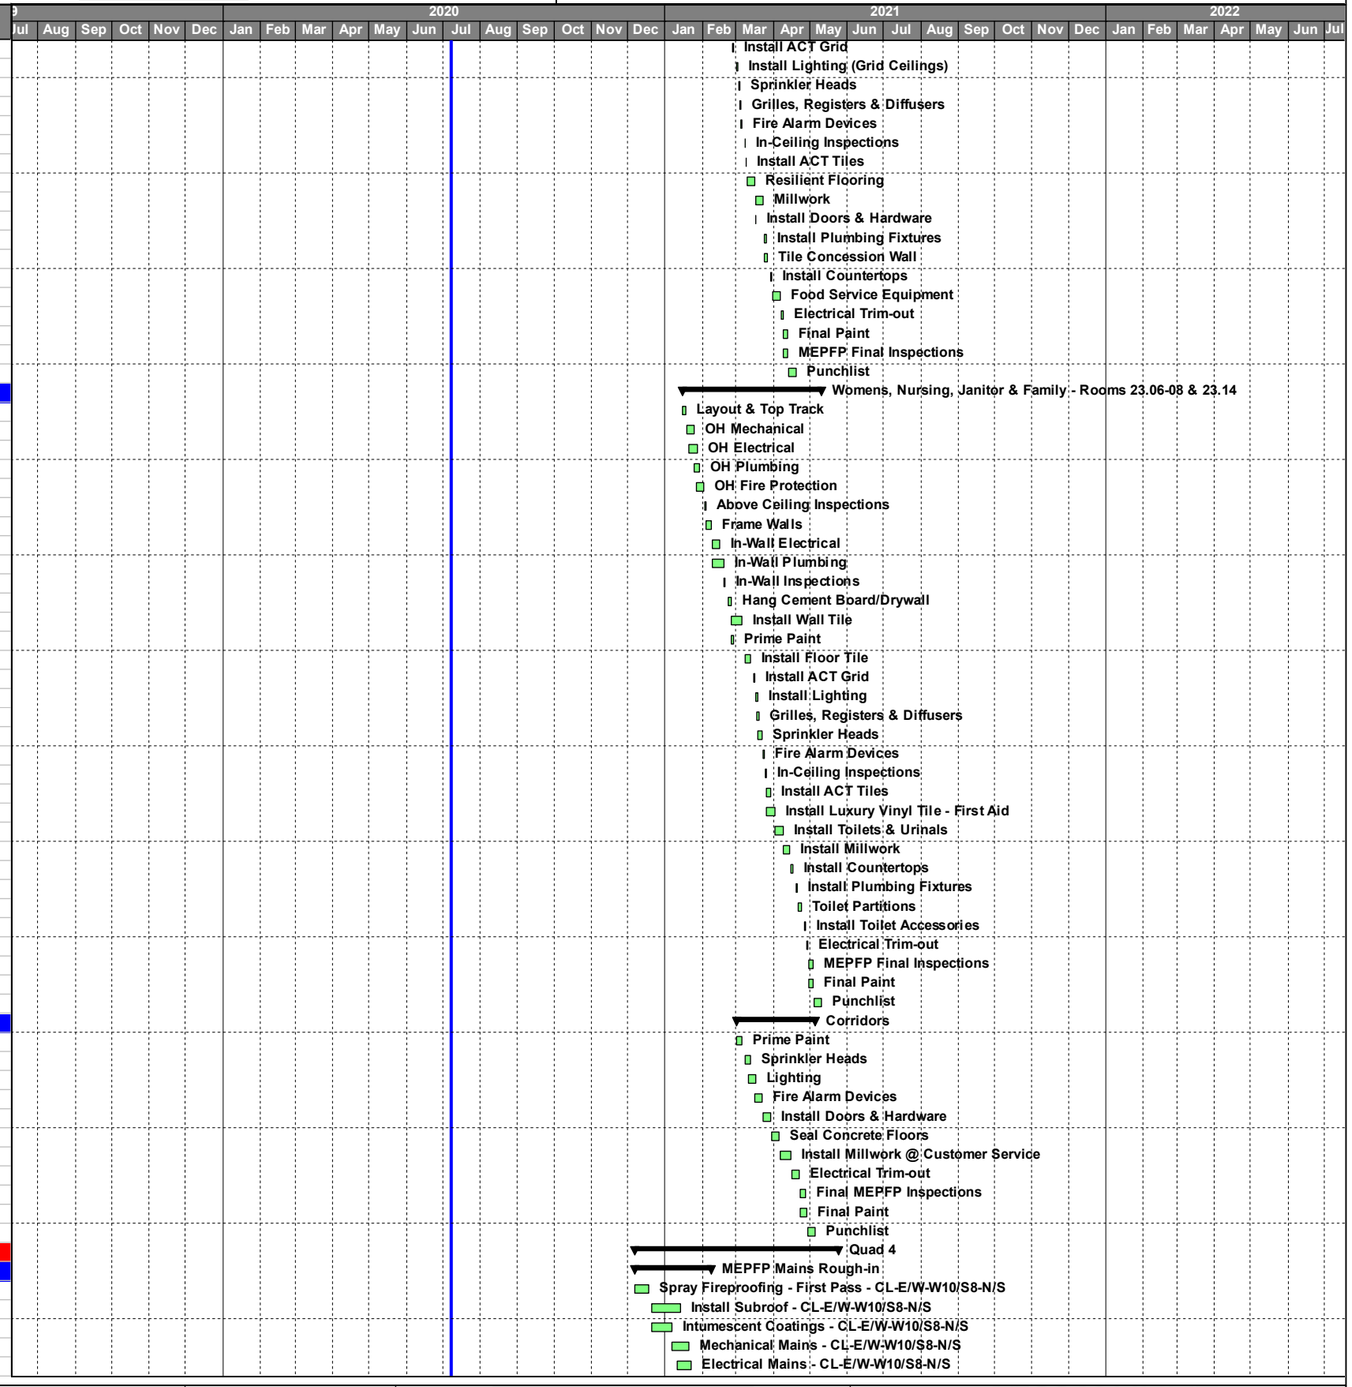


Remaining Level of Effort | Remainin...
Actual Level of Effort | Critical R...
Actual Work | Milestone

**Savannah Arena**
**Current Data Date: 08-Jul-20**



AECOM HUNT
in association with
Brownstone Construction Group
Pat Mathis Construction Company
A. Riley Consultants

| Activity ID | Activity Name | Original Duration | Remaining Duration | Start | Finish |
|---|---|---|---|---|---|
| OHRI-EL-Q4-1 | Plumbing Mains - CL-E/W-W10/S8-N/S | 10 | 10 | 13-Jan-21 | 26-Jan-21 |
| OHRI-EL-Q4-1 | Fire Protection Mains - CL-E/W-W10/S8-N/S | 10 | 10 | 15-Jan-21 | 28-Jan-21 |
| OHRI-EL-Q4-1 | Cable Tray AV/IT Mains - CL-E/W-W10/S8-N/S | 10 | 10 | 19-Jan-21 | 01-Feb-21 |
| OHRI-EL-Q4-1 | Spray Fireproofing - Final Pass - CL-E/W-W10/S8-N/S | 10 | 10 | 26-Jan-21 | 08-Feb-21 |
| Electrical - Room 24.06 | | 52 | 52 | 29-Jan-21 | 12-Apr-21 |
| A22120 | Layout & Top Track | 1 | 1 | 29-Jan-21 | 29-Jan-21 |
| A22130 | Frame Walls | 2 | 2 | 01-Feb-21 | 02-Feb-21 |
| A22140 | Rough-in Electrical | 3 | 3 | 03-Feb-21 | 05-Feb-21 |
| A22150 | In-Wall Inspection | 1 | 1 | 08-Feb-21 | 08-Feb-21 |
| A22160 | In-Wall Insulation | 1 | 1 | 09-Feb-21 | 09-Feb-21 |
| A22170 | Hang, Tape & Finish Drywall | 4 | 4 | 10-Feb-21 | 15-Feb-21 |
| A22180 | OH Mechanical | 5 | 5 | 16-Feb-21 | 22-Feb-21 |
| A22210 | FRP Equipment Pads | 3 | 3 | 16-Feb-21 | 18-Feb-21 |
| A22190 | OH Electrical | 5 | 5 | 17-Feb-21 | 23-Feb-21 |
| A22200 | OH Fire Protection | 3 | 3 | 18-Feb-21 | 22-Feb-21 |
| A22310 | Prime Paint | 2 | 2 | 19-Feb-21 | 22-Feb-21 |
| A22220 | Set Transformers | 2 | 2 | 23-Feb-21 | 24-Feb-21 |
| A22230 | Set IT Racks | 2 | 2 | 23-Feb-21 | 24-Feb-21 |
| A22240 | Set Panel Boxes | 2 | 2 | 23-Feb-21 | 24-Feb-21 |
| A22360 | Set AC Units | 2 | 2 | 23-Feb-21 | 24-Feb-21 |
| A22250 | Install Panel Interiors | 3 | 3 | 25-Feb-21 | 01-Mar-21 |
| A22270 | Pull Cable & Terminate | 15 | 15 | 25-Feb-21 | 17-Mar-21 |
| A22280 | Hook-up Transformers | 5 | 5 | 25-Feb-21 | 03-Mar-21 |
| A22330 | Install Doors & Hardware | 2 | 2 | 25-Feb-21 | 26-Feb-21 |
| A22370 | OH Mechanical Finishes | 2 | 2 | 25-Feb-21 | 26-Feb-21 |
| A22260 | Pull Wire & Terminate | 15 | 15 | 02-Mar-21 | 22-Mar-21 |
| A22290 | Install Lighting | 3 | 3 | 23-Mar-21 | 25-Mar-21 |
| A22300 | Install Electrical Finishes | 2 | 2 | 26-Mar-21 | 29-Mar-21 |
| A22380 | Install Fire Alarm Devices | 2 | 2 | 26-Mar-21 | 29-Mar-21 |
| A22320 | Seal Concrete Floors | 3 | 3 | 30-Mar-21 | 01-Apr-21 |
| A22390 | MEPFP Final Inspections | 2 | 2 | 30-Mar-21 | 31-Mar-21 |
| A22340 | Final Paint | 2 | 2 | 02-Apr-21 | 05-Apr-21 |
| A22350 | Punchlist | 5 | 5 | 06-Apr-21 | 12-Apr-21 |
| Mens Restroom - Rooms 24.04 | | 82 | 82 | 29-Jan-21 | 24-May-21 |
| A20890 | Layout & Top Track | 2 | 2 | 29-Jan-21 | 01-Feb-21 |
| A20900 | OH Mechanical | 5 | 5 | 02-Feb-21 | 08-Feb-21 |
| A20910 | OH Electrical | 5 | 5 | 04-Feb-21 | 10-Feb-21 |
| A20920 | OH Plumbing | 5 | 5 | 08-Feb-21 | 12-Feb-21 |
| A20930 | OH Fire Protection | 5 | 5 | 10-Feb-21 | 16-Feb-21 |
| A20940 | Above Ceiling Inspections | 1 | 1 | 17-Feb-21 | 17-Feb-21 |
| A20950 | Frame Walls | 3 | 3 | 18-Feb-21 | 22-Feb-21 |
| A20960 | In-Wall Electrical | 5 | 5 | 23-Feb-21 | 01-Mar-21 |
| A20970 | In-Wall Plumbing | 8 | 8 | 23-Feb-21 | 04-Mar-21 |
| A20980 | In-Wall Inspections | 1 | 1 | 05-Mar-21 | 05-Mar-21 |
| A20990 | Hang Cement Board/Drywall | 3 | 3 | 08-Mar-21 | 10-Mar-21 |
| A21000 | Install Wall Tile | 7 | 7 | 11-Mar-21 | 19-Mar-21 |
| A21200 | Prime Paint | 2 | 2 | 11-Mar-21 | 12-Mar-21 |
| A21070 | Install Floor Tile | 5 | 5 | 22-Mar-21 | 26-Mar-21 |
| A21010 | Install ACT Grid | 2 | 2 | 29-Mar-21 | 30-Mar-21 |
| A21020 | Install Lighting | 2 | 2 | 31-Mar-21 | 01-Apr-21 |
| A21030 | Grilles, Registers & Diffusers | 2 | 2 | 01-Apr-21 | 02-Apr-21 |
| A21040 | Sprinkler Heads | 2 | 2 | 02-Apr-21 | 05-Apr-21 |
| A21050 | Fire Alarm Devices | 2 | 2 | 06-Apr-21 | 07-Apr-21 |
| A21060 | In-Ceiling Inspections | 1 | 1 | 08-Apr-21 | 08-Apr-21 |
| A21080 | Install ACT Tiles | 2 | 2 | 09-Apr-21 | 12-Apr-21 |
| A21180 | Install Luxury Vinyl Tile - First Aid | 5 | 5 | 09-Apr-21 | 15-Apr-21 |
| A21090 | Install Toilets & Urinals | 5 | 5 | 16-Apr-21 | 22-Apr-21 |
| A21100 | Install Millwork | 4 | 4 | 23-Apr-21 | 28-Apr-21 |
| A21110 | Install Countertops | 2 | 2 | 29-Apr-21 | 30-Apr-21 |
| A21120 | Install Plumbing Fixtures | 2 | 2 | 03-May-21 | 04-May-21 |
| A21130 | Toilet Partitions | 3 | 3 | 05-May-21 | 07-May-21 |
| A21140 | Install Toilet Accessories | 2 | 2 | 10-May-21 | 11-May-21 |
| A21150 | Electrical Trim-out | 2 | 2 | 12-May-21 | 13-May-21 |
| A21160 | MEPFP Final Inspections | 2 | 2 | 14-May-21 | 17-May-21 |
| A21190 | Final Paint | 2 | 2 | 14-May-21 | 17-May-21 |
| A21170 | Punchlist | 5 | 5 | 18-May-21 | 24-May-21 |
| Concession & Prep - Rooms 24.08-09 | | 58 | 58 | 29-Jan-21 | 20-Apr-21 |
| A21790 | Layout & Top Track | 2 | 2 | 29-Jan-21 | 01-Feb-21 |
| A21500 | OH Mechanical | 4 | 4 | 02-Feb-21 | 05-Feb-21 |
| A21510 | OH Electrical | 4 | 4 | 04-Feb-21 | 09-Feb-21 |

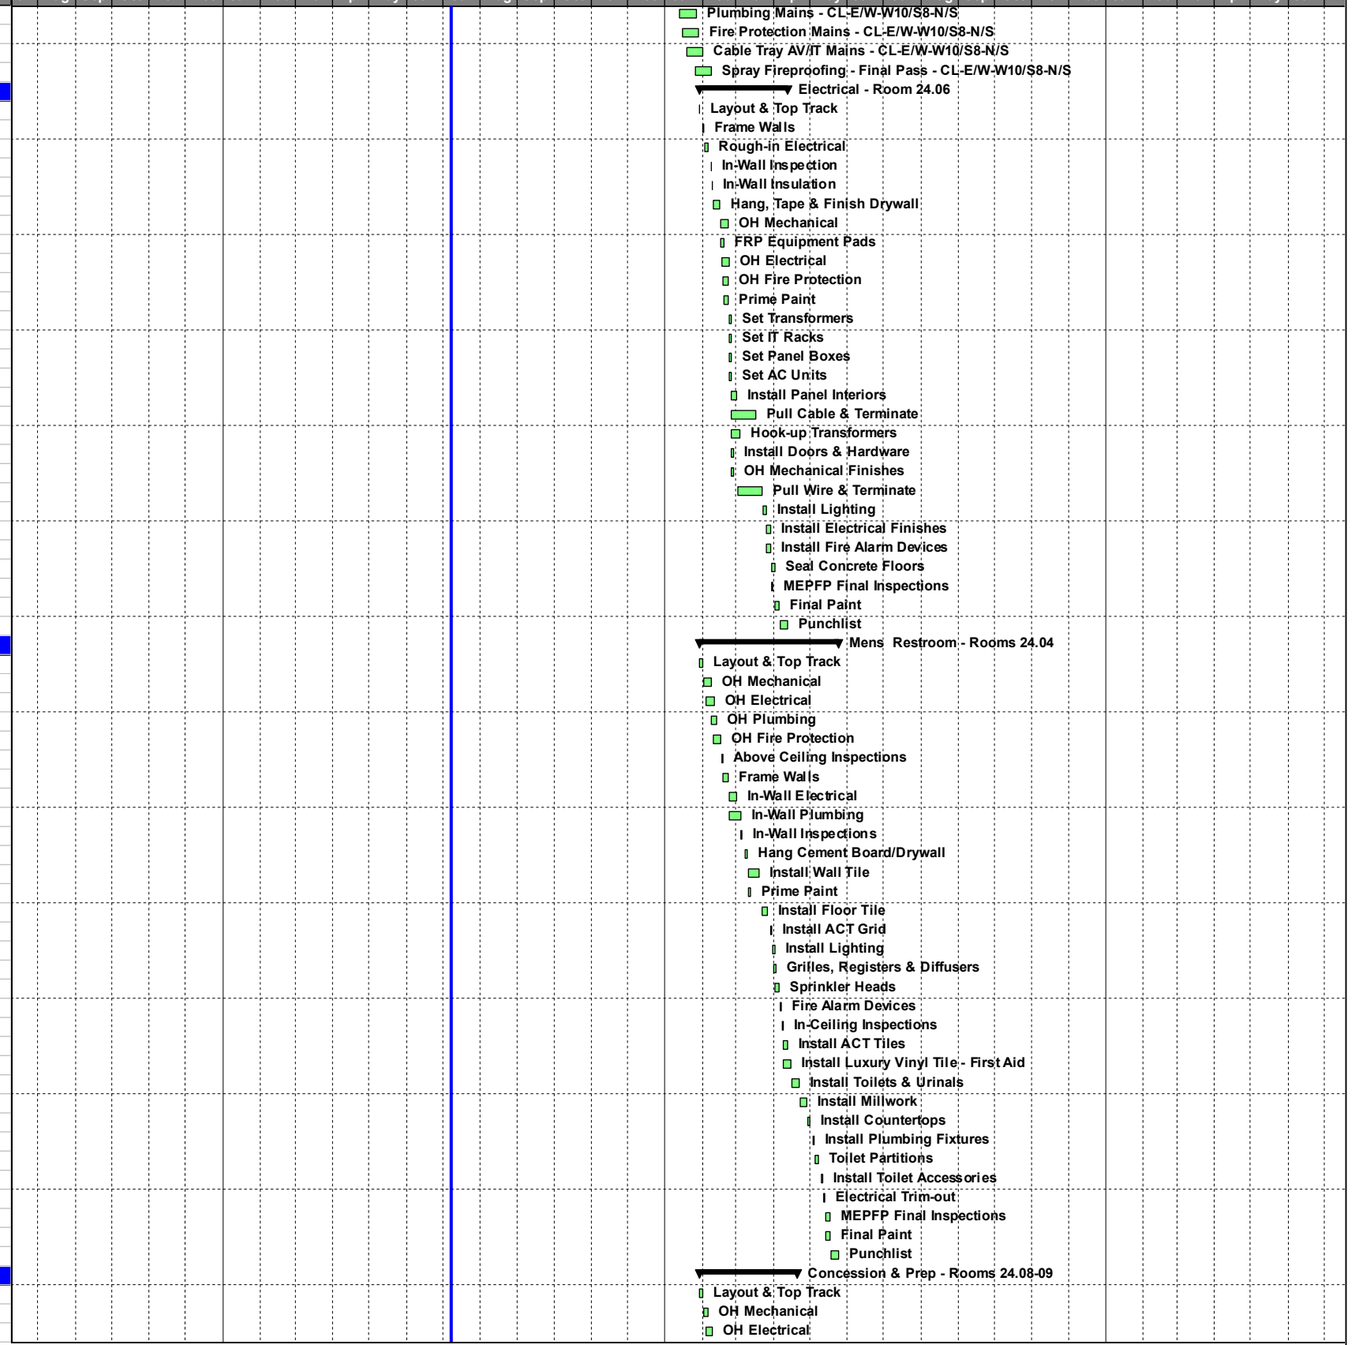

| Activity ID | Activity Name | Original Duration | Remaining Duration | Start | Finish |
|---|---|---|---|---|---|
| A21520 | OH Plumbing | 4 | 4 | 08-Feb-21 | 11-Feb-21 |
| A21530 | OH Fire Protection | 4 | 4 | 10-Feb-21 | 15-Feb-21 |
| A21580 | Frame Ceilings | 2 | 2 | 10-Feb-21 | 11-Feb-21 |
| A21590 | Install Lighting (Drywall Ceilings) | 2 | 2 | 12-Feb-21 | 15-Feb-21 |
| A21540 | Install Exhaust Hood | 5 | 5 | 16-Feb-21 | 22-Feb-21 |
| A21600 | Hang, Tape & Finish Drywall | 5 | 5 | 16-Feb-21 | 22-Feb-21 |
| A21550 | Above Ceiling Inspections | 1 | 1 | 23-Feb-21 | 23-Feb-21 |
| A21560 | Prime Paint | 1 | 1 | 23-Feb-21 | 23-Feb-21 |
| A21660 | FRP Wall Panels | 3 | 3 | 24-Feb-21 | 26-Feb-21 |
| A21570 | Install ACT Grid | 1 | 1 | 01-Mar-21 | 01-Mar-21 |
| A21610 | Install Lighting (Grid Ceilings) | 2 | 2 | 02-Mar-21 | 03-Mar-21 |
| A21620 | Sprinkler Heads | 1 | 1 | 04-Mar-21 | 04-Mar-21 |
| A21630 | Grilles, Registers & Diffusers | 1 | 1 | 05-Mar-21 | 05-Mar-21 |
| A21640 | Fire Alarm Devices | 1 | 1 | 08-Mar-21 | 08-Mar-21 |
| A21770 | In-Ceiling Inspections | 1 | 1 | 09-Mar-21 | 09-Mar-21 |
| A21650 | Install ACT Tiles | 1 | 1 | 10-Mar-21 | 10-Mar-21 |
| A21670 | Resilient Flooring | 5 | 5 | 11-Mar-21 | 17-Mar-21 |
| A21710 | Millwork | 5 | 5 | 18-Mar-21 | 24-Mar-21 |
| A21780 | Install Doors & Hardware | 1 | 1 | 18-Mar-21 | 18-Mar-21 |
| A21680 | Install Plumbing Fixtures | 2 | 2 | 25-Mar-21 | 26-Mar-21 |
| A21750 | Tile Concession Wall | 3 | 3 | 25-Mar-21 | 29-Mar-21 |
| A21760 | Install Countertops | 2 | 2 | 30-Mar-21 | 31-Mar-21 |
| A21700 | Food Service Equipment | 5 | 5 | 01-Apr-21 | 07-Apr-21 |
| A21690 | Electrical Trim-out | 2 | 2 | 08-Apr-21 | 09-Apr-21 |
| A21720 | Final Paint | 2 | 2 | 12-Apr-21 | 13-Apr-21 |
| A21730 | MEPFP Final Inspections | 2 | 2 | 12-Apr-21 | 13-Apr-21 |
| A21740 | Punchlist | 5 | 5 | 14-Apr-21 | 20-Apr-21 |
| **Womens & Family - Rooms 24.10 & 24.11** | | **82** | **82** | **29-Jan-21** | **24-May-21** |
| A21800 | Layout & Top Track | 2 | 2 | 29-Jan-21 | 01-Feb-21 |
| A21810 | OH Mechanical | 5 | 5 | 02-Feb-21 | 08-Feb-21 |
| A21820 | OH Electrical | 5 | 5 | 04-Feb-21 | 10-Feb-21 |
| A21830 | OH Plumbing | 5 | 5 | 08-Feb-21 | 12-Feb-21 |
| A21840 | OH Fire Protection | 5 | 5 | 10-Feb-21 | 16-Feb-21 |
| A21850 | Above Ceiling Inspections | 1 | 1 | 17-Feb-21 | 17-Feb-21 |
| A21860 | Frame Walls | 3 | 3 | 18-Feb-21 | 22-Feb-21 |
| A21870 | In-Wall Electrical | 5 | 5 | 23-Feb-21 | 01-Mar-21 |
| A21880 | In-Wall Plumbing | 8 | 8 | 23-Feb-21 | 04-Mar-21 |
| A21890 | In-Wall Inspections | 1 | 1 | 05-Mar-21 | 05-Mar-21 |
| A21900 | Hang Cement Board/Drywall | 3 | 3 | 08-Mar-21 | 10-Mar-21 |
| A21910 | Install Wall Tile | 7 | 7 | 11-Mar-21 | 19-Mar-21 |
| A22110 | Prime Paint | 2 | 2 | 11-Mar-21 | 12-Mar-21 |
| A21980 | Install Floor Tile | 5 | 5 | 22-Mar-21 | 26-Mar-21 |
| A21920 | Install ACT Grid | 2 | 2 | 29-Mar-21 | 30-Mar-21 |
| A21930 | Install Lighting | 2 | 2 | 31-Mar-21 | 01-Apr-21 |
| A21940 | Grilles, Registers & Diffusers | 2 | 2 | 01-Apr-21 | 02-Apr-21 |
| A21950 | Sprinkler Heads | 2 | 2 | 02-Apr-21 | 05-Apr-21 |
| A21960 | Fire Alarm Devices | 2 | 2 | 06-Apr-21 | 07-Apr-21 |
| A21970 | In-Ceiling Inspections | 1 | 1 | 08-Apr-21 | 08-Apr-21 |
| A21990 | Install ACT Tiles | 2 | 2 | 09-Apr-21 | 12-Apr-21 |
| A22090 | Install Luxury Vinyl Tile - First Aid | 5 | 5 | 09-Apr-21 | 15-Apr-21 |
| A22000 | Install Toilets & Urinals | 5 | 5 | 16-Apr-21 | 22-Apr-21 |
| A22010 | Install Millwork | 4 | 4 | 23-Apr-21 | 28-Apr-21 |
| A22020 | Install Countertops | 2 | 2 | 29-Apr-21 | 30-Apr-21 |
| A22030 | Install Plumbing Fixtures | 2 | 2 | 03-May-21 | 04-May-21 |
| A22040 | Toilet Partitions | 3 | 3 | 05-May-21 | 07-May-21 |
| A22050 | Install Toilet Accessories | 2 | 2 | 10-May-21 | 11-May-21 |
| A22060 | Electrical Trim-out | 2 | 2 | 12-May-21 | 13-May-21 |
| A22070 | MEPFP Final Inspections | 2 | 2 | 14-May-21 | 17-May-21 |
| A22100 | Final Paint | 2 | 2 | 14-May-21 | 17-May-21 |
| A22080 | Punchlist | 5 | 5 | 18-May-21 | 24-May-21 |
| **Corridors** | | **40** | **40** | **15-Mar-21** | **07-May-21** |
| A22430 | Prime Paint | 5 | 5 | 15-Mar-21 | 19-Mar-21 |
| A22400 | Sprinkler Heads | 5 | 5 | 22-Mar-21 | 26-Mar-21 |
| A22410 | Lighting | 5 | 5 | 25-Mar-21 | 31-Mar-21 |
| A22420 | Fire Alarm Devices | 5 | 5 | 30-Mar-21 | 05-Apr-21 |
| A22470 | Install Doors & Hardware | 5 | 5 | 06-Apr-21 | 12-Apr-21 |
| A22440 | Seal Concrete Floors | 5 | 5 | 13-Apr-21 | 19-Apr-21 |
| A22450 | Electrical Trim-out | 5 | 5 | 20-Apr-21 | 26-Apr-21 |
| A22460 | Final MEPFP Inspections | 3 | 3 | 27-Apr-21 | 29-Apr-21 |
| A22480 | Final Paint | 4 | 4 | 27-Apr-21 | 30-Apr-21 |

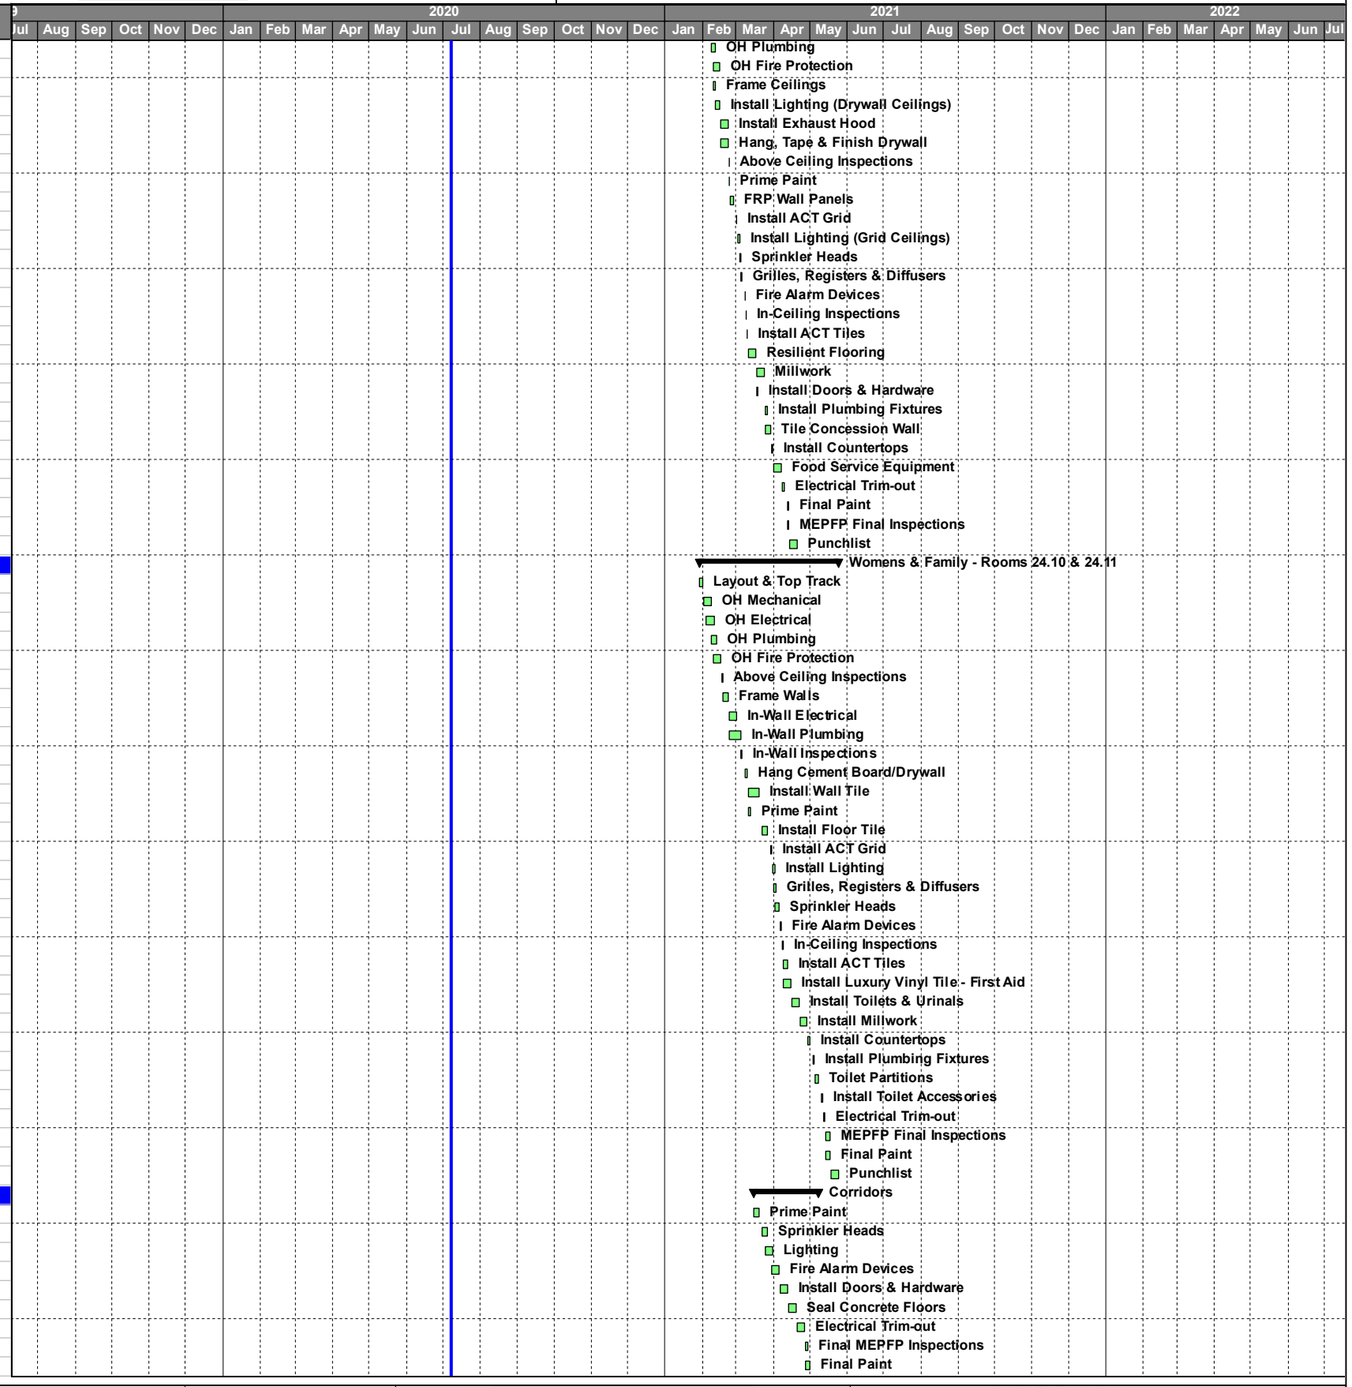

| Activity ID | Activity Name | Original Duration | Remaining Duration | Start | Finish |
|---|---|---|---|---|---|
| A22490 | Punchlist | 5 | 5 | 03-May-21 | 07-May-21 |
| Suite Level | | 140 | 140 | 05-Nov-20 | 26-May-21 |
| A29410 | Suite Level Complete | 0 | 0 | | 26-May-21 |
| Quad 1 | | 130 | 130 | 05-Nov-20 | 12-May-21 |
| MEPFP Mains Rough-in | | 41 | 41 | 05-Nov-20 | 07-Jan-21 |
| OHRI-EL-Q1-1 | Spray Fireproofing - First Pass - CL-W10-N/S/N8-E/W | 10 | 10 | 05-Nov-20 | 18-Nov-20 |
| OHRI-EL-Q1-1 | Install Subroof - CL-W10-N/S/N8-E/W | 15 | 15 | 19-Nov-20 | 11-Dec-20 |
| OHRI-EL-Q1-1 | Mechanical Mains - CL-W10-N/S/N8-E/W | 10 | 10 | 03-Dec-20 | 16-Dec-20 |
| OHRI-EL-Q1-1 | Electrical Mains - CL-W10-N/S/N8-E/W | 10 | 10 | 07-Dec-20 | 18-Dec-20 |
| OHRI-EL-Q1-1 | Plumbing Mains - CL-W10-N/S/N8-E/W | 10 | 10 | 09-Dec-20 | 22-Dec-20 |
| OHRI-EL-Q1-1 | Fire Protection Mains - CL-W10-N/S/N8-E/W | 10 | 10 | 11-Dec-20 | 28-Dec-20 |
| OHRI-EL-Q1-1 | Cable Tray AV/IT Mains - CL-W10-N/S/N8-E/W | 10 | 10 | 15-Dec-20 | 30-Dec-20 |
| OHRI-EL-Q1-1 | Spray Fireproofing - Final Pass - CL-W10-N/S/N8-E/W | 10 | 10 | 22-Dec-20 | 07-Jan-21 |
| Electrical & IT - Rooms 31.05 & 31.06 | | 52 | 52 | 29-Dec-20 | 11-Mar-21 |
| A23180 | Layout & Top Track | 1 | 1 | 29-Dec-20 | 29-Dec-20 |
| A23190 | Frame Walls | 2 | 2 | 30-Dec-20 | 31-Dec-20 |
| A23200 | Rough-in Electrical | 3 | 3 | 04-Jan-21 | 06-Jan-21 |
| A23210 | In-Wall Inspection | 1 | 1 | 07-Jan-21 | 07-Jan-21 |
| A23220 | In-Wall Insulation | 1 | 1 | 08-Jan-21 | 08-Jan-21 |
| A23230 | Hang, Tape & Finish Drywall | 4 | 4 | 11-Jan-21 | 14-Jan-21 |
| A23240 | OH Mechanical | 5 | 5 | 15-Jan-21 | 21-Jan-21 |
| A23270 | FRP Equipment Pads | 3 | 3 | 15-Jan-21 | 19-Jan-21 |
| A23250 | OH Electrical | 5 | 5 | 18-Jan-21 | 22-Jan-21 |
| A23260 | OH Fire Protection | 3 | 3 | 19-Jan-21 | 21-Jan-21 |
| A23370 | Prime Paint | 2 | 2 | 20-Jan-21 | 21-Jan-21 |
| A23280 | Set Transformers | 2 | 2 | 22-Jan-21 | 25-Jan-21 |
| A23290 | Set IT Racks | 2 | 2 | 22-Jan-21 | 25-Jan-21 |
| A23300 | Set Panel Boxes | 2 | 2 | 22-Jan-21 | 25-Jan-21 |
| A23420 | Set AC Units | 2 | 2 | 22-Jan-21 | 25-Jan-21 |
| A23310 | Install Panel Interiors | 3 | 3 | 26-Jan-21 | 28-Jan-21 |
| A23330 | Pull Cable & Terminate | 15 | 15 | 26-Jan-21 | 15-Feb-21 |
| A23340 | Hook-up Transformers | 5 | 5 | 26-Jan-21 | 01-Feb-21 |
| A23390 | Install Doors & Hardware | 2 | 2 | 26-Jan-21 | 27-Jan-21 |
| A23430 | OH Mechanical Finishes | 2 | 2 | 26-Jan-21 | 27-Jan-21 |
| A23320 | Pull Wire & Terminate | 15 | 15 | 29-Jan-21 | 18-Feb-21 |
| A23350 | Install Lighting | 3 | 3 | 19-Feb-21 | 23-Feb-21 |
| A23360 | Install Electrical Finishes | 2 | 2 | 24-Feb-21 | 25-Feb-21 |
| A23440 | Install Fire Alarm Devices | 2 | 2 | 24-Feb-21 | 25-Feb-21 |
| A23380 | Seal Concrete Floors | 3 | 3 | 26-Feb-21 | 02-Mar-21 |
| A23450 | MEPFP Final Inspections | 2 | 2 | 26-Feb-21 | 01-Mar-21 |
| A23400 | Final Paint | 2 | 2 | 03-Mar-21 | 04-Mar-21 |
| A23410 | Punchlist | 5 | 5 | 05-Mar-21 | 11-Mar-21 |
| Mens, Womens & Family Restrooms - Rooms 31.07, 31.08 & 31.09 | | 91 | 91 | 30-Dec-20 | 06-May-21 |
| A22600 | Layout & Top Track | 2 | 2 | 30-Dec-20 | 31-Dec-20 |
| A22610 | OH Mechanical | 5 | 5 | 04-Jan-21 | 08-Jan-21 |
| A22620 | OH Electrical | 5 | 5 | 06-Jan-21 | 12-Jan-21 |
| A22630 | OH Plumbing | 5 | 5 | 08-Jan-21 | 14-Jan-21 |
| A22640 | OH Fire Protection | 5 | 5 | 12-Jan-21 | 18-Jan-21 |
| A22650 | Above Ceiling Inspections | 1 | 1 | 19-Jan-21 | 19-Jan-21 |
| A22660 | Frame Walls | 3 | 3 | 20-Jan-21 | 22-Jan-21 |
| A22670 | In-Wall Electrical | 5 | 5 | 25-Jan-21 | 29-Jan-21 |
| A22680 | In-Wall Plumbing | 8 | 8 | 25-Jan-21 | 03-Feb-21 |
| A22690 | In-Wall Inspections | 1 | 1 | 04-Feb-21 | 04-Feb-21 |
| A22700 | Hang Cement Board | 3 | 3 | 05-Feb-21 | 09-Feb-21 |
| A24770 | Frame Ceilings | 3 | 3 | 10-Feb-21 | 12-Feb-21 |
| A25200 | Install Lighting (Drywall Ceiling Area) | 2 | 2 | 15-Feb-21 | 16-Feb-21 |
| A25210 | Hang, Tape & Finish Drywall Ceilings | 5 | 5 | 17-Feb-21 | 23-Feb-21 |
| A25220 | Prime Paint | 2 | 2 | 24-Feb-21 | 25-Feb-21 |
| A22710 | Install Wall Tile | 7 | 7 | 26-Feb-21 | 08-Mar-21 |
| A22780 | Install Floor Tile | 5 | 5 | 09-Mar-21 | 15-Mar-21 |
| A22720 | Install ACT Grid | 2 | 2 | 16-Mar-21 | 17-Mar-21 |
| A22730 | Install Lighting | 2 | 2 | 18-Mar-21 | 19-Mar-21 |
| A22740 | Grilles, Registers & Diffusers | 2 | 2 | 19-Mar-21 | 22-Mar-21 |
| A22750 | Sprinkler Heads | 2 | 2 | 22-Mar-21 | 23-Mar-21 |
| A22760 | Fire Alarm Devices | 2 | 2 | 24-Mar-21 | 25-Mar-21 |
| A22770 | In-Ceiling Inspections | 1 | 1 | 26-Mar-21 | 26-Mar-21 |
| A22790 | Install ACT Tiles | 2 | 2 | 29-Mar-21 | 30-Mar-21 |
| A22800 | Install Toilets & Urinals | 5 | 5 | 31-Mar-21 | 06-Apr-21 |
| A22810 | Install Millwork | 4 | 4 | 07-Apr-21 | 12-Apr-21 |
| A22820 | Install Countertops | 2 | 2 | 13-Apr-21 | 14-Apr-21 |

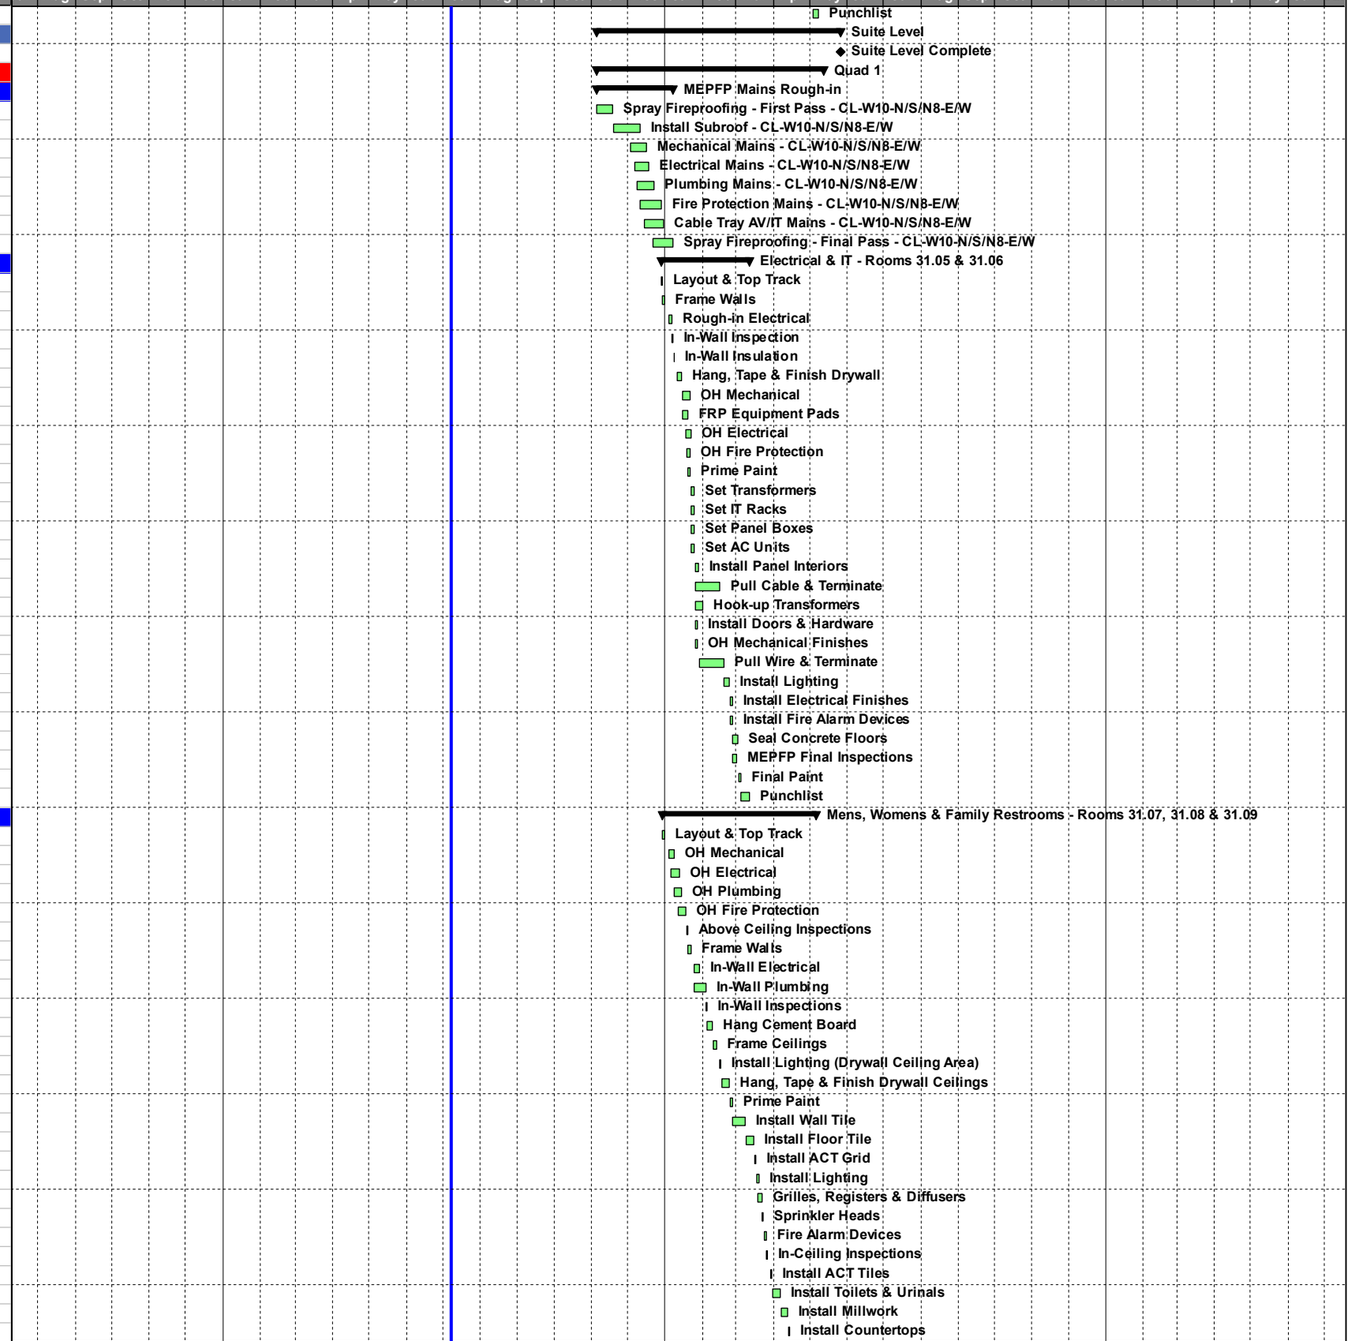

| Activity ID | Activity Name | Original Duration | Remaining Duration | Start | Finish |
|---|---|---|---|---|---|
| A22830 | Install Plumbing Fixtures | 2 | 2 | 15-Apr-21 | 16-Apr-21 |
| A22840 | Toilet Partitions | 3 | 3 | 19-Apr-21 | 21-Apr-21 |
| A22850 | Install Toilet Accessories | 2 | 2 | 22-Apr-21 | 23-Apr-21 |
| A22860 | Electrical Trim-out | 2 | 2 | 26-Apr-21 | 27-Apr-21 |
| A22870 | MEPFP Final Inspections | 2 | 2 | 28-Apr-21 | 29-Apr-21 |
| A22880 | Punchlist | 5 | 5 | 30-Apr-21 | 06-May-21 |
| NW Suite Bar - Room 31.03 & 31.01 | | 72 | 72 | 29-Dec-20 | 08-Apr-21 |
| A23460 | Layout & Top Track | 5 | 5 | 29-Dec-20 | 05-Jan-21 |
| A22890 | OH Mechanical | 4 | 4 | 06-Jan-21 | 11-Jan-21 |
| A22900 | OH Electrical | 4 | 4 | 08-Jan-21 | 13-Jan-21 |
| A22910 | OH Plumbing | 4 | 4 | 12-Jan-21 | 15-Jan-21 |
| A22920 | OH Fire Protection | 4 | 4 | 14-Jan-21 | 19-Jan-21 |
| A22970 | Frame Ceilings | 2 | 2 | 14-Jan-21 | 15-Jan-21 |
| A22930 | Install Exhaust Hood | 5 | 5 | 20-Jan-21 | 26-Jan-21 |
| A25240 | Frame Walls | 3 | 3 | 20-Jan-21 | 22-Jan-21 |
| A25250 | In-Wall Electrical | 5 | 5 | 25-Jan-21 | 29-Jan-21 |
| A25260 | In-Wall Plumbing | 5 | 5 | 26-Jan-21 | 01-Feb-21 |
| A22940 | Above Ceiling Inspections | 1 | 1 | 27-Jan-21 | 27-Jan-21 |
| A25270 | In-Wall Inspections | 1 | 1 | 02-Feb-21 | 02-Feb-21 |
| A22990 | Hang, Tape & Finish Drywall | 8 | 8 | 03-Feb-21 | 12-Feb-21 |
| A22950 | Prime Paint | 2 | 2 | 15-Feb-21 | 16-Feb-21 |
| A23050 | FRP Wall Panels | 3 | 3 | 17-Feb-21 | 19-Feb-21 |
| A22960 | Install ACT Grid | 1 | 1 | 22-Feb-21 | 22-Feb-21 |
| A23000 | Install Lighting (Grid Ceilings) | 2 | 2 | 23-Feb-21 | 24-Feb-21 |
| A23010 | Sprinkler Heads | 1 | 1 | 25-Feb-21 | 25-Feb-21 |
| A23020 | Grilles, Registers & Diffusers | 1 | 1 | 26-Feb-21 | 26-Feb-21 |
| A23030 | Fire Alarm Devices | 1 | 1 | 01-Mar-21 | 01-Mar-21 |
| A23160 | In-Ceiling Inspections | 1 | 1 | 02-Mar-21 | 02-Mar-21 |
| A23040 | Install ACT Tiles | 1 | 1 | 03-Mar-21 | 03-Mar-21 |
| A23060 | Resilient Flooring | 5 | 5 | 04-Mar-21 | 10-Mar-21 |
| A23140 | Install Floor Tile | 5 | 5 | 04-Mar-21 | 10-Mar-21 |
| A23100 | Millwork | 5 | 5 | 11-Mar-21 | 17-Mar-21 |
| A23170 | Install Doors & Hardware | 1 | 1 | 11-Mar-21 | 11-Mar-21 |
| A23070 | Install Plumbing Fixtures | 2 | 2 | 18-Mar-21 | 19-Mar-21 |
| A23150 | Install Countertops | 2 | 2 | 18-Mar-21 | 19-Mar-21 |
| A25230 | Install Wood Ceiling | 5 | 5 | 18-Mar-21 | 24-Mar-21 |
| A23090 | Food Service Equipment | 5 | 5 | 22-Mar-21 | 26-Mar-21 |
| A22980 | Install Lighting (Drywall Ceilings) | 2 | 2 | 25-Mar-21 | 26-Mar-21 |
| A23080 | Electrical Trim-out | 2 | 2 | 29-Mar-21 | 30-Mar-21 |
| A23110 | Final Paint | 2 | 2 | 31-Mar-21 | 01-Apr-21 |
| A23120 | MEPFP Final Inspections | 2 | 2 | 31-Mar-21 | 01-Apr-21 |
| A23130 | Punchlist | 5 | 5 | 02-Apr-21 | 08-Apr-21 |
| Loge 1-5 - Rooms 31.10-19 | | 73 | 73 | 29-Dec-20 | 09-Apr-21 |
| A24590 | Layout & Top Track | 5 | 5 | 29-Dec-20 | 05-Jan-21 |
| A24600 | OH Mechanical | 5 | 5 | 06-Jan-21 | 12-Jan-21 |
| A24610 | OH Electrical | 5 | 5 | 08-Jan-21 | 14-Jan-21 |
| A24620 | OH Plumbing | 5 | 5 | 12-Jan-21 | 18-Jan-21 |
| A24630 | OH Fire Protection | 5 | 5 | 14-Jan-21 | 20-Jan-21 |
| A24660 | Frame Walls | 5 | 5 | 21-Jan-21 | 27-Jan-21 |
| A24700 | In-Wall Plumbing | 7 | 7 | 25-Jan-21 | 02-Feb-21 |
| A24710 | In-Wall Electrical | 7 | 7 | 27-Jan-21 | 04-Feb-21 |
| A24640 | Frame Ceilings | 2 | 2 | 28-Jan-21 | 29-Jan-21 |
| A24680 | Above Ceiling Inspections | 1 | 1 | 01-Feb-21 | 01-Feb-21 |
| A24650 | Install Lighting (Drywall Ceilings) | 3 | 3 | 02-Feb-21 | 04-Feb-21 |
| A24730 | Sprinkler Heads | 3 | 3 | 02-Feb-21 | 04-Feb-21 |
| A24720 | In-Wall Inspections | 2 | 2 | 05-Feb-21 | 08-Feb-21 |
| A24670 | Hang, Tape & Finish Drywall | 10 | 10 | 09-Feb-21 | 22-Feb-21 |
| A24740 | Grilles, Registers & Diffusers | 3 | 3 | 23-Feb-21 | 25-Feb-21 |
| A24750 | Fire Alarm Devices | 3 | 3 | 26-Feb-21 | 02-Mar-21 |
| A24760 | In-Ceiling Inspections | 1 | 1 | 03-Mar-21 | 03-Mar-21 |
| A24690 | Prime Paint | 1 | 1 | 04-Mar-21 | 04-Mar-21 |
| A24790 | Millwork | 5 | 5 | 05-Mar-21 | 11-Mar-21 |
| A24820 | Install Suite Partition Dividers | 8 | 8 | 05-Mar-21 | 16-Mar-21 |
| A24830 | Install Countertops | 2 | 2 | 12-Mar-21 | 15-Mar-21 |
| A24890 | Install Wood Cap & Glass Rail | 8 | 8 | 12-Mar-21 | 23-Mar-21 |
| A24810 | Install Plumbing Fixtures | 2 | 2 | 16-Mar-21 | 17-Mar-21 |
| A24840 | Food Service Equipment | 5 | 5 | 16-Mar-21 | 22-Mar-21 |
| A24800 | Install Doors & Hardware | 1 | 1 | 16-Mar-21 | 16-Mar-21 |
| A24850 | Electrical Trim-out | 2 | 2 | 23-Mar-21 | 24-Mar-21 |
| A24780 | Install Carpet | 5 | 5 | 25-Mar-21 | 31-Mar-21 |

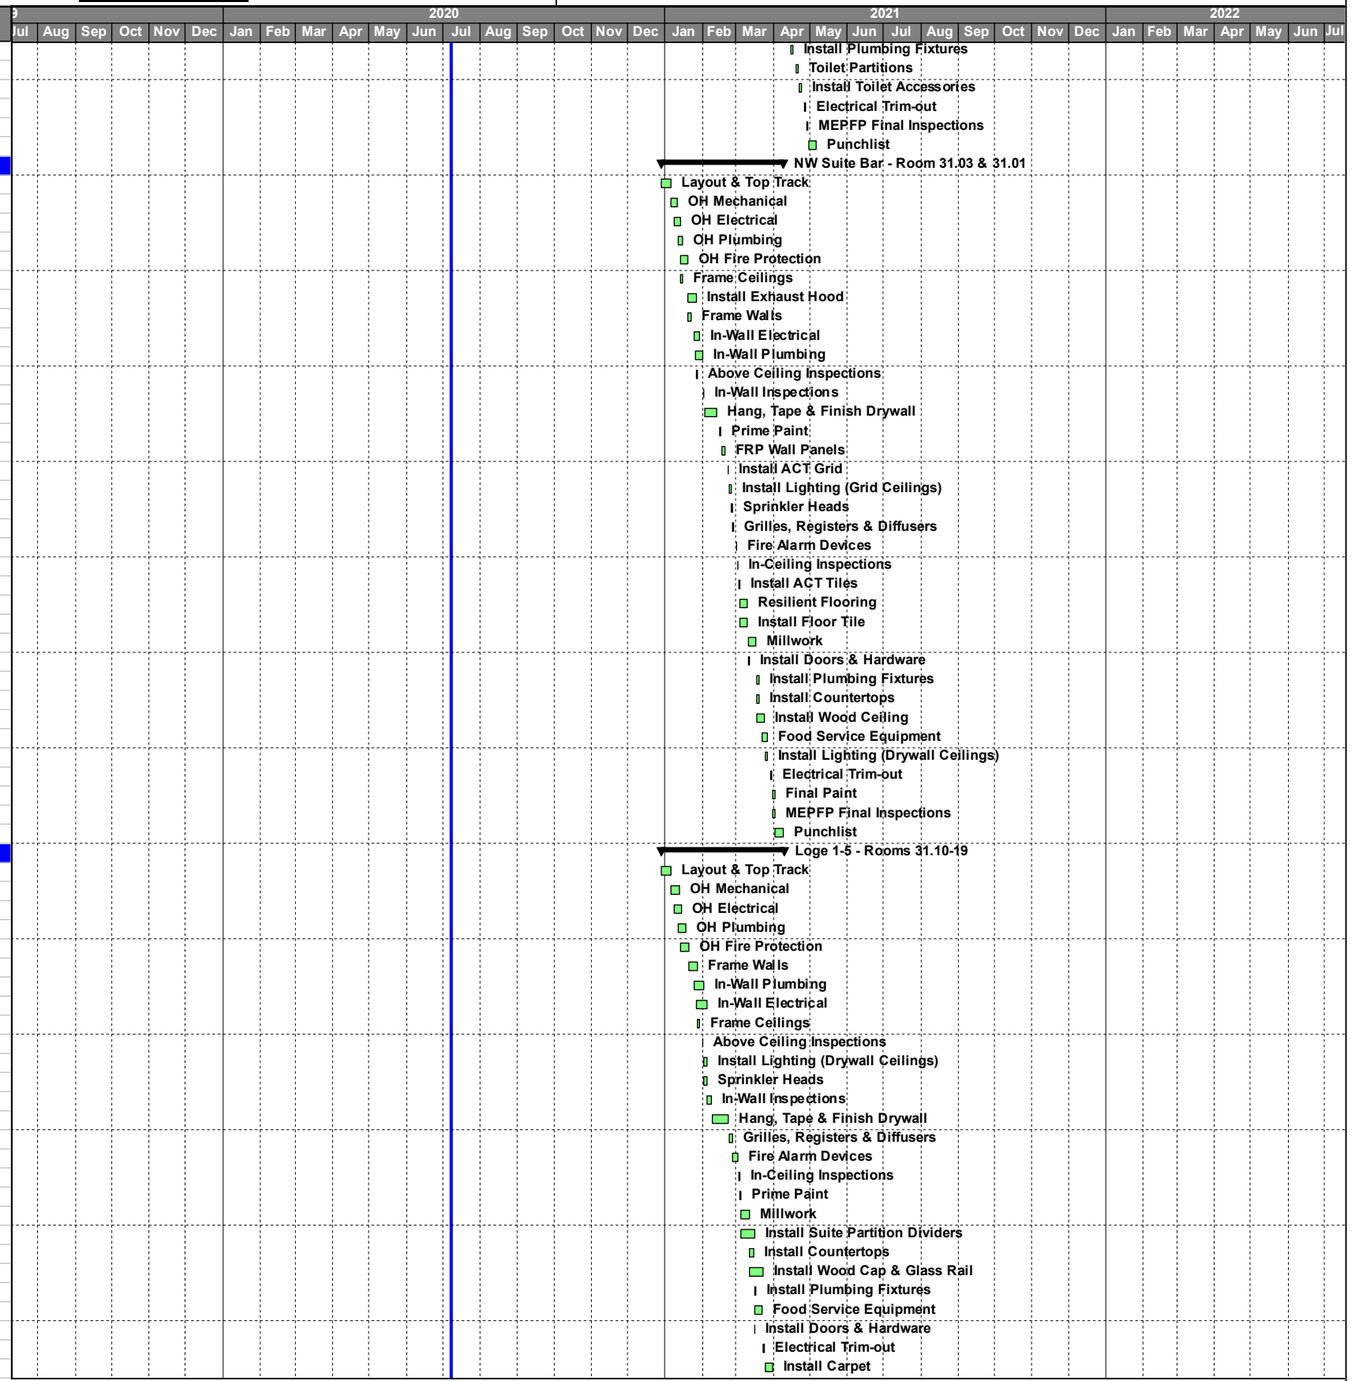

| Activity ID | Activity Name | Original Duration | Remaining Duration | Start | Finish |
|---|---|---|---|---|---|
| A24870 | MEPFP Final Inspections | 2 | 2 | 25-Mar-21 | 26-Mar-21 |
| A24860 | Final Paint | 2 | 2 | 01-Apr-21 | 02-Apr-21 |
| A24880 | Punchlist | 5 | 5 | 05-Apr-21 | 09-Apr-21 |
| Suite 1-5 - Rooms 31.12-16 | | 78 | 78 | 29-Dec-20 | 16-Apr-21 |
| A24900 | Layout & Top Track | 5 | 5 | 29-Dec-20 | 05-Jan-21 |
| A24910 | OH Mechanical | 5 | 5 | 06-Jan-21 | 12-Jan-21 |
| A24920 | OH Electrical | 5 | 5 | 08-Jan-21 | 14-Jan-21 |
| A24930 | OH Plumbing | 5 | 5 | 12-Jan-21 | 18-Jan-21 |
| A24940 | OH Fire Protection | 5 | 5 | 14-Jan-21 | 20-Jan-21 |
| A24950 | Frame Walls | 5 | 5 | 21-Jan-21 | 27-Jan-21 |
| A24960 | In-Wall Plumbing | 7 | 7 | 25-Jan-21 | 02-Feb-21 |
| A24970 | In-Wall Electrical | 7 | 7 | 27-Jan-21 | 04-Feb-21 |
| A24980 | Frame Ceilings | 2 | 2 | 28-Jan-21 | 29-Jan-21 |
| A24990 | Above Ceiling Inspections | 1 | 1 | 01-Feb-21 | 01-Feb-21 |
| A25000 | Install Lighting (Drywall Ceilings) | 3 | 3 | 02-Feb-21 | 04-Feb-21 |
| A25010 | Sprinkler Heads | 3 | 3 | 02-Feb-21 | 04-Feb-21 |
| A25020 | In-Wall Inspections | 2 | 2 | 05-Feb-21 | 08-Feb-21 |
| A25030 | Hang, Tape & Finish Drywall | 10 | 10 | 09-Feb-21 | 22-Feb-21 |
| A25280 | Install ACT Grid | 5 | 5 | 23-Feb-21 | 01-Mar-21 |
| A25040 | Grilles, Registers & Diffusers | 3 | 3 | 02-Mar-21 | 04-Mar-21 |
| A25050 | Fire Alarm Devices | 3 | 3 | 05-Mar-21 | 09-Mar-21 |
| A25060 | In-Ceiling Inspections | 1 | 1 | 10-Mar-21 | 10-Mar-21 |
| A25070 | Prime Paint | 1 | 1 | 11-Mar-21 | 11-Mar-21 |
| A25290 | Install ACT Tiles | 5 | 5 | 11-Mar-21 | 17-Mar-21 |
| A25080 | Millwork | 5 | 5 | 12-Mar-21 | 18-Mar-21 |
| A25090 | Install Suite Partition Dividers | 8 | 8 | 12-Mar-21 | 23-Mar-21 |
| A25100 | Install Countertops | 2 | 2 | 19-Mar-21 | 22-Mar-21 |
| A25110 | Install Wood Cap & Glass Rail | 8 | 8 | 19-Mar-21 | 30-Mar-21 |
| A25120 | Install Plumbing Fixtures | 2 | 2 | 23-Mar-21 | 24-Mar-21 |
| A25130 | Food Service Equipment | 5 | 5 | 23-Mar-21 | 29-Mar-21 |
| A25140 | Install Doors & Hardware | 1 | 1 | 23-Mar-21 | 23-Mar-21 |
| A25150 | Electrical Trim-out | 2 | 2 | 30-Mar-21 | 31-Mar-21 |
| A25160 | Install Carpet | 5 | 5 | 01-Apr-21 | 07-Apr-21 |
| A25170 | MEPFP Final Inspections | 2 | 2 | 01-Apr-21 | 02-Apr-21 |
| A25180 | Final Paint | 2 | 2 | 08-Apr-21 | 09-Apr-21 |
| A25190 | Punchlist | 5 | 5 | 12-Apr-21 | 16-Apr-21 |
| NW Suite Balcony | | 45 | 45 | 11-Mar-21 | 12-May-21 |
| A31700 | Install Wall Tile | 10 | 10 | 11-Mar-21 | 24-Mar-21 |
| A31670 | Sprinkler Heads | 5 | 5 | 25-Mar-21 | 31-Mar-21 |
| A31680 | Lighting | 5 | 5 | 30-Mar-21 | 05-Apr-21 |
| A31690 | Fire Alarm Devices | 5 | 5 | 02-Apr-21 | 08-Apr-21 |
| A31740 | Install Doors & Hardware | 5 | 5 | 09-Apr-21 | 15-Apr-21 |
| A31710 | Seal Concrete Floors | 5 | 5 | 16-Apr-21 | 22-Apr-21 |
| A31720 | Electrical Trim-out | 5 | 5 | 23-Apr-21 | 29-Apr-21 |
| A31730 | Final MEPFP Inspections | 3 | 3 | 30-Apr-21 | 04-May-21 |
| A31750 | Final Paint | 4 | 4 | 30-Apr-21 | 05-May-21 |
| A31760 | Punchlist | 5 | 5 | 06-May-21 | 12-May-21 |
| Quad 2 | | 140 | 140 | 05-Nov-20 | 26-May-21 |
| MEPFP Mains Rough-in | | 41 | 41 | 05-Nov-20 | 07-Jan-21 |
| OHRI-EL-Q2-1 | Spray Fireproofing - First Pass - CL-N/S-E8/N8-E/W | 10 | 10 | 05-Nov-20 | 18-Nov-20 |
| OHRI-EL-Q2-1 | Install Subroof - CL-N/S-E8/N8-E/W | 15 | 15 | 19-Nov-20 | 11-Dec-20 |
| OHRI-EL-Q2-1 | Mechanical Mains - CL-N/S-E8/N8-E/W | 10 | 10 | 03-Dec-20 | 16-Dec-20 |
| OHRI-EL-Q2-1 | Electrical Mains - CL-N/S-E8/N8-E/W | 10 | 10 | 07-Dec-20 | 18-Dec-20 |
| OHRI-EL-Q2-1 | Plumbing Mains - CL-N/S-E8/N8-E/W | 10 | 10 | 09-Dec-20 | 22-Dec-20 |
| OHRI-EL-Q2-1 | Fire Protection Mains - CL-N/S-E8/N8-E/W | 10 | 10 | 11-Dec-20 | 28-Dec-20 |
| OHRI-EL-Q2-1 | Cable Tray AV/IT Mains - CL-N/S-E8/N8-E/W | 10 | 10 | 15-Dec-20 | 30-Dec-20 |
| OHRI-EL-Q2-1 | Spray Fireproofing - Final Pass - CL-N/S-E8/N8-E/W | 10 | 10 | 22-Dec-20 | 07-Jan-21 |
| Electrical & IT - Rooms 32.14 & 32.15 | | 52 | 52 | 29-Dec-20 | 11-Mar-21 |
| A24050 | Layout & Top Track | 1 | 1 | 29-Dec-20 | 29-Dec-20 |
| A24060 | Frame Walls | 2 | 2 | 30-Dec-20 | 31-Dec-20 |
| A24070 | Rough-in Electrical | 3 | 3 | 04-Jan-21 | 06-Jan-21 |
| A24080 | In-Wall Inspection | 1 | 1 | 07-Jan-21 | 07-Jan-21 |
| A24090 | In-Wall Insulation | 1 | 1 | 08-Jan-21 | 08-Jan-21 |
| A24100 | Hang, Tape & Finish Drywall | 4 | 4 | 11-Jan-21 | 14-Jan-21 |
| A24110 | OH Mechanical | 5 | 5 | 15-Jan-21 | 21-Jan-21 |
| A24140 | FRP Equipment Pads | 3 | 3 | 15-Jan-21 | 19-Jan-21 |
| A24120 | OH Electrical | 5 | 5 | 18-Jan-21 | 22-Jan-21 |
| A24130 | OH Fire Protection | 3 | 3 | 19-Jan-21 | 21-Jan-21 |
| A24240 | Prime Paint | 2 | 2 | 20-Jan-21 | 21-Jan-21 |
| A24150 | Set Transformers | 2 | 2 | 22-Jan-21 | 25-Jan-21 |

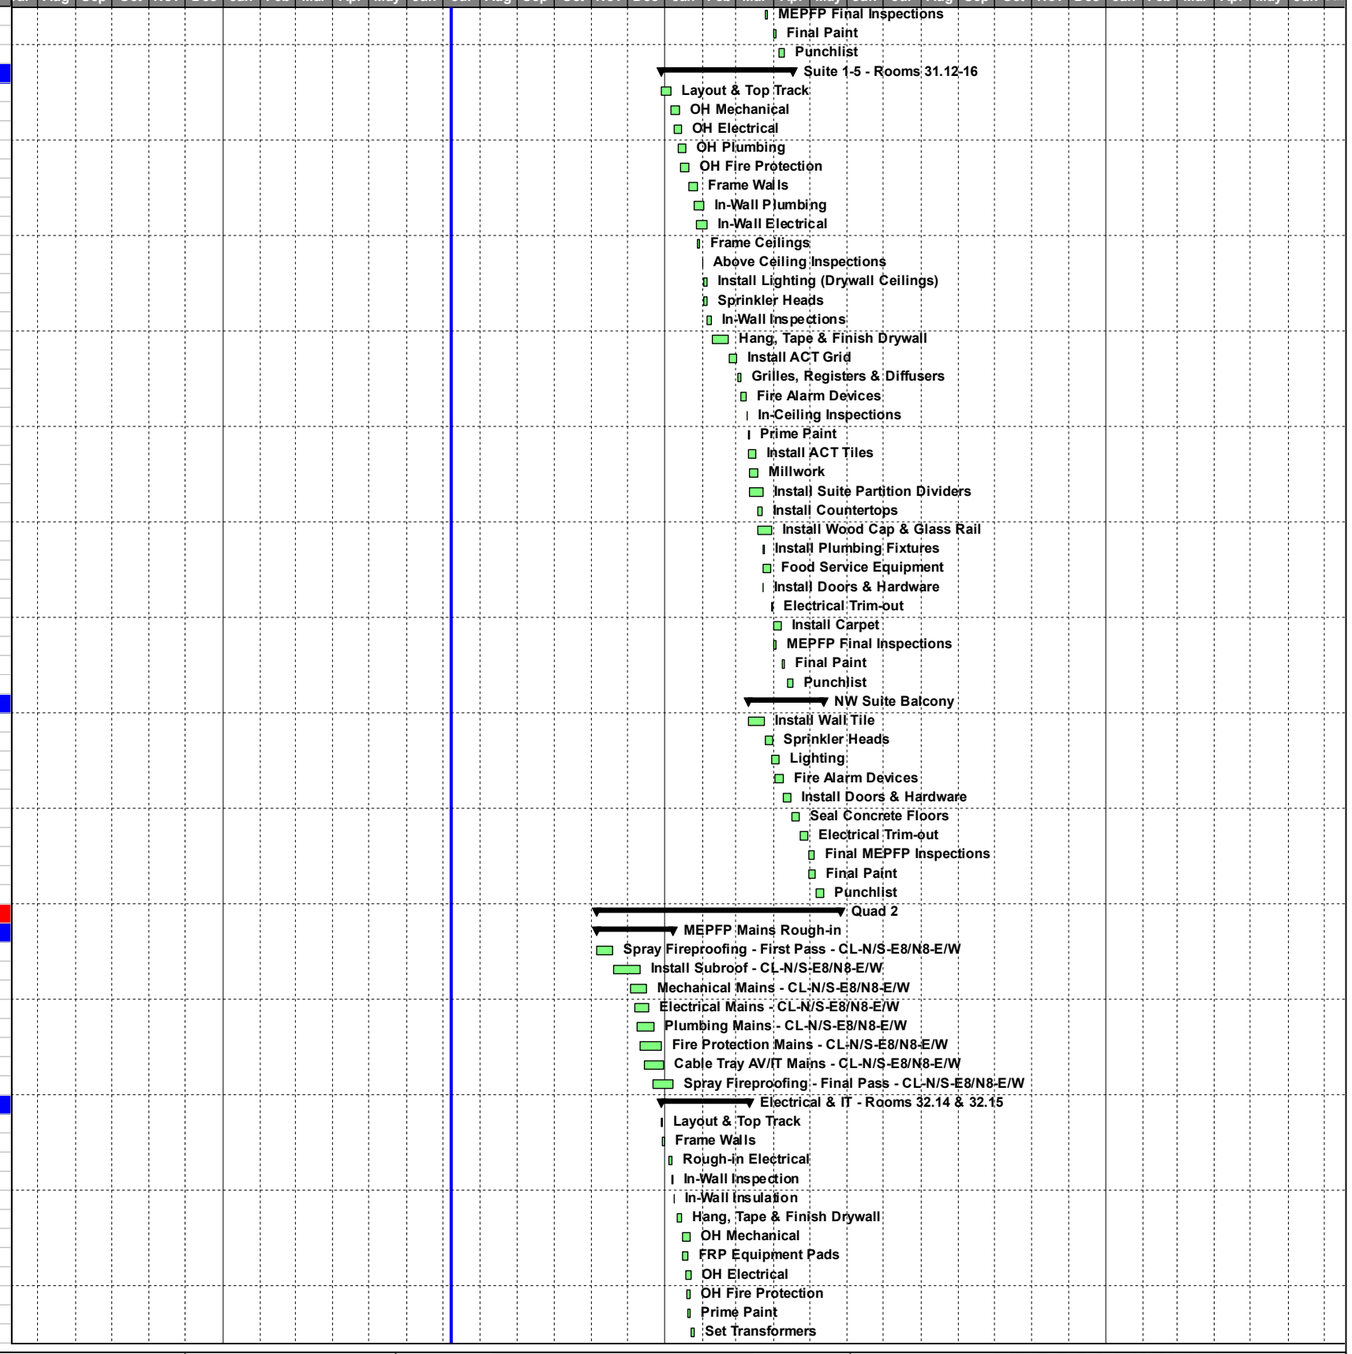

| Activity ID | Activity Name | Original Duration | Remaining Duration | Start | Finish |
|---|---|---|---|---|---|
| A24160 | Set IT Racks | 2 | 2 | 22-Jan-21 | 25-Jan-21 |
| A24170 | Set Panel Boxes | 2 | 2 | 22-Jan-21 | 25-Jan-21 |
| A24290 | Set AC Units | 2 | 2 | 22-Jan-21 | 25-Jan-21 |
| A24180 | Install Panel Interiors | 3 | 3 | 26-Jan-21 | 28-Jan-21 |
| A24200 | Pull Cable & Terminate | 15 | 15 | 26-Jan-21 | 15-Feb-21 |
| A24210 | Hook-up Transformers | 5 | 5 | 26-Jan-21 | 01-Feb-21 |
| A24260 | Install Doors & Hardware | 2 | 2 | 26-Jan-21 | 27-Jan-21 |
| A24300 | OH Mechanical Finishes | 2 | 2 | 26-Jan-21 | 27-Jan-21 |
| A24190 | Pull Wire & Terminate | 15 | 15 | 29-Jan-21 | 18-Feb-21 |
| A24220 | Install Lighting | 3 | 3 | 19-Feb-21 | 23-Feb-21 |
| A24230 | Install Electrical Finishes | 2 | 2 | 24-Feb-21 | 25-Feb-21 |
| A24310 | Install Fire Alarm Devices | 2 | 2 | 24-Feb-21 | 25-Feb-21 |
| A24250 | Seal Concrete Floors | 3 | 3 | 26-Feb-21 | 02-Mar-21 |
| A24320 | MEPFP Final Inspections | 2 | 2 | 26-Feb-21 | 01-Mar-21 |
| A24270 | Final Paint | 2 | 2 | 03-Mar-21 | 04-Mar-21 |
| A24280 | Punchlist | 5 | 5 | 05-Mar-21 | 11-Mar-21 |
| Family, Mens & Womens Restrooms - Rooms 32.12, 32.16-17 | | 91 | 91 | 29-Dec-20 | 05-May-21 |
| A25300 | Layout & Top Track | 2 | 2 | 29-Dec-20 | 30-Dec-20 |
| A25310 | OH Mechanical | 5 | 5 | 31-Dec-20 | 07-Jan-21 |
| A25320 | OH Electrical | 5 | 5 | 05-Jan-21 | 11-Jan-21 |
| A25330 | OH Plumbing | 5 | 5 | 07-Jan-21 | 13-Jan-21 |
| A25340 | OH Fire Protection | 5 | 5 | 11-Jan-21 | 15-Jan-21 |
| A25350 | Above Ceiling Inspections | 1 | 1 | 18-Jan-21 | 18-Jan-21 |
| A25360 | Frame Walls | 3 | 3 | 19-Jan-21 | 21-Jan-21 |
| A25370 | In-Wall Electrical | 5 | 5 | 22-Jan-21 | 28-Jan-21 |
| A25380 | In-Wall Plumbing | 8 | 8 | 22-Jan-21 | 02-Feb-21 |
| A25390 | In-Wall Inspections | 1 | 1 | 03-Feb-21 | 03-Feb-21 |
| A25400 | Hang Cement Board | 3 | 3 | 04-Feb-21 | 08-Feb-21 |
| A25410 | Frame Ceilings | 3 | 3 | 09-Feb-21 | 11-Feb-21 |
| A25420 | Install Lighting (Drywall Ceiling Area) | 2 | 2 | 12-Feb-21 | 15-Feb-21 |
| A25430 | Hang, Tape & Finish Drywall Ceilings | 5 | 5 | 16-Feb-21 | 22-Feb-21 |
| A25440 | Prime Paint | 2 | 2 | 23-Feb-21 | 24-Feb-21 |
| A25450 | Install Wall Tile | 7 | 7 | 25-Feb-21 | 05-Mar-21 |
| A25460 | Install Floor Tile | 5 | 5 | 08-Mar-21 | 12-Mar-21 |
| A25470 | Install ACT Grid | 2 | 2 | 15-Mar-21 | 16-Mar-21 |
| A25480 | Install Lighting | 2 | 2 | 17-Mar-21 | 18-Mar-21 |
| A25490 | Grilles, Registers & Diffusers | 2 | 2 | 18-Mar-21 | 19-Mar-21 |
| A25500 | Sprinkler Heads | 2 | 2 | 19-Mar-21 | 22-Mar-21 |
| A25510 | Fire Alarm Devices | 2 | 2 | 23-Mar-21 | 24-Mar-21 |
| A25520 | In-Ceiling Inspections | 1 | 1 | 25-Mar-21 | 25-Mar-21 |
| A25530 | Install ACT Tiles | 2 | 2 | 26-Mar-21 | 29-Mar-21 |
| A25540 | Install Toilets & Urinals | 5 | 5 | 30-Mar-21 | 05-Apr-21 |
| A25550 | Install Millwork | 4 | 4 | 06-Apr-21 | 09-Apr-21 |
| A25560 | Install Countertops | 2 | 2 | 12-Apr-21 | 13-Apr-21 |
| A25570 | Install Plumbing Fixtures | 2 | 2 | 14-Apr-21 | 15-Apr-21 |
| A25580 | Toilet Partitions | 3 | 3 | 16-Apr-21 | 20-Apr-21 |
| A25590 | Install Toilet Accessories | 2 | 2 | 21-Apr-21 | 22-Apr-21 |
| A25600 | Electrical Trim-out | 2 | 2 | 23-Apr-21 | 26-Apr-21 |
| A25610 | MEPFP Final Inspections | 2 | 2 | 27-Apr-21 | 28-Apr-21 |
| A25620 | Punchlist | 5 | 5 | 29-Apr-21 | 05-May-21 |
| Suite - 6-12 & Party Suite - Rooms 32.01-32.09 | | 106 | 106 | 29-Dec-20 | 26-May-21 |
| A25980 | Layout & Top Track | 5 | 5 | 29-Dec-20 | 05-Jan-21 |
| A25990 | OH Mechanical | 5 | 5 | 06-Jan-21 | 12-Jan-21 |
| A26000 | OH Electrical | 5 | 5 | 08-Jan-21 | 14-Jan-21 |
| A26010 | OH Plumbing | 5 | 5 | 12-Jan-21 | 18-Jan-21 |
| A26020 | OH Fire Protection | 5 | 5 | 14-Jan-21 | 20-Jan-21 |
| A26030 | Frame Walls | 5 | 5 | 21-Jan-21 | 27-Jan-21 |
| A26040 | In-Wall Plumbing | 7 | 7 | 25-Jan-21 | 02-Feb-21 |
| A26050 | In-Wall Electrical | 7 | 7 | 27-Jan-21 | 04-Feb-21 |
| A26060 | Frame Ceilings | 5 | 5 | 28-Jan-21 | 03-Feb-21 |
| A26070 | Above Ceiling Inspections | 1 | 1 | 04-Feb-21 | 04-Feb-21 |
| A26080 | Install Lighting (Drywall Ceilings) | 5 | 5 | 05-Feb-21 | 11-Feb-21 |
| A26090 | Sprinkler Heads | 5 | 5 | 05-Feb-21 | 11-Feb-21 |
| A26100 | In-Wall Inspections | 2 | 2 | 05-Feb-21 | 08-Feb-21 |
| A26110 | Hang, Tape & Finish Drywall | 13 | 13 | 12-Feb-21 | 02-Mar-21 |
| A26120 | Install ACT Grid | 5 | 5 | 03-Mar-21 | 09-Mar-21 |
| A26130 | Grilles, Registers & Diffusers | 3 | 3 | 10-Mar-21 | 12-Mar-21 |
| A26140 | Fire Alarm Devices | 5 | 5 | 15-Mar-21 | 19-Mar-21 |
| A26150 | In-Ceiling Inspections | 1 | 1 | 22-Mar-21 | 22-Mar-21 |
| A26160 | Prime Paint | 5 | 5 | 23-Mar-21 | 29-Mar-21 |

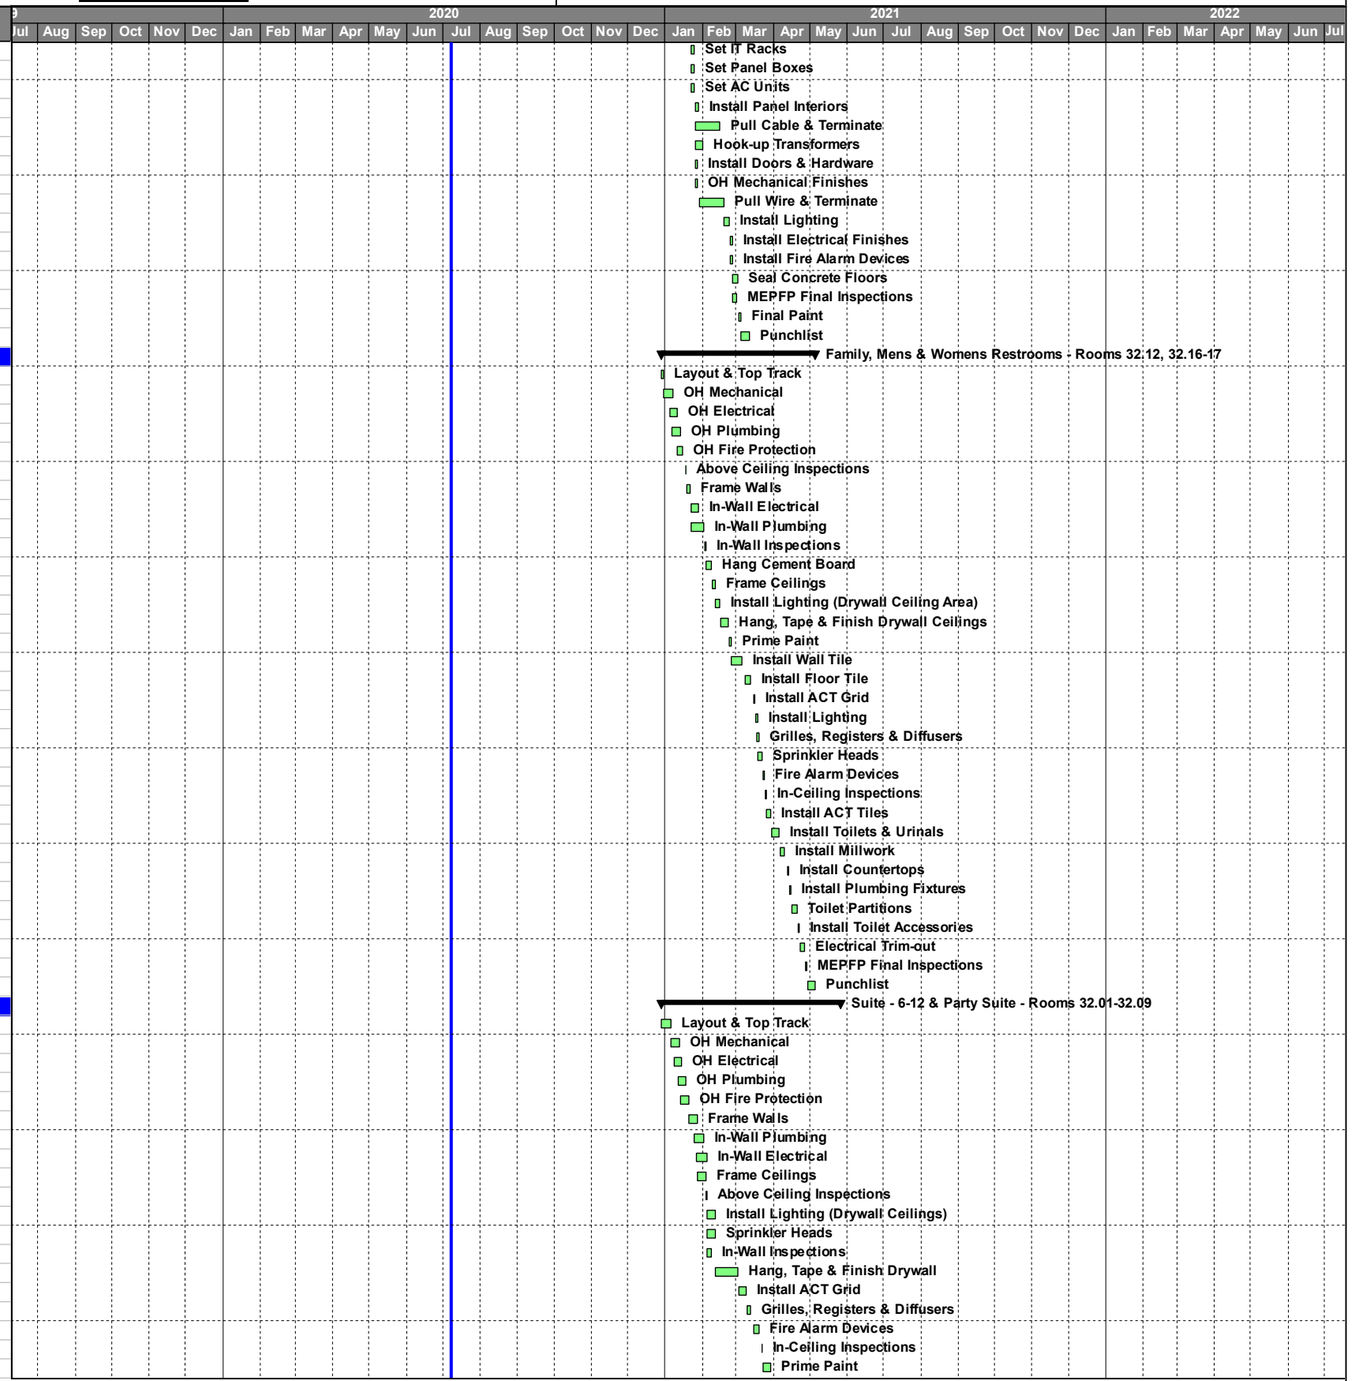

| Activity ID | Activity Name | Original Duration | Remaining Duration | Start | Finish |
|---|---|---|---|---|---|
| A26170 | Install ACT Tiles | 5 | 5 | 23-Mar-21 | 29-Mar-21 |
| A26180 | Millwork | 15 | 15 | 30-Mar-21 | 19-Apr-21 |
| A26190 | Install Suite Partition Dividers | 12 | 12 | 30-Mar-21 | 14-Apr-21 |
| A26210 | Install Wood Cap & Glass Rail | 10 | 10 | 06-Apr-21 | 19-Apr-21 |
| A26200 | Install Countertops | 2 | 2 | 20-Apr-21 | 21-Apr-21 |
| A26220 | Install Plumbing Fixtures | 5 | 5 | 22-Apr-21 | 28-Apr-21 |
| A26230 | Food Service Equipment | 5 | 5 | 22-Apr-21 | 28-Apr-21 |
| A26240 | Install Doors & Hardware | 1 | 1 | 22-Apr-21 | 22-Apr-21 |
| A26250 | Electrical Trim-out | 4 | 4 | 29-Apr-21 | 04-May-21 |
| A26260 | Install Carpet | 8 | 8 | 05-May-21 | 14-May-21 |
| A26270 | MEPFP Final Inspections | 2 | 2 | 05-May-21 | 06-May-21 |
| A26280 | Final Paint | 3 | 3 | 17-May-21 | 19-May-21 |
| A26290 | Punchlist | 5 | 5 | 20-May-21 | 26-May-21 |
| Suite Bar & Pantry Prep - Room 32.10-.11 | | 72 | 72 | 29-Dec-20 | 08-Apr-21 |
| A25630 | Layout & Top Track | 5 | 5 | 29-Dec-20 | 05-Jan-21 |
| A25640 | OH Mechanical | 4 | 4 | 06-Jan-21 | 11-Jan-21 |
| A25650 | OH Electrical | 4 | 4 | 08-Jan-21 | 13-Jan-21 |
| A25660 | OH Plumbing | 4 | 4 | 12-Jan-21 | 15-Jan-21 |
| A25670 | OH Fire Protection | 4 | 4 | 14-Jan-21 | 19-Jan-21 |
| A25680 | Frame Ceilings | 2 | 2 | 14-Jan-21 | 15-Jan-21 |
| A25690 | Install Exhaust Hood | 5 | 5 | 20-Jan-21 | 26-Jan-21 |
| A25700 | Frame Walls | 3 | 3 | 20-Jan-21 | 22-Jan-21 |
| A25710 | In-Wall Electrical | 5 | 5 | 25-Jan-21 | 29-Jan-21 |
| A25720 | In-Wall Plumbing | 5 | 5 | 26-Jan-21 | 01-Feb-21 |
| A25730 | Above Ceiling Inspections | 1 | 1 | 27-Jan-21 | 27-Jan-21 |
| A25740 | In-Wall Inspections | 1 | 1 | 02-Feb-21 | 02-Feb-21 |
| A25750 | Hang, Tape & Finish Drywall | 8 | 8 | 03-Feb-21 | 12-Feb-21 |
| A25760 | Prime Paint | 2 | 2 | 15-Feb-21 | 16-Feb-21 |
| A25770 | FRP Wall Panels | 3 | 3 | 17-Feb-21 | 19-Feb-21 |
| A25780 | Install ACT Grid | 1 | 1 | 22-Feb-21 | 22-Feb-21 |
| A25790 | Install Lighting (Grid Ceilings) | 2 | 2 | 23-Feb-21 | 24-Feb-21 |
| A25800 | Sprinkler Heads | 1 | 1 | 25-Feb-21 | 25-Feb-21 |
| A25810 | Grilles, Registers & Diffusers | 1 | 1 | 26-Feb-21 | 26-Feb-21 |
| A25820 | Fire Alarm Devices | 1 | 1 | 01-Mar-21 | 01-Mar-21 |
| A25830 | In-Ceiling Inspections | 1 | 1 | 02-Mar-21 | 02-Mar-21 |
| A25840 | Install ACT Tiles | 1 | 1 | 03-Mar-21 | 03-Mar-21 |
| A25850 | Resilient Flooring | 5 | 5 | 04-Mar-21 | 10-Mar-21 |
| A25860 | Install Floor Tile | 5 | 5 | 04-Mar-21 | 10-Mar-21 |
| A25870 | Millwork | 5 | 5 | 11-Mar-21 | 17-Mar-21 |
| A25880 | Install Doors & Hardware | 1 | 1 | 11-Mar-21 | 11-Mar-21 |
| A25890 | Install Plumbing Fixtures | 2 | 2 | 18-Mar-21 | 19-Mar-21 |
| A25900 | Install Countertops | 2 | 2 | 18-Mar-21 | 19-Mar-21 |
| A25910 | Install Wood Ceiling | 5 | 5 | 18-Mar-21 | 24-Mar-21 |
| A25920 | Food Service Equipment | 5 | 5 | 22-Mar-21 | 26-Mar-21 |
| A25930 | Install Lighting (Drywall Ceilings) | 2 | 2 | 25-Mar-21 | 26-Mar-21 |
| A25940 | Electrical Trim-out | 2 | 2 | 29-Mar-21 | 30-Mar-21 |
| A25950 | Final Paint | 2 | 2 | 31-Mar-21 | 01-Apr-21 |
| A25960 | MEPFP Final Inspections | 2 | 2 | 31-Mar-21 | 01-Apr-21 |
| A25970 | Punchlist | 5 | 5 | 02-Apr-21 | 08-Apr-21 |
| NE Suite Balcony | | 45 | 45 | 25-Mar-21 | 26-May-21 |
| A31800 | Install Wall Tile | 10 | 10 | 25-Mar-21 | 07-Apr-21 |
| A31770 | Sprinkler Heads | 5 | 5 | 08-Apr-21 | 14-Apr-21 |
| A31780 | Lighting | 5 | 5 | 13-Apr-21 | 19-Apr-21 |
| A31790 | Fire Alarm Devices | 5 | 5 | 16-Apr-21 | 22-Apr-21 |
| A31840 | Install Doors & Hardware | 5 | 5 | 23-Apr-21 | 29-Apr-21 |
| A31810 | Seal Concrete Floors | 5 | 5 | 30-Apr-21 | 06-May-21 |
| A31820 | Electrical Trim-out | 5 | 5 | 07-May-21 | 13-May-21 |
| A31830 | Final MEPFP Inspections | 3 | 3 | 14-May-21 | 18-May-21 |
| A31850 | Final Paint | 4 | 4 | 14-May-21 | 19-May-21 |
| A31860 | Punchlist | 5 | 5 | 20-May-21 | 26-May-21 |
| Overlook Level | | 130 | 130 | 05-Feb-21 | 09-Aug-21 |
| A29420 | Overlook Level Completion | 0 | 0 | | 09-Aug-21 |
| Quad 1 | | 117 | 117 | 24-Feb-21 | 09-Aug-21 |
| MEPFP Mains Rough-in | | 33 | 33 | 24-Feb-21 | 09-Apr-21 |
| OHRI-EL-Q1-1 | Spray Fireproofing - First Pass - CL-W10-N/S/N8-E/W | 10 | 10 | 24-Feb-21 | 09-Mar-21 |
| OHRI-EL-Q1-1 | Mechanical Mains - CL-W10-N/S/N8-E/W | 10 | 10 | 10-Mar-21 | 23-Mar-21 |
| OHRI-EL-Q1-1 | Electrical Mains - CL-W10-N/S/N8-E/W | 10 | 10 | 12-Mar-21 | 25-Mar-21 |
| OHRI-EL-Q1-1 | Plumbing Mains - CL-W10-N/S/N8-E/W | 10 | 10 | 16-Mar-21 | 29-Mar-21 |
| OHRI-EL-Q1-1 | Fire Protection Mains - CL-W10-N/S/N8-E/W | 10 | 10 | 18-Mar-21 | 31-Mar-21 |
| OHRI-EL-Q1-1 | Cable Tray AV/IT Mains - CL-W10-N/S/N8-E/W | 10 | 10 | 22-Mar-21 | 02-Apr-21 |

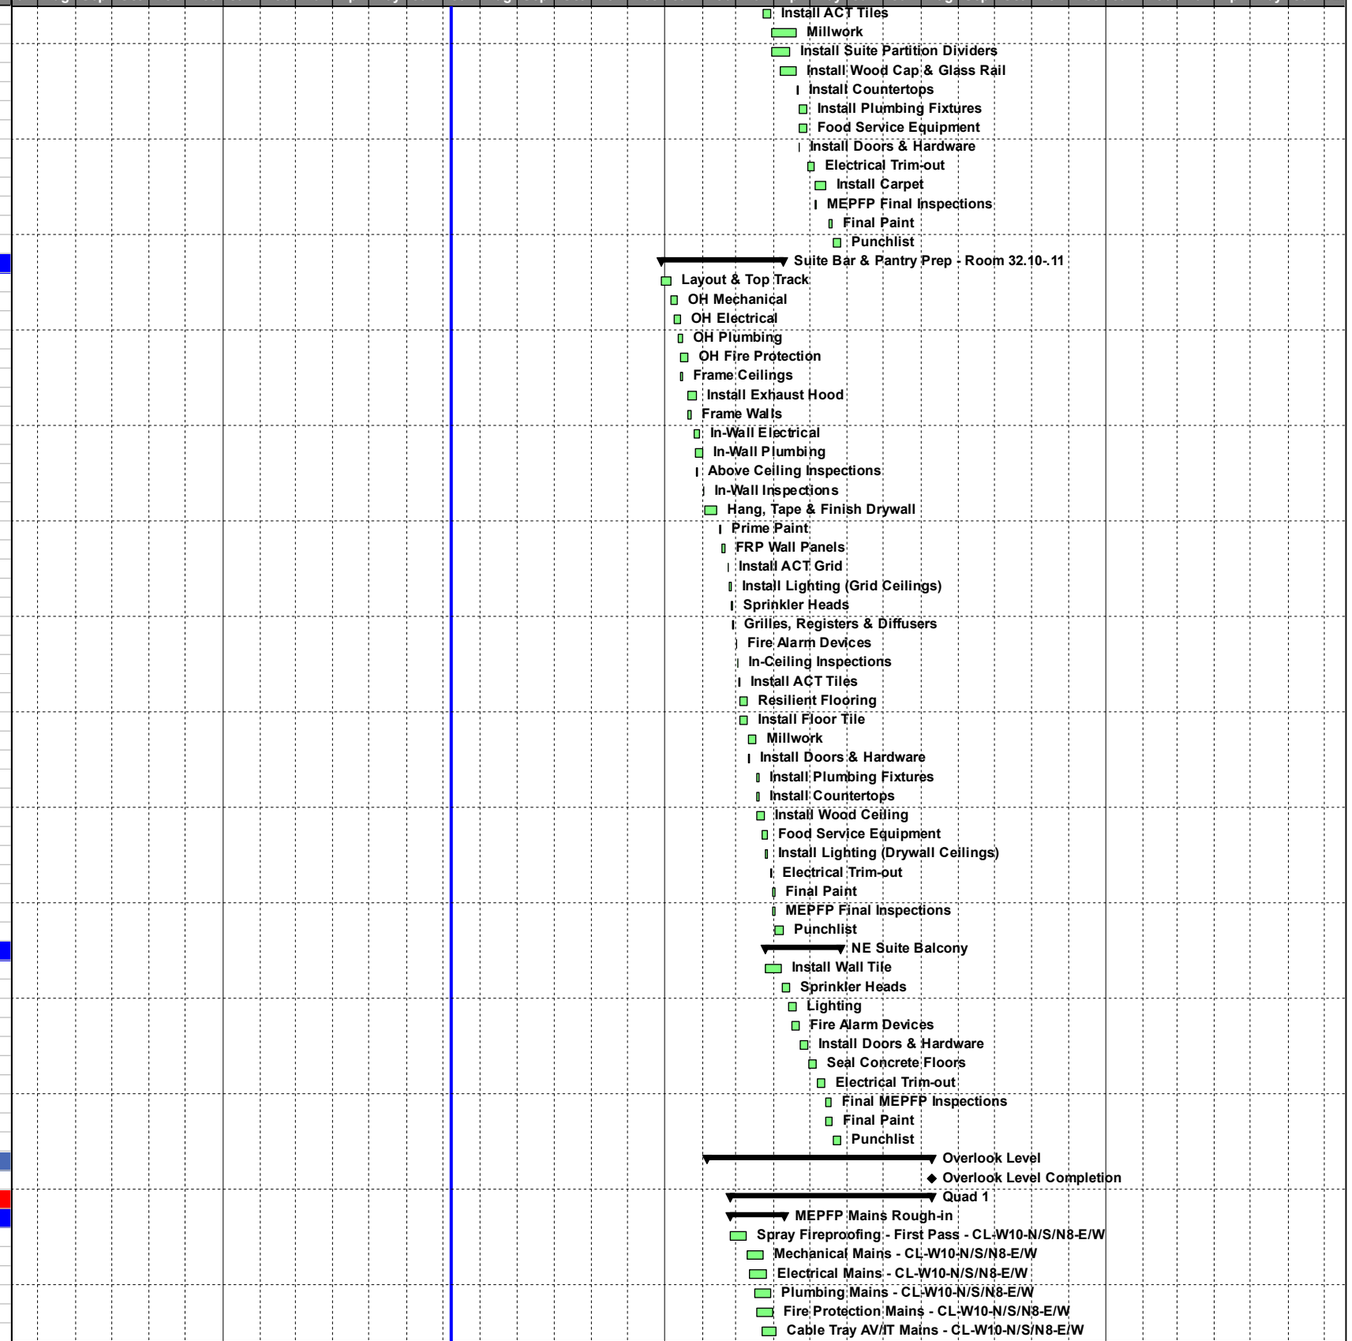

| Activity ID | Activity Name | Original Duration | Remaining Duration | Start | Finish |
|---|---|---|---|---|---|
| OHRI-EL-Q1-1 | Spray Fireproofing - Final Pass - CL-W10-N/S/N8-E/W | 10 | 10 | 29-Mar-21 | 09-Apr-21 |
| Electrical & IT - Rooms 41.04-05 | | 52 | 52 | 01-Apr-21 | 14-Jun-21 |
| A26300 | Layout & Top Track | 1 | 1 | 01-Apr-21 | 01-Apr-21 |
| A26310 | Frame Walls | 2 | 2 | 02-Apr-21 | 05-Apr-21 |
| A26320 | Rough-in Electrical | 3 | 3 | 06-Apr-21 | 08-Apr-21 |
| A26330 | In-Wall Inspection | 1 | 1 | 09-Apr-21 | 09-Apr-21 |
| A26340 | In-Wall Insulation | 1 | 1 | 12-Apr-21 | 12-Apr-21 |
| A26350 | Hang, Tape & Finish Drywall | 4 | 4 | 13-Apr-21 | 16-Apr-21 |
| A26360 | OH Mechanical | 5 | 5 | 19-Apr-21 | 23-Apr-21 |
| A26390 | FRP Equipment Pads | 3 | 3 | 19-Apr-21 | 21-Apr-21 |
| A26370 | OH Electrical | 5 | 5 | 20-Apr-21 | 26-Apr-21 |
| A26380 | OH Fire Protection | 3 | 3 | 21-Apr-21 | 23-Apr-21 |
| A26490 | Prime Paint | 2 | 2 | 22-Apr-21 | 23-Apr-21 |
| A26400 | Set Transformers | 2 | 2 | 26-Apr-21 | 27-Apr-21 |
| A26410 | Set IT Racks | 2 | 2 | 26-Apr-21 | 27-Apr-21 |
| A26420 | Set Panel Boxes | 2 | 2 | 26-Apr-21 | 27-Apr-21 |
| A26540 | Set AC Units | 2 | 2 | 26-Apr-21 | 27-Apr-21 |
| A26430 | Install Panel Interiors | 3 | 3 | 28-Apr-21 | 30-Apr-21 |
| A26450 | Pull Cable & Terminate | 15 | 15 | 28-Apr-21 | 18-May-21 |
| A26460 | Hook-up Transformers | 5 | 5 | 28-Apr-21 | 04-May-21 |
| A26510 | Install Doors & Hardware | 2 | 2 | 28-Apr-21 | 29-Apr-21 |
| A26550 | OH Mechanical Finishes | 2 | 2 | 28-Apr-21 | 29-Apr-21 |
| A26440 | Pull Wire & Terminate | 15 | 15 | 03-May-21 | 21-May-21 |
| A26470 | Install Lighting | 3 | 3 | 24-May-21 | 26-May-21 |
| A26480 | Install Electrical Finishes | 2 | 2 | 27-May-21 | 28-May-21 |
| A26560 | Install Fire Alarm Devices | 2 | 2 | 27-May-21 | 28-May-21 |
| A26500 | Seal Concrete Floors | 3 | 3 | 01-Jun-21 | 03-Jun-21 |
| A26570 | MEPFP Final Inspections | 2 | 2 | 01-Jun-21 | 02-Jun-21 |
| A26520 | Final Paint | 2 | 2 | 04-Jun-21 | 07-Jun-21 |
| A26530 | Punchlist | 5 | 5 | 08-Jun-21 | 14-Jun-21 |
| Family, Mens & Womens Restrooms - Rooms 41.06-08 | | 91 | 91 | 01-Apr-21 | 09-Aug-21 |
| A26580 | Layout & Top Track | 2 | 2 | 01-Apr-21 | 02-Apr-21 |
| A26590 | OH Mechanical | 5 | 5 | 05-Apr-21 | 09-Apr-21 |
| A26600 | OH Electrical | 5 | 5 | 07-Apr-21 | 13-Apr-21 |
| A26610 | OH Plumbing | 5 | 5 | 09-Apr-21 | 15-Apr-21 |
| A26620 | OH Fire Protection | 5 | 5 | 13-Apr-21 | 19-Apr-21 |
| A26630 | Above Ceiling Inspections | 1 | 1 | 20-Apr-21 | 20-Apr-21 |
| A26640 | Frame Walls | 3 | 3 | 21-Apr-21 | 23-Apr-21 |
| A26650 | In-Wall Electrical | 5 | 5 | 26-Apr-21 | 30-Apr-21 |
| A26660 | In-Wall Plumbing | 8 | 8 | 26-Apr-21 | 05-May-21 |
| A26670 | In-Wall Inspections | 1 | 1 | 06-May-21 | 06-May-21 |
| A26680 | Hang Cement Board | 3 | 3 | 07-May-21 | 11-May-21 |
| A26870 | Frame Ceilings | 3 | 3 | 12-May-21 | 14-May-21 |
| A26880 | Install Lighting (Drywall Ceiling Area) | 2 | 2 | 17-May-21 | 18-May-21 |
| A26890 | Hang, Tape & Finish Drywall Ceilings | 5 | 5 | 19-May-21 | 25-May-21 |
| A26900 | Prime Paint | 2 | 2 | 26-May-21 | 27-May-21 |
| A26690 | Install Wall Tile | 7 | 7 | 28-May-21 | 08-Jun-21 |
| A26760 | Install Floor Tile | 5 | 5 | 09-Jun-21 | 15-Jun-21 |
| A26700 | Install ACT Grid | 2 | 2 | 16-Jun-21 | 17-Jun-21 |
| A26710 | Install Lighting | 2 | 2 | 18-Jun-21 | 21-Jun-21 |
| A26720 | Grilles, Registers & Diffusers | 2 | 2 | 21-Jun-21 | 22-Jun-21 |
| A26730 | Sprinkler Heads | 2 | 2 | 22-Jun-21 | 23-Jun-21 |
| A26740 | Fire Alarm Devices | 2 | 2 | 24-Jun-21 | 25-Jun-21 |
| A26750 | In-Ceiling Inspections | 1 | 1 | 28-Jun-21 | 28-Jun-21 |
| A26770 | Install ACT Tiles | 2 | 2 | 29-Jun-21 | 30-Jun-21 |
| A26780 | Install Toilets & Urinals | 5 | 5 | 01-Jul-21 | 08-Jul-21 |
| A26790 | Install Millwork | 4 | 4 | 09-Jul-21 | 14-Jul-21 |
| A26800 | Install Countertops | 2 | 2 | 15-Jul-21 | 16-Jul-21 |
| A26810 | Install Plumbing Fixtures | 2 | 2 | 19-Jul-21 | 20-Jul-21 |
| A26820 | Toilet Partitions | 3 | 3 | 21-Jul-21 | 23-Jul-21 |
| A26830 | Install Toilet Accessories | 2 | 2 | 26-Jul-21 | 27-Jul-21 |
| A26840 | Electrical Trim-out | 2 | 2 | 28-Jul-21 | 29-Jul-21 |
| A26850 | MEPFP Final Inspections | 2 | 2 | 30-Jul-21 | 02-Aug-21 |
| A26860 | Punchlist | 5 | 5 | 03-Aug-21 | 09-Aug-21 |
| NW Overlook Bar - Room 41.01-02 | | 72 | 72 | 01-Apr-21 | 13-Jul-21 |
| A27200 | Layout & Top Track | 5 | 5 | 01-Apr-21 | 07-Apr-21 |
| A26910 | OH Mechanical | 4 | 4 | 08-Apr-21 | 13-Apr-21 |
| A26920 | OH Electrical | 4 | 4 | 12-Apr-21 | 15-Apr-21 |
| A26930 | OH Plumbing | 4 | 4 | 14-Apr-21 | 19-Apr-21 |
| A26940 | OH Fire Protection | 4 | 4 | 16-Apr-21 | 21-Apr-21 |

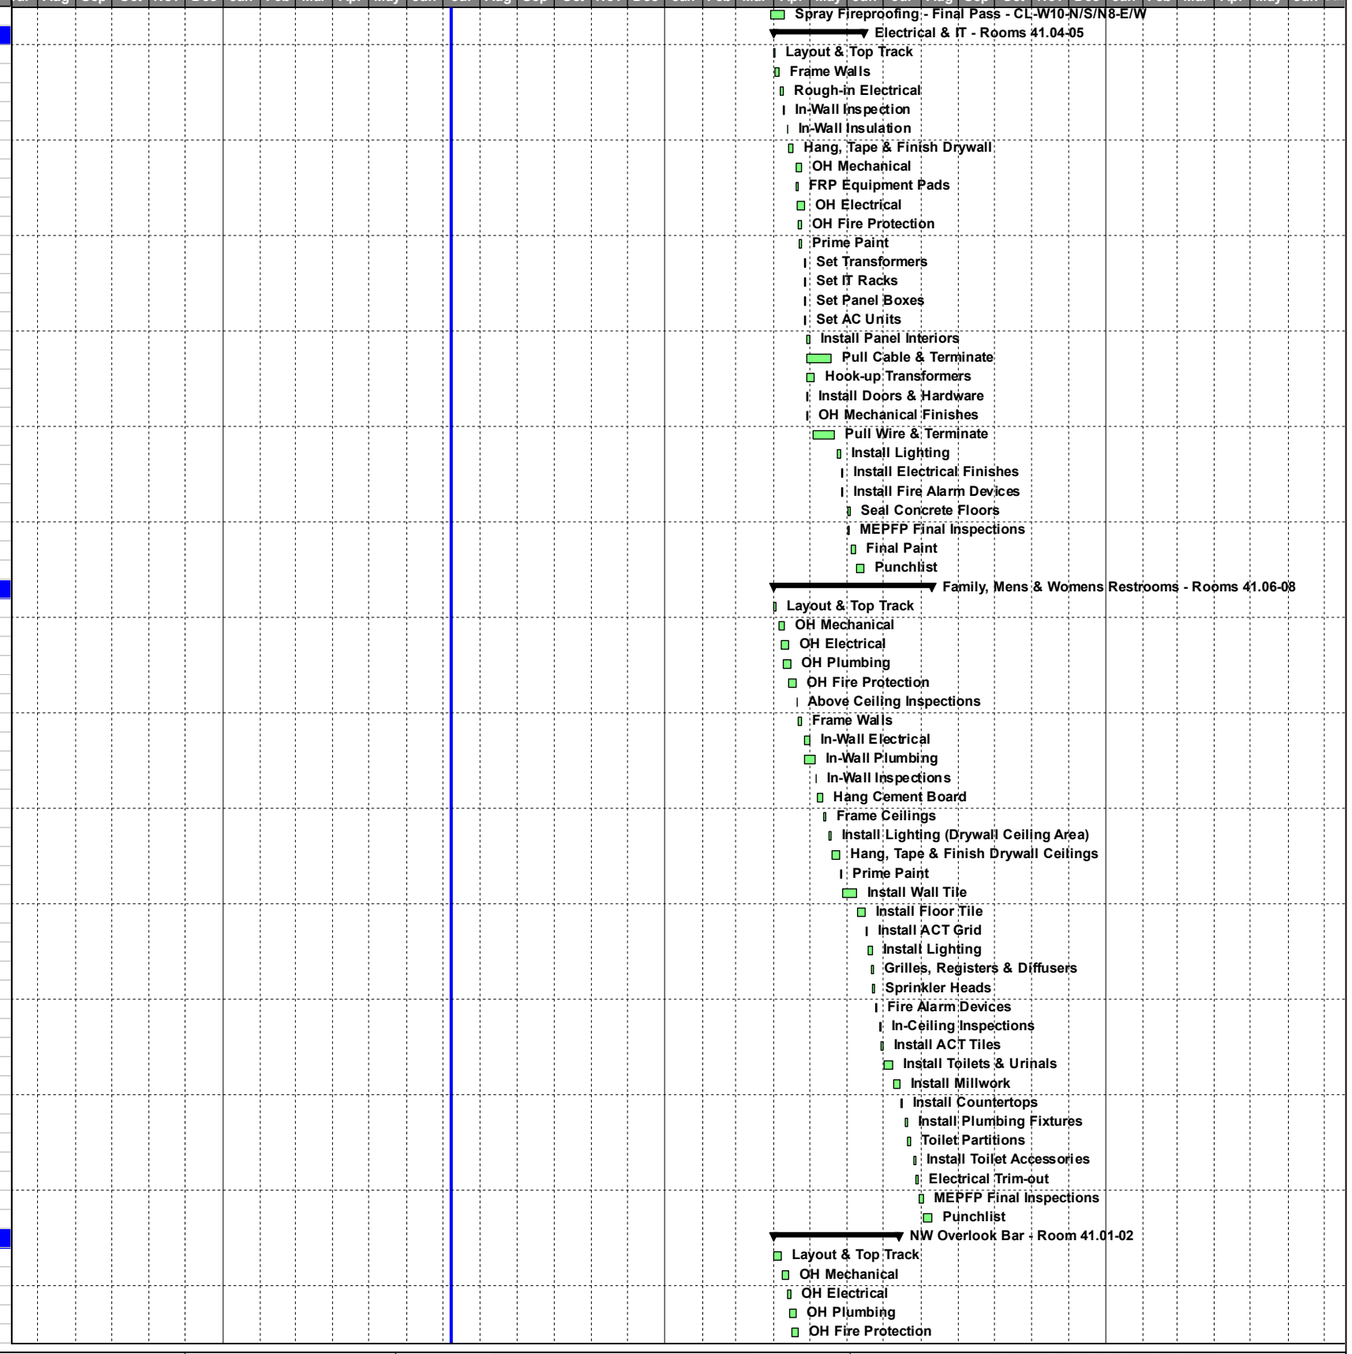

| Activity ID | Activity Name | Original Duration | Remaining Duration | Start | Finish |
|---|---|---|---|---|---|
| A26990 | Frame Ceilings | 2 | 2 | 16-Apr-21 | 19-Apr-21 |
| A26950 | Install Exhaust Hood | 5 | 5 | 22-Apr-21 | 28-Apr-21 |
| A27220 | Frame Walls | 3 | 3 | 22-Apr-21 | 26-Apr-21 |
| A27230 | In-Wall Electrical | 5 | 5 | 27-Apr-21 | 03-May-21 |
| A27240 | In-Wall Plumbing | 5 | 5 | 28-Apr-21 | 04-May-21 |
| A26960 | Above Ceiling Inspections | 1 | 1 | 29-Apr-21 | 29-Apr-21 |
| A27250 | In-Wall Inspections | 1 | 1 | 05-May-21 | 05-May-21 |
| A27010 | Hang, Tape & Finish Drywall | 8 | 8 | 06-May-21 | 17-May-21 |
| A26970 | Prime Paint | 2 | 2 | 18-May-21 | 19-May-21 |
| A27070 | FRP Wall Panels | 3 | 3 | 20-May-21 | 24-May-21 |
| A26980 | Install ACT Grid | 1 | 1 | 25-May-21 | 25-May-21 |
| A27020 | Install Lighting (Grid Ceilings) | 2 | 2 | 26-May-21 | 27-May-21 |
| A27030 | Sprinkler Heads | 1 | 1 | 28-May-21 | 28-May-21 |
| A27040 | Grilles, Registers & Diffusers | 1 | 1 | 01-Jun-21 | 01-Jun-21 |
| A27050 | Fire Alarm Devices | 1 | 1 | 02-Jun-21 | 02-Jun-21 |
| A27180 | In-Ceiling Inspections | 1 | 1 | 03-Jun-21 | 03-Jun-21 |
| A27060 | Install ACT Tiles | 1 | 1 | 04-Jun-21 | 04-Jun-21 |
| A27080 | Resilient Flooring | 5 | 5 | 07-Jun-21 | 11-Jun-21 |
| A27160 | Install Floor Tile | 5 | 5 | 07-Jun-21 | 11-Jun-21 |
| A27120 | Millwork | 5 | 5 | 14-Jun-21 | 18-Jun-21 |
| A27190 | Install Doors & Hardware | 1 | 1 | 14-Jun-21 | 14-Jun-21 |
| A27090 | Install Plumbing Fixtures | 2 | 2 | 21-Jun-21 | 22-Jun-21 |
| A27170 | Install Countertops | 2 | 2 | 21-Jun-21 | 22-Jun-21 |
| A27210 | Install Wood Ceiling | 5 | 5 | 21-Jun-21 | 25-Jun-21 |
| A27110 | Food Service Equipment | 5 | 5 | 23-Jun-21 | 29-Jun-21 |
| A27000 | Install Lighting (Drywall Ceilings) | 2 | 2 | 28-Jun-21 | 29-Jun-21 |
| A27100 | Electrical Trim-out | 2 | 2 | 30-Jun-21 | 01-Jul-21 |
| A27130 | Final Paint | 2 | 2 | 02-Jul-21 | 06-Jul-21 |
| A27140 | MEPFP Final Inspections | 2 | 2 | 02-Jul-21 | 06-Jul-21 |
| A27150 | Punchlist | 5 | 5 | 07-Jul-21 | 13-Jul-21 |
| AV Control, TV, Radio/Press - Rooms - 41.09-13 | | 70 | 70 | 01-Apr-21 | 09-Jul-21 |
| A27260 | Layout & Top Track | 2 | 2 | 01-Apr-21 | 02-Apr-21 |
| A27270 | OH Mechanical | 5 | 5 | 05-Apr-21 | 09-Apr-21 |
| A27280 | OH Electrical | 5 | 5 | 07-Apr-21 | 13-Apr-21 |
| A27290 | OH Plumbing | 5 | 5 | 09-Apr-21 | 15-Apr-21 |
| A27300 | OH Fire Protection | 5 | 5 | 13-Apr-21 | 19-Apr-21 |
| A27310 | Above Ceiling Inspections | 1 | 1 | 20-Apr-21 | 20-Apr-21 |
| A27320 | Frame Walls | 3 | 3 | 21-Apr-21 | 23-Apr-21 |
| A27330 | In-Wall Plumbing | 3 | 3 | 26-Apr-21 | 28-Apr-21 |
| A27340 | In-Wall Electrical | 5 | 5 | 28-Apr-21 | 04-May-21 |
| A27350 | In-Wall Inspections | 1 | 1 | 05-May-21 | 05-May-21 |
| A27360 | Hang, Tape & Finish Drywall | 6 | 6 | 06-May-21 | 13-May-21 |
| A27370 | Epoxy Walls | 2 | 2 | 14-May-21 | 17-May-21 |
| A27410 | Prime Paint | 2 | 2 | 14-May-21 | 17-May-21 |
| A27380 | Install Floor Tile | 2 | 2 | 18-May-21 | 19-May-21 |
| A27420 | Install ACT Grid | 2 | 2 | 18-May-21 | 19-May-21 |
| A27390 | Install Plumbing Fixtures | 2 | 2 | 20-May-21 | 21-May-21 |
| A27430 | Install Lighting | 4 | 4 | 20-May-21 | 25-May-21 |
| A27570 | Fire Alarm Devices | 3 | 3 | 20-May-21 | 24-May-21 |
| A27400 | Install Toilet Accessories | 1 | 1 | 24-May-21 | 24-May-21 |
| A27440 | Sprinkler Heads | 2 | 2 | 26-May-21 | 27-May-21 |
| A27450 | Grilles, Registers & Diffusers | 2 | 2 | 28-May-21 | 01-Jun-21 |
| A27460 | Grid Inspections | 1 | 1 | 02-Jun-21 | 02-Jun-21 |
| A27470 | Install ACT Tiles | 1 | 1 | 03-Jun-21 | 03-Jun-21 |
| A27480 | Install Millwork | 5 | 5 | 04-Jun-21 | 10-Jun-21 |
| A27490 | Install Countertops | 2 | 2 | 11-Jun-21 | 14-Jun-21 |
| A27500 | Install Doors & Hardware | 2 | 2 | 15-Jun-21 | 16-Jun-21 |
| A27560 | Electrical Trim-out | 3 | 3 | 15-Jun-21 | 17-Jun-21 |
| A27510 | Seal Concrete Floors | 5 | 5 | 17-Jun-21 | 23-Jun-21 |
| A27540 | MEPFP Final Inspections | 2 | 2 | 18-Jun-21 | 21-Jun-21 |
| A27520 | Install Carpet | 4 | 4 | 24-Jun-21 | 29-Jun-21 |
| A27530 | Final Paint | 2 | 2 | 30-Jun-21 | 01-Jul-21 |
| A27550 | Punchlist | 5 | 5 | 02-Jul-21 | 09-Jul-21 |
| Quad 2 | | 125 | 125 | 05-Feb-21 | 02-Aug-21 |
| MEPFP Mains Rough-in | | 41 | 41 | 05-Feb-21 | 02-Apr-21 |
| OHRI-EL-Q2-1 | Spray Fireproofing - First Pass - CL-N/S-E8/N8-E/W | 10 | 10 | 05-Feb-21 | 18-Feb-21 |
| OHRI-EL-Q2-1 | Install Subroof - CL-N/S-E8/N8-E/W | 15 | 15 | 19-Feb-21 | 11-Mar-21 |
| OHRI-EL-Q2-1 | Mechanical Mains - CL-N/S-E8/N8-E/W | 10 | 10 | 03-Mar-21 | 16-Mar-21 |
| OHRI-EL-Q2-1 | Electrical Mains - CL-N/S-E8/N8-E/W | 10 | 10 | 05-Mar-21 | 18-Mar-21 |
| OHRI-EL-Q2-1 | Plumbing Mains - CL-N/S-E8/N8-E/W | 10 | 10 | 09-Mar-21 | 22-Mar-21 |

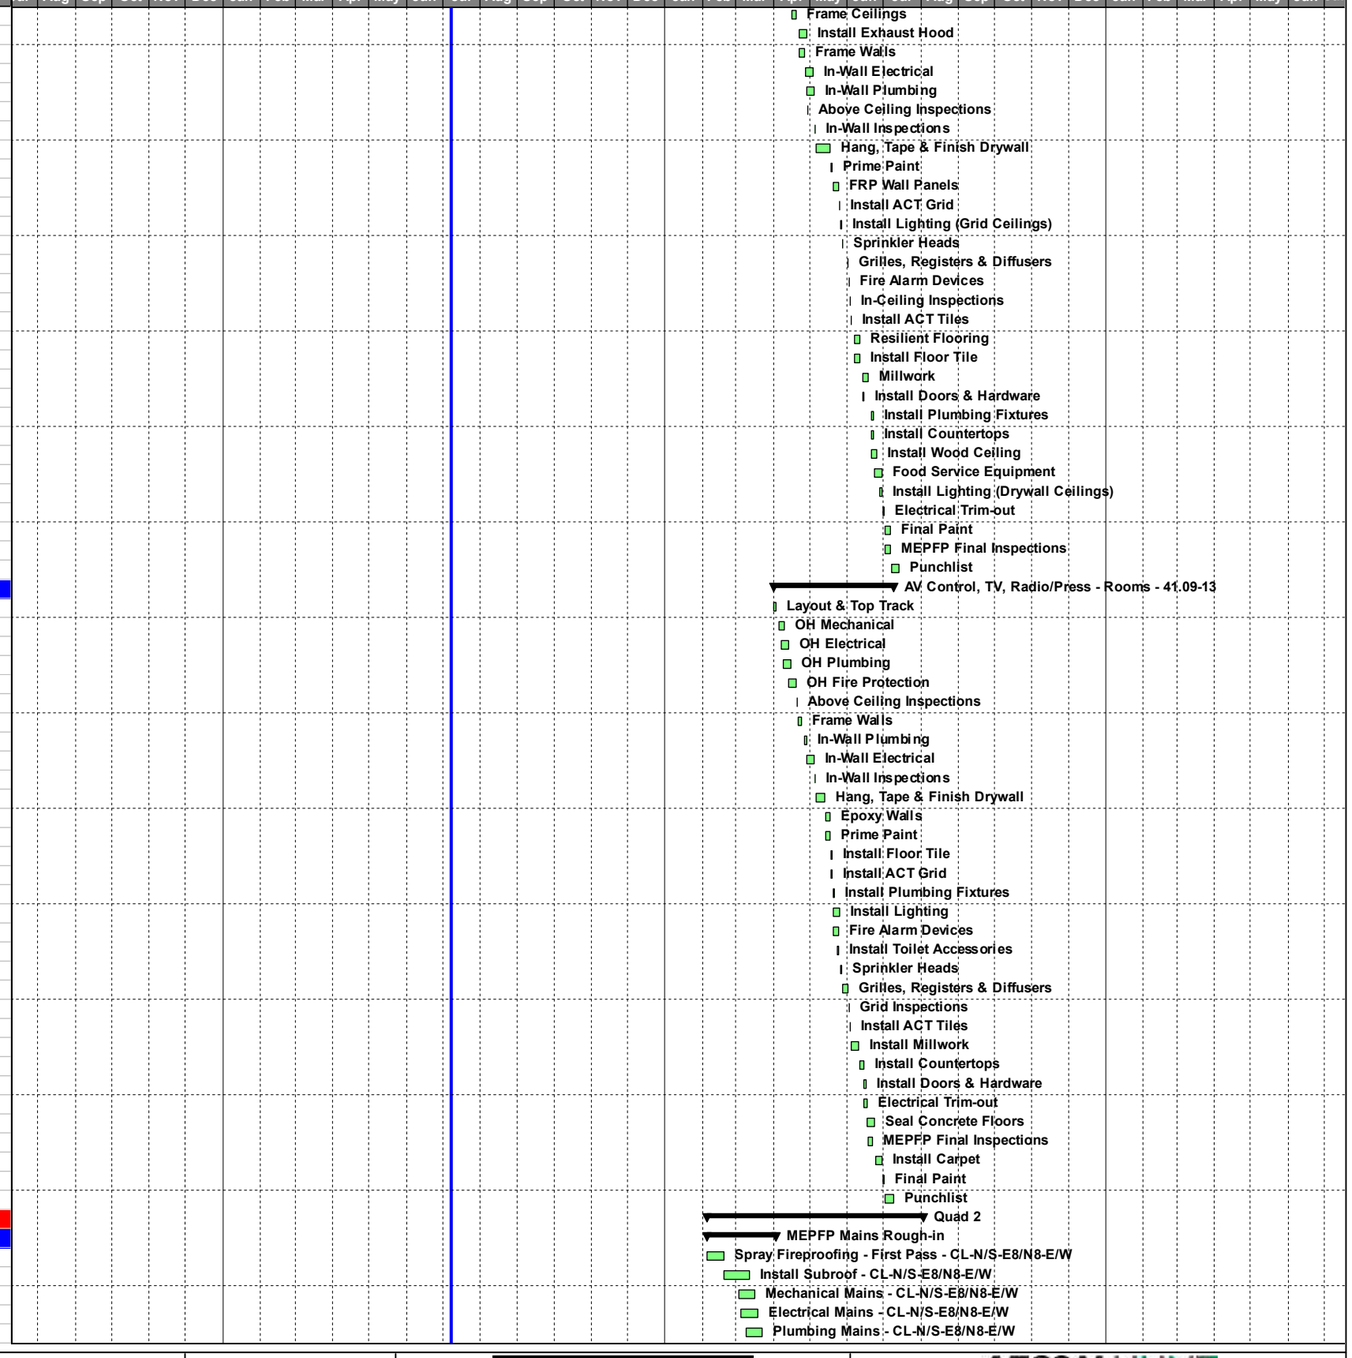


Remaining Level of Effort | Remainin...
Actual Level of Effort | Critical R...
Actual Work | Milestone



AECOM HUNT
in association with
Brownstone Construction Group
Pat Mathis Construction Company
A. Riley Consultants

| Activity ID | Activity Name | Original Duration | Remaining Duration | Start | Finish |
|---|---|---|---|---|---|
| OHRI-EL-Q2-1 | Fire Protection Mains - CL-N/S-E8/N8-E/W | 10 | 10 | 11-Mar-21 | 24-Mar-21 |
| OHRI-EL-Q2-1 | Cable Tray AV/IT Mains - CL-N/S-E8/N8-E/W | 10 | 10 | 15-Mar-21 | 26-Mar-21 |
| OHRI-EL-Q2-1 | Spray Fireproofing - Final Pass - CL-N/S-E8/N8-E/W | 10 | 10 | 22-Mar-21 | 02-Apr-21 |
| Electrical & IT - Rooms 42.11-12 | | 52 | 52 | 25-Mar-21 | 07-Jun-21 |
| A27580 | Layout & Top Track | 1 | 1 | 25-Mar-21 | 25-Mar-21 |
| A27590 | Frame Walls | 2 | 2 | 26-Mar-21 | 29-Mar-21 |
| A27600 | Rough-in Electrical | 3 | 3 | 30-Mar-21 | 01-Apr-21 |
| A27610 | In-Wall Inspection | 1 | 1 | 02-Apr-21 | 02-Apr-21 |
| A27620 | In-Wall Insulation | 1 | 1 | 05-Apr-21 | 05-Apr-21 |
| A27630 | Hang, Tape & Finish Drywall | 4 | 4 | 06-Apr-21 | 09-Apr-21 |
| A27640 | OH Mechanical | 5 | 5 | 12-Apr-21 | 16-Apr-21 |
| A27670 | FRP Equipment Pads | 3 | 3 | 12-Apr-21 | 14-Apr-21 |
| A27650 | OH Electrical | 5 | 5 | 13-Apr-21 | 19-Apr-21 |
| A27660 | OH Fire Protection | 3 | 3 | 14-Apr-21 | 16-Apr-21 |
| A27770 | Prime Paint | 2 | 2 | 15-Apr-21 | 16-Apr-21 |
| A27680 | Set Transformers | 2 | 2 | 19-Apr-21 | 20-Apr-21 |
| A27690 | Set IT Racks | 2 | 2 | 19-Apr-21 | 20-Apr-21 |
| A27700 | Set Panel Boxes | 2 | 2 | 19-Apr-21 | 20-Apr-21 |
| A27820 | Set AC Units | 2 | 2 | 19-Apr-21 | 20-Apr-21 |
| A27710 | Install Panel Interiors | 3 | 3 | 21-Apr-21 | 23-Apr-21 |
| A27730 | Pull Cable & Terminate | 15 | 15 | 21-Apr-21 | 11-May-21 |
| A27740 | Hook-up Transformers | 5 | 5 | 21-Apr-21 | 27-Apr-21 |
| A27790 | Install Doors & Hardware | 2 | 2 | 21-Apr-21 | 22-Apr-21 |
| A27830 | OH Mechanical Finishes | 2 | 2 | 21-Apr-21 | 22-Apr-21 |
| A27720 | Pull Wire & Terminate | 15 | 15 | 26-Apr-21 | 14-May-21 |
| A27750 | Install Lighting | 3 | 3 | 17-May-21 | 19-May-21 |
| A27760 | Install Electrical Finishes | 2 | 2 | 20-May-21 | 21-May-21 |
| A27840 | Install Fire Alarm Devices | 2 | 2 | 20-May-21 | 21-May-21 |
| A27780 | Seal Concrete Floors | 3 | 3 | 24-May-21 | 26-May-21 |
| A27850 | MEPFP Final Inspections | 2 | 2 | 24-May-21 | 25-May-21 |
| A27800 | Final Paint | 2 | 2 | 27-May-21 | 28-May-21 |
| A27810 | Punchlist | 5 | 5 | 01-Jun-21 | 07-Jun-21 |
| Family, Mens & Womens Restrooms - Rooms 42.06, 08, 09, & 13 | | 91 | 91 | 25-Mar-21 | 02-Aug-21 |
| A27860 | Layout & Top Track | 2 | 2 | 25-Mar-21 | 26-Mar-21 |
| A27870 | OH Mechanical | 5 | 5 | 29-Mar-21 | 02-Apr-21 |
| A27880 | OH Electrical | 5 | 5 | 31-Mar-21 | 06-Apr-21 |
| A27890 | OH Plumbing | 5 | 5 | 02-Apr-21 | 08-Apr-21 |
| A27900 | OH Fire Protection | 5 | 5 | 06-Apr-21 | 12-Apr-21 |
| A27910 | Above Ceiling Inspections | 1 | 1 | 13-Apr-21 | 13-Apr-21 |
| A27920 | Frame Walls | 3 | 3 | 14-Apr-21 | 16-Apr-21 |
| A27930 | In-Wall Electrical | 5 | 5 | 19-Apr-21 | 23-Apr-21 |
| A27940 | In-Wall Plumbing | 8 | 8 | 19-Apr-21 | 28-Apr-21 |
| A27950 | In-Wall Inspections | 1 | 1 | 29-Apr-21 | 29-Apr-21 |
| A27960 | Hang Cement Board | 3 | 3 | 30-Apr-21 | 04-May-21 |
| A28150 | Frame Ceilings | 3 | 3 | 05-May-21 | 07-May-21 |
| A28160 | Install Lighting (Drywall Ceiling Area) | 2 | 2 | 10-May-21 | 11-May-21 |
| A28170 | Hang, Tape & Finish Drywall Ceilings | 5 | 5 | 12-May-21 | 18-May-21 |
| A28180 | Prime Paint | 2 | 2 | 19-May-21 | 20-May-21 |
| A27970 | Install Wall Tile | 7 | 7 | 21-May-21 | 01-Jun-21 |
| A28040 | Install Floor Tile | 5 | 5 | 02-Jun-21 | 08-Jun-21 |
| A27980 | Install ACT Grid | 2 | 2 | 09-Jun-21 | 10-Jun-21 |
| A27990 | Install Lighting | 2 | 2 | 11-Jun-21 | 14-Jun-21 |
| A28000 | Grilles, Registers & Diffusers | 2 | 2 | 14-Jun-21 | 15-Jun-21 |
| A28010 | Sprinkler Heads | 2 | 2 | 15-Jun-21 | 16-Jun-21 |
| A28020 | Fire Alarm Devices | 2 | 2 | 17-Jun-21 | 18-Jun-21 |
| A28030 | In-Ceiling Inspections | 1 | 1 | 21-Jun-21 | 21-Jun-21 |
| A28050 | Install ACT Tiles | 2 | 2 | 22-Jun-21 | 23-Jun-21 |
| A28060 | Install Toilets & Urinals | 5 | 5 | 24-Jun-21 | 30-Jun-21 |
| A28070 | Install Millwork | 4 | 4 | 01-Jul-21 | 07-Jul-21 |
| A28080 | Install Countertops | 2 | 2 | 08-Jul-21 | 09-Jul-21 |
| A28090 | Install Plumbing Fixtures | 2 | 2 | 12-Jul-21 | 13-Jul-21 |
| A28100 | Toilet Partitions | 3 | 3 | 14-Jul-21 | 16-Jul-21 |
| A28110 | Install Toilet Accessories | 2 | 2 | 19-Jul-21 | 20-Jul-21 |
| A28120 | Electrical Trim-out | 2 | 2 | 21-Jul-21 | 22-Jul-21 |
| A28130 | MEPFP Final Inspections | 2 | 2 | 23-Jul-21 | 26-Jul-21 |
| A28140 | Punchlist | 5 | 5 | 27-Jul-21 | 02-Aug-21 |
| Bar, Pantry & Keg Storage - Room 42.07, 10 & 16 | | 72 | 72 | 25-Mar-21 | 06-Jul-21 |
| A28480 | Layout & Top Track | 5 | 5 | 25-Mar-21 | 31-Mar-21 |
| A28190 | OH Mechanical | 4 | 4 | 01-Apr-21 | 06-Apr-21 |
| A28200 | OH Electrical | 4 | 4 | 05-Apr-21 | 08-Apr-21 |

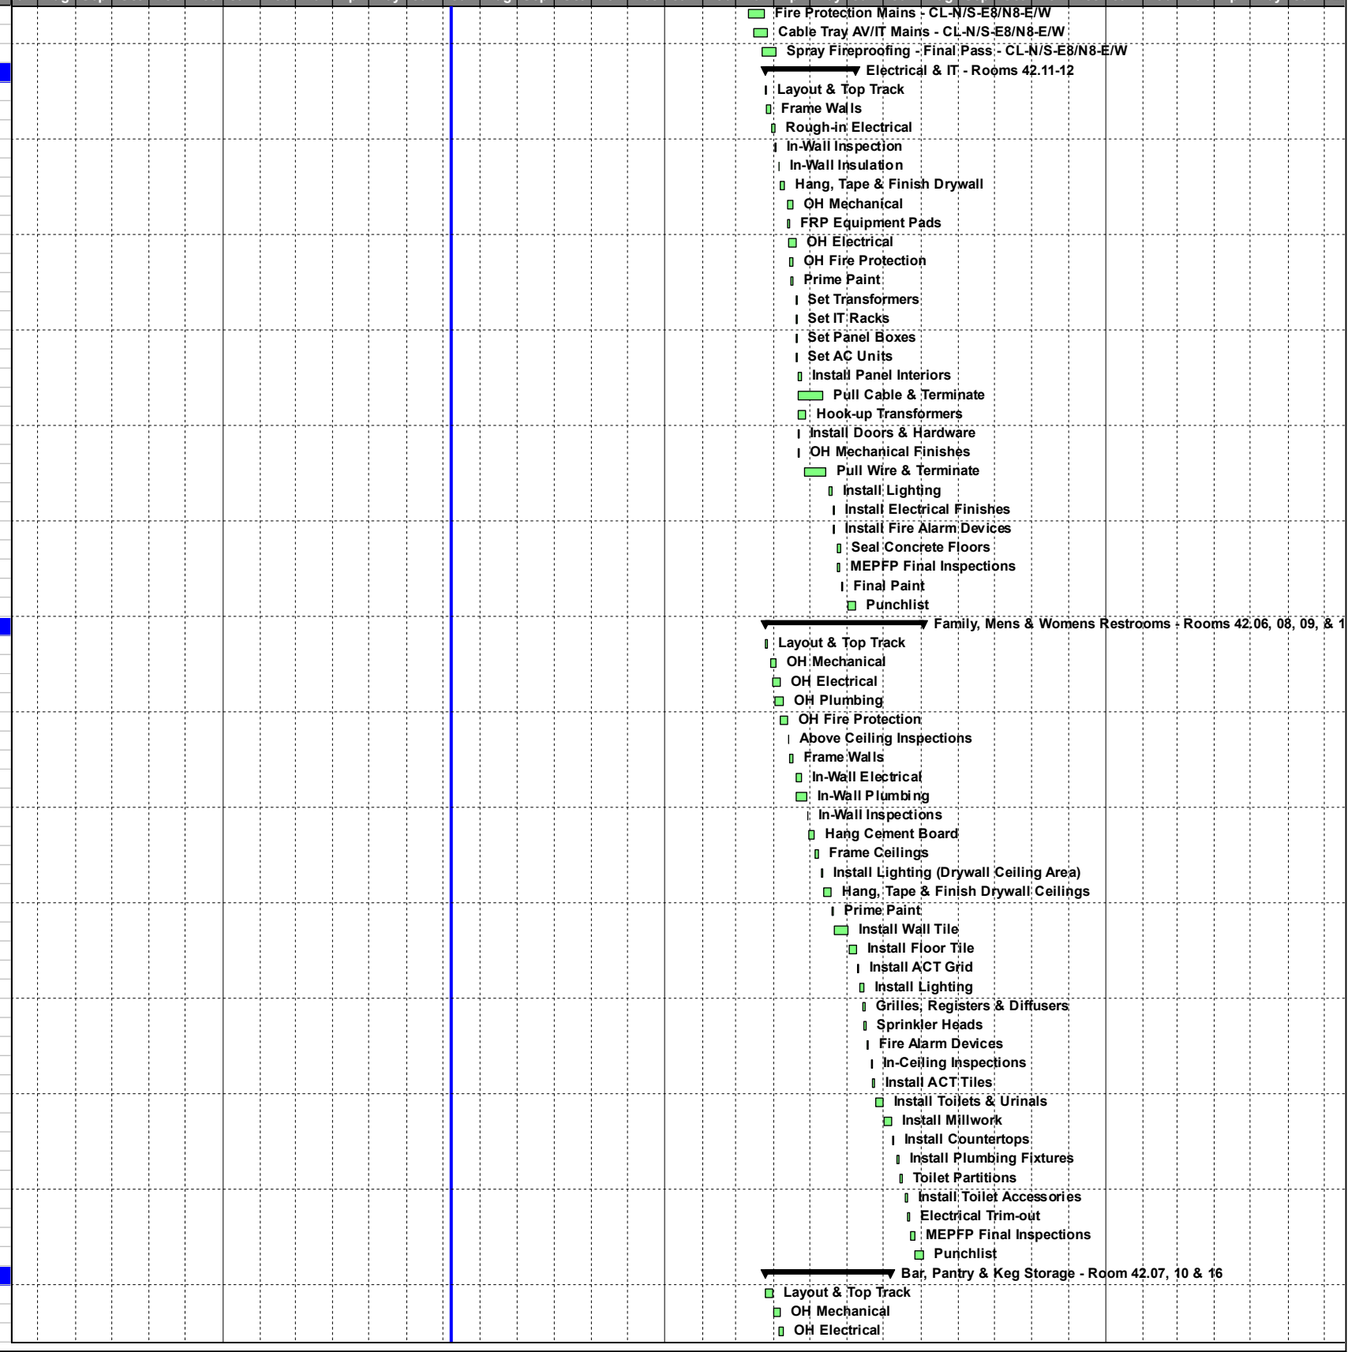

| Activity ID | Activity Name | Original Duration | Remaining Duration | Start | Finish |
|---|---|---|---|---|---|
| A28210 | OH Plumbing | 4 | 4 | 07-Apr-21 | 12-Apr-21 |
| A28220 | OH Fire Protection | 4 | 4 | 09-Apr-21 | 14-Apr-21 |
| A28270 | Frame Ceilings | 2 | 2 | 09-Apr-21 | 12-Apr-21 |
| A28230 | Install Exhaust Hood | 5 | 5 | 15-Apr-21 | 21-Apr-21 |
| A28500 | Frame Walls | 3 | 3 | 15-Apr-21 | 19-Apr-21 |
| A28510 | In-Wall Electrical | 5 | 5 | 20-Apr-21 | 26-Apr-21 |
| A28520 | In-Wall Plumbing | 5 | 5 | 21-Apr-21 | 27-Apr-21 |
| A28240 | Above Ceiling Inspections | 1 | 1 | 22-Apr-21 | 22-Apr-21 |
| A28530 | In-Wall Inspections | 1 | 1 | 28-Apr-21 | 28-Apr-21 |
| A28290 | Hang, Tape & Finish Drywall | 8 | 8 | 29-Apr-21 | 10-May-21 |
| A28250 | Prime Paint | 2 | 2 | 11-May-21 | 12-May-21 |
| A28350 | FRP Wall Panels | 3 | 3 | 13-May-21 | 17-May-21 |
| A28260 | Install ACT Grid | 1 | 1 | 18-May-21 | 18-May-21 |
| A28300 | Install Lighting (Grid Ceilings) | 2 | 2 | 19-May-21 | 20-May-21 |
| A28310 | Sprinkler Heads | 1 | 1 | 21-May-21 | 21-May-21 |
| A28320 | Grilles, Registers & Diffusers | 1 | 1 | 24-May-21 | 24-May-21 |
| A28330 | Fire Alarm Devices | 1 | 1 | 25-May-21 | 25-May-21 |
| A28460 | In-Ceiling Inspections | 1 | 1 | 26-May-21 | 26-May-21 |
| A28340 | Install ACT Tiles | 1 | 1 | 27-May-21 | 27-May-21 |
| A28360 | Resilient Flooring | 5 | 5 | 28-May-21 | 04-Jun-21 |
| A28440 | Install Floor Tile | 5 | 5 | 28-May-21 | 04-Jun-21 |
| A28400 | Millwork | 5 | 5 | 07-Jun-21 | 11-Jun-21 |
| A28470 | Install Doors & Hardware | 1 | 1 | 07-Jun-21 | 07-Jun-21 |
| A28370 | Install Plumbing Fixtures | 2 | 2 | 14-Jun-21 | 15-Jun-21 |
| A28450 | Install Countertops | 2 | 2 | 14-Jun-21 | 15-Jun-21 |
| A28490 | Install Wood Ceiling | 5 | 5 | 14-Jun-21 | 18-Jun-21 |
| A28390 | Food Service Equipment | 5 | 5 | 16-Jun-21 | 22-Jun-21 |
| A28280 | Install Lighting (Drywall Ceilings) | 2 | 2 | 21-Jun-21 | 22-Jun-21 |
| A28380 | Electrical Trim-out | 2 | 2 | 23-Jun-21 | 24-Jun-21 |
| A28410 | Final Paint | 2 | 2 | 25-Jun-21 | 28-Jun-21 |
| A28420 | MEPFP Final Inspections | 2 | 2 | 25-Jun-21 | 28-Jun-21 |
| A28430 | Punchlist | 5 | 5 | 29-Jun-21 | 06-Jul-21 |
| Quad 3 | | 116 | 116 | 19-Feb-21 | 03-Aug-21 |
| MEPFP Mains Rough-in | | 41 | 41 | 19-Feb-21 | 16-Apr-21 |
| OHRI-EL-Q3-1 | Spray Fireproofing - First Pass - CL-N/S-S8/E8-E/W | 10 | 10 | 19-Feb-21 | 04-Mar-21 |
| OHRI-EL-Q3-1 | Install Subroof - CL-N/S-S8/E8-E/W | 15 | 15 | 05-Mar-21 | 25-Mar-21 |
| OHRI-EL-Q3-1 | Mechanical Mains - CL-N/S-S8/E8-E/W | 10 | 10 | 17-Mar-21 | 30-Mar-21 |
| OHRI-EL-Q3-1 | Electrical Mains - CL-N/S-S8/E8-E/W | 10 | 10 | 19-Mar-21 | 01-Apr-21 |
| OHRI-EL-Q3-1 | Plumbing Mains - CL-N/S-S8/E8-E/W | 10 | 10 | 23-Mar-21 | 05-Apr-21 |
| OHRI-EL-Q3-1 | Fire Protection Mains - CL-N/S-S8/E8-E/W | 10 | 10 | 25-Mar-21 | 07-Apr-21 |
| OHRI-EL-Q3-1 | Cable Tray AV/IT Mains - CL-N/S-S8/E8-E/W | 10 | 10 | 29-Mar-21 | 09-Apr-21 |
| OHRI-EL-Q3-1 | Spray Fireproofing - Final Pass - CL-N/S-S8/E8-E/W | 10 | 10 | 05-Apr-21 | 16-Apr-21 |
| Electrical & IT - Rooms 23.11 & 23.12 | | 52 | 52 | 08-Apr-21 | 21-Jun-21 |
| A28860 | Layout & Top Track | 1 | 1 | 08-Apr-21 | 08-Apr-21 |
| A28870 | Frame Walls | 2 | 2 | 09-Apr-21 | 12-Apr-21 |
| A28880 | Rough-in Electrical | 3 | 3 | 13-Apr-21 | 15-Apr-21 |
| A28890 | In-Wall Inspection | 1 | 1 | 16-Apr-21 | 16-Apr-21 |
| A28900 | In-Wall Insulation | 1 | 1 | 19-Apr-21 | 19-Apr-21 |
| A28910 | Hang, Tape & Finish Drywall | 4 | 4 | 20-Apr-21 | 23-Apr-21 |
| A28920 | OH Mechanical | 5 | 5 | 26-Apr-21 | 30-Apr-21 |
| A28950 | FRP Equipment Pads | 3 | 3 | 26-Apr-21 | 28-Apr-21 |
| A28930 | OH Electrical | 5 | 5 | 27-Apr-21 | 03-May-21 |
| A28940 | OH Fire Protection | 3 | 3 | 28-Apr-21 | 30-Apr-21 |
| A29050 | Prime Paint | 2 | 2 | 29-Apr-21 | 30-Apr-21 |
| A28960 | Set Transformers | 2 | 2 | 03-May-21 | 04-May-21 |
| A28970 | Set IT Racks | 2 | 2 | 03-May-21 | 04-May-21 |
| A28980 | Set Panel Boxes | 2 | 2 | 03-May-21 | 04-May-21 |
| A29100 | Set AC Units | 2 | 2 | 03-May-21 | 04-May-21 |
| A28990 | Install Panel Interiors | 3 | 3 | 05-May-21 | 07-May-21 |
| A29010 | Pull Cable & Terminate | 15 | 15 | 05-May-21 | 25-May-21 |
| A29020 | Hook-up Transformers | 5 | 5 | 05-May-21 | 11-May-21 |
| A29070 | Install Doors & Hardware | 2 | 2 | 05-May-21 | 06-May-21 |
| A29110 | OH Mechanical Finishes | 2 | 2 | 05-May-21 | 06-May-21 |
| A29000 | Pull Wire & Terminate | 15 | 15 | 10-May-21 | 28-May-21 |
| A29030 | Install Lighting | 3 | 3 | 01-Jun-21 | 03-Jun-21 |
| A29040 | Install Electrical Finishes | 2 | 2 | 04-Jun-21 | 07-Jun-21 |
| A29120 | Install Fire Alarm Devices | 2 | 2 | 04-Jun-21 | 07-Jun-21 |
| A29060 | Seal Concrete Floors | 3 | 3 | 08-Jun-21 | 10-Jun-21 |
| A29130 | MEPFP Final Inspections | 2 | 2 | 08-Jun-21 | 09-Jun-21 |
| A29080 | Final Paint | 2 | 2 | 11-Jun-21 | 14-Jun-21 |

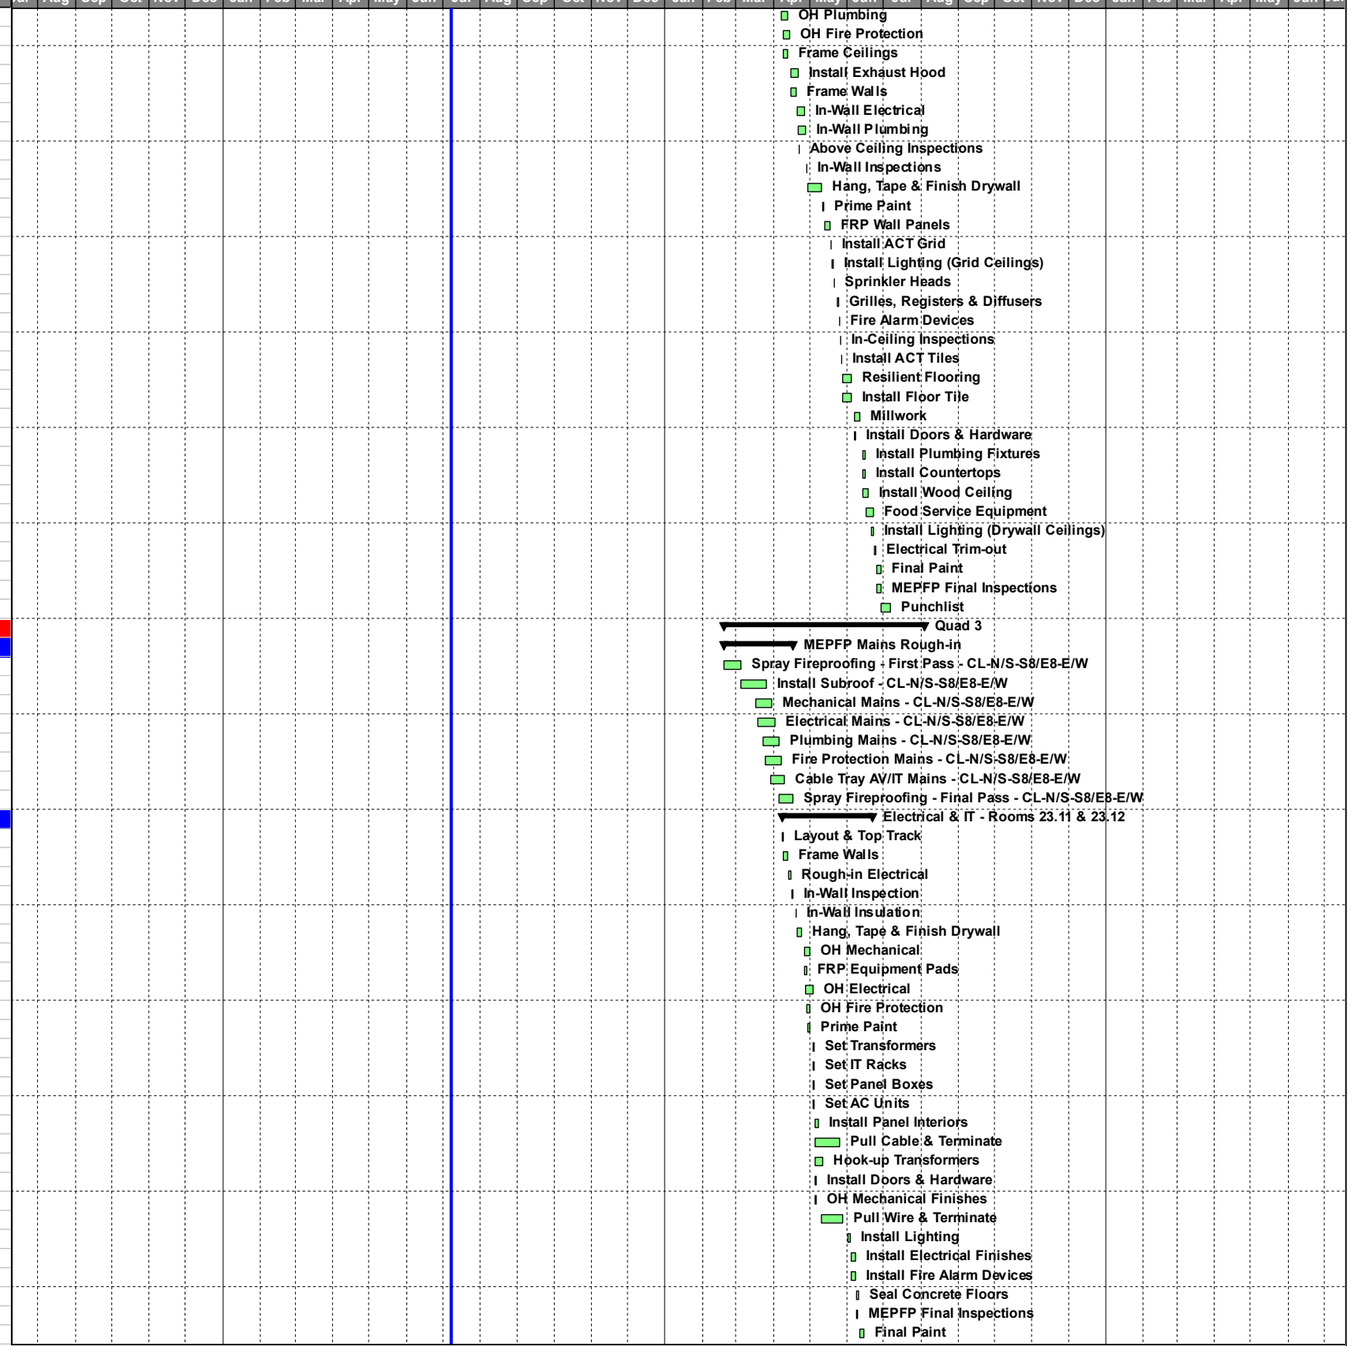

| Activity ID | Activity Name | Original Duration | Remaining Duration | Start | Finish |
|---|---|---|---|---|---|
| A29090 | Punchlist | 5 | 5 | 15-Jun-21 | 21-Jun-21 |
| **Mens & Womens Restrooms - Rooms 21.02 & 23.09** | | **82** | **82** | **08-Apr-21** | **03-Aug-21** |
| A28540 | Layout & Top Track | 2 | 2 | 08-Apr-21 | 09-Apr-21 |
| A28550 | OH Mechanical | 5 | 5 | 12-Apr-21 | 16-Apr-21 |
| A28560 | OH Electrical | 5 | 5 | 14-Apr-21 | 20-Apr-21 |
| A28570 | OH Plumbing | 5 | 5 | 16-Apr-21 | 22-Apr-21 |
| A28580 | OH Fire Protection | 5 | 5 | 20-Apr-21 | 26-Apr-21 |
| A28590 | Above Ceiling Inspections | 1 | 1 | 27-Apr-21 | 27-Apr-21 |
| A28600 | Frame Walls | 3 | 3 | 28-Apr-21 | 30-Apr-21 |
| A28610 | In-Wall Electrical | 5 | 5 | 03-May-21 | 07-May-21 |
| A28620 | In-Wall Plumbing | 8 | 8 | 03-May-21 | 12-May-21 |
| A28630 | In-Wall Inspections | 1 | 1 | 13-May-21 | 13-May-21 |
| A28640 | Hang Cement Board/Drywall | 3 | 3 | 14-May-21 | 18-May-21 |
| A28650 | Install Wall Tile | 7 | 7 | 19-May-21 | 27-May-21 |
| A28850 | Prime Paint | 2 | 2 | 19-May-21 | 20-May-21 |
| A28720 | Install Floor Tile | 5 | 5 | 28-May-21 | 04-Jun-21 |
| A28660 | Install ACT Grid | 2 | 2 | 07-Jun-21 | 08-Jun-21 |
| A28670 | Install Lighting | 2 | 2 | 09-Jun-21 | 10-Jun-21 |
| A28680 | Grilles, Registers & Diffusers | 2 | 2 | 10-Jun-21 | 11-Jun-21 |
| A28690 | Sprinkler Heads | 2 | 2 | 11-Jun-21 | 14-Jun-21 |
| A28700 | Fire Alarm Devices | 2 | 2 | 15-Jun-21 | 16-Jun-21 |
| A28710 | In-Ceiling Inspections | 1 | 1 | 17-Jun-21 | 17-Jun-21 |
| A28730 | Install ACT Tiles | 2 | 2 | 18-Jun-21 | 21-Jun-21 |
| A28830 | Install Luxury Vinyl Tile - First Aid | 5 | 5 | 18-Jun-21 | 24-Jun-21 |
| A28740 | Install Toilets & Urinals | 5 | 5 | 25-Jun-21 | 01-Jul-21 |
| A28750 | Install Millwork | 4 | 4 | 02-Jul-21 | 08-Jul-21 |
| A28760 | Install Countertops | 2 | 2 | 09-Jul-21 | 12-Jul-21 |
| A28770 | Install Plumbing Fixtures | 2 | 2 | 13-Jul-21 | 14-Jul-21 |
| A28780 | Toilet Partitions | 3 | 3 | 15-Jul-21 | 19-Jul-21 |
| A28790 | Install Toilet Accessories | 2 | 2 | 20-Jul-21 | 21-Jul-21 |
| A28800 | Electrical Trim-out | 2 | 2 | 22-Jul-21 | 23-Jul-21 |
| A28810 | MEPFP Final Inspections | 2 | 2 | 26-Jul-21 | 27-Jul-21 |
| A28840 | Final Paint | 2 | 2 | 26-Jul-21 | 27-Jul-21 |
| A28820 | Punchlist | 5 | 5 | 28-Jul-21 | 03-Aug-21 |
| **South Bar - Rooms 24.01** | | **52** | **52** | **08-Apr-21** | **21-Jun-21** |
| A29380 | Layout & Top Track | 5 | 5 | 08-Apr-21 | 14-Apr-21 |
| A29140 | OH Mechanical | 4 | 4 | 15-Apr-21 | 20-Apr-21 |
| A29150 | OH Electrical | 4 | 4 | 19-Apr-21 | 22-Apr-21 |
| A29160 | OH Plumbing | 4 | 4 | 21-Apr-21 | 26-Apr-21 |
| A29170 | OH Fire Protection | 4 | 4 | 23-Apr-21 | 28-Apr-21 |
| A29210 | Frame Ceilings | 2 | 2 | 23-Apr-21 | 26-Apr-21 |
| A29180 | Above Ceiling Inspections | 1 | 1 | 29-Apr-21 | 29-Apr-21 |
| A29200 | Install Suspended Wood Ceiling | 1 | 1 | 30-Apr-21 | 30-Apr-21 |
| A29220 | Install Lighting | 2 | 2 | 03-May-21 | 04-May-21 |
| A29230 | Sprinkler Heads | 1 | 1 | 05-May-21 | 05-May-21 |
| A29240 | Grilles, Registers & Diffusers | 1 | 1 | 06-May-21 | 06-May-21 |
| A29250 | Fire Alarm Devices | 1 | 1 | 07-May-21 | 07-May-21 |
| A29360 | In-Ceiling Inspections | 1 | 1 | 10-May-21 | 10-May-21 |
| A29260 | Resilient Flooring | 5 | 5 | 11-May-21 | 17-May-21 |
| A29300 | Millwork | 5 | 5 | 18-May-21 | 24-May-21 |
| A29370 | Install Doors & Hardware | 1 | 1 | 18-May-21 | 18-May-21 |
| A29190 | Prime Paint | 1 | 1 | 25-May-21 | 25-May-21 |
| A29270 | Install Plumbing Fixtures | 2 | 2 | 25-May-21 | 26-May-21 |
| A29340 | Tile Concession Wall | 3 | 3 | 25-May-21 | 27-May-21 |
| A29350 | Install Countertops | 2 | 2 | 28-May-21 | 01-Jun-21 |
| A29290 | Food Service Equipment | 5 | 5 | 02-Jun-21 | 08-Jun-21 |
| A29280 | Electrical Trim-out | 2 | 2 | 09-Jun-21 | 10-Jun-21 |
| A29310 | Final Paint | 2 | 2 | 11-Jun-21 | 14-Jun-21 |
| A29320 | MEPFP Final Inspections | 2 | 2 | 11-Jun-21 | 14-Jun-21 |
| A29330 | Punchlist | 5 | 5 | 15-Jun-21 | 21-Jun-21 |
| **Bowl Work** | | **105** | **105** | **23-Feb-21** | **21-Jul-21** |
| A1750 | Bowl Ductwork | 25 | 25 | 23-Feb-21 | 29-Mar-21 |
| A32090 | Install Arena Curtains/Half-House | 15 | 15 | 30-Mar-21 | 19-Apr-21 |
| A32100 | Install Blackout Curtains | 15 | 15 | 30-Mar-21 | 19-Apr-21 |
| A32110 | Install Shade System | 15 | 15 | 30-Mar-21 | 19-Apr-21 |
| A1300 | Ice Floor Cure | 20 | 20 | 11-May-21 | 08-Jun-21 |
| A1310 | Install Scoreboard | 30 | 30 | 09-Jun-21 | 21-Jul-21 |
| **Seating** | | **75** | **75** | **30-Mar-21** | **14-Jul-21** |
| A1360 | Seating - Upper Bowl - General Admission | 20 | 20 | 30-Mar-21 | 26-Apr-21 |
| A1380 | Seating - Suite Level - Premium Fixed | 20 | 20 | 15-Apr-21 | 12-May-21 |

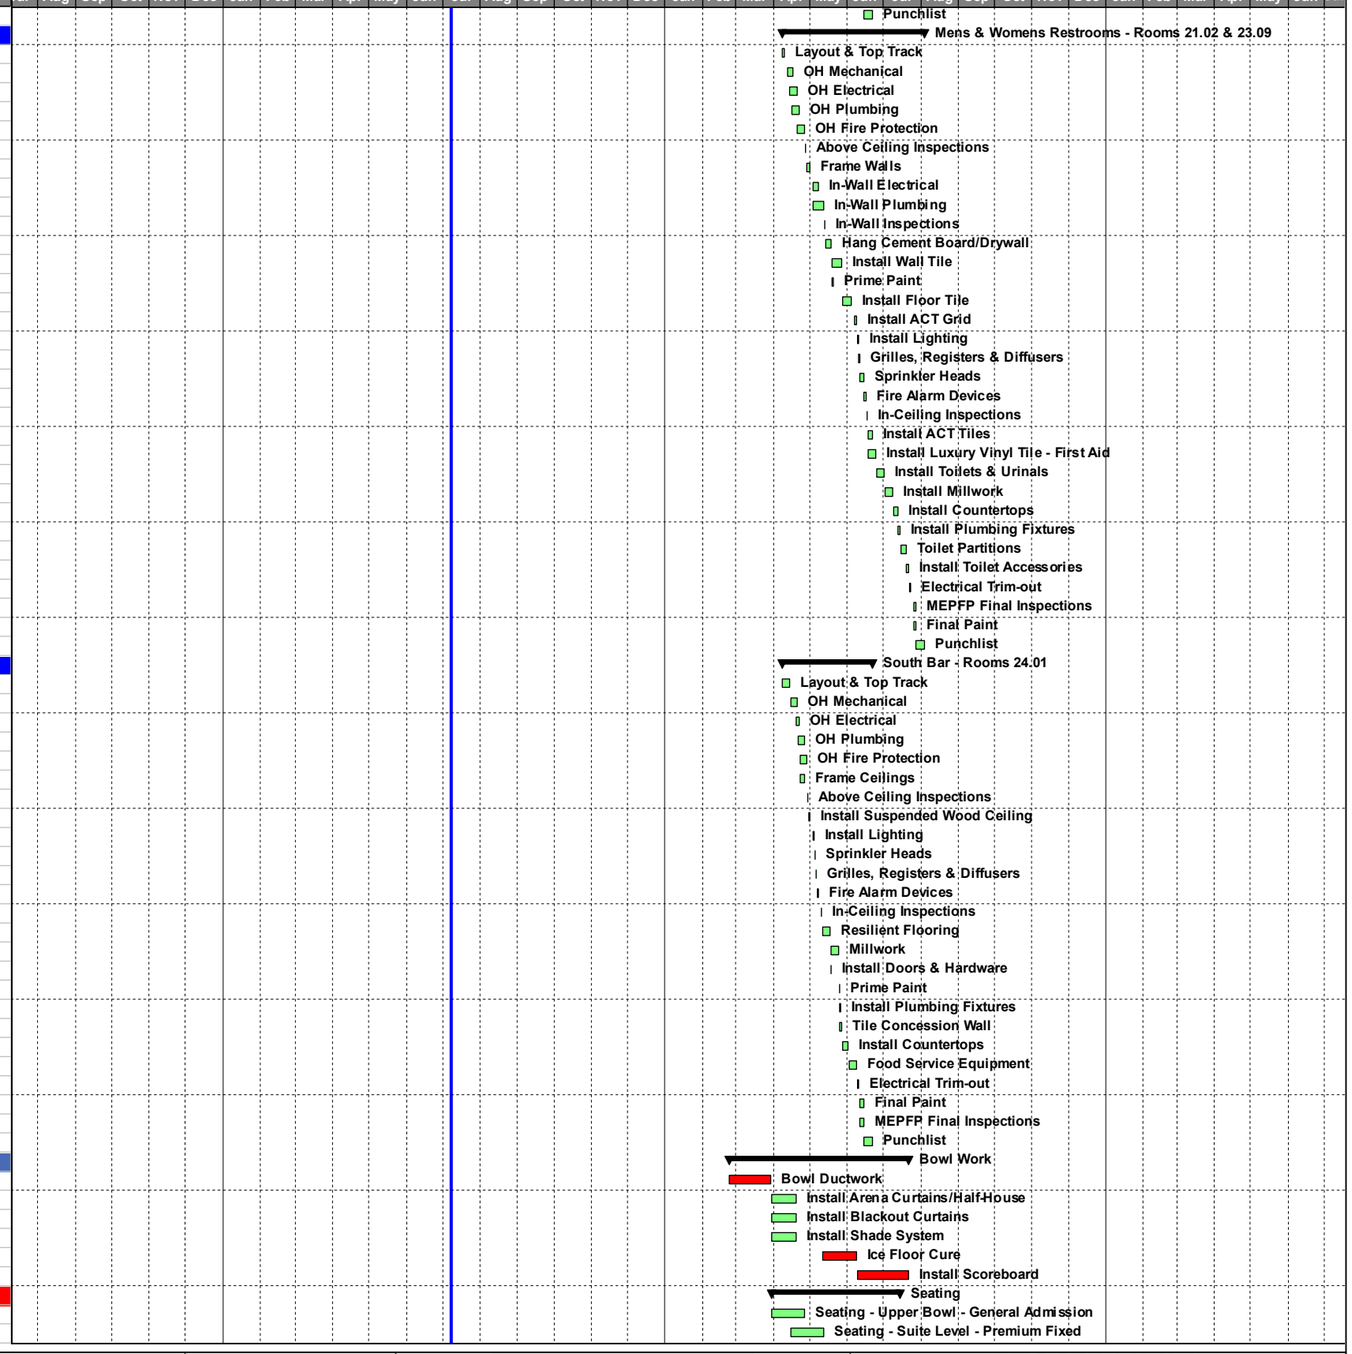

Project: Savannah Arena

**Update - 08-Jul-20**

Date: 09-Jul-20 Time: 11:57

| Activity ID | Activity Name | Original Duration | Remaining Duration | Start | Finish |
|---|---|---|---|---|---|
| A1320 | Seating - Lower Bowl - General Admission | 40 | 40 | 27-Apr-21 | 22-Jun-21 |
| A1390 | Seating - Retractable Seating | 15 | 15 | 09-Jun-21 | 29-Jun-21 |
| A1400 | Seating - Retractable, Telescoping & Removable Platforms | 15 | 15 | 09-Jun-21 | 29-Jun-21 |
| A1410 | Seating - Basketball Setup Retractables/Platforms | 15 | 15 | 09-Jun-21 | 29-Jun-21 |
| A1370 | Seating - Lower Bowl - Club | 15 | 15 | 23-Jun-21 | 14-Jul-21 |
| Testing & Close-out | | 117 | 117 | 06-Jul-21 | 20-Dec-21 |
| A1340 | Elevators & Escalators - State Rough Inspections | 5 | 5 | 06-Jul-21 | 12-Jul-21 |
| A1290 | Start-Up & Commission Systems | 50 | 50 | 09-Jul-21 | 17-Sep-21 |
| A32740 | Fire Alarm Testing | 30 | 30 | 09-Jul-21 | 19-Aug-21 |
| A1350 | Elevators & Escalators - State Final Inspections | 5 | 5 | 13-Jul-21 | 19-Jul-21 |
| A3720 | Final Inspections | 20 | 20 | 20-Aug-21 | 17-Sep-21 |
| A32750 | Superflush | 1 | 1 | 20-Aug-21 | 20-Aug-21 |
| A32730 | Life Safety Inspections | 10 | 10 | 03-Sep-21 | 17-Sep-21 |
| A3710 | Weather | 64 | 64 | 20-Sep-21 | 20-Dec-21 |
| Final Sitework | | 233 | 233 | 04-Jan-21 | 01-Dec-21 |
| A1790 | Install Hardscape / Landscape | 100 | 100 | 12-Jul-21* | 01-Dec-21 |
| Stile Ave | | 126 | 126 | 01-Mar-21 | 25-Aug-21 |
| A32120 | Stiles Ave | 126 | 126 | 01-Mar-21* | 25-Aug-21 |
| Force Main/Lift Station | | 126 | 126 | 01-Feb-21 | 28-Jul-21 |
| A2030 | Install Lift Station / Force Main | 126 | 126 | 01-Feb-21* | 28-Jul-21 |
| Canal Widening | | 90 | 90 | 04-Jan-21 | 07-May-21 |
| A32130 | Canal Widening | 90 | 90 | 04-Jan-21* | 07-May-21 |
| Parking Garage | | 321 | 238 | 28-Feb-20 A | 15-Jun-21 |
| A3300 | Received Parking Deck Drawings - DD Set | 0 | 0 | | 28-Feb-20 A |
| A3310 | Parking Deck Drawings - DD Set | 5 | 0 | 06-Apr-20 A | 12-May-20 A |
| A3340 | Parking Deck Drawings - CD Set | 25 | 0 | 13-May-20 A | 19-Jun-20 A |
| PCI-00060-01 | Unforeseen Condition - Underground Obstruction @ CL B\10 Pile 912 | 5 | 0 | 20-May-20 A | 04-Jun-20 A |
| A3280 | Install Deep Foundations - Parking Garage (248 Total Piles) | 40 | 0 | 20-May-20 A | 17-Jun-20 A |
| A3350 | Price CD Set of Parking Deck Drawings | 15 | 18 | 22-Jun-20 A | 31-Jul-20 |
| A3290 | Install Foundations - Parking Garage | 40 | 40 | 31-Aug-20 | 26-Oct-20 |
| A1420 | Construct Parking Garage | 160 | 160 | 27-Oct-20 | 15-Jun-21 |

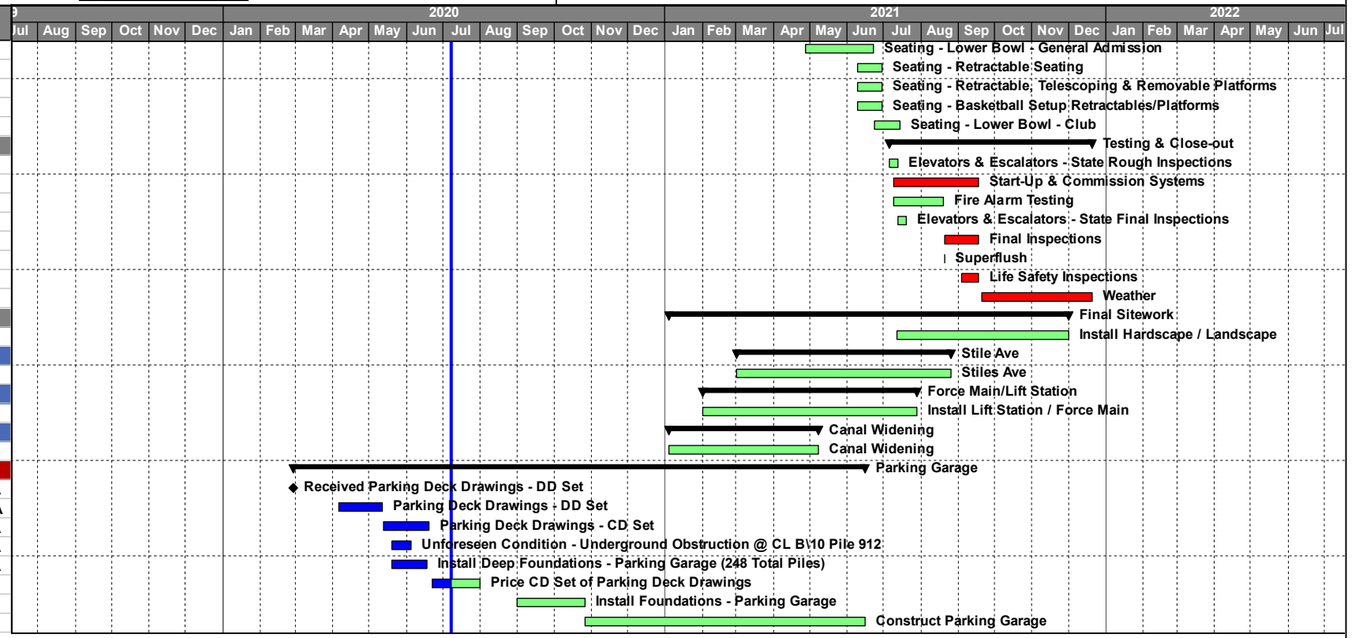

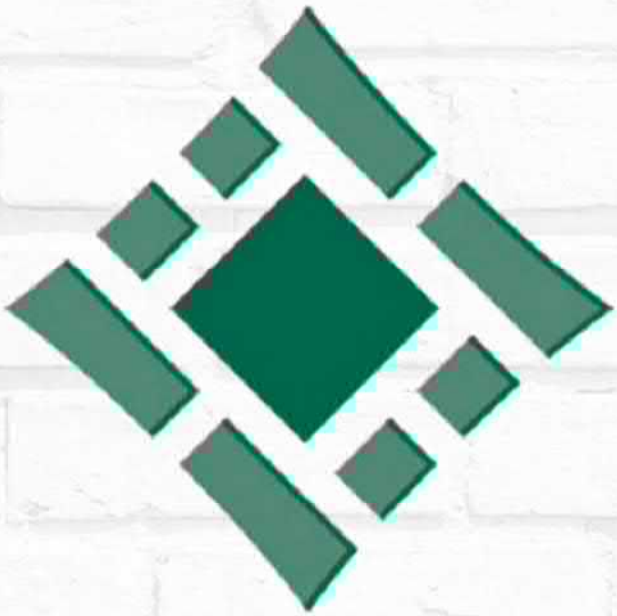

*Section 9*

# *VE Log*

AECOM HUNT

*in association with*

**Brownstone Construction Group**
**Pat Mathis Construction Company**
**A. Riley Consultants**

AECOM HUNT
in association with
Brownstone Construction Group
Pat Mathis Construction Company
A. Riley Consultants

# Value Engineering Log

Savannah Arena
Savannah, GA

| Budget Analysis | Accepted Only | Accepted & Pending |
|---|---|---|
| Current Estimate | $ 148,005,172 | $ 148,005,172 |
| Accepted / Pending Savings | $ - | $ (3,281,048) |
| Revised Estimate | $ 148,005,172 | $ 144,724,124 |
| Target Estimate | | $ - |
| Over / (Under) Target | $ 148,005,172 | $ 144,724,124 |

| Status Legend | Estimate Type Legend |
|---|---|
| I = Incorporated in Current Estimate | EST = AECOM Hunt Estimate |
| A = Accepted | ROM = Rough Order of Magnitude |
| P = Pending Savings | SUB = Sub Input |
| ADD = Pending Add | |
| R = Rejected | |

Estimate Date: 6/12/20
Estimate Type: 100% CD

| | | | | | | $ (3,281,048) | <---Totals with Indirects ---> | | | | $ - | $ - | $ (3,281,048) | $ - | $ - | |
|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|
| Item # | Date | Discipline | Location | Source | Description | Amount | Status | Estimate Type | Ball in Court | Affects Item(s) | Incorporated (I) | Accepted (A) | Pending Savings (P) | Pending Add (Add) | Rejected (R) | Comments |
| | | | | | | $ - | | | | | | | | | | |
| VE-1001 | | | | | Alternate # 01 - Replace tile wainscoting at concourse with painted Gyp | $ (73,413) | P | | | | | | $ (73,413) | | | |
| VE-1002 | | | | | Alternate # 02 - Remove Wood Ceiling (WD-04) from lobby and paint exposed steel. | $ (321,171) | P | | | | | | $ (321,171) | | | |
| VE-1003 | | | | | Alternate # 03 - Change Concourse and Overlook floors from polished concrete to sealed concrete. | $ - | P | | | | | | $ - | | | |
| VE-1004 | | | | | Alternate # 04 - Replace Lobby Tile Walls (TW-03) with painted gyp. | $ (42,360) | P | | | | | | $ (42,360) | | | |
| VE-1005 | | | | | Alternate # 05 - Reduce wall covering at North Club by 75% and replace with painted gyp | $ (4,387) | P | | | | | | $ (4,387) | | | |
| VE-1006 | | | | | Alternate # 06 - Shell the East Club | $ (410,226) | P | | | | | | $ (410,226) | | | |
| VE-1007 | | | | | Alternate # 07 - Omit all under counter lighting at the North Club | $ (800) | P | | | | | | $ (800) | | | |
| VE-1008 | | | | | Alternate # 08 - Shell the home locker space | $ (555,709) | P | | | | | | $ (555,709) | | | |
| VE-1009 | | | | | Alternate # 09 - Reduce Ribbon Boards to 40' Section at North and South. | $ (282,479) | P | | | | | | $ (282,479) | | | |
| VE-1010 | | | | | Reductions of food service equipment back to DD budget | $ (450,000) | P | | | | | | $ (450,000) | | | Based on Ricca's food service estimate and bids |
| VE-1011 | | | | | Reduction of dasher system from NHL to AHL standards | $ - | R | | | | | | | | $ - | |
| VE-1012 | | | | | Deduct if Ice floor cover not required | $ (150,000) | P | | | | | | $ (150,000) | | | |
| VE-1013 | | | | | Deduct to remove the East Club Bar Ceiling element. | $ - | R | | | | | | | | $ - | Included in shell East Club VE |
| VE-1014 | | | | | Replace the terrazzo at grand stair steps with tile | $ (100,000) | P | | | | | | $ (100,000) | | | |
| VE-1015 | | | | | Reduce Polished Concrete from a level 3 finish to a Level 1 finish | $ - | R | | | | | | | | $ - | Minimal savings |
| VE-1016 | | | | | Use Concrete Curb and Gutter ILO Granite | $ - | P | | | | | | $ - | | | |
| VE-1017 | | | | | Provide Solid Surface Tops in lieu of Quartz Tops | $ (161,858) | P | | | | | | $ (161,858) | | | Provide Corian solid surface (any color from groups 1-3) in lieu of specified quartz materials (QZ-1 through QZ-10) |
| VE-1018 | | | | | Replace TF-01 at GA restrooms (Service, Main Concourse, and Terrace) with polished concrete. | $ - | P | | | | | | $ - | | | |
| VE-1019 | | | | | Review of blackout curtains/motorized window shades | $ - | P | | | | | | $ - | | | |
| VE-1020 | | | | | Roofing - Use Lightweight Insulated Concrete | $ (300,000) | P | | | | | | $ (300,000) | | | |
| VE-1021 | | | | | Roofing - Mechanically attach roof system | $ (150,000) | P | | | | | | $ (150,000) | | | |
| VE-1022 | | | | | Change of exterior brick from Belden to Cherokee Brick | $ (72,432) | P | | | | | | $ (72,432) | | | |
| VE-1023 | | | | | | $ - | P | | | | | | $ - | | | |
| VE-1024 | | | | | | $ - | P | | | | | | $ - | | | |
| VE-1025 | | | | | | $ - | P | | | | | | $ - | | | |
| VE-1026 | | | | | | $ - | P | | | | | | $ - | | | |
| VE-1027 | | | | | | $ - | P | | | | | | $ - | | | |



Printed: 7/9/2020 3:09 PM

AECOM HUNT
in association with
Brownstone Construction Group
Pat Mathis Construction Company
A. Riley Consultants

# Value Engineering Log

Savannah Arena
Savannah, GA

| Budget Analysis | Accepted Only | Accepted & Pending |
|---|---|---|
| Current Estimate | $ 148,005,172 | $ 148,005,172 |
| Accepted / Pending Savings | $ - | $ (3,281,048) |
| Revised Estimate | $ 148,005,172 | $ 144,724,124 |
| Target Estimate | | $ - |
| Over / (Under) Target | $ 148,005,172 | $ 144,724,124 |

| Status Legend | Estimate Type Legend |
|---|---|
| I = Incorporated in Current Estimate | EST = AECOM Hunt Estimate |
| A = Accepted | ROM = Rough Order of Magnitude |
| P = Pending Savings | SUB = Sub Input |
| ADD = Pending Add | |
| R = Rejected | |

Estimate Date: 6/12/20
Estimate Type: 100% CD

| | | | | | | $ (3,281,048) | <---Totals with Indirects ---> | | | | $ - | $ - | $ (3,281,048) | $ - | $ - | |
|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|
| Item # | Date | Discipline | Location | Source | Description | Amount | Status | Estimate Type | Ball in Court | Affects Item(s) | Incorporated (I) | Accepted (A) | Pending Savings (P) | Pending Add (Add) | Rejected (R) | Comments |
| VE-1028 | | | | | | $ - | P | | | | | | $ - | | | |
| VE-1029 | | | | | | $ - | P | | | | | | $ - | | | |
| VE-1030 | | | | | | $ - | P | | | | | | $ - | | | |
| | | | | | | | | | | | | | | | | |
| | | | | | | | | | | | | | | | | |
| | | | | | FILTERED SUBTOTALS | $ (3,074,835) | | | | | $ - | $ - | $ (3,074,835) | $ - | $ - | |
| | | | | | DIRECT COST TOTALS | $ (3,074,835) | | | | | $ - | $ - | $ (3,074,835) | $ - | $ - | |
| | | | | 2.250% | Construction Contingency | $ (69,184) | | | | | $ - | $ - | $ (69,184) | $ - | $ - | |
| | | | | 0.700% | General Liability | $ (22,967) | | | | | $ - | $ - | $ (22,967) | $ - | $ - | |
| | | | | 0.800% | Bond | $ (26,248) | | | | | $ - | $ - | $ (26,248) | $ - | $ - | |
| | | | | 2.750% | CM Fee | $ (87,814) | | | | | $ - | $ - | $ (87,814) | $ - | $ - | |
| | | | | | TOTALS WITH INDIRECTS | $ (3,281,048) | | | | | $ - | $ - | $ (3,281,048) | $ - | $ - | |



Printed: 7/9/2020 3:09 PM
